

Atkins China Limited
Chief Resident Engineer's Office
No. 17 Cheung Chau Sai Tai Road
Cheung Chau, New Territories
Hong Kong

Attn: Mr. Elwyn Lo – Chief Resident Engineer

Your Reference

Contract No. CM 04/2021

Our Reference
AFK/EC/TC/LL/kl/
T601424122/L087

**Independent Environmental Checker for Environmental Monitoring Works for
Upgrading of Cheung Chau Sewage Treatment and Disposal Facilities**

Environmental Permit No. EP-488/2014/A

Mott MacDonald
3/F Manulife Tower
348 Kwun Tong Road
Kwun Tong
Kowloon
Hong Kong

Monthly EM&A Report for August 2024 (Rev. 2)

13 September 2024

T +852 2828 5757
F +852 2827 1823
mottmac.hk

By Email


Dear Sir,

I refer to the Monthly EM&A Report for August 2024 (Rev. 2) under the captioned Project, which was certified on 13 September 2024 by the Environmental Team Leader appointed under Condition 2.1 of Environmental Permit No. EP-488/2014/A (hereafter referred to as "EP").

I hereby verify the abovementioned submission in accordance with EP Conditions 1.9 and 4.4.

Should you have any queries regarding the captioned or require any further information, please contact the undersigned at 2828 5751.

Yours faithfully
for MOTT MACDONALD HONG KONG LIMITED



Liz Lo
Independent Environmental Checker
T +852 2828 5751

Liz.Lo@mottmac.com

Encl.

c.c. DSD
Atkins China Limited

Acuity Sustainability Consulting Limited
Build King Civil Engineering Limited

Ir. QIU Yujing, Eugene By Email
Ir. Dennis Cheung / By Email
Ir. Winnie Choi
Mr. Kevin Li By Email
Mr. Alvin Lei / By Email
Mr. Lawrence Lam



Drainage Services Department

The Government of the Hong Kong Special Administrative Region



Contract No. DC/2019/07

**Environmental Monitoring Works for
Outlying Islands Sewerage Stage 2 –
Upgrading of Cheung Chau Sewage Treatment and
Disposal Facilities**

**37th Monthly Environmental Monitoring and Audit Report –
August 2024**

Document No.

ASCL	/	210168173	/	EMA082024	/	2
Publisher		Project Code		Sequential No.		Revision Index

	Reviewed by:	Certified by:
Name	Tandy TSE	Kevin LI
Position	Environmental Team Member	Environmental Team Leader
Signature		
Date:	9/9/2024	13/9/2024

REVISION HISTORY

REV.	DESCRIPTION OF MODIFICATION	DATE
0	First Issue for Comments	10 September 2024
1	Updated according to IEC's comments	12 September 2024
2	Updated according to IEC's further comments.	13 September 2024

CONTENTS

Executive Summary.....	4
1. Introduction.....	7
2. Air Quality.....	10
3. Noise.....	17
4. Water Quality.....	22
5. Waste Management.....	23
6. Landscape & Visual	25
7. Site Inspection Audit	26
8. Environmental Non-conformance	26
9. Conclusion.....	28
Appendix A <u>Location Plan and Noise and Dust Monitoring Stations</u>	
Appendix B <u>Construction Programme</u>	
Appendix C <u>Calibration Certificates (Air Monitoring)</u>	
Appendix D <u>Monitoring Data (Air)</u>	
Appendix E <u>Calibration Certificates (Noise)</u>	
Appendix F <u>Monitoring Data (Noise)</u>	
Appendix G <u>Implementation Schedule</u>	
Appendix H <u>Summary of All Complaints Received, Notification of Summons and Successful Prosecutions</u>	
Appendix I <u>EM&A Monitoring Schedules in the Reporting Period and the Next Reporting Period (Tentative)</u>	

EXECUTIVE SUMMARY

- A.1 Pursuant to the Environmental Impact Assessment Ordinance (EIAO), the Director of Environmental Protection (DEP) granted the Environmental Permit (No. EP-488/2014/A) to DSD for the Project.
- A.2 Upon the requirement of the Environmental Permit (EP), the Monthly EM&A Monitoring Report shall be submitted to the DEP within 10 working days after the end of the reporting month. The submissions shall be verified by the Independent Environmental Checker (IEC) and complied with the requirements set out in the Environmental Monitoring and Audit (EM&A) Manual before submission to the DEP as stipulated in Condition 4.4 of the EP.
- A.3 The commencement date of the Project was 6 August 2021. Impact environmental monitoring of 24-hour TSP, 1-hour TSP and noise was conducted as stipulated in Condition 4.2 of the EP. This is the 37th Monthly EM&A Report for the Project summarizing the monitoring results and audit findings of the EM&A programme at selected locations at and around Cheung Chau during the reporting period from 1 to 31 August 2024.
- A.4 Key activities carried out in this reporting period for the Project included the followings:
- Trial Pit and Ground Investigation
 - Construction of MBR Treatment Facilities
 - MVAC Installation Works
 - Lifting Appliance Installation for Sludge Digester Building
 - FS Installation
 - Construction of Preliminary Treatment Facilities
 - Laying of Underground Pipes, Utilities and Construction of Manholes
 - Mechanical Installation of MBR
 - Temporary Diversion Works from Inlet Chamber to Preliminary Treatment Facilities
- A.5 The major environmental impacts brought by the above construction works include:
- Construction dust and noise generation from construction works and piling works
 - Wastewater generated from construction activities
 - Waste generation from the construction activities
- A.6 The key environmental mitigation measures implemented for the Project in this reporting period associated with the above construction works include:
- Dust suppression by regular wetting and water spraying for construction works
 - Reduction of noise from equipment and machinery on-site
 - Mitigation measures preventing seepage of muddy water
 - Sorting and storage of general refuse and construction waste
- A.7 Five (5) sessions of air monitoring were carried out at all designated monitoring locations. No exceedance of Action or Limit Level was recorded.
- A.8 Four (4) sessions of noise monitoring were carried out at all designated monitoring locations. No exceedance of Action or Limit Level was recorded.
- A.9 Results of the monitoring for air quality and airborne noise are given in **Table A** and **Table B** as follows:

Table A – Monitoring Results (Dust)

Locations	Dust in µg/m ³			
	Average		Range	
	TSP-1hr	TSP-24hr	TSP-1hr	TSP-24hr
A1a	60	61	50 – 69	33 – 120
A2a	58	63	48 - 69	35 - 124

Table B – Monitoring Results (Noise)

Locations	Noise in dB(A)	
	Average	Range
	L _{eq} (30 min) (7:00-19:00)	L _{eq} (30 min) (7:00-19:00)
N2a	68.4	65.6 – 70.9
N3a	72.6	71.2 – 73.9

s: +3 dB(A) free-field corrections have been made to N3a.

- A.10 According to Section 4.3.3 of the EM&A Manual, Site inspection shall be carried out by the ET and attention shall be paid to the mitigation measures recommended for water pollution control. Weekly site inspections were carried out and no non-compliance was spotted during the reporting month.
- A.11 According to the EM&A Manual section 4.4.1, baseline water quality monitoring should be carried out prior to the operation of the upgraded Cheung Chau STW to establish a baseline ambient condition. A six-month baseline water quality covering both dry and wet seasons is commenced in June 2024. Baseline water quality monitoring was carried out on 8 and 22 in August 2024.
- A.12 Waste management mitigation measures were properly implemented in the reporting period.
- A.13 For cultural heritage impact, as this Project does not involve proposed sewers works, according to Section 6.1.5 of the EM&A Manual, no EM&A requirement is considered necessary during the construction and operational phase of upgrading of Cheung Chau STW and Pak She SPS.
- A.14 The recommended landscape and visual mitigation measures were properly implemented in the reporting period.
- A.15 Weekly site inspections of the construction work by ET were carried out on 6, 13, 20 and

26 August 2024.

- A.16 No environmental complaint was received during the reporting period.
- A.17 No notification of summons or prosecution was received in the reporting period.
- A.18 A map of the construction site and monitoring locations are shown in [Appendix A](#).
- A.19 The summary of permit / licences for this Project is presented in **Table C** below:

Table C – Summary of Permit / Licences

Nature	Number	Issue Date	Expiry Date
Environmental Permit	EP-488/2014/A	13/05/2021	N/A
Notification pursuant to Air Pollution Control (Construction Dust) Regulation	462303	26/11/2020	N/A
Waste Disposal Billing Account	7039094	7/12/2020	N/A
	7040870	9/07/2024	10/10/2024
Chemical Waste Producer	5213-920-B2500-05	31/12/2020	N/A
Effluent Discharge Licence under Water Pollution Control Ordinance	WT00038597-2021	20/08/2021	31/08/2026

1. INTRODUCTION

1.1. BACKGROUND

- 1.1.1. Drainage Services Department (DSD) has contracted Build King Civil Engineering Limited (BK) to carry out the Outlying Islands Sewerage Stage 2 – Upgrading of Cheung Chau Sewage Treatment and Disposal Facilities under Contract No. DC/2019/07.
- 1.1.2. Acuity Sustainability Consulting Limited (ASCL) is commissioned by BK to undertake the Environmental Team (ET) services as required and/or implied, both explicitly and implicitly, in the Environmental Permit (EP), Environmental Impact Assessment Report (EIA Report) (Register No. AEIAR-181/2013) and Environmental Monitoring and Audit Manual (EM&A Manual) for the Project; and to carry out the Environmental Monitoring and Audit (EM&A) programme in fulfillment of the EIA Report's EM&A requirements under Agreement No. CE 15/2010 (DS).


1.2. PROJECT DESCRIPTION

- 1.2.1 The purpose of the Project is to upgrade the sewerage collection, treatment and disposal facilities in Cheung Chau in order to cater for the projected ultimate population and planned developments in Cheung Chau to meet the increased demand and to achieve more stringent effluent quality standards. The key elements of the proposed works for the Project will include as follows:
- Expansion of the sewage treatment capacity and upgrading of the treatment level of the existing Cheung Chau Sewage Treatment Works (Cheung Chau STW) to secondary treatment level; and
 - Expansion of the pumping capacity of the existing Pak She Sewage Pumping Station (Pak She SPS).

1.3. PROJECT ORGANIZATION STRUCTURE

1.3.1 The Project organization structure is presented in **Figure 1.1**.

Figure 1.1 Project Organization Structure

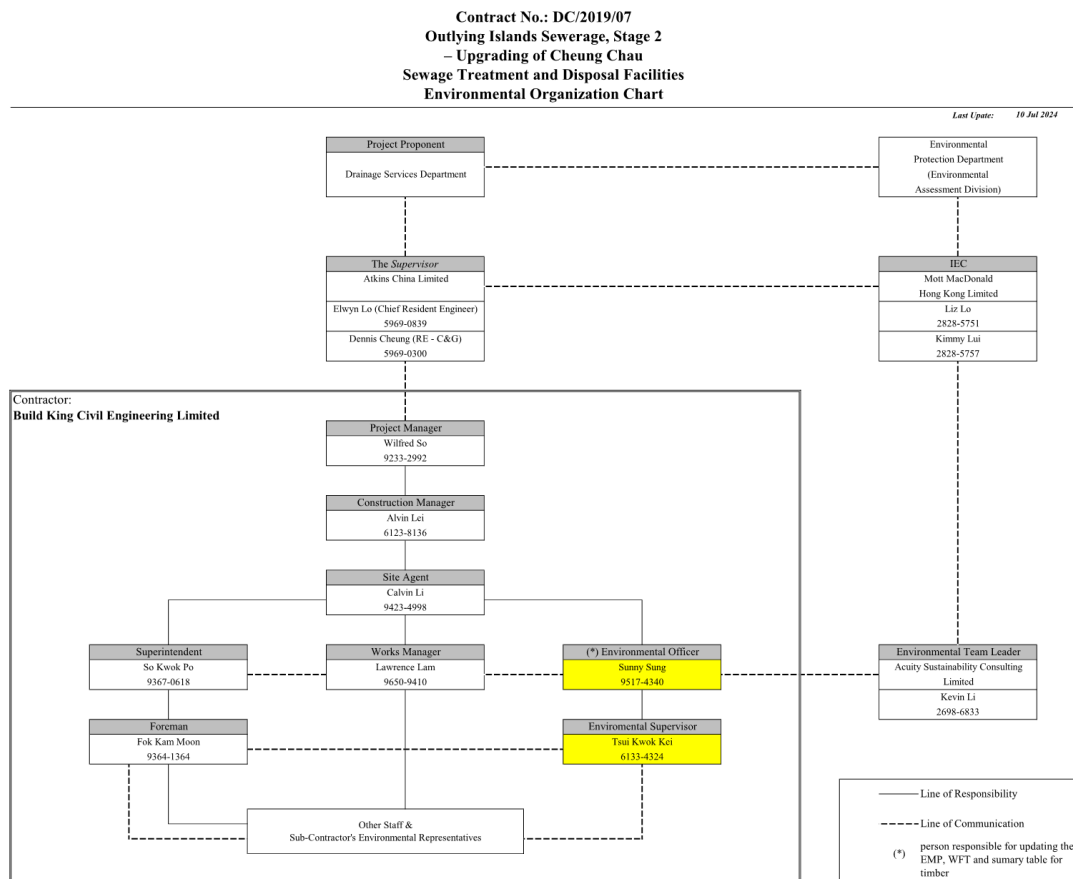

Party	Role	Contact Person	Phone No.
Drainage Services Department HKSAR (DSD)	Project Proponent	QIU Yujiing, Eugene	2594 7298
Supervisor / Supervisor's Representative (Atkins China Limited)	Resident Engineer	Dennis Cheung	2675 3910
Environmental Team (Acuity Sustainability Consulting Limited)	Environmental Team Leader	Kevin Li	2698 6833
Independent Environmental Checker (Mott Macdonald Hong Kong Limited)	Independent Environmental Checker	Liz Lo	2828 5751
Contractor (Build King Construction Limited)	Site Agent Environmental Officer Environmental Supervisor	Calvin Li Sunny Sung Tsui Kwok Kei	9423 4998 9517 4340 6133 4324

1.4. SUMMARY OF CONSTRUCTION WORKS

1.4.1 Details of the major construction activities undertaken in this and the next reporting periods are shown below. The construction programme is presented in **Appendix B**.

Key activities carried out in this reporting period for the Project included the followings:

- Trial Pit and Ground Investigation
- Construction of MBR Treatment Facilities
- MVAC Installation Works
- Lifting Appliance Installation for Sludge Digester Building
- FS Installation
- Construction of Preliminary Treatment Facilities
- Laying of Underground Pipes, Utilities and Construction of Manholes
- Mechanical Installation of MBR
- Temporary Diversion Works from Inlet Chamber to Preliminary Treatment Facilities

Key activities to be carried out in the next reporting period for the Project included the followings:

- Trial Pit and Ground Investigation
- Construction of MBR Treatment Facilities
- MVAC Installation Works
- Lifting Appliance Installation for Sludge Digester Building
- FS Installation
- Construction of Preliminary Treatment Facilities
- Laying of Underground Pipes, Utilities and Construction of Manholes
- Mechanical Installation of MBR
- Temporary Diversion Works from Inlet Chamber to Preliminary Treatment Facilities

1.5. PURPOSE OF THE REPORT

1.5.1 According to the EM&A Manual for the Project, monitoring for air quality and noise should be conducted throughout the construction period of the Project.

1.5.2 The EM&A requirements for environmental monitoring are set out in the EM&A Manual. Environmental aspect of construction noise and air quality were identified as the key issues requiring implementation of monitoring programme during the construction phase of the Project.

1.5.3 This report is summarizing the monitoring results and audit findings of the EM&A programme during the reporting period from **1 August to 31 August 2024**.

2. AIR QUALITY

2.1. AIR QUALITY PARAMETERS

2.1.1 The air quality parameters to be monitored includes:

- 24-hour TSP;
- 1-hour TSP; and the

2.2. MONITORING CRITERIA

2.2.1 Dust monitoring was carried out at the designated monitoring location at least once in every six-days to obtain 24-hour TSP samples. One-hour TSP sampling shall also be done at least 3 times in every six-days while the highest dust impact occurs.

2.2.2 Before commencing the impact monitoring, the ET Leader shall inform the IEC of the impact monitoring programme such that the IEC can conduct on-site audit to ensure accuracy of the impact monitoring results.

2.2.3 In case of non-compliance with the air quality criteria, additional monitoring as specified in the Action Plan shall be conducted within 24 hours after the result is obtained. This additional monitoring shall be continued until the excessive dust emission or the deterioration in air quality is rectified.

2.3. MONITORING REQUIREMENTS AND EQUIPMENT

2.3.1 1-hour and 24-hour TSP levels were measured to indicate the impacts of construction dust on air quality. The 24-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the Title 40 of the United States Code of Federal Regulations, Chapter 1 (Part 50), Appendix B.

2.3.2 High volume samplers (HVSs) in compliance with the following specifications shall be used for carrying out the 1-hour and 24-hour TSP monitoring:

- (i) 0.6 – 1.7 m³ per minute adjustable flow range;
- (ii) equipped with a timing / control device with +/- 5 minutes accuracy for 24 hours operation;
- (iii) installed with elapsed-time meter with +/- 2 minutes accuracy for 24 hours operation;
- (iv) capable of providing a minimum exposed area of 406 cm²;
- (v) flow control accuracy: +/- 2.5% deviation over 24-hour sampling period;
- (vi) equipped with a shelter to protect the filter and sampler;
- (vii) incorporated with an electronic mass flow rate controller or other equivalent devices;
- (viii) equipped with a flow recorder for continuous monitoring;
- (ix) provided with a peaked roof inlet;
- (x) incorporated with a manometer;
- (xi) able to hold and seal the filter paper to the sampler housing at horizontal position;
- (xii) easily changeable filter; and
- (xiii) capable of operating continuously for a 24-hour period.

- 2.3.3 The ET is responsible for provision of the monitoring equipment. They shall ensure that sufficient number of HVSs with an appropriate calibration kit is available for carrying out the impact monitoring, and ad hoc monitoring. The HVSs shall be equipped with an electronic mass flow controller and be calibrated against a traceable standard at regular intervals. All the equipment, calibration kit, filter papers, etc., shall be clearly labelled.
- 2.3.4 Initial calibration of dust monitoring equipment shall be conducted upon installation and thereafter at bi-monthly intervals. The transfer standard shall be traceable to the internationally recognized primary standard and be calibrated annually. The concerned parties such as ER shall properly document the calibration data for future reference. All the data shall be converted into standard temperature and pressure condition.
- 2.3.5 If the ET proposes to use a direct reading dust meter to measure 1-hour TSP levels, he shall submit sufficient information to the ER to prove that the instrument is capable of achieving a comparable result to the HVS. The instrument shall also be calibrated regularly, and the 1-hour sampling shall be determined periodically by the HVS to check the validity and accuracy of the results measured by direct reading method.

Laboratory Measurement / Analysis

- 2.3.6 A clean laboratory with constant temperature and humidity control and equipped with necessary measuring and conditioning instruments to handle the dust samples collected, shall be available for sample analysis, and equipment calibration and maintenance. The laboratory shall be HOKLAS accredited.
- 2.3.7 Filter paper of size 8" x 10" shall be labelled before sampling. It shall be a clean filter paper with no pinholes and shall be conditioned in a humidity-controlled chamber for over 24-hours and be pre-weighed before use for the sampling.
- 2.3.8 After sampling, the filter paper loaded with dust shall be kept in a clean and tightly sealed plastic bag. The filter paper shall then be returned to the laboratory for reconditioning in the humidity-controlled chamber followed by accurate weighing by an electronic balance with readout down to 0.1 mg. The balance shall be regularly calibrated against a traceable standard.

2.3.9 1-hour TSP levels and 24-hour TSP had been measured with direct reading dust meters and High Volume Samplers respectively. The details of equipment used for monitoring are listed in **Table 2.1**, and the calibration certificates are presented in [Appendix C](#).

Table 2.1 Equipment Used for Air Quality Monitoring

Equipment	Model	Serial Number
Portable Dust Meter – 1-hour TSP	SIBATA Digital Dust Indicator (Model: LD-5R)	2Y6550 2Y6549
High Volume Samplers – 24-hour TSP	Tisch TE-5170X High Volume Air Sampler	1048 1085
Calibrator Kit	Tisch TE-5025A Calibration Kit	3465

2.4. MONITORING LOCATIONS

2.4.1 The ET agreed with the ER and the IEC on the position of the HVS for the installation of the monitoring equipment. When positioning the samplers, the following points were noted:

- (i) a horizontal platform with appropriate support to secure the samplers against gusty wind shall be provided;
- (ii) no two samplers shall be placed less than 2 meters apart;
- (iii) the distance between the sampler and an obstacle, such as buildings, must be at least twice the height that the obstacle protrudes above the sampler;
- (iv) a minimum of 2 meters of separation from walls, parapets and penthouses is required for rooftop samplers;
- (v) a minimum of 2 meters separation from any supporting structure, measured horizontally is required;
- (vi) no furnace or incinerator flue is nearby;
- (vii) airflow around the sampler is unrestricted;
- (viii) the sampler is more than 20 meters from the dripline;
- (ix) any wire fence and gate, to protect the sampler, shall not cause any obstruction during monitoring
- (x) permission must be obtained to set up the samplers and to obtain access to the monitoring stations; and
- (xi) a secured supply of electricity is needed to operate the samplers.

2.4.2 The proposed dust monitoring station is presented in **Table 2.2** and the respective locations are shown in Figure 2.1 of the EM&A Manual.

Table 2.2 Proposed Dust Monitoring Stations


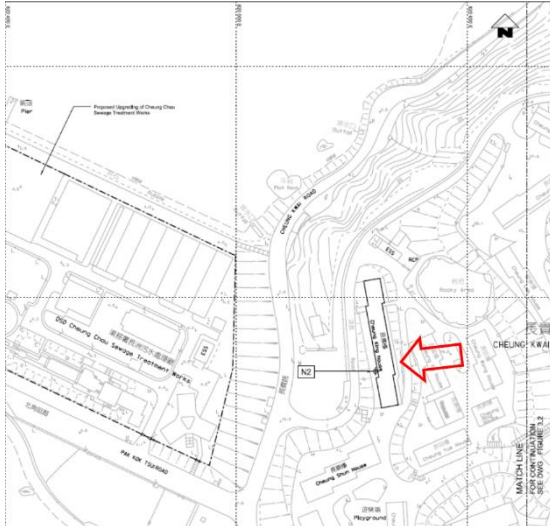
ID No.	Location	Nature of Use	Remarks
A1	Cheung King House, Cheung Kwai Estate	Residential	Specified in the EM&A Manual but proposed to change location
A1a	The admin building inside the construction site	Institutional	Proposed alternative location to replace A1
A2	Cheung Chau Slaughter House	Slaughter house	Specified in the EM&A Manual but proposed to change location
A2a	The existing outfall pumping station inside the construction site	Institutional	Proposed alternative location to replace A2

2.4.3 As secured electricity supply was not able to be provided at Monitoring Station A1, Monitoring Station A1a was then proposed. The proposed Monitoring Station A1a is the Admin Building inside the construction site. It is located at a similar direction as A1 from the construction site, but much closer to any major dust emission source than A1.



2.4.4 Monitoring Station A2 is now abandoned, only limited access can be granted and power supply cannot be guaranteed which may not be feasible to be a monitoring location. An alternative location A2a, which is the existing outfall pumping station Building inside the construction site. Location A2a is about 30 meters away from the Cheung Chau slaughter house and closer to the dust emission source.

2.4.5 The proposed alternative monitoring locations meet the guidelines and requirements specified in Section 2.4.1 and 2.4.2 of the EM&A Manual. **Table 2.3** shows the photographs of the air monitoring locations.

Table 2.3 Photo of Proposed HVS Position at Dust Monitoring Stations


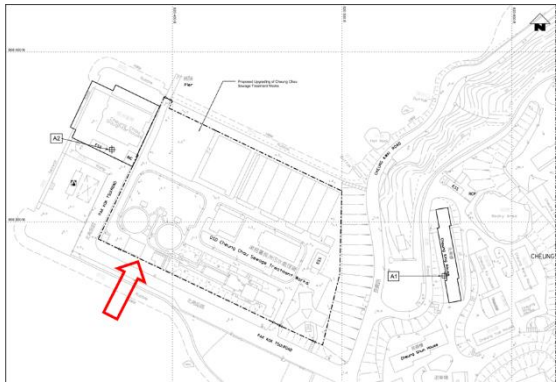
ID	HVS Position	Direction of Photo
A1		

The proposed Monitoring Station A1a is the Admin Building inside the construction site. It is located at a similar direction as A1 from the construction site, but much closer to any major dust emission source than A1.

A1a		
-----	--	---

A2		
----	---	--

Because Monitoring Station A2 is now abandoned, only limited access can be granted and power supply cannot be guaranteed which may not be feasible to be a monitoring location.

ID	HVS Position	Direction of Photo
A2a		

2.5. RESULTS AND ANALYSIS

2.5.1 The 1-hour TSP and 24-hour TSP measurement data are shown in [Appendix D](#) and summarized in **Table 2.4** and **Table 2.5** respectively.

Table 2.4 Summary of 1-hour TSP Monitoring Results

Monitoring Location	Average($\mu\text{g}/\text{m}^3$)	Range($\mu\text{g}/\text{m}^3$)
A1a	60	50 - 69
A2a	58	48 - 69

Table 2.5 Summary of 24-hour TSP Monitoring Results

Monitoring Location	Average($\mu\text{g}/\text{m}^3$)	Range($\mu\text{g}/\text{m}^3$)
A1a	61	33 - 120
A2a	63	35 - 124

2.6. ENVIRONMENTAL QUALITY PERFORMANCE LIMITS

2.6.1 The baseline monitoring results formed the basis for determining the air quality criteria for the impact monitoring. The ET shall compare the impact monitoring results with air quality criteria set up for 24-hour TSP and 1-hour TSP. **Table 2.6** shows the air quality criteria, namely Action and Limit levels to be used.

Table 2.6 Action / Limit Levels for Air Quality

Parameters	Action Level	Limit Level
1-hour TSP Level in $\mu\text{g}/\text{m}^3$	<p><u>For baseline level $\leq 200 \mu\text{g}/\text{m}^3$</u> $AL = (BL * 1.3 + LL)/2$ <u>For baseline level $> 200 \mu\text{g}/\text{m}^3$</u> $AL = LL$</p>	260 $\mu\text{g}/\text{m}^3$

Parameters	Action Level	Limit Level
24-hour TSP Level in $\mu\text{g}/\text{m}^3$	<p><u>For baseline level $\leq 384 \mu\text{g}/\text{m}^3$</u> $AL = (BL * 1.3 + LL)/2$ <u>For baseline level $> 384 \mu\text{g}/\text{m}^3$</u> $AL = LL$</p>	500 $\mu\text{g}/\text{m}^3$

2.6.2 The derived Action/Limit Levels are presented in **Table 2.7**.

Table 2.7 Derived Action / Limit Levels for Air Quality

Parameters	Monitoring Location	Action Level $\mu\text{g}/\text{m}^3$	Limit Level $\mu\text{g}/\text{m}^3$
1-hour TSP Level in $\mu\text{g}/\text{m}^3$	A1a	151	260
	A2a	154	
24-hour TSP Level in $\mu\text{g}/\text{m}^3$	A1a	270	500
	A2a	271	

2.7. EVENT AND ACTION PLAN

2.7.1 Should non-compliance of the air quality criteria occur, actions in accordance with the Action Plan in **Table 2.8** shall be carried out.

Table 2.8 Event and Action Plan for Air Quality (Construction Dust)

EVENT	ACTION PLAN FOR CONSTRUCTION DUST			
	ET	IEC	ER	CONTRACTOR
ACTION LEVEL				
Exceedance for one sample	<ol style="list-style-type: none"> Identify source, investigate the causes of exceedance and propose remedial measures; Inform IEC and ER; Repeat measurement to confirm finding; and Increase monitoring frequency to daily. 	<ol style="list-style-type: none"> Check monitoring data submitted by ET; and Check Contractor's working method. 	<ol style="list-style-type: none"> Notify Contractor. 	<ol style="list-style-type: none"> Rectify any unacceptable practice; and Amend working methods if appropriate.
Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> Identify source; Inform IEC and ER; Advise the ER on the effectiveness of the proposed remedial measures; Repeat measurements to confirm findings; Increase monitoring frequency to daily; Discuss with IEC and Contractor on remedial actions required; If exceedance continues, arrange meeting with IEC and ER; and If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> Check monitoring data submitted by ET; Check Contractor's working method; Discuss with ET and Contractor on possible remedial measures; Advise the ET on the effectiveness of the proposed remedial measures; and Supervise implementation of remedial measures 	<ol style="list-style-type: none"> Confirm receipt of notification of failure in writing; Notify Contractor; and Ensure remedial measures properly implemented. 	<ol style="list-style-type: none"> Submit proposals for remedial to IEC within 3 working days of notification; Implement the agreed proposals; and Amend proposal if appropriate.

3. NOISE

3.1. MONITORING CRITERIA

- 3.1.1 Impact monitoring was conducted once a week between 07:00-19:00 hours on normal weekdays.
- 3.1.2 **Table 3.1** summarizes the monitoring parameters, frequency and duration of the noise monitoring.

Table 3.1 Noise Monitoring Parameters, Time, Frequency and Duration

Time	Duration	Interval	Parameters
Daytime: 0700-1900 hrs	Once per week	Continuously in $L_{eq\ 5min}/L_{eq\ 30min}$ (average of 6 consecutive $L_{eq\ 5min}$)	$L_{eq\ 5min}$, $L_{eq\ 30min}$, L_{10} & L_{90}

3.2. MONITORING REQUIREMENTS AND EQUIPMENT

- 3.2.1 Sound level meters and calibrators shall comply with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specification as referred to in the Technical Memorandum (TM) issued under the Noise Control Ordinance.
- 3.2.2 Sound level meters were calibrated using a portable calibrator prior to and following each noise measurement. Where the difference between the calibration levels is greater than 1.0 dB(A), the measurement shall be repeated. Calibrated hand-held anemometers were supplied for the measurement of wind speeds during noise monitoring periods.
- 3.2.3 Noise measurements should not be made in fog, rain, wind with a steady speed exceeding 5 m/s or wind with gusts exceeding 10 m/s. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m/s.
- 3.2.4 The details of equipment used for impact monitoring are listed in **Table 3.2**, and the calibration certificates are presented in [Appendix E](#).

Table 3.2 Equipment Used for Noise Monitoring

Equipment	Model	Serial Number
Sound Level Meter	SVANTEK 971	96062
Acoustic Calibrator	Rion NC-75	34524163

3.3. MONITORING LOCATION

3.3.1 According to the environmental findings detailed in the EIA report, the designated locations for the construction noise monitoring are listed in **Table 3.3** and shown in Figure 3.1 – 3.8 of the EM&A Manual.

Table 3.3 Noise Monitoring Stations for Noise Monitoring

ID No.	Location	Nature of Uses	Remarks	Façade/Free-field
N2	Cheung King House, Cheung Kwai Estate	Residential	Specified in the EM&A Manual but proposed to change location	Façade
N2a	Admin Building inside the Construction Site	Institutional	Proposed alternative location to replace N2	Façade
N3	No. 1A Pak She Second Lane	Residential	Specified in the EM&A Manual but proposed to change location	Free-field
N3a	Cheung Chau Fire Station	Fire Station	Proposed alternative location to replace N3	Free-field


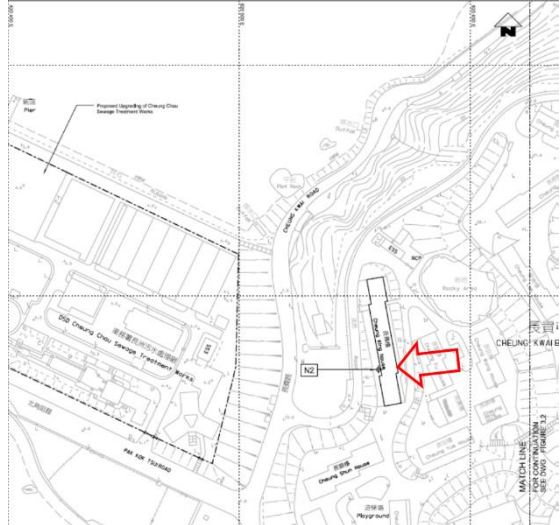

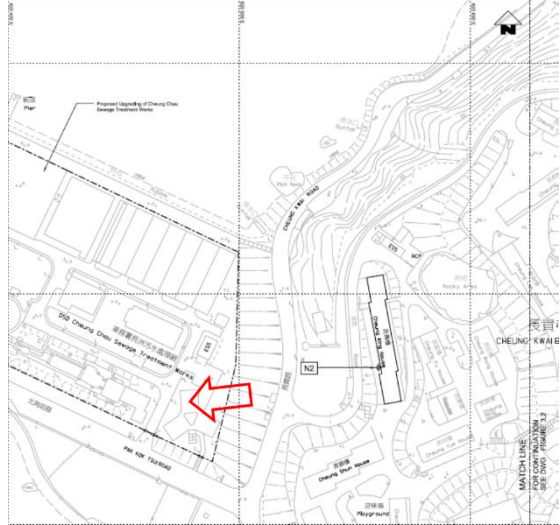


3.3.2 For this Contract, only N2 and N3 need to be monitored since all the other monitoring stations specified in the EM&A Manual are for sewers works but this Contract does not include sewers works.

3.3.3 The proposed Monitoring Station N2a is the Admin Building inside the construction site. It is located at a similar direction as N2 from the construction site, but much closer to any major noise emission source than N2.


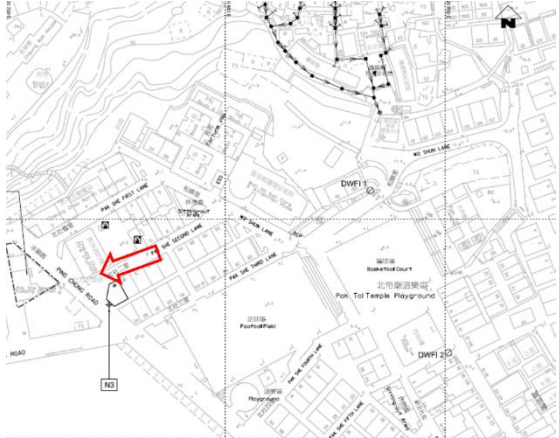
3.3.4 According to Figure 3.3 of the EM&A Manual, Location N3 is placed in front of a restaurant on Ping Chong Road. It may pose potential danger to pedestrians, cyclists, drivers and the equipment. A proposed monitoring location N3a, which is about 5 m away from the original monitoring location. N3a is at the corner of the Cheung Chau Fire Station. This location is safer and meets the guidelines and requirements specified in Section 3.4.1 and 3.4.2 of the EM&A Manual.

3.3.5 The monitoring locations should normally be made at a point 1m from the exterior of the NSRs building façade and be at a position 1.2m above the ground. **Table 3.4** showed photographs and indications of the proposed position of sound level meters to be placed for the baseline and impact monitoring.

Table 3.4 Photo of Proposed Sound Level Meter Position at Noise Monitoring Stations

ID	Sound Level Meter Position	Direction of Photo
N2		
<p>The proposed Monitoring Station N2a is the Admin Building inside the construction site. It is located at a similar direction as N2 from the construction site, but much closer to any major noise emission source than N2.</p>		
N2a		
N3		

According to Figure 3.3 of the EM&A Manual, Location N3 is placed in front of a restaurant on Ping Chong Road. It may pose potential danger to pedestrians, cyclists, drivers and the equipment.

ID	Sound Level Meter Position	Direction of Photo
N3a		

3.4. RESULTS AND ANALYSIS

3.4.1 The noise monitoring was carried out in **August** 2024. The measurement data are shown in [Appendix F](#) and summarized in **Table 3.5**.

Table 3.5 Summary of Noise Monitoring Results

Monitoring Location	Time Period	Average[dB(A)]	Range[dB(A)]
N2a	Daytime (0700-1900)	68.4	65.6 – 70.9
N3a	Daytime (0700-1900)	72.6	71.2 – 73.9

s: +3 dB(A) free-field corrections have been made to the data of N3a.

3.5. ENVIRONMENTAL QUALITY PERFORMANCE LIMITS

3.5.1 The Action and Limit levels for construction noise are shown in **Table 3.6**. All NSRs identified in the Project are classified with an Area Sensitivity Rating (ASR) A in accordance with the Technical Memorandum on Noise from Construction Work Other Than Percussive Piling.

Table 3.6 Action / Limit Levels for Construction Noise

Time Period	Action	Limit
07:00-19:00 hours on normal weekdays;	When one or more documented complaints are received	75dB(A)

3.6. EVENT AND ACTION PLAN

3.6.1 Should non-compliance of the noise monitoring criteria occur, actions in accordance with the Action Plan in **Table 3.7** shall be carried out.

Table 3.7 Event and Action Plan for Construction Noise

Event	ET	IEC	ER	CONTRACTOR
Action Level	<ol style="list-style-type: none"> 1. Notify ER, IEC and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IEC, ER and Contractor; 4. Discuss with the IEC and contractor and formulate remedial measures; and 5. Increase monitoring frequency to check the effectiveness of mitigation measures. 	<ol style="list-style-type: none"> 1. Review the investigation results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly; and 3. Advise the ER on the effectiveness of the proposed remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; and 4. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Submit noise mitigation proposals to IEC and ER; and 2. Implement noise mitigation proposals.
Limit Level	<ol style="list-style-type: none"> 1. Notify IEC, ER, EPD & Contractor; 2. Identify source and investigate the cause of exceedance; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Discuss with the IEC, Contractor and ER on remedial measures required; 7. Assess the effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; and 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Discuss amongst ER, ER and Contractor on the potential Discuss amongst ET, ER and Contractor on the potential remedial actions; and actions whenever necessary to assure their effectiveness and advise the ER accordingly. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the EIC, agree with the Contractor on the remedial measures to be implemented; 4. Supervise the implementation of remedial measures; and 5. If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the exceedance until the exceedance is abated. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC and ER within 3 working days of notification; 3. Implement the agreed proposals; 4. Submit further proposal if problem still not under control; and 5. Stop the relevant portion of works as determined by ER, until the exceedance is abated.

4. WATER QUALITY

- 4.1 As suggested in Section 4.3 of the EM&A Manual, regular site audit was carried out to ensure that the recommended mitigation measures were properly implemented during the construction phase of upgrading of Cheung Chau STW and Pak She SPS. Site audit included site inspections and compliance audits were conducted in the reporting period.
- 4.2 Site inspections were carried out by the ET on 6, 13, 20 and 26 August 2024. No major deficiency was observed and the implementation of recommended for water pollution control was considered satisfactory.
- 4.3 The Contractor was reminded to make sure any effluent discharge from construction activities of the Project site should meet the requirements stipulated in the discharge license and monitoring of the treated effluent quality from the Works Areas should be carried out in accordance with the Water Pollution Control Ordinance license that is under the ambit of the relevant regional EPD office.
- 4.4 According to the Specific Conditions B2 in Part B of the discharge licence issued under WPCO, a sample of discharge was taken on 12 August 2024 for testing. The test results were under the limitations of the requirements. The quality of the discharge compliant with the requirements of the discharge licence.
- 4.5 According to the EM&A Manual section 4.4.1, marine water quality monitoring should be carried out during the operational phase of the Project is to quantify the variability of pollutant concentrations in the marine waters. Measured pollutant concentrations are to be compared to the relevant Water Quality Objectives and to the baseline data to identify any significant impact on water quality from the operation of upgraded Cheung Chau STW (DP component). Baseline water quality monitoring should be carried out at all monitoring stations prior to the operation of the upgraded Cheung Chau STW to establish a baseline ambient condition.
- 4.6 A six-month baseline water quality covering both dry and wet seasons is commenced in June 2024. Baseline water quality monitoring was carried out on 8 and 22 in August 2024. Water monitoring locations are shown in Table 4.1. Table 4.2 showing the baseline water quality monitoring schedule in August 2024. Any update on the monitoring schedule shall notify the IEC and EPD. A baseline water quality monitoring report will be submitted after finished the baseline monitoring. The baseline water quality monitoring report shall be verified by the IEC.

Table 4.1: Water Quality Monitoring Locations

Locations	Station	Easting	Northing
Cheung Chau STW	w1	820151.20	808236.90
Cheung Chau Wan	w2	820579.40	807761.65
Tung Wan	w3	821221.73	808130.84
Kwun Yam Wan	w4	821469.22	807804.01
Tai Kwai Wan	w5	820493.00	808822.31
Chi Ma Wan	w6	817649.00	811487.00

Table 4.2: Baseline Water Quality Monitoring Schedule in August 2024

Month	Dates of Water Sampling	Tidal Period	Sampling Time
August	8	Ebb Tide: :11:00 – 18:00 Flood Tide: 05:00 – 11:00	12:53 – 16:23 08:00 – 10:51
	22	Ebb Tide: 11:00 – 17:20 Flood Tide: 04:30 – 11:00	12:22 – 15:52 08:00 – 10:33

5. WASTE MANAGEMENT

5.1 The waste generated from this Project includes inert construction and demolition (C&D) materials, and non-inert C&D materials. Non-inert C&D materials are made up of general refuse, vegetative wastes, and recyclable wastes such as plastics and paper/cardboard packaging waste. Steel materials generated from the project are also grouped into non-inert C&D materials as the materials were not disposed of with other inert C&D materials. With reference to relevant handling records and trip tickets of this Project, the quantities of different types of waste generated in the reporting month are presented in **Table 5.1**.

Contract No. DC/2019/07
 Environmental Monitoring Works for Outlying Islands Sewerage Stage 2 -
 Upgrading of Cheung Chau Sewerage Treatment and Disposal Facilities
 37th EM&A Report – August 2024



Contract No: DC/2019/07
 Outlying Islands Sewerage Stage 2 – Upgrading of Cheung Chau Sewerage Treatment and Disposal Facilities

Name of Department : **Drainage Services Department** Contract No./ Work Order No. : **DC/2019/07**
 Project Title: **Outlying Islands Sewerage Stage 2 – Upgrading of Cheung Chau Sewerage Treatment and Disposal Facilities**
 Contractor: **Build King Civil Engineering Limited**
 Trip Ticket Account (Main Account): **7039094**
 Trip Ticket Account (Vessel Account): **7040870**
 Marine Dumping Permit (Type 1 - Open Sea Disposal): **EP/MD/23-041**
 Marine Dumping Permit (Type 2 - Confined Marine Disposal): **EP/MD/23-033**

Table 5.1 Monthly Summary Waste Flow Table for 2024 (in Weight)

(All quantities shall be rounded off to 3 decimal places) updated on: 30-Aug-2024

Month	Actual Quantities of Inert C&D Materials Generated / Imported (in '000 kg)						Actual Quantities of Other C&D Materials / Wastes Generated					Marine Dumping	
	Total Quantities Generated	Broken Concrete (including rock for recycling into aggregate)	Reused in the Contract	Reused in Other Projects	Disposed as Public Fill	Imported C&D Material	Metal	Paper/ Cardboard Packaging	Plastic (g) (bottles/containers, plastic sheets/foam from package material)	Chemical Waste	Others (i) (e.g. General Refuse etc.)	Type 1 - Open Sea Disposal	Type 2 - Confined Marine Disposal
	[a+b+c+d+e+f+g+h+i]	(a)	(b)	(c)	(d)	(e)	(f)	(g)	(h)	(i)	(in m ³)	(in m ³)	
Jan-2024	1588.4400	0.0000	0.0000	0.0000	1563.0000	0.0000	0.0000	0.0000	0.0000	25.4400	0.0000	0.0000	
Feb-2024	44.9600	0.0000	0.0000	0.0000	18.1200	0.0000	0.0000	0.0000	0.0000	26.8400	0.0000	0.0000	
Mar-2024	46.6700	0.0000	0.0000	0.0000	18.1100	0.0000	0.0000	0.0000	0.0000	22.5600	0.0000	0.0000	
Apr-2024	30.2400	0.0000	0.0000	0.0000	24.6400	0.0000	0.0000	0.0000	0.0000	5.6000	0.0000	0.0000	
May-2024	817.6600	0.0000	0.0000	0.0000	783.0000	0.0000	0.0000	0.0000	0.0000	34.6600	0.0000	0.0000	
Jun-2024	47.2800	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	47.2800	0.0000	0.0000	
Half-year total	2569.2500	0.0000	0.0000	0.0000	2406.8700	0.0000	0.0000	0.0000	0.0000	162.3800	0.0000	0.0000	
Jul-2024	38.3400	0.0000	0.0000	0.0000	37.5800	0.0000	0.0000	0.0000	0.0000	0.7600	0.0000	0.0000	
Aug-2024	1909.8500	0.0000	0.0000	0.0000	1855.0000	0.0000	0.0000	0.0000	0.0000	54.8500	0.0000	0.0000	
Sep-2024		0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	
Oct-2024		0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	
Nov-2024		0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	
Dec-2024		0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	
Yearly Total	4517.4400	0.0000	0.0000	0.0000	4299.4500	0.0000	0.0000	0.0000	0.0000	217.9900	0.0000	0.0000	

(All quantities shall be rounded off to 3 decimal places)

Year	Actual Quantities of Inert C&D Materials Generated / Imported (in '000 kg)						Actual Quantities of Other C&D Materials / Wastes Generated					Marine Dumping	
	Total Quantities Generated	Broken Concrete (including rock for recycling into aggregate)	Reused in the Contract	Reused in Other Projects	Disposed as Public Fill	Imported C&D Material	Metal	Paper/ Cardboard Packaging	Plastic (g) (bottles/containers, plastic sheets/foam from package material)	Chemical Waste	Others (i) (e.g. General Refuse etc.)	Type 1 - Open Sea Disposal	Type 2 - Confined Marine Disposal
	[a+b+c+d+e+f+g+h+i]	(a)	(b)	(c)	(d)	(e)	(f)	(g)	(h)	(i)	(in m ³)	(in m ³)	
2020	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000
2021	858.3600	0.0000	0.0000	0.0000	786.3000	0.0000	0.0000	0.0000	0.0000	72.0600	0.0000	0.0000	
2022	17081.7200	0.0000	0.0000	0.0000	17032.3700	0.0000	0.0000	0.0000	0.0000	49.3500	525.0000	203.0000	
2023	49757.9100	0.0000	0.0000	0.0000	49610.8700	0.0000	0.0000	0.0000	0.2000	146.8400	835.0000	1350.0000	
2024	4517.4400	0.0000	0.0000	0.0000	4299.4500	0.0000	0.0000	0.0000	0.0000	217.9900	0.0000	0.0000	
2025	0.0000												
2026	0.0000												
Total	72215.4300	0.0000	0.0000	0.0000	71728.9900	0.0000	0.0000	0.0000	0.2000	486.2400	1360.0000	1553.0000	

Remark:
 1) Density of C&D material to be 2 metric ton/m³
 2) Density of General Refuse to be 1.6 metric ton/m³
 3) Density of Chemical Waste to be 0.88 metric ton/m³

Notes:
 (1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Sites.
 (2) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material.
 (3) The summary table shall be submitted to the Project Manager monthly together with the Waste Flow Table for review and monitoring in accordance with the PS Clause 25.20(8)

6. LANDSCAPE & VISUAL

- 6.1 The EIA Report has recommended landscape and visual mitigation measures to be undertaken during construction and operational phases of the upgrading of Cheung Chau STW under this Project. The implementation and maintenance of landscape mitigation measures were checked to ensure that they are fully realized and that potential conflicts between the proposed landscape measures and any other project works and without compromise to the intention of the mitigation measures.

- 6.2 Regular audits were carried out to ensure all the recommended landscape and visual mitigation measures were effectively implemented.

- 6.3 The EM&A Manual proposed mitigation measures were checked on a regular basis to ensure compliance with the intended aims of the EIA.

7. SITE INSPECTION AUDIT

- 7.1 Site inspections were carried out on a weekly basis to monitor the implementation of proper environmental pollution control and mitigation measures under the Contract. In the reporting period, site inspections were carried out on 6, 13, 20 and 26 August 2024. A joint site inspection with IEC was carried out on 26 August 2024.
- 7.2 Environmental deficiencies were observed during weekly site inspections. Key observations during the site inspections and during the reporting period are summarized in **Table 7.1**.

Table 7.1 Site Observations

Date	Environmental Observations	Follow-up Status	Reminders
6 August 2024	NIL	N.A.	NIL
13 August 2024	NIL	N.A.	NIL
20 August 2024	NIL	N.A.	NIL
26 August 2024	Stone breaker should be put on tarpaulin to avoid oil contamination	Stone breaker was removed	NIL

- 7.3 According to the EIA Study Report, Environmental Permit, contract documents and EM&A Manual, the mitigation measures detailed in the documents should be implemented as much as practical during the reporting period. An updated Implementation Status of Environmental Mitigation Measures (EMIS) is provided in **Appendix G**.

8. ENVIRONMENTAL NON-CONFORMANCE

8.1. SUMMARY OF EXCEEDANCES

- 8.1.1 No exceedance of Action and Limit Levels of air quality and construction noise was recorded in the reporting month.

8.2. Summary of Environmental Complaint

8.2.1 No environmental complaint was recorded in the reporting month.

8.3. SUMMARY OF ENVIRONMENTAL SUMMON AND SUCCESSFUL PROSECUTION

8.3.1 There was no successful environmental prosecution or notification of summons received since the Project commencement.

9. CONCLUSION


- 9.1 This is the 37th Monthly EM&A Report for the Project which summarizes the key findings of the programme during the reporting period from 1 August to 31 August 2024 in accordance with the EM&A Manual and the requirement under EP-488/2014/A.
- 9.2 Five (5) sessions of air and four (4) sessions of noise monitoring were carried out at the monitoring locations sited at Cheung Chau in the reporting month.
- 9.3 Site audits were conducted as mitigation measures recommended for water pollution control and landscape and visual impact monitoring in the reporting period. Proper mitigation measures were implemented.
- 9.4 Weekly environmental site inspections were conducted during the reporting period. Only minor deficiencies were observed during site inspections. The environmental performance of the project was therefore considered satisfactory.
- 9.5 A six-month baseline water quality covering both dry and wet seasons is commenced in June 2024 to establish a baseline ambient condition. Baseline water quality monitoring was carried out on 8 and 22 in August 2024.
- 9.6 No exceedance of Action or Limit Level was recorded in the reporting period.
- 9.7 No environmental complaint was received in the reporting period.
- 9.8 No notification of summons or prosecution was received during the reporting period.


APPENDIX A

Location Plan and Noise and Dust Monitoring Stations

Contract No. DC/2019/07
 Environmental Monitoring Works for Outlying Islands Sewerage Stage 2 -
 Upgrading of Cheung Chau Sewage Treatment and Disposal Facilities
 37th EM&A Report – August 2024

Aug 24

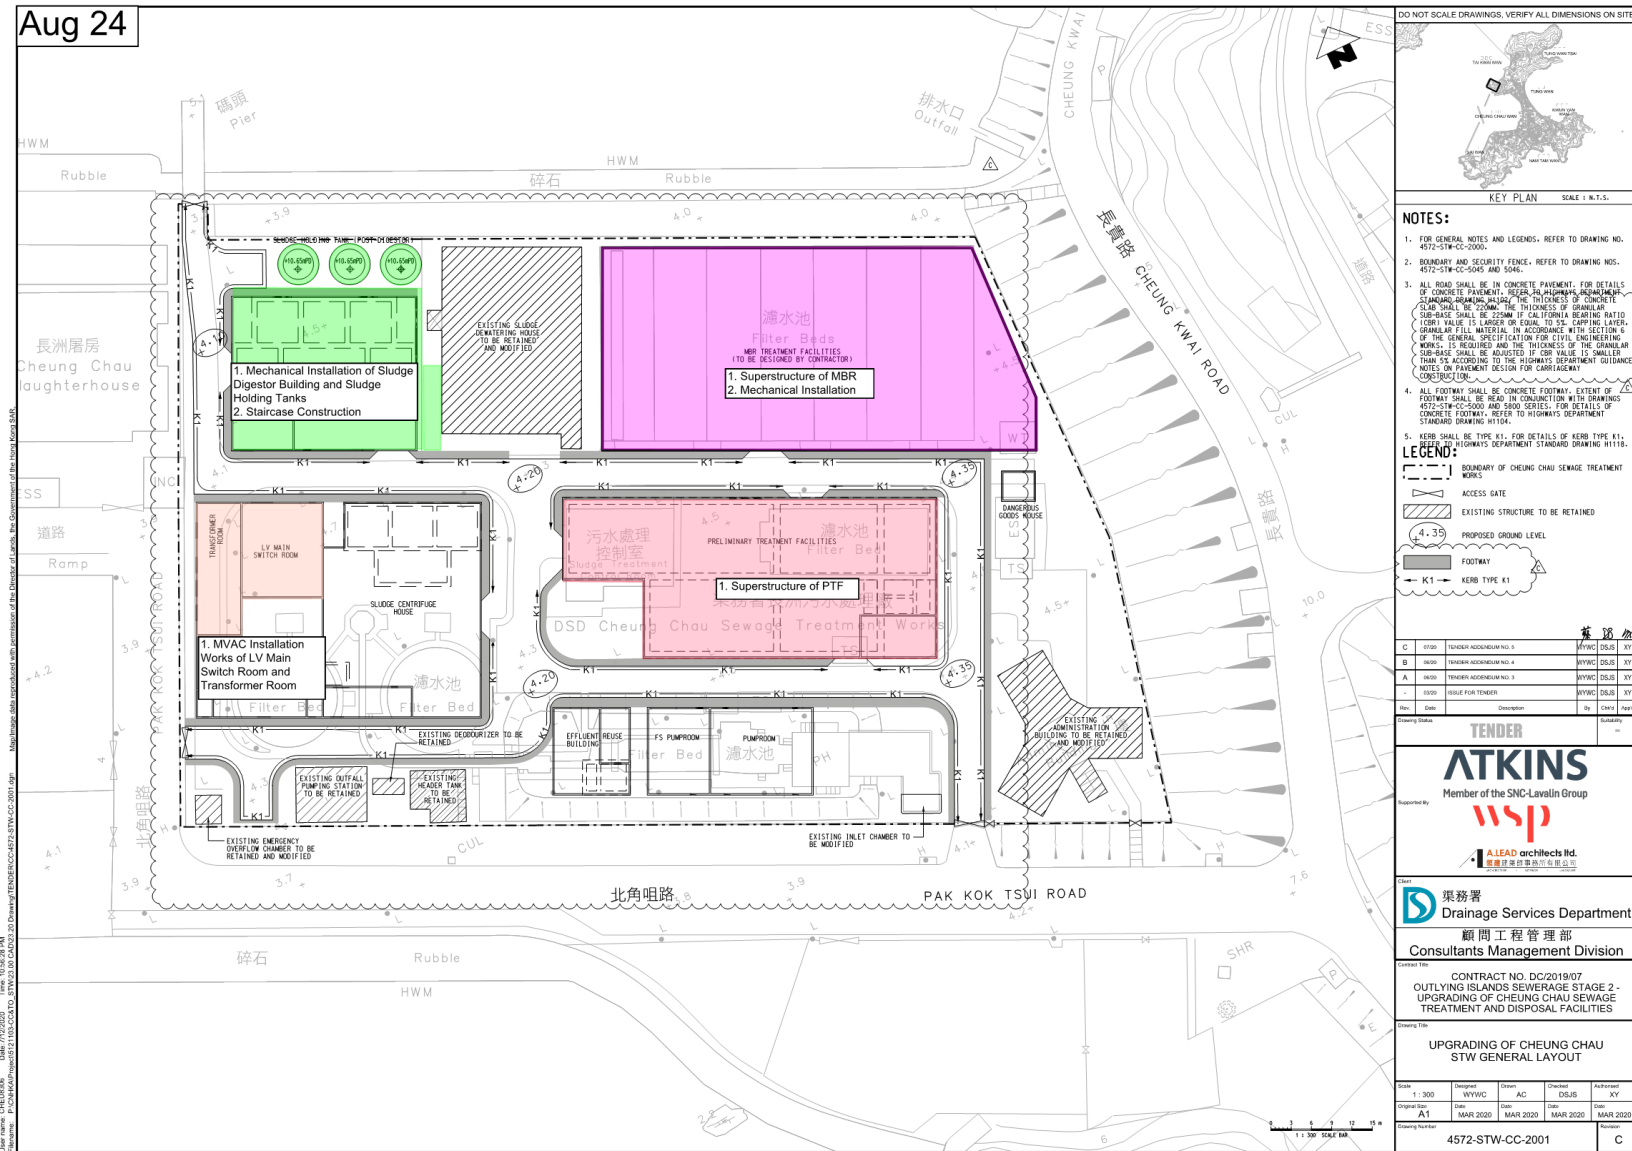

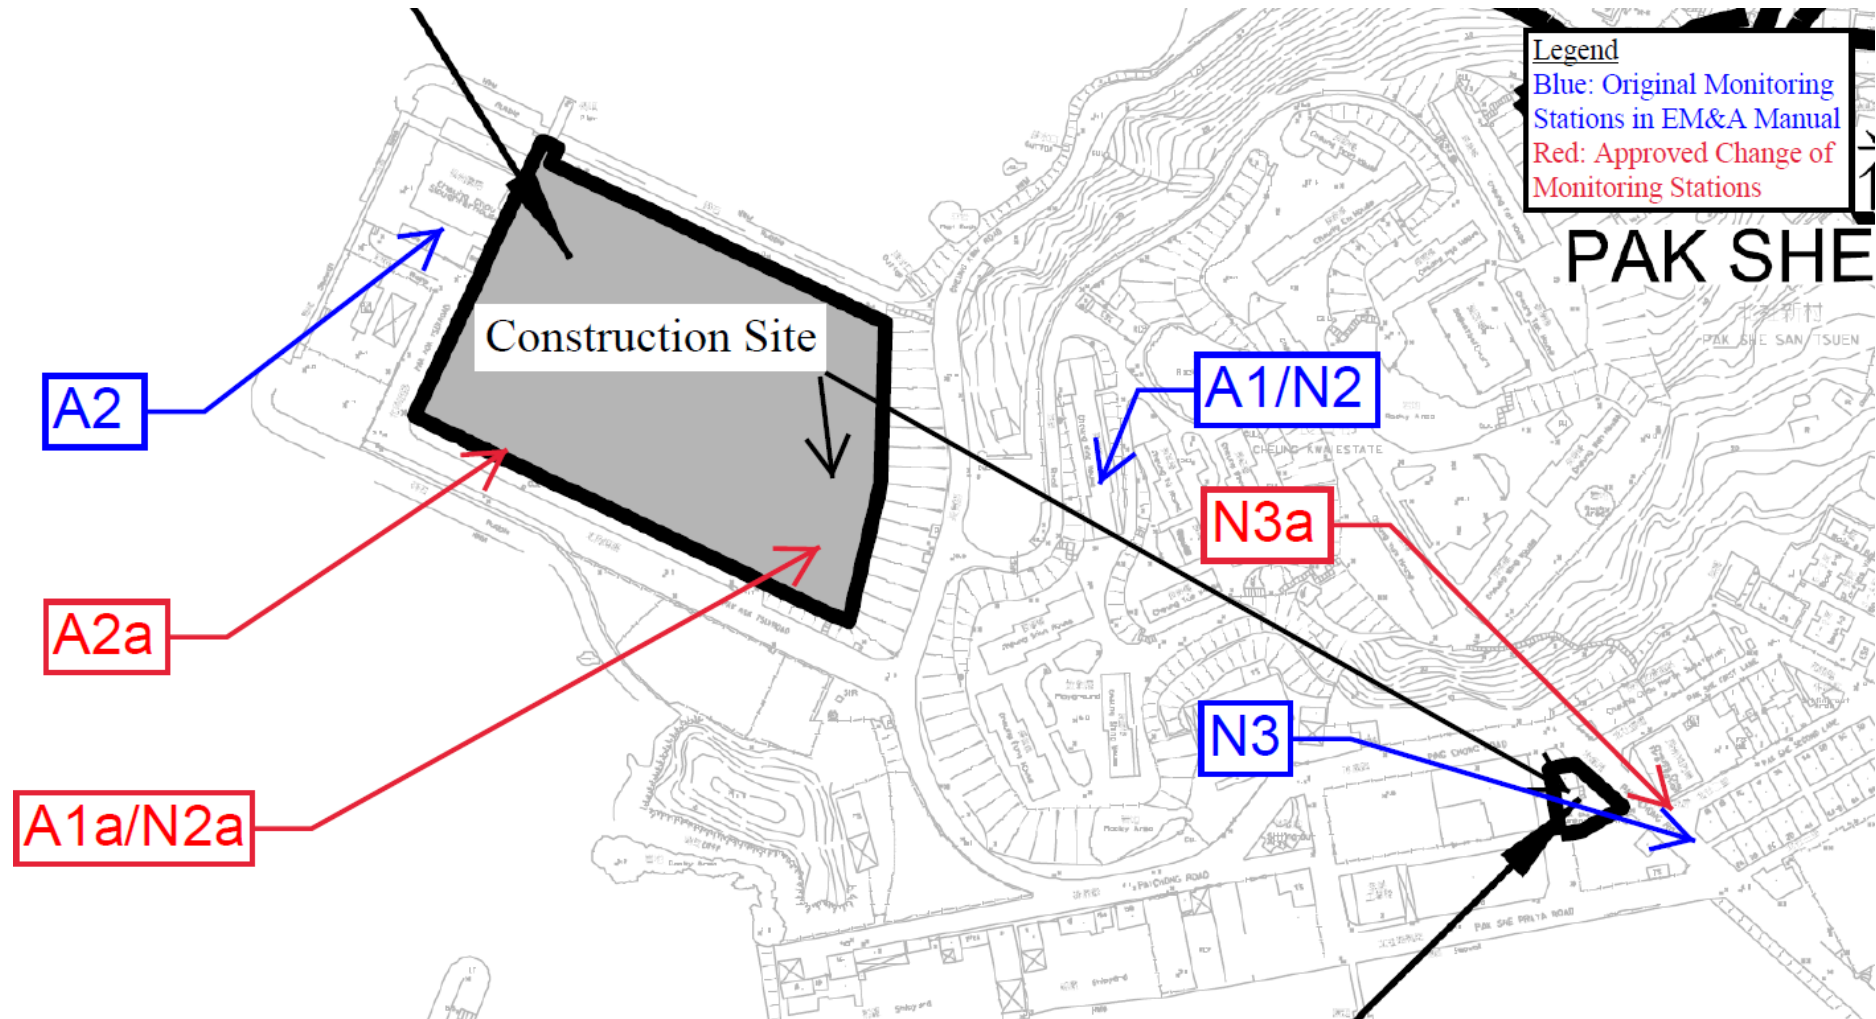

APPENDIX B


Construction Programme

Contract No. DC/2019/07
 Environmental Monitoring Works for Outlying Islands Sewerage Stage 2 -
 Upgrading of Cheung Chau Sewage Treatment and Disposal Facilities
 37th EM&A Report – August 2024



Activity ID	Activity Name	On/Off	TRA	Time Elapsed %	Actual Workdone %	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Early Start (Rev. 20)	Early Finish (Rev. 20)	Total Float	Amended Activities	2021	2022	2023	2024	2025	2026	2027		
DC.S3.145a	Subsetting of Fabling Works	151	0	100%	100%	19-Jul-22	31-Jan-23	19-Jul-22 A	31-Jan-23 A			19-Jul-22 A	31-Jan-23 A											
DC.S3.145b	Constructor of RC Structure (Renewing)	133	2	100%	100%	15-Aug-22	19-Dec-22	15-Aug-22 A	19-Dec-22 A			15-Aug-22 A	19-Dec-22 A											
EM&A Works				1.62%	0%	25-Feb-23		25-Feb-23 A	02-Aug-23	23-Jul-23	17-Dec-23	16-Feb-23	05-Aug-23	137										
DC.S3.150c	Installation of other EM&A equipments	72	2	0%	0%			01-Apr-23	03-Jul-23	23-Aug-23	17-Nov-23	15-Apr-23	03-Jul-23	117										
DC.S3.150d	Installation of Electrical System	72	2	0%	0%			01-Apr-23	28-Jun-23	23-Aug-23	17-Nov-23	15-Apr-23	03-Jul-23	117										
DC.S3.150e	Installation of SCADA	35	0	0%	0%			19-May-23	28-Jun-23	27-Oct-23	17-Nov-23			200										
DC.S3.150d	Installation of BS System	46	0	0%	0%			03-May-23	28-Jun-23	23-Sep-23	17-Nov-23			200										
DC.S3.151c	Site Acceptance Test	32	0	0%	0%			04-Jul-23	02-Aug-23	19-Nov-23	17-Dec-23	04-Jul-23	02-Aug-23	137										
Internal Infrastructure Works				2.38%	0%	25-Feb-23		25-Feb-23 A	30-Jun-23	17-Nov-23	16-Feb-23			140										
DC.S3.153a	Installation of BS equipment in CLP Transformer Room	34	2	5.52%	0%	25-Feb-23		25-Feb-23 A	14-Apr-23	23-Jul-23	30-Aug-23	16-Feb-23	25-Mar-23	116										
DC.S3.153b	Site Acceptance Test	4	0	0%	0%			13-Apr-23	16-Apr-23	31-Aug-23	03-Sep-23	30-Mar-23	02-Apr-23	140										
DC.S3.153c	CLP Inspection and Defect Rectification	0	0	0%	0%			17-Apr-23	26-Apr-23	01-Sep-23	13-Sep-23	02-Apr-23	20-Apr-23	116										
DC.S3.153d	CLP Reinforcement and Minor Defect Rectification	4	0	0%	0%			27-Apr-23	02-May-23	14-Sep-23	18-Sep-23	21-Apr-23	25-Apr-23	116										
DC.S3.153e	Temporary Reinforcement of Access for CLP Works	12	0	0%	0%			17-Apr-23	28-Apr-23	25-Sep-23	18-Sep-23			117										
DC.S3.153f	Handover to CLP for CLP Works	48	0	0%	0%			03-May-23	28-Jun-23	19-Sep-23	19-Nov-23	28-Apr-23	19-Jun-23	116										
DC.S3.153g	Demolition	1	0	0%	0%			25-Jun-23	28-Jun-23	17-Nov-23	17-Nov-23	22-Jul-23	22-Jul-23	116										
Internal Architectural Works				45.1%	0%	01-Feb-23		01-Feb-23 A	31-Mar-23	29-Mar-23	22-Aug-23	01-Feb-23	24-Mar-23	115										
DC.S3.152c	Architectural Works (Internal)	46	5	45.1%	33%	01-Feb-23		01-Feb-23 A	31-Mar-23	21-Jul-23	22-Aug-23	01-Feb-23	24-Mar-23	115										
DC.S3.152d	Architectural Works for CLP Transformer Room (Internal)	42	1	53.81%	100%	01-Feb-23		01-Feb-23 A	22-Mar-23	28-Mar-23	31-Mar-23	01-Feb-23	15-Feb-23	8										
Construction of Underground Utilities				0%	0%			18-Sep-23	30-Oct-23	09-Oct-23	17-Nov-23	14-Jun-23	25-Jul-23	0										
DC.S3.160d	Construction of Drainage and Sewerage System: Fire Services, Electrical & Plumbing Underground Utilities	32	2	0%	0%			18-Sep-23	30-Oct-23	09-Oct-23	17-Nov-23	14-Jun-23	25-Jul-23	0										
Temporary Sludge Digestion System				97.66%	0%	24-Jun-22		21-Jun-22 A	30-Dec-22	18-Dec-22	30-Dec-22	24-Jun-22	28-Nov-22	0										
DC.S3.170d	Construction of Temporary Sludge Digester System: 1&C	68	3	100%	100%	24-Jun-22	10-Oct-22	24-Jun-22 A	10-Oct-22 A			24-Jun-22	10-Oct-22	0										
DC.S3.170e	Temporary Flow Divider and Inlet to existing aerobic sludge digester and relevant buildings	6	1	100%	100%	11-Oct-22	20-Oct-22	11-Oct-22 A	20-Oct-22 A			11-Oct-22	20-Oct-22	0										
DC.S3.170f	Removal of Temporary Sludge Digester System	15	0	0%	0%			18-Dec-22	30-Dec-22	19-Dec-22	30-Dec-22	13-Nov-23	29-Nov-23	0										
PHASE 2 - Site Clearance at the area of Proposed Preliminary Treatment Facilities				100%	0%	21-Oct-22		24-Nov-22	30-Oct-22 A	24-Nov-22 A		21-Oct-22	09-Dec-22	0										
Demolition works				100%	0%	21-Oct-22		24-Nov-22	30-Oct-22 A	24-Nov-22 A		21-Oct-22	09-Dec-22	0										
DC.S3.201a	Demolition of existing Aerobic Sludge Digester	29	0	100%	100%	21-Oct-22	24-Nov-22	21-Oct-22 A	24-Nov-22 A			21-Oct-22	09-Dec-22	0										
DC.S3.201b	Demolition of existing Blower and Pump House	28	0	100%	100%	21-Oct-22	24-Nov-22	21-Oct-22 A	24-Nov-22 A			21-Oct-22	09-Dec-22	0										
DC.S3.201c	Demolition of existing Genset Room	28	0	100%	100%	21-Oct-22	24-Nov-22	21-Oct-22 A	24-Nov-22 A			21-Oct-22	09-Dec-22	0										
DC.S3.201d	Disconnecting data link of removed existing equipment from the existing SCADA system	7	0	100%	100%	20-Oct-22	26-Oct-22	20-Oct-22 A	26-Oct-22 A			20-Oct-22	26-Oct-22	0										
PHASE 3 - Construction of Preliminary Treatment Facilities				53.31%	0%	12-Jul-21		12-Jul-21 A	08-Aug-21	28-Feb-21	28-Aug-21	12-Jul-21	23-Apr-21	0										
Construction of Preliminary Treatment Facilities				53.31%	0%	12-Jul-21		12-Jul-21 A	08-Aug-21	28-Feb-21	28-Aug-21	12-Jul-21	23-Apr-21	0										
Procurement, Fabrication and Delivery of Major EM&A Equipment				81.25%	0%	12-Jul-21		12-Jul-21 A	10-Mar-21	21-Mar-21	29-Jun-21	12-Jul-21	14-Dec-21	83										
DC.S3.3005a	Tendering of Subcontractor	45	0	100%	100%	12-Jul-21	25-Aug-21	12-Jul-21 A	25-Aug-21 A			12-Jul-21	25-Aug-21	0										
DC.S3.3005b	Equipment Submittal and Approval	544	0	83.02%	50%	03-Dec-21	03-Dec-21	03-Dec-21 A	30-May-22	21-Mar-23	29-Jun-23	03-Dec-21	14-Dec-21	21										
Procurement				0%	0%			01-Jun-23	01-Dec-23	14-Oct-23	11-Feb-24			72										
DC.S3.3015	Stopgap	1	0	0%	0%			01-Aug-23	01-Aug-23	22-Dec-23	22-Dec-23			123										
DC.S3.3025	Peristaltic	1	0	0%	0%			01-Aug-23	01-Aug-23	22-Dec-23	22-Dec-23			123										
DC.S3.3035	Mechanical Bar Screen - Coarse Screen	1	0	0%	0%			01-Aug-23	01-Aug-23	22-Dec-23	22-Dec-23			123										
DC.S3.3045	Sewer Conveyor	1	0	0%	0%			01-Aug-23	01-Aug-23	22-Dec-23	22-Dec-23			123										
DC.S3.3055	Sewer Compressor	1	0	0%	0%			01-Aug-23	01-Aug-23	22-Dec-23	22-Dec-23			123										
DC.S3.3065	Submersible Pump	1	0	0%	0%			01-Aug-23	01-Aug-23	22-Dec-23	22-Dec-23			123										
DC.S3.3075	Submersible Jet Mixer	1	0	0%	0%			01-Aug-23	01-Aug-23	22-Dec-23	22-Dec-23			123										
DC.S3.3085	Grit Pump	1	0	0%	0%			01-Aug-23	01-Aug-23	22-Dec-23	22-Dec-23			123										
DC.S3.3095	Grit Classifier & Grit Filter	1	0	0%	0%			01-Aug-23	01-Aug-23	22-Dec-23	22-Dec-23			123										
DC.S3.3105	Mechanical Filter Mesh	1	0	0%	0%			01-Aug-23	01-Aug-23	22-Dec-23	22-Dec-23			123										
DC.S3.3115	Lifting Appliance	1	0	0%	0%			05-Jul-23	05-Jul-23	26-Dec-23	26-Dec-23			136										
DC.S3.3125	Oil Skimmer Pump	1	0	0%	0%			01-Aug-23	01-Aug-23	22-Dec-23	22-Dec-23			123										
DC.S3.3135	Disinfection Unit (DOU)	1	0	0%	0%			01-Aug-23	01-Aug-23	22-Dec-23	22-Dec-23			123										
DC.S3.3145	LV Switchgear/MCC	1	0	0%	0%			01-Aug-23	01-Aug-23	13-Dec-23	13-Dec-23			134										
DC.S3.3155	VSD	1	0	0%	0%			01-Aug-23	01-Aug-23	13-Dec-23	13-Dec-23			134										
DC.S3.3165	UPS with Isolation Transformer	1	0	0%	0%			02-Oct-23	02-Oct-23	11-Feb-24	11-Feb-24			132										
DC.S3.3175	R/C Panel	1	0	0%	0%			01-Dec-23	01-Dec-23	26-Feb-24	26-Feb-24			87										
DC.S3.3185	Instrumentation	1	0	0%	0%			01-Jun-23	01-Jun-23	14-Oct-23	14-Oct-23			135										
Hardware				0%	0%			05-Jun-23	04-Feb-24	15-Oct-23	28-May-24			91										
DC.S3.3195	Stopgap	125	0	0%	0%			02-Aug-23	04-Dec-23	23-Dec-23	23-Apr-24			125										
DC.S3.3205	Peristaltic	125	0	0%	0%			02-Aug-23	04-Dec-23	23-Dec-23	23-Apr-24			125										
DC.S3.3215	Mechanical Bar Screen - Coarse Screen	125	0	0%	0%			02-Aug-23	04-Dec-23															

Contract No. DC/2019/07
 Environmental Monitoring Works for Outlying Islands Sewerage Stage 2 -
 Upgrading of Cheung Chau Sewage Treatment and Disposal Facilities
 37th EM&A Report – August 2024

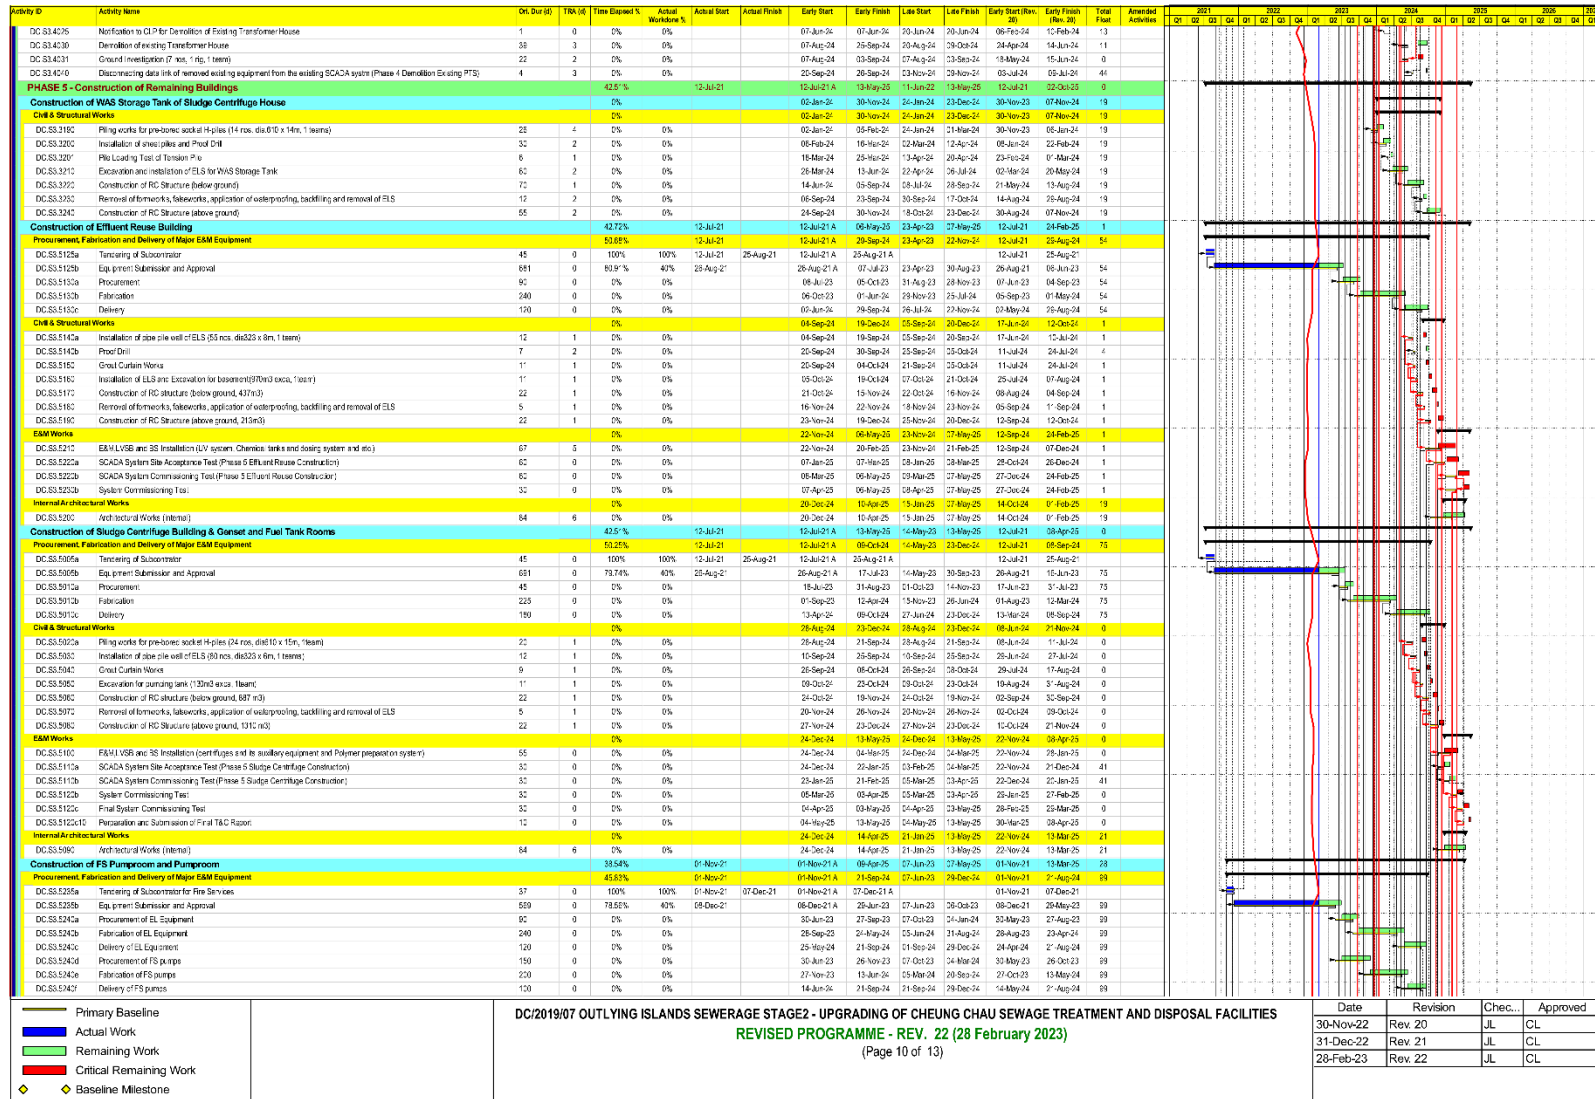

DC/2019/07 OUTLYING ISLANDS SEWERAGE STAGE2 - UPGRADING OF CHEUNG CHAU SEWAGE TREATMENT AND DISPOSAL FACILITIES
 REVISED PROGRAMME - REV. 22 (28 February 2023)
 (Page 10 of 13)

APPENDIX C

Calibration Certificates (Air Monitoring)



RECALIBRATION DUE DATE:
January 15, 2025

Certificate of Calibration

Calibration Certification Information			
Cal. Date: January 15, 2024	Rootsmeter S/N: 438320	Ta: 294	°K
Operator: Jim Tisch		Pa: 755.9	mm Hg
Calibration Model #: TE-5025A	Calibrator S/N: 3465		

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.4350	3.3	2.00
2	3	4	1	1.0180	6.4	4.00
3	5	6	1	0.9090	8.0	5.00
4	7	8	1	0.8670	8.9	5.50
5	9	10	1	0.7150	12.9	8.00

Data Tabulation					
Vstd (m3)	Qstd (x-axis)	$\sqrt{\Delta H \left(\frac{Pa}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)}$ (y-axis)	Va	Qa (x-axis)	$\sqrt{\Delta H \left(\frac{Ta}{Pa} \right)}$ (y-axis)
1.0037	0.6995	1.4200	0.9956	0.6938	0.8820
0.9996	0.9819	2.0081	0.9915	0.9740	1.2473
0.9975	1.0973	2.2452	0.9894	1.0885	1.3945
0.9963	1.1491	2.3547	0.9882	1.1398	1.4626
0.9909	1.3859	2.8399	0.9829	1.3747	1.7639
QSTD	m=	2.06920	QA	m=	1.29570
	b=	-0.02547		b=	-0.01582
	r=	0.99999		r=	0.99999

Calculations	
Vstd= $\Delta Vol((Pa-\Delta P)/Pstd)(Tstd/Ta)$	Va= $\Delta Vol((Pa-\Delta P)/Pa)$
Qstd= $Vstd/\Delta Time$	Qa= $Va/\Delta Time$
For subsequent flow rate calculations:	
Qstd= $1/m \left(\left(\sqrt{\Delta H \left(\frac{Pa}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)} \right) - b \right)$	Qa= $1/m \left(\left(\sqrt{\Delta H \left(\frac{Ta}{Pa} \right)} \right) - b \right)$

Standard Conditions	
Tstd:	298.15 °K
Pstd:	760 mm Hg
Key	
ΔH:	calibrator manometer reading (in H2O)
ΔP:	rootsmeter manometer reading (mm Hg)
Ta:	actual absolute temperature (°K)
Pa:	actual barometric pressure (mm Hg)
b:	intercept
m:	slope

RECALIBRATION
US EPA recommends annual recalibration per 1998 40 Code of Federal Regulations Part 50 to 51, Appendix B to Part 50, Reference Method for the Determination of Suspended Particulate Matter in the Atmosphere, 9.2.17, page 30

Tisch Environmental, Inc.
 145 South Miami Avenue
 Village of Cleves, OH 45002

www.tisch-env.com
 TOLL FREE: (877)263-7610
 FAX: (513)467-9009



HIVOL SAMPLER CALIBRATION DATA SHEET (TSP)

Site Information

Location:	The admin building inside the construction site	Site ID:	A1a	Date:	01-Aug-2024
Serial No.:	1048	Model:	TE-5170X	Operator:	Andy Li

Ambient Condition

Actual Pressure during Calibration (P _a) (mm Hg):	756.2	Actual Temperature during Calibration (T _a) (deg K):	303.4
---	-------	--	-------

Calibration Orifice

Model:	TE-5025A	Slope (m _c):	2.06920
Serial No.:	3465	Intercept (b _c):	-0.02547
Calibration Due Date:	15-Jan-25	Corr. Coeff:	0.99999

Calibration Data

Plate or Test #	ΔH ₂ O (in)	Qa, X-Axis (m ³ /min)	I, CFM (chart)	IC, Y-Axis (corrected)
18	9.80	1.508	60.0	59.31
13	7.80	1.347	56.0	55.36
10	5.20	1.102	50.0	49.43
7	3.60	0.919	46.0	45.47
5	2.00	0.688	42.0	41.52


Sampler Calibration Relationship (Qa on x-axis, IC on y-axis)

m = 21.9576 b = 25.7895 Corr. Coeff: 0.9973

$Qa = 1/m_c * [\text{Sqrt} (\Delta H_2O * (P_a/P_{std}) * (T_{std}/T_a)) - b_c]$
 $IC = I * (\text{Sqrt} (P_a/P_{std}) * (T_{std}/T_a))$

Calculations

- Qa = actual flow rate
- IC = corrected chart response
- I = actual chart response
- m_c = calibrator slope
- b_c = calibrator intercept
- m = sampler slope
- b = sampler intercept
- T_{std} = 298 deg K
- P_{std} = 760 mm Hg
- T_a = actual temperature during calibration (deg K)
- P_a = actual pressure during calibration (mm Hg)

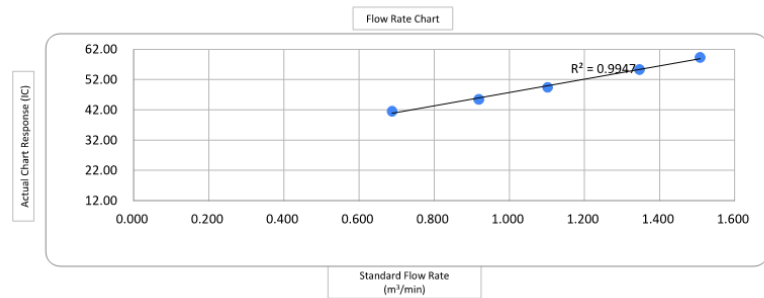

Checked by Tandy Tse Senior Consultant, Environmental

Date: 01-Aug-2024



HIVOL SAMPLER CALIBRATION DATA SHEET (TSP)

Site Information

Location:	The existing outfall pumping station inside the construction site	Site ID:	A2a	Date:	01-Aug-2024
Serial No.:	1085	Model:	TE-5170X	Operator:	Andy Li

Ambient Condition

Actual Pressure during Calibration (P _a) (mm Hg):	756.2	Actual Temperature during Calibration (T _a) (deg K):	303.4
---	-------	--	-------

Calibration Orifice

Model:	TE-5025A	Slope (m _c):	2.06920
Serial No.:	3465	Intercept (b _c):	-0.02547
Calibration Due Date:	15-Jan-25	Corr. Coeff:	0.99994

Calibration Data

Plate or Test #	ΔH ₂ O (in)	Qa, X-Axis (m ³ /min)	I, CFM (chart)	IC, Y-Axis (corrected)
1	9.80	1.508	60.0	59.31
2	7.60	1.329	56.0	55.36
3	4.80	1.059	51.0	50.42
4	3.00	0.840	46.0	45.47
5	2.00	0.688	40.0	39.54

Sampler Calibration Relationship (Qa on x-axis, IC on y-axis)

m = 22.9745 b = 25.0988 Corr. Coeff: 0.9913


Calculations


$$Qa = 1/m_c * [\text{Sqrt} (\Delta H_2O * (P_a/P_{std}) * (T_{std}/T_a)) - b_c]$$

$$IC = I * (\text{Sqrt} (P_a/P_{std}) * (T_{std}/T_a))$$

Qa = actual flow rate
 IC = corrected chart response
 I = actual chart response
 m_c = calibrator slope
 b_c = calibrator intercept

m = sampler slope
 b = sampler intercept
 T_{std} = 298 deg K
 P_{std} = 760 mm Hg
 T_a = actual temperature during calibration (deg K)
 P_a = actual pressure during calibration (mm Hg)

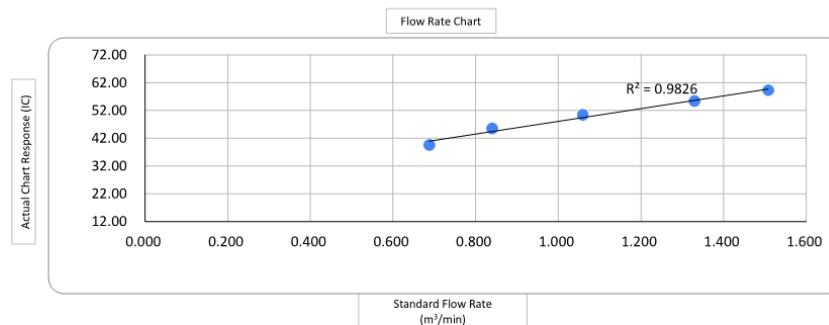

Checked by Tandy Tse 
 Environmental Team Leader

Date: 01-Aug-2024



Sibata LD-5R K-Factor Verification Test by Total Suspended Particulates HVS Test Report

Information of Calibrated Equipment

Verification Test Date:	19-Mar-24	to	24-Mar-24	Next Verification Test Date:	24-Mar-25
Unit-under-Test- Model No.:	Sibata LD-5R				
Unit-under-Test Serial No.:	2Y6549				
Our Report Reference No.:	PRT-24-HVS-0024				
Calibration Location:	Emax				

Standard Equipment Information


Verification Equipment Type:	Tisch TSP HVS	Tisch HVS Calibrator
Standard Equipment Model No.:	TE-5170X	TE-5025A
Equipment serial no.:	1085	3465
Last Calibration Date:	19-Mar-24	15-Jan-24
Next Calibration Date:	2-Apr-24	14-Jan-25


Equipment Verification Result


Verification Test No.	Date	Duration			Results from Calibrated Equipment		Results from Standard Equipment
		Start-time	End-time	Elapsed Time (in min)	Total Counts	Counts/ Minute x-axis	Dust Concentration (µg/m ³) y-axis
1	19/3/2024	7339.85	7342.85	180.00	26514	147	162
2	19/3/2024	7342.85	7345.85	180.00	27180	151	160
3	19/3/2024	7345.85	7348.85	180.00	30474	169	182
4	24/3/2024	7349.74	7352.74	180.00	6840	38	40
5	24/3/2024	7352.76	7355.76	180.00	15354	85	92
6	24/3/2024	7355.77	7358.77	180.00	12780	71	72

Linear Regression of y on x

Slope, K factor:	33.1857	Intercept:	11.2093	*Correlation Coefficient, R:	0.9991
Verification Test Result: Strong Correlation. Results were accepted.				* If the Correlation Coefficient, R is <0.5. Checking and Re-verification are required.	

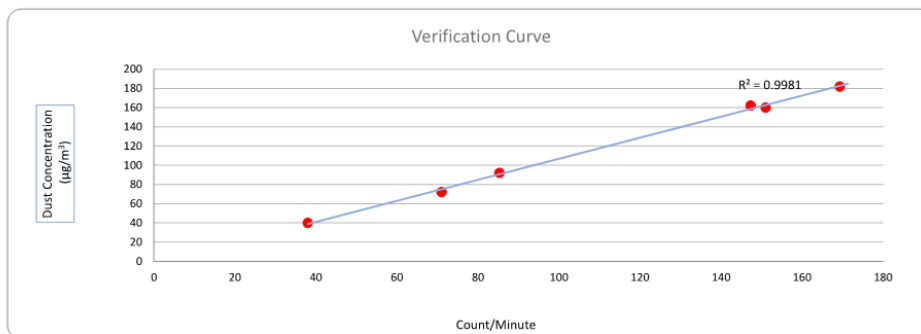

Operated By: Andy Li  Date: 29-03-2024
 Project Technician, Environmental

Checked By: Tandy Tse  Date: 29-03-2024
 Senior Consultant, Environmental



Sibata LD-5R K-Factor Verification Test by Total Suspended Particulates HVS Test Report

Information of Calibrated Equipment

Verification Test Date:	19-Mar-24	to	24-Mar-24	Next Verification Test Date:	24-Mar-25
Unit-under-Test- Model No.:	Sibata LD-5R				
Unit-under-Test Serial No.:	2Y6550				
Our Report Reference No.:	RPT-24-HVS-0028				
Calibration Location:	Emax				

Standard Equipment Information


Verification Equipment Type:	Tisch TSP HVS	Tisch HVS Calibrator
Standard Equipment Model No.:	TE-5170X	TE-5025A
Equipment serial no.:	1048	3465
Last Calibration Date:	19-Mar-24	15-Jan-24
Next Calibration Date:	2-Apr-24	14-Jan-25

Equipment Verification Result

Verification Test No.	Date	Duration			Results from Calibrated Equipment		Results from Standard Equipment
		Start-time	End-time	Elapsed Time (in min)	Total Counts	Counts/ Minute x-axis	Dust Concentration (µg/m ³) y-axis
1	19/3/2024	7339.85	7342.85	180.00	27486	153	162
2	19/3/2024	7342.85	7345.85	180.00	26586	148	160
3	19/3/2024	7345.85	7348.85	180.00	31500	175	182
4	24/3/2024	7349.74	7352.74	180.00	7146	40	40
5	24/3/2024	7352.76	7355.76	180.00	15480	86	92
6	24/3/2024	7355.77	7358.77	180.00	12654	70	72

Linear Regression of y on x

Slope, K factor:	33.1857	Intercept:	11.2093	*Correlation Coefficient, R:	0.9990
Verification Test Result: <u>Strong Correlation, Results were accepted.</u>			* If the Correlation Coefficient, R is <0.5. Checking and Re-verification are required.		

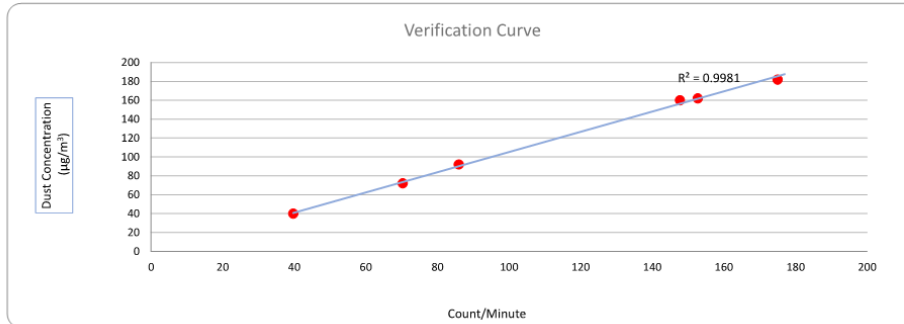

Operated By: Andy Li
 Project Technician, Environmental
 Date: 29-03-2024

Checked By: Tandy Tse
 Senior Consultant, Environmental
 Date: 29-03-2024

APPENDIX D

Monitoring Data (Air)

Location: A1a

Monitoring Period: August 2024

Parameter: TSP 1-hour

Major Dust Source Construction activities and daily operation of the sewerage treatment plant

Other Factors NA

Date	Weather	Start Time	1 st Hour ($\mu\text{g}/\text{m}^3$)	2 nd Hour ($\mu\text{g}/\text{m}^3$)	3 rd Hour ($\mu\text{g}/\text{m}^3$)
1/08/2024	Fine	13:50	50	55	63
5/08/2024	Cloudy	13:31	61	57	67
12/08/2024	Cloudy	14:16	57	67	69
19/08/2024	Sunny	13:31	54	63	58
26/08/2024	Sunny	14:43	62	59	60
Average			60		
Range			50 - 69		

Location: A2a

Monitoring Period: August 2024

Parameter: TSP 1-hour

Major Dust Source Construction activities and daily operation of the sewerage treatment plant

Other Factors NA

Date	Weather	Start Time	1 st Hour ($\mu\text{g}/\text{m}^3$)	2 nd Hour ($\mu\text{g}/\text{m}^3$)	3 rd Hour ($\mu\text{g}/\text{m}^3$)
1/08/2024	Fine	13:33	54	58	65
5/08/2024	Cloudy	13:16	60	55	67
12/08/2024	Cloudy	13:01	52	54	69
19/08/2024	Sunny	13:11	56	48	58
26/08/2024	Sunny	14:21	61	61	58
Average			58		
Range			48 - 69		

Figure D.1 Measured 1-Hour TSP at the admin building inside the construction site (A1a)


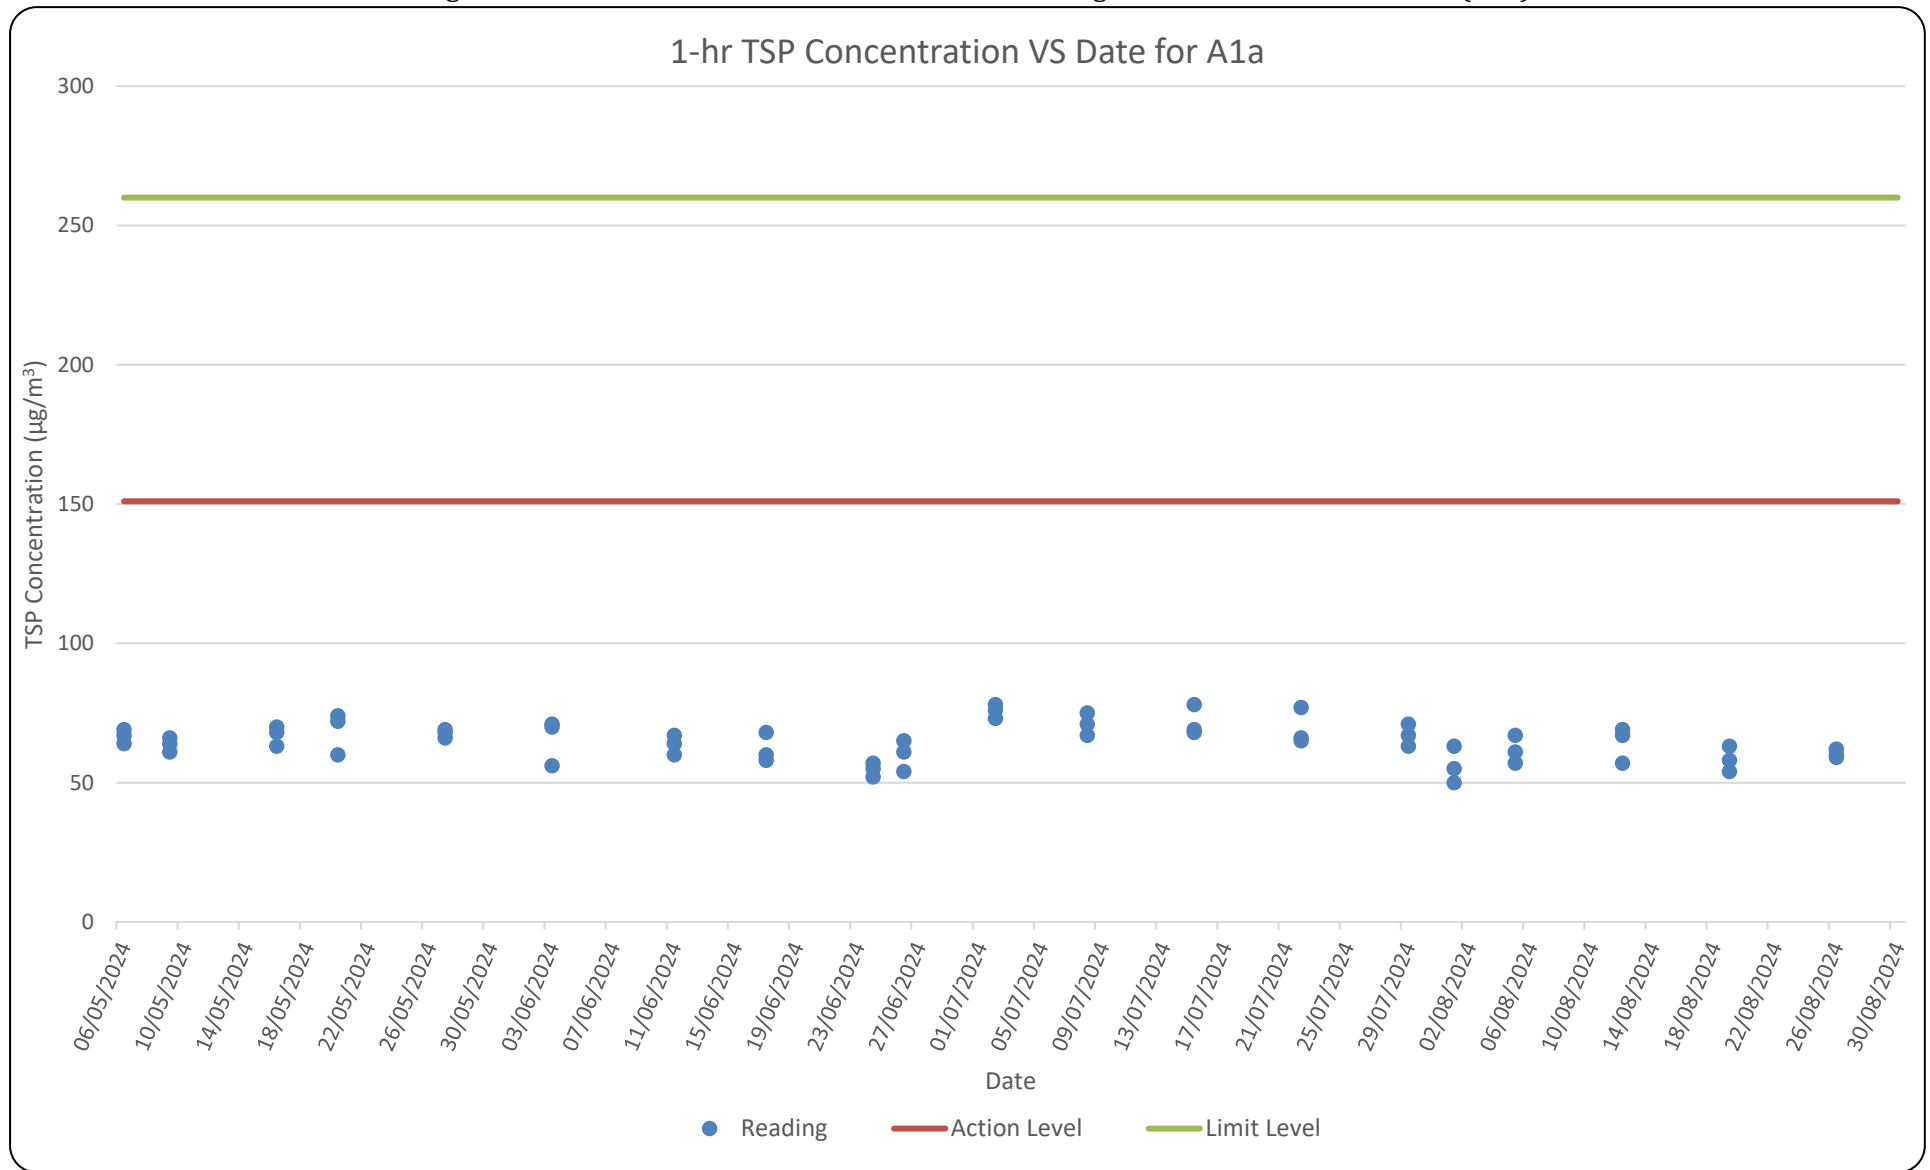


Figure D.2 Measured 1-Hour TSP at the existing outfall pumping station inside the construction site (A2a)

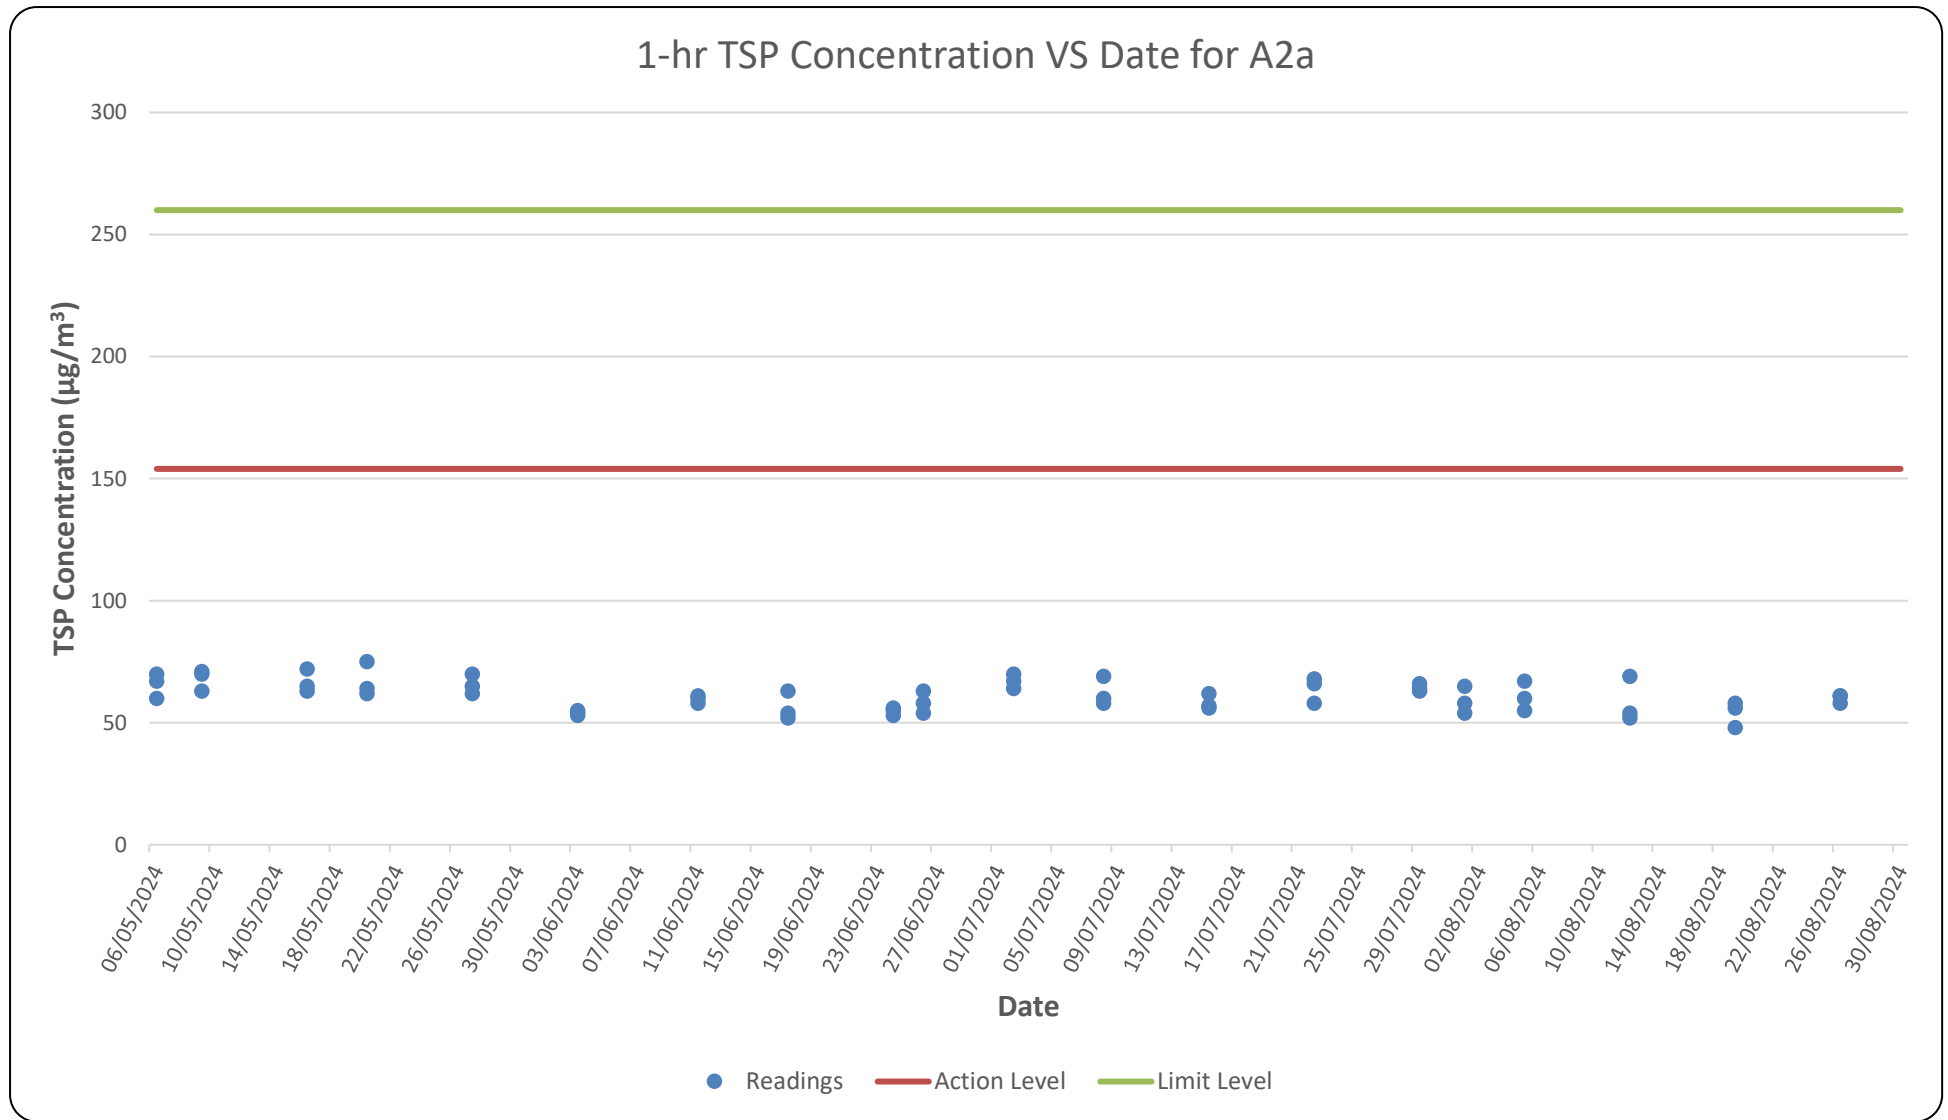

Location: A1a
 Parameter: TSP 24-hour
 Major dust source: Construction activities and daily operation of the sewerage treatment plant
 Major dust source: Routine operation of the Sewage Treatment Plant
 Other Factors: NA

Start Date	Avg Air Temp	Avg Atmospheric Pressure	Weather Condition	Elapse Time		Sampling Time	Flow Rate	Standard Air Volume	Filter Weight (g)		Particulate weight	Conc.
	(°C)	(mm Hg)		Initial (min)	Final (min)	Actual (min)	(m ³ /min)	(m ³)	Initial	Final	(g)	(µg/m ³)
1/08/2024	30	1008.0	Sunny	350210	351660	1450	0.67	968	2.6656	2.7222	0.0566	58
5/08/2024	31.2	1005.6	Sunny	351660	353160	1500	0.66	989	2.6729	2.7918	0.1189	120
12/08/2024	27.7	1005.2	Cloudy	353160	354660	1500	0.67	1004	2.6929	2.7260	0.0331	33
19/08/2024	27.8	1005.4	Sunny	354660	356170	1510	0.62	943	2.6875	2.7198	0.0323	34
26/08/2024	30.5	1006.1	Sunny	356170	357611	1441	0.62	890	2.6619	2.7136	0.0517	58
											Average	61
											Range	33 - 120

Location: A2a
 Parameter: TSP 24-hour
 Major Site Activities: Construction activities and daily operation of the sewerage treatment plant
 Major dust source: Routine operation of the Sewage Treatment Plant
 Other Factors: NA

Start Date	Avg Air Temp	Avg Atmospheric Pressure	Weather Condition	Elapse Time		Sampling Time	Flow Rate	Standard Air Volume	Filter Weight (g)		Particulate weight	Conc.
	(°C)	(mm Hg)		Initial (min)	Final (min)	Actual (min)	(m ³ /min)	(m ³)	Initial	Final	(g)	(µg/m ³)
1/08/2024	30	1008.0	Sunny	568701	570156	1455	0.63	910	2.6661	2.7102	0.0441	48
5/08/2024	31.2	1005.6	Sunny	570156	571596	1440	0.45	643	2.7044	2.7841	0.0797	124
12/08/2024	27.7	1005.2	Cloudy	571596	573096	1500	0.45	682	2.6935	2.7175	0.0240	35
19/08/2024	27.8	1005.4	Sunny	573096	574596	1500	0.46	683	2.6965	2.7237	0.0272	40
26/08/2024	30.5	1006.1	Sunny	574596	576036	1440	0.45	647	2.6720	2.7168	0.0448	69
											Average	63
											Range	35 - 124

Figure D.3 Measured 24-Hour TSP at the admin building inside the construction site (A1a)


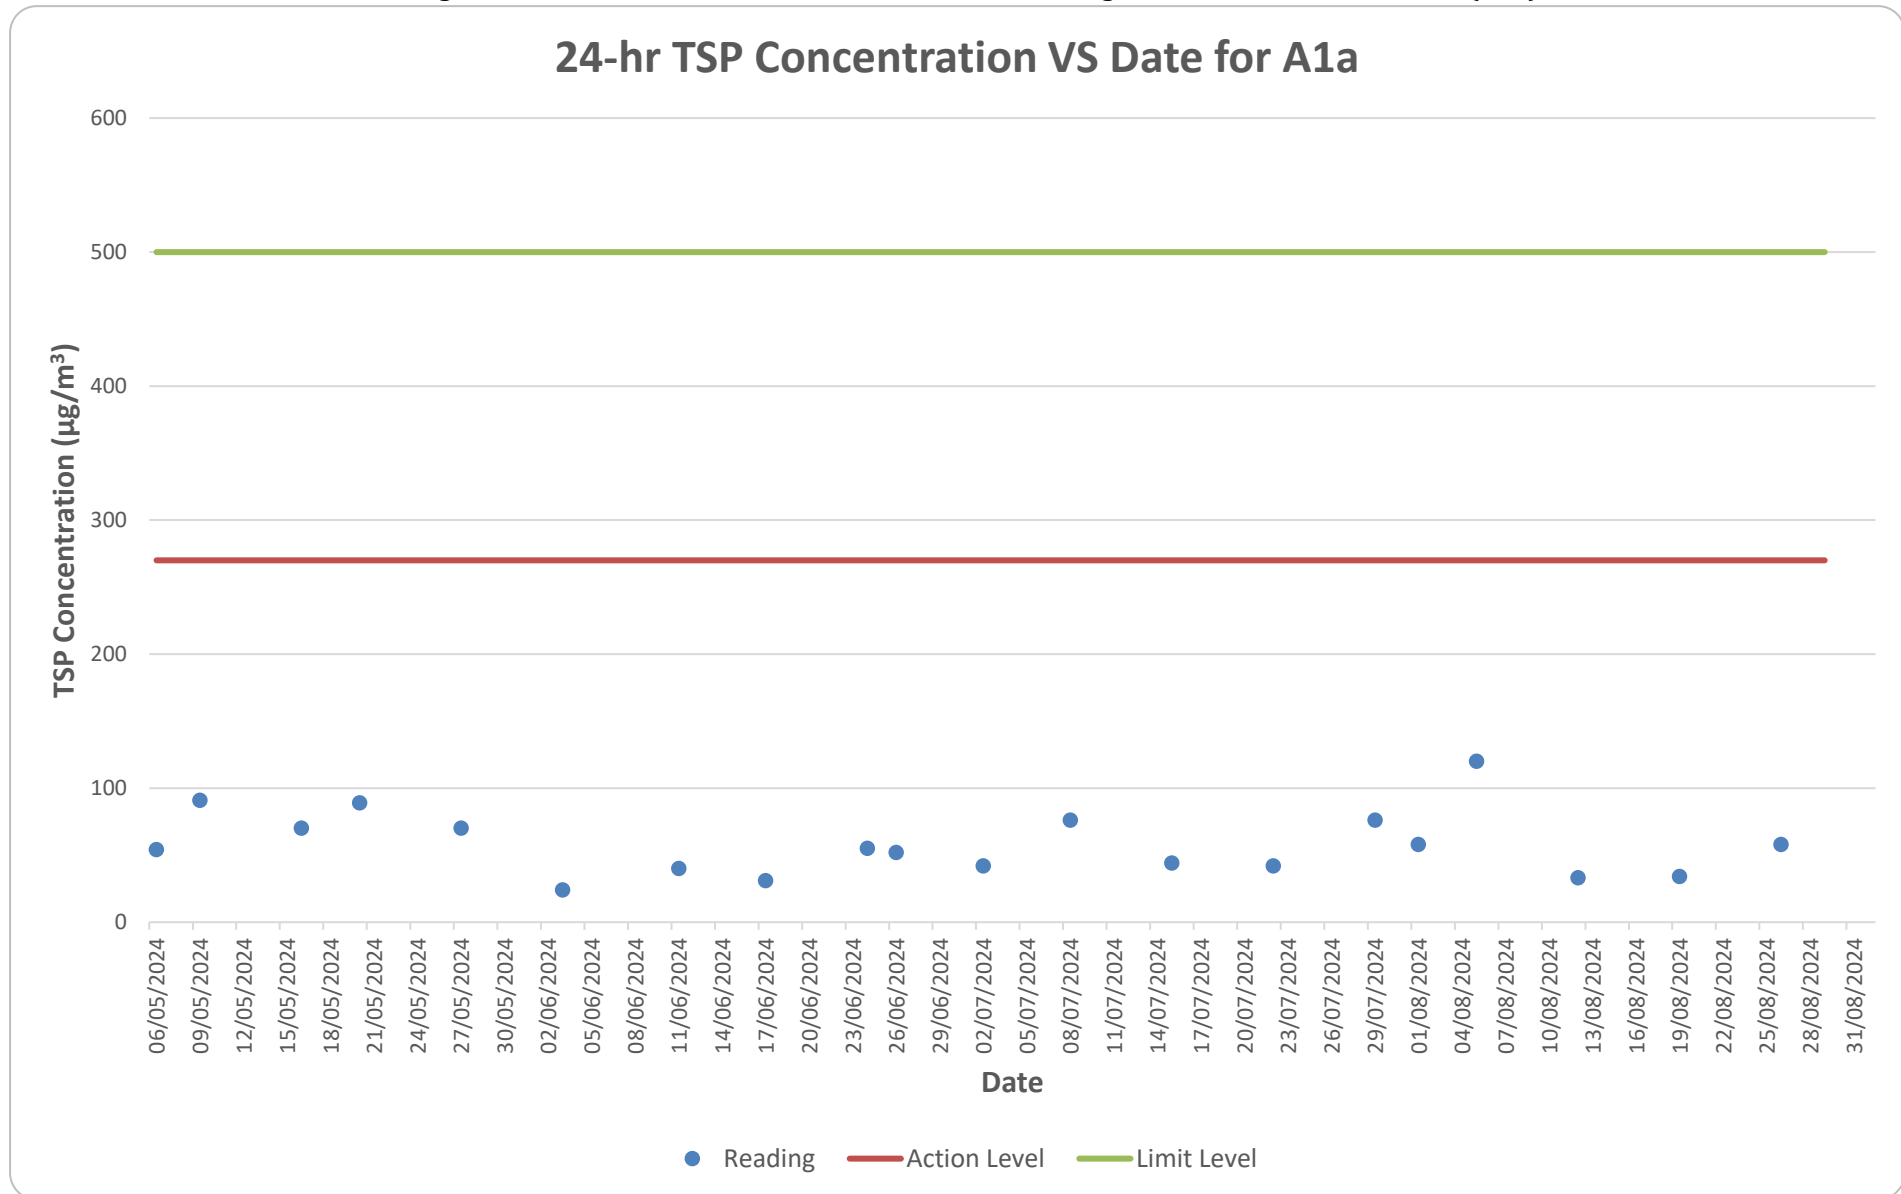


Figure D.4 Measured 24-Hour TSP at the existing outfall pumping station inside the construction site (A2a)

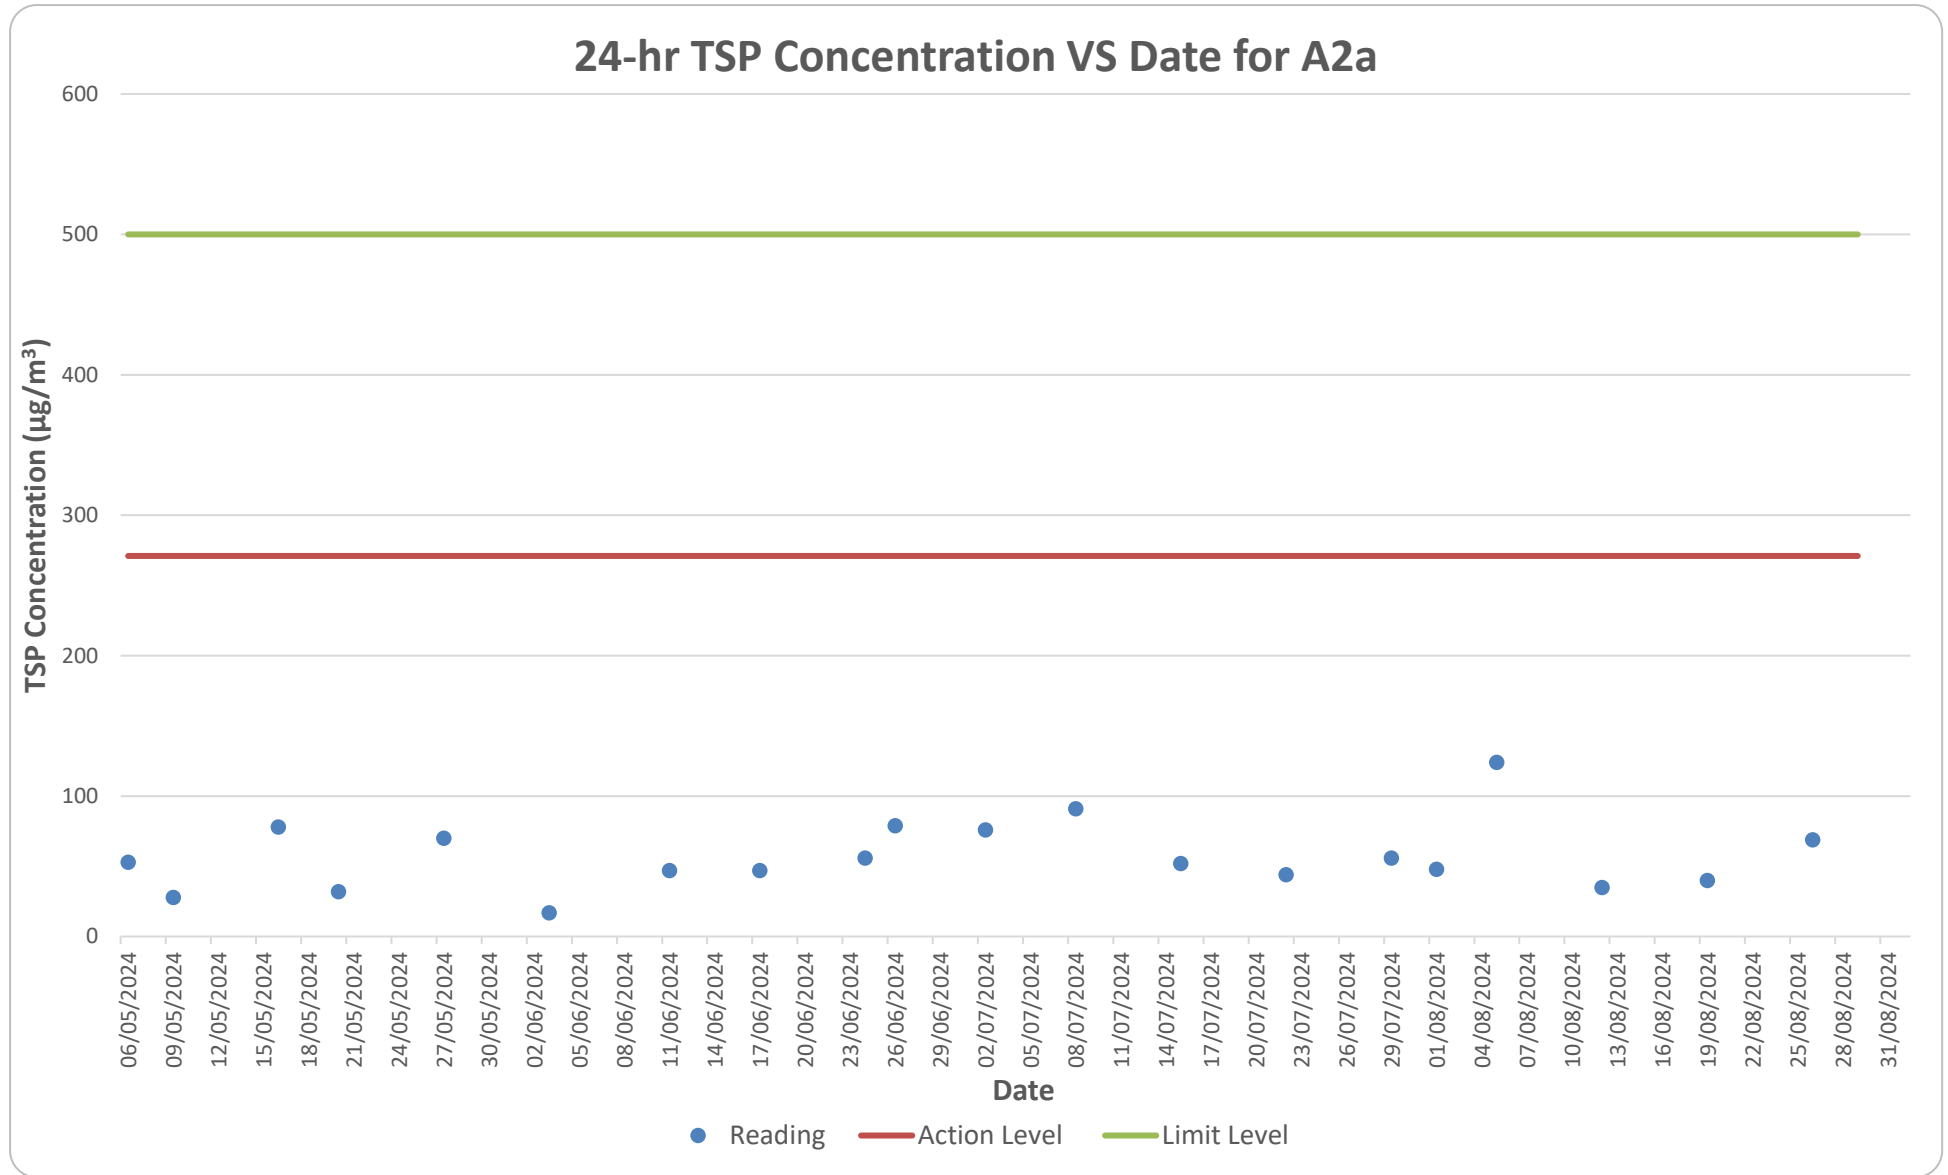

APPENDIX E

Calibration Certificates (Noise)

Certificate of Calibration

for

Description: Sound Level Calibrator
Manufacturer: RION
Type No.: NC-75
Serial No.: 34524163

Submitted by:

Customer: Aurecon Hong Kong Limited
Address: Unit 1608, 16/F, Tower B, Manulife Financial Centre,
223-231 Wai Yip Street, Kwun Tong,
Kowloon, Hong Kong

Upon receipt for calibration, the instrument was found to be:

- Within
 Outside

the allowable tolerance.

The test equipments used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory

Date of receipt: 22 July 2024

Date of calibration: 24 July 2024

Date of NEXT calibration: 23 July 2025

Calibrated by: _____

Calibration Technician

Certified by: _____

Mr. Ng Yan Wa
Laboratory Manager

Date of issue: 24 July 2024



Certificate No.: APJ24-010-CC001

Page 1 of 2



1. Calibration Precautions:

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 24 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.

2. Calibration Specifications:

Calibration check

3. Calibration Conditions:

Air Temperature: 23.4 °C
Air Pressure: 1005 hPa
Relative Humidity: 56.7 %

4. Calibration Equipment:

Test Equipment	Type	Serial No.	Calibration Report Number	Traceable to
Multifunction Calibrator	B&K 4226	2288467	AV240081	HOKLAS
Sound Level Meter	RION NA-28	30721812	AV230128	HOKLAS

5. Calibration Results

5.1 Sound Pressure Level

Nominal value dB	Accept lower level dB	Accept upper level dB	Measured value dB
94.0	93.6	94.4	93.9

Note:

The values given in this certification only related to the values measured at the time of the calibration.



Certificate No.: APJ24-010-CC001

Page 2 of 2

Room 422, Leader Industrial Centre, 57-59 Au Pui Wan Street, Fo Tan, Shatin, N.T., Hong Kong
Tel: (852) 2668 3423 Fax: (852) 2668 6946
Homepage: <http://www.aa-lab.com> E-mail: inquiry@aa-lab.com



Certificate of Calibration

for

Description: Sound Level Meter
Manufacturer: SVANTEK
Type No.: SVAN 971 (Serial No.: 96062)
Microphone: ACO 7052E (Serial No.: 85231)
Preamplifier: SV-18 (Serial No.: 121481)

Submitted by:

Customer: Aurecon Hong Kong Limited
Address: Unit 1608, 16/F, Tower B, Manulife Financial Centre,
223-231 Wai Yip Street,
Kwun Tong, Kowloon, Hong Kong

Upon receipt for calibration, the instrument was found to be:

- Within (31.5Hz – 4kHz)
 Outside

the allowable tolerance.


The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory


Date of receipt: 22 July 2024

Date of calibration: 24 July 2024

Date of NEXT calibration: 23 July 2025

Calibrated by: 
Calibration Technician

Date of issue: 24 July 2024

Certified by: 
Mr. Ng Yan Wa
Laboratory Manager



Certificate No.: APJ23-155-CC002

Page 1 of 4



1. Calibration Precaution:

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 24 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.

2. Calibration Conditions:

Air Temperature: 23.4 °C
 Air Pressure: 1005 hPa
 Relative Humidity: 56.7 %

3. Calibration Equipment:

	Type	Serial No.	Calibration Report Number	Traceable to
Multifunction Calibrator	B&K 4226	2288467	AV240081	HOKLAS

4. Calibration Results

Sound Pressure Level

Reference Sound Pressure Level

Setting of Unit-under-test (UUT)				Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
35-137	dBA SPL	Fast	94	1000	94.0	±0.4	

Linearity

Setting of Unit-under-test (UUT)				Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
35-137	dBA SPL	Fast	94	1000	94.0	Ref	
			104		104.0	±0.3	
			114		114.0	±0.3	

Time Weighting

Setting of Unit-under-test (UUT)				Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
35-137	dBA SPL	Fast	94	1000	94.0	Ref	
		Slow			94.0	±0.3	

Certificate No.: APJ23-155-CC002



Page 2 of 4

Room 422, Leader Industrial Centre, 57-59 Au Pui Wan Street, Fo Tan, Shatin, N.T., Hong Kong
 Tel: (852) 2668 3423 Fax: (852) 2668 6946
 Homepage: <http://www.aa-lab.com> E-mail: inquiry@aa-lab.com



Frequency Response

Linear Response

Setting of Unit-under-test (UUT)			Applied value		UUT Reading,	IEC 61672 Class 1	
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
35-137	dB	SPL	Fast	94	31.5	94.6	±2.0
					63	94.4	±1.5
					125	94.4	±1.5
					250	94.3	±1.4
					500	94.2	±1.4
					1000	94.0	Ref
					2000	93.6	±1.6
4000	93.5	±1.6					

A-weighting

Setting of Unit-under-test (UUT)			Applied value		UUT Reading,	IEC 61672 Class 1	
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
35-137	dBA	SPL	Fast	94	31.5	55.2	-39.4±2.0
					63	68.3	-26.2±1.5
					125	78.2	-16.1±1.5
					250	85.6	-8.6±1.4
					500	90.9	-3.2±1.4
					1000	94.0	Ref
					2000	94.8	+1.2±1.6
4000	94.5	+1.0±1.6					

C-weighting

Setting of Unit-under-test (UUT)			Applied value		UUT Reading,	IEC 61672 Class 1	
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
35-137	dBC	SPL	Fast	94	31.5	91.6	-3.0±2.0
					63	93.6	-0.8±1.5
					125	94.2	-0.2±1.5
					250	94.3	-0.0±1.4
					500	94.2	-0.0±1.4
					1000	94.0	Ref
					2000	93.4	-0.2±1.6
4000	92.7	-0.8±1.6					



Certificate No.: APJ23-155-CC002

Page 3 of 4

Room 422, Leader Industrial Centre, 57-59 Au Pui Wan Street, Fo Tan, Shatin, N.T., Hong Kong
 Tel: (852) 2668 3423 Fax: (852) 2668 6946
 Homepage: <http://www.aa-lab.com> E-mail: inquiry@aa-lab.com



5. Calibration Results Applied

The results apply to the particular unit-under-test only. All calibration points are within manufacture’s specification as IEC 61672 Class 1.

Uncertainties of Applied Value:

94 dB	31.5 Hz	± 0.05
	63 Hz	± 0.05
	125 Hz	± 0.10
	250 Hz	± 0.05
	500 Hz	± 0.05
	1000 Hz	± 0.05
	2000 Hz	± 0.05
	4000 Hz	± 0.05
104 dB	1000 Hz	± 0.05
114 dB	1000 Hz	± 0.05

The uncertainties are evaluated for a 95% confidence level.

Note:

The values given in this certification only related to the values measured at the time of the calibration and any uncertainties quoted will not allow for the equipment long-term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the calibration. (A+A)*L shall not be liable for any loss or damage resulting from the use of the equipment.



Certificate No.: APJ23-155-CC002

Page 4 of 4

Room 422, Leader Industrial Centre, 57-59 Au Pui Wan Street, Fo Tan, Shatin, N.T., Hong Kong
 Tel: (852) 2668 3423 Fax: (852) 2668 6946
 Homepage: <http://www.aa-lab.com> E-mail: inquiry@aa-lab.com

APPENDIX F

Monitoring Data (Noise)

Location: N2a

Monitoring Period: August 2024

Parameter: Noise

Major Noise Source: Construction activities and daily operation of the sewerage treatment plant

Other Factors NA

Date	Weather	Start Time	L _{eq}	L ₁₀	L ₉₀
6/8/2024	Cloudy	14:17	70.9	73.7	67.2
13/8/2024	Sunny	14:16	65.6	68.1	62.0
20/8/2024	Sunny	14:42	67.3	69.9	63.3
27/8/2024	Sunny	14:45	68.3	71.1	63.6
Average			68.4		
Range			65.6 – 70.9		

Location: N3a

Monitoring Period: August 2024

Parameter: Noise

Major Noise Source: Construction activities and daily operation of the sewerage treatment plant

Other Factors: Many noisy vehicles passed by during monitoring

Date	Weather	Start Time	L _{eq}	L ₁₀	L ₉₀
6/8/2024	Cloudy	13:20	72.5	75.2	61.9
13/8/2024	Cloudy	13:24	73.9	75.9	55.8
20/8/2024	Sunny	13:36	71.2	74.3	53.9
27/8/2024	Sunny	13:59	72.5	74.9	54.8
Average			72.6		
Range			71.2 – 73.9		

Remarks: +3 dB(A) free-field corrections have been made to N3a.

Figure F.1 Measured daytime (0700-1900) noise level at the admin building inside the construction site (N2a)


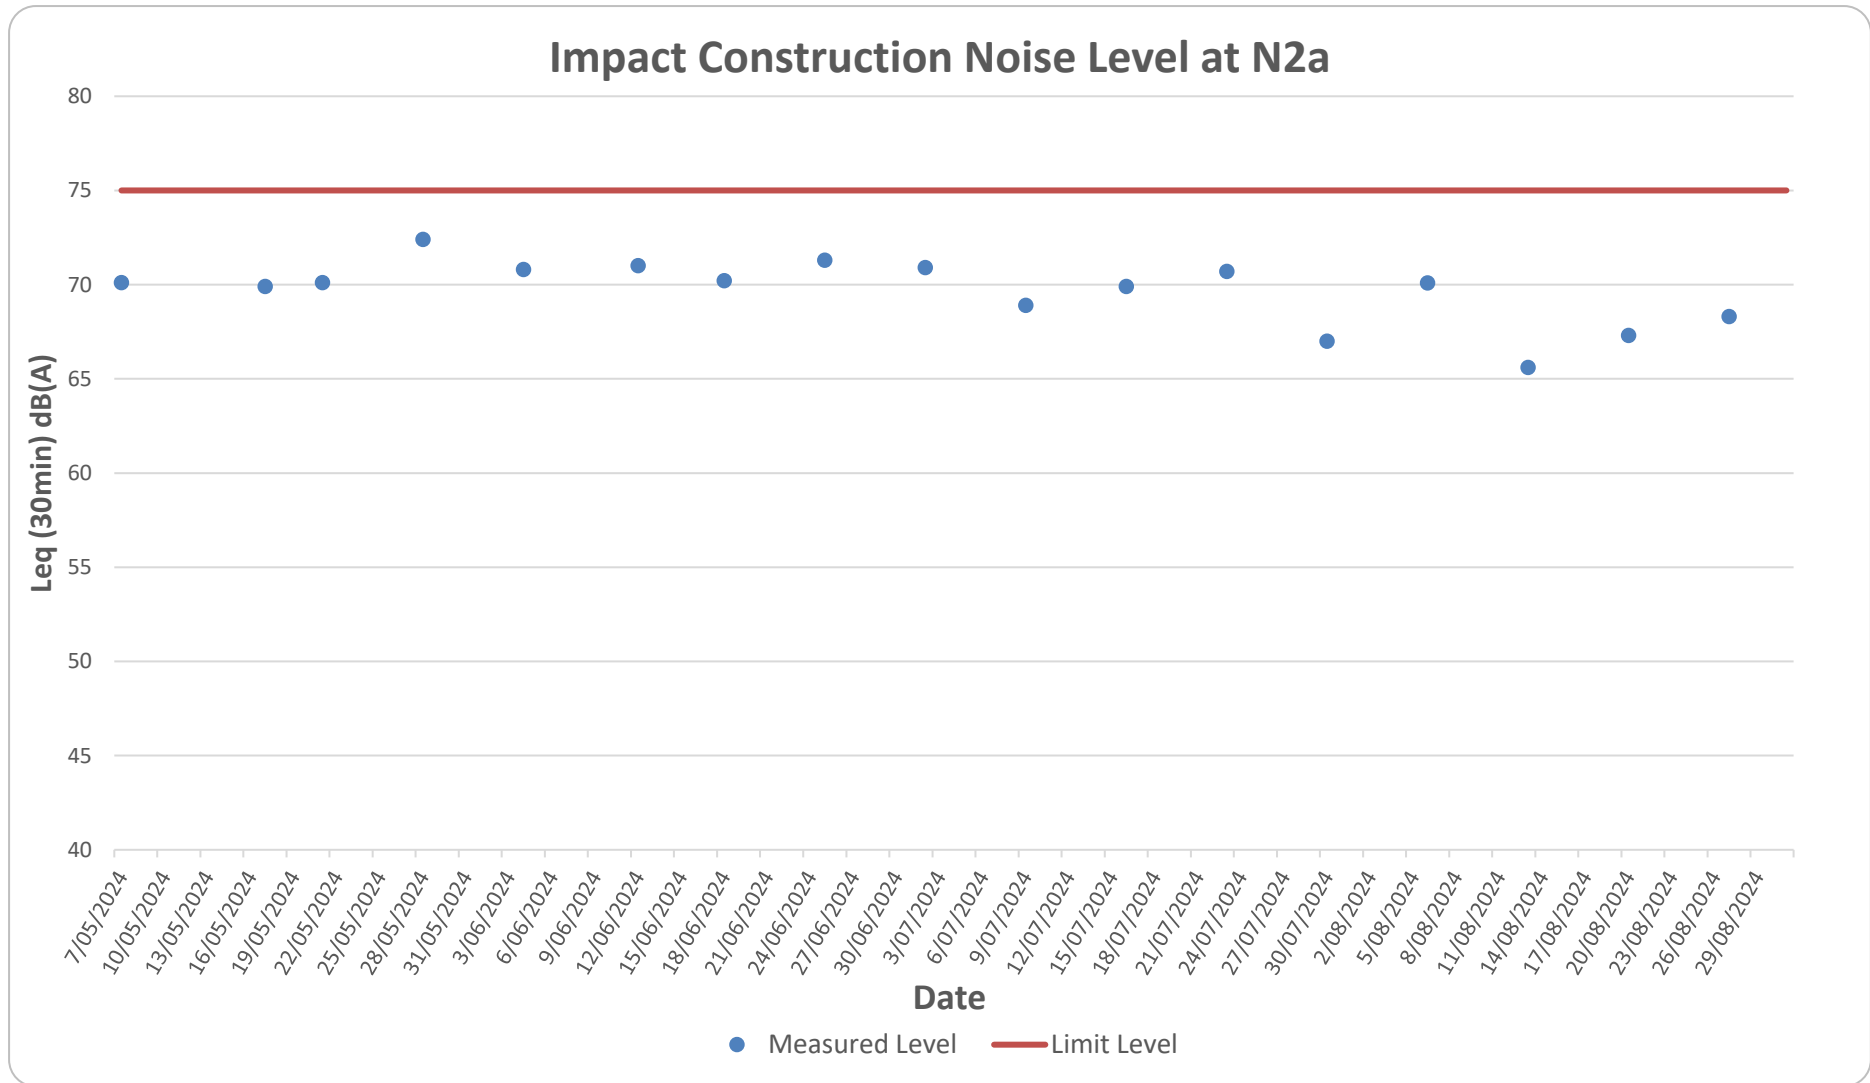


Figure F.2 Measured daytime (0700-1900) noise level at Cheung Chau Fire Station (N3a)

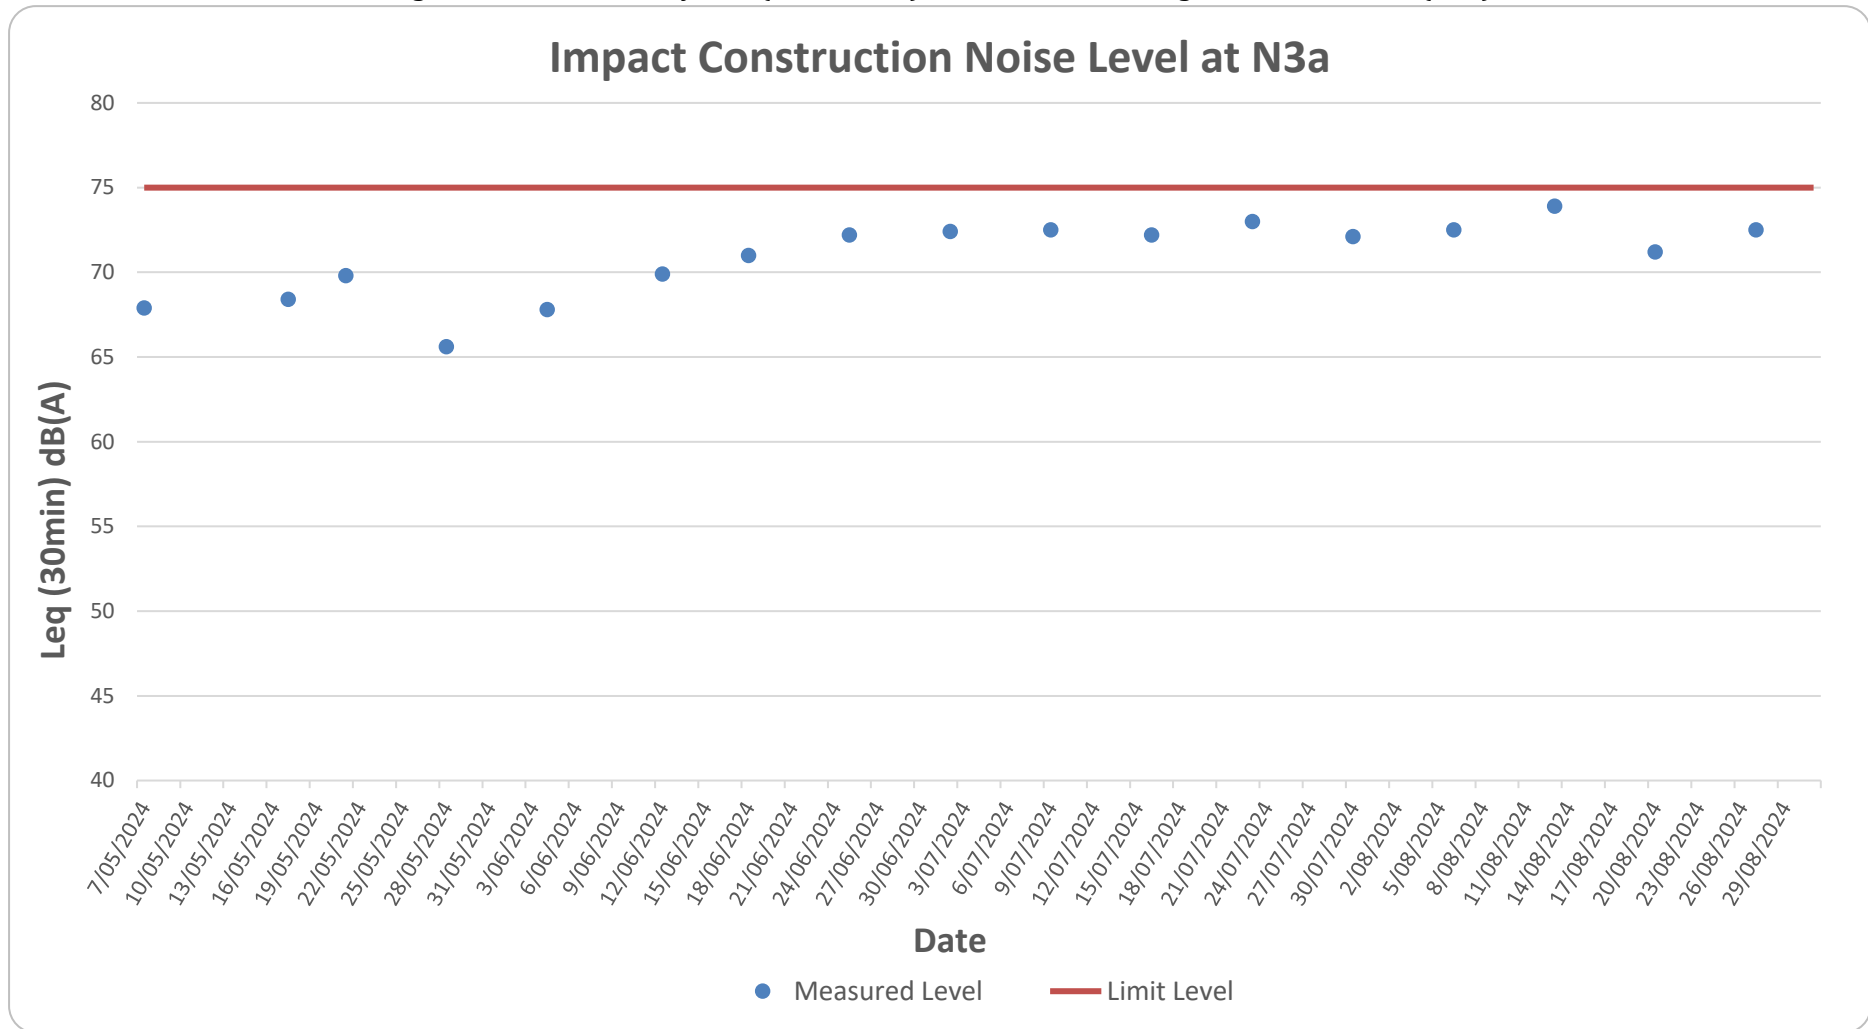

s: +3 dB(A) free-field corrections have been made to the data in the graph.

APPENDIX G

Implementation Schedule

EIA Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location / Timing of implementation of Measures			What requirements or standards for the measures to achieve?
				D	C	O	
Construction Phase (Upgrading Works of Cheung Chau STW and Pak She SPS (DP Component))							
S.3.5.5	Appropriate dust control measures should be implemented during the construction stage in accordance with the requirements in the Air Pollution Control (Construction Dust) Regulation. Dust control techniques should be considered to control dust to a level not exceeding the AQOs as well as the 1-hour TSP guideline level of 500 µg/m ³ . These measures include, but are not limited to, the following: <ul style="list-style-type: none"> • Adoption of good site practices; • Avoid practices likely to raise dust level; • Frequent cleaning and damping down of stockpiles and dusty areas of the site; • Covering the exposed areas with tarpaulin; • Reducing drop height during material handling; • Provision of wheel-washing facilities for site vehicles leaving the site; • Regular plant maintenance to minimize exhaust emission; and • Sweep up dust and debris at the end of each shift. 	Air Quality (fugitive dust) Control during Construction Phase	Contractors		√		Annex 4 and Annex 12 of EIAO -TM, Air Pollution Control (Construction Dust) Regulation
S.3.10.1	All the dust control measures as recommended in the Air Pollution Control (Construction Dust) Regulation, where applicable, should be implemented. Typical dust control measures include:	Air Quality (fugitive dust) Control during Construction Phase	Contractors		√		Annex 4 and Annex 12 of EIAO -TM, Air Pollution Control (Construction Dust) Regulation

Contract No. DC/2019/07
 Environmental Monitoring Works for Outlying Islands Sewerage Stage 2 -
 Upgrading of Cheung Chau Sewage Treatment and Disposal Facilities
 37th EM&A Report – August 2024

EIA Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location / Timing of implementation of Measures			What requirements or standards for the measures to achieve?
				D	C	O	
S.3.10.1	Watering every 1.5 hours on active works areas and paved haul roads to reduce dust emissions by 90.9% (e.g. watering intensity at 0.5 litres/m ² . Actual application shall depend on the site condition and weather conditions).	Air Quality (fugitive dust) Control during Construction Phase	Contractors		√		EIA, Annex 4 and Annex 12 of EIAO -TM, Air Pollution Control (Construction Dust) Regulation
S.3.10.1	Watering every hour on unpaved areas and stockpiles of dusty materials (if no tarpaulin is provided) to reduce dust emissions by 90% (e.g. watering intensity at 1.5 litre/m ² during the first hour, subsequent application at 0.2 litre/m ² . Actual application shall depend on the site condition and weather conditions).	Air Quality (fugitive dust) Control during Construction Phase	Contractors		√		EIA, Annex 4 and Annex 12 of EIAO -TM, Air Pollution Control (Construction Dust) Regulation
S.3.10.1	Use of regular watering, with complete coverage, to reduce dust emissions from exposed site surfaces and unpaved roads, particularly during dry weather	Air Quality (fugitive dust) Control during Construction Phase	Contractors		√		Annex 4 and Annex 12 of EIAO -TM, Air Pollution Control (Construction Dust) Regulation
S.3.10.1	Use of frequent watering for particularly dusty construction areas and areas close to ASRs	Air Quality (fugitive dust) Control during Construction Phase	Contractors		√		Annex 4 and Annex 12 of EIAO -TM, Air Pollution Control (Construction Dust) Regulation
S.3.10.1	Vehicle washing facilities should be provided at every vehicle exit point	Air Quality (fugitive dust) Control during Construction Phase	Contractors		√		Annex 4 and Annex 12 of EIAO -TM, Air Pollution Control (Construction Dust) Regulation

EIA Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location / Timing of implementation of Measures			What requirements or standards for the measures to achieve?
				D	C	O	
S.3.10.1	Where a site boundary adjoins a road, streets or other areas accessible to the public, hoarding of not less than 2.4 m high from ground level should be provided along the entire length except for a site entrance or exit	Air Quality (fugitive dust) Control during Construction Phase	Contractors		√		Annex 4 and Annex 12 of EIAO -TM, Air Pollution Control (Construction Dust) Regulation
S.3.10.1	Stockpiles of imported material kept on site shall be contained within hoarding, dampened and/or covered during dry and windy weather	Air Quality (fugitive dust) Control during Construction Phase	Contractors		√		Annex 4 and Annex 12 of EIAO -TM, Air Pollution Control (Construction Dust) Regulation
S.3.10.1	Material stockpiled alongside trenches should be covered with tarpaulins	Air Quality (fugitive dust) Control during Construction Phase	Contractors		√		Annex 4 and Annex 12 of EIAO -TM, Air Pollution Control (Construction Dust) Regulation
S.3.10.1	Open stockpiles shall be avoided or covered. Where possible, prevent placing dusty material storage piles near ASRs	Air Quality (fugitive dust) Control during Construction Phase	Contractors		√		Annex 4 and Annex 12 of EIAO -TM, Air Pollution Control (Construction Dust) Regulation

EIA Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location / Timing of implementation of Measures			What requirements or standards for the measures to achieve?
				D	C	O	
S.3.10.1	Any excavated or stockpile of dusty material should be covered entirely by impervious sheeting or sprayed with water to maintain the entire surface wet during the non-working hours	Air Quality (fugitive dust) Control during Construction Phase	Contractors		√		Annex 4 and Annex 12 of EIAO -TM, Air Pollution Control (Construction Dust) Regulation
S.3.10.1	All dusty materials shall be sprayed with water prior to any loading, unloading or transfer operation so as to keep the dusty materials wet	Air Quality (fugitive dust) Control during Construction Phase	Contractors		√		Annex 4 and Annex 12 of EIAO -TM, Air Pollution Control (Construction Dust) Regulation
S.3.10.1	Water sprays shall be used during the delivery and handling of sands aggregates and the like	Air Quality (fugitive dust) Control during Construction Phase	Contractors		√		Annex 4 and Annex 12 of EIAO -TM, Air Pollution Control (Construction Dust) Regulation
S.3.10.1	All demolished items that may emit dust particles should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides within a day of demolition	Air Quality (fugitive dust) Control during Construction Phase	Contractors		√		Annex 4 and Annex 12 of EIAO -TM, Air Pollution Control (Construction Dust) Regulation

EIA Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location / Timing of implementation of Measures			What requirements or standards for the measures to achieve?
				D	C	O	
S.3.10.1	<p><u>Good site practices for concrete batching plant</u></p> <p>Every stock of more than 20 bags of cement or dry pulverized fuel ash(PFA) should be cover entirely by impervious sheeting or placed in an area sheltered on the top and the sides.</p> <p>Cement or dry PFA delivered in bulk should stored in a closed silo fitted with an audible high level alarm which is interlocked with the material filling line and no overfilling is allowed.</p> <p>Loading, unloading, transfer, handling or storage of bulk cement or dry PFA should be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with effective fabric filter or equivalent air pollution control system (Maximum TSP emission factor of Silos and Mising Tower: 50mg/m³)</p>	Air Quality (fugitive dust) Control during Construction Phase	Contractors		√		<p>Annex 4 and Annex 12 of EIAO -TM, Air Pollution Control (Construction Dust) Regulation</p> <p>Best Practical Means for Cement Works (Concrete Batching Plant) BPM 3/2(93)</p>

Contract No. DC/2019/07
 Environmental Monitoring Works for Outlying Islands Sewerage Stage 2 -
 Upgrading of Cheung Chau Sewerage Treatment and Disposal Facilities
 37th EM&A Report – August 2024

EIA Ref.	Recommended Environmental Protection Measures / Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location / Timing of implementation of Measures	What requirements or standards for the measures to achieve?
Construction Phase (Upgrading Works of Cheung Chau STW and Pak She SPS (DP Component))					
S.4.4.12	Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction works.	Noise control during construction	Contractors	At all construction areas of the site during the entire construction period	EIA, Contractual requirements
S.4.4.12	Machines and plant that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum.	Noise control during construction	Contractors	At all construction areas of the site during the entire construction period	EIA, Contractual requirements
S.4.4.12	Plant known to emit noise strongly in one direction should, where possible, be orientated to direct noise away from the NSRs.	Noise control during construction	Contractors	At all construction areas of the site during the entire construction period	EIA, Contractual requirements
S.4.4.12	Mobile plant should be sited as far away from NSRs as possible.	Noise control during construction	Contractors	At all construction areas of the site during the entire construction period	EIA, Contractual requirements
S.4.4.12	Material stockpiles and other structures should be effectively utilized, where practicable, to screen noise from on-site construction activities.	Noise control during construction	Contractors	At all construction areas of the site during the entire construction period	EIA, Contractual requirements

Contract No. DC/2019/07
Environmental Monitoring Works for Outlying Islands Sewerage Stage 2 -
Upgrading of Cheung Chau Sewage Treatment and Disposal Facilities
37th EM&A Report – August 2024

EIA Ref.	Recommended Environmental Protection Measures / Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location / Timing of implementation of Measures	What requirements or standards for the measures to achieve?
S.4.4.13	Use of quiet plant (PME): <ul style="list-style-type: none"> • Generator • Poker, vibratory, hand-held • Breaker, excavator mounted (hydraulic) • Excavator • Tracked Mobile Crane • Vibratory Compactor • Dumper • Air compressor • Concrete Pump • Piling Rig 	Noise control during construction	Contractors	At all construction areas of the site during the entire construction period	EIA, Contractual requirements
S.4.4.14	Temporary site hoardings of 2.4 m high are recommended for the works at the Pak She SPS. The hoardings will be erected along the works boundary facing the NSRs. The PME involved in the works would be screened by the erected site hoardings. Without direct line of sight from the affected NSRs, a noise reduction of 10 dB(A) could be achieved provided that the hoardings have no openings or gaps and have a surface mass of at least 7 kg/m ² . Nonetheless, a -5 dB(A) screening correction for site hoardings has been applied as a more conservative approach.	Noise control during construction	Contractors	At Pak She SPS during the entire construction period	EIA
S.4.4.23	For NSRs which would be affected by more than one Works Types, good scheduling works is recommended to minimize the cumulative construction noise impacts due to different Works Types.	Noise control during construction	Contractors	Construction areas near the specified locations during the construction period	EIA, Contractual requirements

Contract No. DC/2019/07
Environmental Monitoring Works for Outlying Islands Sewerage Stage 2 -
Upgrading of Cheung Chau Sewage Treatment and Disposal Facilities
37th EM&A Report – August 2024

EIA Ref.	Recommended Environmental Protection Measures / Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location / Timing of implementation of Measures	What requirements or standards for the measures to achieve?
S.4.4.29	In order to prevent potential cumulative construction noise impacts to NSRs, the works at Tai Kwai Wan San Tsuen are recommended to be scheduled to avoid concurrent works at the areas near Tai Kwai Wan of the Improvement of Fresh Water Supply to Cheung Chau project.	Noise control during construction	DSD and Contractors	Construction areas near the specified locations during the construction period	EIA, Contractual requirements
S.4.4.30	The contractor shall liaise with “Replacement and Rehabilitation of Water Mains Stage 4, Mains on Hong Kong and Islands – Investigation, Design and Construction” contractors so as to avoid undertaking works concurrently with the works when they are in the close proximity as far as practicable.	Noise control during construction	DSD and Contractors	Construction areas near the specified locations during the construction period	EIA, Contractual requirements
S.4.4.31	The contractor shall liaise with Improvement to Existing Roads and Drains in Cheung Chau Old Town, Remaining Engineering Works Stage 3 works contractors so as to avoid undertaking works concurrently with the works when they are in the close proximity as far as practicable.	Noise control during construction	DSD and Contractors	Construction areas near the specified locations during the construction period	EIA, Contractual requirements

EIA Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	When to implement the measures?			What requirements or standards for the measures to achieve?
				D	C	O	
Construction Phase (Upgrading Works of Cheung Chau STW and Pak She SPS (DP Component) and Sewers Works (non-DP Component))							
S.5.7.1	<p>Practices outlined in ProPECC PN 1/94 Construction Site Drainage are recommended, as highlighted below:</p> <ul style="list-style-type: none"> Perimeter channels are to be installed in works areas to intercept runoff at the site boundary prior to the commencement of any earthworks. Surface runoff should be discharged into storm drains via sand/ silt removal facilities with an adequate capacity; Works programme should be designed to minimize works areas to reduce soil exposure and site runoff; Silt removal facilities, channels and manholes should be maintained and cleaned regularly to ensure their proper functions; Works programme should be carefully planned to minimize the scale of soil excavation during the rainy season; Earthworks surfaces should be well compacted and subsequent permanent works or surface protection measures should be carried out immediately; All vehicles should be washed before they leave the construction site to avoid earth, mud, and debris being carried off from the site. Wash-water should be treated to remove sand and silt at least on a weekly basis to ensure the continued efficiency of the washing facility; 	Water Quality Control	Contractors		√		<ul style="list-style-type: none"> WPCO; TM –Effluent Standards for Effluents Discharged into Drainage and Sewerage Systems, Inland and Coastal Water

EIA Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	When to implement the measures?			What requirements or standards for the measures to achieve?
				D	C	O	
(cont...)	<ul style="list-style-type: none"> Open stockpiles of construction materials on site should be covered with tarpaulin or similar fabric materials during storms; For sections of pipes that need to be laid underneath water courses with the open cut method, site works should be carried out during the dry season with a temporary drainage diversion; and; Any construction works along Hak Pai Road immediately by the Kwun Yam beach and Cheung Chau Tung Wan beach should be avoided during the swimming season. 	Water Quality Control	Contractors		√		<ul style="list-style-type: none"> WPCO; TM –Effluent Standards for Effluents Discharged into Drainage and Sewerage Systems, Inland and Coastal Water
S.5.7.2 and S.5.7.3	<p>Mitigations Measures for General Construction Activities:</p> <ul style="list-style-type: none"> Good site practices should be adopted to regularly clean the construction sites to avoid rubbish, debris and litter from entering to nearby water bodies; and Good construction and site management practices should be implemented to ensure that litter, fuels, and solvents would not enter the public drainage systems. 	Water Quality Control	Contractors		√		<ul style="list-style-type: none"> WPCO; TM –Effluent Standards for Effluents Discharged into Drainage and Sewerage Systems, Inland and Coastal Water

EIA Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	When to implement the measures?			What requirements or standards for the measures to achieve?
				D	C	O	
S.5.7.4	Domestic sewage generated by workforce would be collected and discharged to the STW for proper treatment. Portable toilets should be provided by the Contractor, where necessary, to handle sewage from the workforce. The Contractor should also be responsible for waste disposal.	Water Quality Control	Contractors		√		<ul style="list-style-type: none"> • WPCO; • TM –Effluent Standards for Effluents Discharged into Drainage and Sewerage Systems, Inland and Coastal Water
S.5.7.5 and S.5.7.6	Mitigations Measures for Spillage of Chemicals: <ul style="list-style-type: none"> • Registration to EPD as a Chemical Waste Producer if chemical wastes are generated and need to be disposed of; • Illegal disposal of chemicals should be strictly prohibited; and • Oils and fuels should only be used and stored in the designated area which has polluting prevention facilities. 	Water Quality Control	Contractors		√		<ul style="list-style-type: none"> • WPCO; • TM –Effluent Standards for Effluents Discharged into Drainage and Sewerage Systems, Inland and Coastal Water

Contract No. DC/2019/07
Environmental Monitoring Works for Outlying Islands Sewerage Stage 2 -
Upgrading of Cheung Chau Sewage Treatment and Disposal Facilities
37th EM&A Report – August 2024

EIA Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	When to implement the measures?			What requirements or standards for the measures to achieve?
				D	C	O	
Construction Phase (Upgrading Works of Cheung Chau STW and Pak She SPS (DP Component) and Sewers Works (non-DP Component))							
S.6.6.1	The Contractor shall prepare a Waste Management Plan in accordance with the requirements set out in the ETWB TCW No. 19/2005, Waste Management on Construction Site, for the ER's approval. The WMP shall include monthly and yearly Waste Flow Tables that indicate the amounts of waste generated, recycled and disposed of (including final disposal site).	Waste management during construction	Contractors		√		ETWB TCW No. 19/2005, Waste Management on Construction Sites
S.6.6.1	The Contractor's waste management practices and effectiveness shall be audited by the Engineer's Representative on regular basis.	Waste management during construction	DSD		√		Waste Disposal Ordinance
S.6.6.1	The Contractor shall provide training for site staff concept of site cleanliness and appropriate waste management procedures, including waste reduction, reuse and recycling.	Waste management during construction	Contractors		√		Waste Disposal Ordinance
S.6.6.1	Sufficient waste disposal points and regular collection of waste shall be provided.	Waste management during construction	Contractors		√		Waste Disposal Ordinance
S.6.6.1	Trucks with covering for the open-box bed and enclosed container shall be used to minimise windblown litter and dust during transportation of waste.	Waste management during construction	Contractors		√		Waste Disposal Ordinance
S.6.6.1	Regular cleaning and maintenance programme for drainage systems, pumps and oil interceptors.	Waste management during construction	Contractors		√		Waste Disposal Ordinance

Contract No. DC/2019/07
Environmental Monitoring Works for Outlying Islands Sewerage Stage 2 -
Upgrading of Cheung Chau Sewage Treatment and Disposal Facilities
37th EM&A Report – August 2024

EIA Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	When to implement the measures?			What requirements or standards for the measures to achieve?
				D	C	O	
S.6.6.1	Separation of chemical wastes for special handling and appropriate treatment at a Chemical Waste Treatment Facility (CWTF).	Waste management during construction	Contractors		√		Waste Disposal (Chemical Waste) (General) Regulation
S.6.6.1	Encourage collection of aluminium cans, paper and plastic bottles by providing separate labelled bins to enable these wastes to be segregated from other general refuse generated by the workforce.	Waste management during construction	Contractors		√		Waste Disposal Ordinance
S.6.6.1	Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal.	Waste management during construction	Contractors		√		Waste Disposal Ordinance
S.6.6.1	A recording system for the amount of wastes generated, recycled and disposed (including disposal sites) should be proposed.	Waste management during construction	Contractors		√		Waste Disposal Ordinance
S.6.6.1	Plan and stock construction materials to minimise amount of waste generated and avoid unnecessary generation of waste.	Waste management during construction	Contractors		√		Waste Disposal Ordinance
S.6.6.2	Alternatives C&D materials such as steel frameworks and plastic fencing can be considered to increase the chances for reuse.	Waste management during construction	Contractors		√		Waste Disposal Ordinance
S.6.6.3	In order to minimise the potential environmental impacts resulting from collection and transportation of C&D materials for off-site disposal, the excavated materials comprising fill materials should be reused on-site as backfilling materials as far as practicable.	Waste management during construction	Contractors		√		Waste Disposal Ordinance

Contract No. DC/2019/07
 Environmental Monitoring Works for Outlying Islands Sewerage Stage 2 -
 Upgrading of Cheung Chau Sewerage Treatment and Disposal Facilities
 37th EM&A Report – August 2024

EIA Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	When to implement the measures?			What requirements or standards for the measures to achieve?
				D	C	O	
S.6.6.4	C&D waste, such as wood, plastic, steel and other metals should be reused or recycled and, as a last resort, disposed of to landfill sites. A suitable area should be designated within the site for temporary stockpiling of C&D materials and to facilitate the sorting process. In order to monitor the disposal of C&D materials at the designated public fill reception facility and landfill and to control fly-tipping, a trip ticket system should be included. Reference can be made to Development Bureau Technical Circular (Works) (TC(W)) No. 6/2010 for details.	Waste management during construction	Contractors		√		Development Bureau Technical Circular (Works) (TC(W)) No. 6/2010, Waste Disposal Ordinance
S.6.6.5	The C&D materials to be disposed of at public filling reception facilities shall be only materials consist of brick, concrete, cement plaster, soil and inert building debris. The materials shall be free from plastics, chemical waste, industrial metals and other materials that are considered unsuitable at the facility.	Waste management during construction	Contractors		√		Waste Disposal Ordinance
S.6.6.6	General refuse should be stored in enclosed bins or compaction units separate from C&D materials. A reputable waste collector should be employed by the contractor to remove general refuse from the site regularly, separately from C&D materials. An enclosed and covered area is preferred to reduce the occurrence of 'wind blown' light materials. In addition, a sufficient number of enclosed bins shall be provided on site for containment of general refuse to prevent visual impacts and nuisance to the sensitive surrounding.	Waste management during construction	Contractors		√		Waste Disposal Ordinance

EIA Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	When to implement the measures?			What requirements or standards for the measures to achieve?
				D	C	O	
S.6.6.7	For the disposal of chemical wastes produced at the construction site, the Contractor is required to register with the EPD as a Chemical Waste Producer and to follow the requirements stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Good quality containers compatible with the chemical wastes should be used. Appropriate labels should be securely attached on each chemical waste container indicating the chemical characteristics of the chemical waste, such as explosives, flammable oxidizing, irritant, toxic, harmful, corrosive, etc. The Contractor shall also use a licensed waste collector engaged to transport and dispose of the chemical wastes in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.	Waste management during construction	Contractors		√		Waste Disposal (Chemical Waste) (General) Regulation
S.6.6.8	Chemical toilets to be provided on-site shall be regularly cleaned and the night-soil collected and transported by a licensed contractor to a Government Sewerage Treatment Works facility for disposal.	Waste management during construction	Contractors		√		Waste Disposal Ordinance

EIA Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	When to implement the measures?			What requirements or standards for the measures to achieve?
				D	C	O	
Construction Phase (Upgrading Works of Cheung Chau STW (DP Component))							
Table 11.8	Visual Screen/Hoarding Decorative hoarding or boundary fence for construction sites shall be considered, and designed to be compatible to the surroundings.	To minimise the potential visual impacts	Contractors		√		N/A

EIA Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	When to implement the measures?			What requirements or standards for the measures to achieve?
				D	C	O	
Table 11.8	<p>Protection to Existing Trees within Works Areas</p> <p>All existing trees which are not in direct conflict with the proposed works will be retained. The existing trees proposed to be retained shall be properly maintained and protected by means of fencing to prevent vehicular or pedestrian intrusion that may potentially damage tree canopies, trunks and root zones. Detailed tree protection specifications shall be allowed and included in the Contract Specification, which specifying the tree protection requirement, submission and approval system, and tree monitoring system. For trees with high preservation value, individual tree assessments and continuous tree monitoring reports shall be provided by a certified Arborist, Landscape Architect or related professional during construction. All retained trees shall be recorded photographically at the commencement of contract.</p> <p>Root pruning to the retained trees should be prohibited. Retained trees should be well-preserved by setting up a tree protection zone throughout the construction period for protecting the retained trees from damages.</p> <p>To maximize protection to existing trees and ground vegetation, construction contracts may designate “No-intrusion Zone” to various areas within the site boundary with rigid and durable fencing for each individual no-intrusion zone. The contractor should close monitor and restrict the site working staff not to enter the “no-intrusion zone”, even for non-direct construction activities and storage of equipment.</p>	Landscape mitigation measures	DSD and Contractors	√	√		EIA, Annex 10 and Annex 18 of EIAO-TM

EIA Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	When to implement the measures?			What requirements or standards for the measures to achieve?
				D	C	O	
Table 11.8	<p>Tree Transplanting</p> <p>Existing trees to be affected shall be directly transplanted to the proposed tree receiving sites, or to temporary tree nurseries alternatively. Temporary tree nurseries may be set up for the transplanted tree and proposed trees at an early stage to allow small trees to grow during the construction stage. By the time when planting area becomes available, trees have been mature and required minimal pruning and suffer much less damage during transplanting. The construction programme should also allow sufficient time for root pruning and root ball preparation prior to transplanting, if necessary, and transplanting operations to be carried out in planting season.</p> <p>Tree pruning such as topping, lion tailing would be prohibited as far as possible. Also, frequent keep watering would be necessary for transplanting trees. The proposed tree preservation measures during construction would be carried out and approved by the competent persons.</p>	Landscape mitigation measures	DSD and Contractors	√	√		EIA, Annex 10 and Annex 18 of EIAO-TM
Table 11.8	<p>Construction Light</p> <p>Security floodlight for construction areas shall be controlled, such as equipped with adjustable shield, frosted diffusers and reflective covers, at night to avoid excessive glare to the nearby areas and residents. Other security measures shall also be considered to minimize the visual impacts by construction light.</p>	To reduce the night-time glare effect to the surrounding environs.	Contractors		√		EIA, Annex 10 and Annex 18 of EIAO-TM

EIA Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	When to implement the measures?			What requirements or standards for the measures to achieve?
				D	C	O	
Table 11.8	Dust and Erosion Control for Exposed Soil Excavation works and demolition of existing building blocks shall be well planned with precautions to suppress dust. Exposed soil shall be covered or watered often. Areas that are expected to be left with bare soil for a long period of time after excavation shall be properly covered with suitable protective fabric. Suitable drainage shall be provided around construction sites to avoid discharge of contaminants and sediments into sensitive water-based habitats.	To minimise the disturbance to existing landscape resources and minimise the impacts on the visual amenity of the area	Contractors		√		EIA, Annex 10 and Annex 18 of EIAO-TM
Table 11.8	Reinstatement of Works Areas The affected works areas shall be properly reinstated to the satisfaction of relevant government departments.	Landscape mitigation measures	Contractors		√		EIA, Annex 10 and Annex 18 of EIAO-TM

APPENDIX H

Summary of All Complaints Received, Notification of Summons and Successful Prosecutions

Statistical Summary of Environmental Complaints

Reporting Period	Environmental Complaints Statistics		
	Frequency	Nature	Follow-up Actions
1 August 2024 - 31 August 2024	0	N/A	N/A
Cumulative	1*	Water	N/A

*Follow-up action is mentioned in Complaint Investigation Report of the Complaint Log No. C-001 submitted on 21 Dec 2023.

Statistical Summary of Environmental Summons

Reporting Period	Environmental Summons Statistics		
	Frequency	Nature	Follow-up Actions
1 August 2024 - 31 August 2024	0	N/A	N/A
Cumulative	0	N/A	N/A

Statistical Summary of Environmental Prosecution

Reporting Period	Environmental Prosecution Statistics		
	Frequency	Nature	Follow-up Actions
1 August 2024 - 31 August 2024	0	N/A	N/A
Cumulative	0	N/A	N/A

APPENDIX I

EM&A Monitoring Schedules in the Reporting Period and the Next Reporting Period (Tentative)

Impact Monitoring Schedule for Upgrading of Cheung Chau Sewage Collection, Treatment and Disposal Facilities						
Aug-24						
Sun	Mon	Tue	Wed	Thu	Fri	Sat
31				1	2	3
	24-hour TSP monitoring for A1a & A2a 1-hour TSP monitoring for A1a & A2a	Daytime Noise monitoring for N2a & N3a		24-hour TSP monitoring for A1a & A2a 1-hour TSP monitoring for A1a & A2a		
4	5	6	7	8	9	10
	24-hour TSP monitoring for A1a & A2a 1-hour TSP monitoring for A1a & A2a	Daytime Noise monitoring for N2a & N3a				
11	12	13	14	15	16	17
	24-hour TSP monitoring for A1a & A2a 1-hour TSP monitoring for A1a & A2a	Daytime Noise monitoring for N2a & N3a				
18	19	20	21	22	23	24
	24-hour TSP monitoring for A1a & A2a 1-hour TSP monitoring for A1a & A2a	Daytime Noise monitoring for N2a & N3a				
25	26	27	28	29	30	31
	24-hour TSP monitoring for A1a & A2a 1-hour TSP monitoring for A1a & A2a	Daytime Noise monitoring for N2a & N3a				

Impact Monitoring Schedule for Upgrading of Cheung Chau Sewerage Collection, Treatment and Disposal Facilities						
Sep-24						
Sun	Mon	Tue	Wed	Thu	Fri	Sat
1	2	3	4	5	6	7
	24-hour TSP monitoring for A1a & A2a 1-hour TSP monitoring for A1a & A2a	Daytime Noise monitoring for N2a & N3a				
8	9	10	11	12	13	14
	24-hour TSP monitoring for A1a & A2a 1-hour TSP monitoring for A1a & A2a	24-hour TSP monitoring for A1a & A2a 1-hour TSP monitoring for A1a & A2a	Daytime Noise monitoring for N2a & N3a			
15	16	17	18	19	20	21
	24-hour TSP monitoring for A1a & A2a 1-hour TSP monitoring for A1a & A2a	Daytime Noise monitoring for N2a & N3a				
22	23	24	25	26	27	28
	24-hour TSP monitoring for A1a & A2a 1-hour TSP monitoring for A1a & A2a	Daytime Noise monitoring for N2a & N3a				
29	30					
			24-hour TSP monitoring for A1a & A2a 1-hour TSP monitoring for A1a & A2a	Daytime Noise monitoring for N2a & N3a		
