

## **Drainage Services Department**

## Port Shelter Sewerage, Stage 3 – Sewerage Works at Po Toi O Monthly EM&A Report (October 2024)

Prepared by SGS Hong Kong Limited

**Certified by:** 

Verified by:

Johnathan Ho

Toang Fauldeng

F.C. Tsang

Environmental Team Leader Independent Environmental Checker

SGS Hong Kong Ltd. Units 303 & 305, 3/F, Building 22E Phase 3, Hong Kong Science Park Pak Shek Kok, New Territories Hong Kong, China





Our Ref: PL-202411024

Drainage Services Department Special Duty Division 42/F, Revenue Tower, 5 Gloucester Road, Wan Chai, Hong Kong.

Attention: Mr. Gary CHUNG

13 November 2024

Dear Gary,

## Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O Monthly EM&A Report for October 2024

Reference is made to your submission of the Monthly EM&A Report for October 2024 received by email on 08 November 2024 and the subsequent revision on 13 November 2024. We are pleased to inform you that we have no adverse comment on the captioned report.

Thank you for your attention. Please do not hesitate to contact the undersigned should you have any queries.

Yours faithfully,

Toam Jan Bearg

F.C. Tsang Independent Environmental Checker

cc. ETL – Johnathan HO



## Drainage Services Department Port Shelter Sewerage, Stage 3 – Sewerage Works at Po Toi O Monthly EM&A Report (Period from 1 to 31 October 2024)

Prepared by

**Drainage Services Department** 

**SGS Hong Kong Limited** 

Revision	Description	Prepared by	Checked by	Approved by	Date
01	Submission	Various	Johnathan Ho	Grace Fung	Nov 2024

#### Disclaimer

This document is issued by the Company under its General Conditions of Service accessible at <u>http://www.sgs.com/en-hk/Terms-and-Conditions.aspx</u>. Attention is drawn to the limitation of liability, indemnification and jurisdiction issues defined therein.

Any holder of this document is advised that information contained hereon reflects the Company's findings at the time of its intervention only and within the limits of Client's instructions, if any. The Company's sole responsibility is to its Client and this document does not exonerate parties to a transaction from exercising all their rights and obligations under the transaction documents. Any unauthorized alteration, forgery or falsification of the content or appearance of this document is unlawful and offenders may be prosecuted to the fullest extent of the law.

SGS	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	3
	Works at Po Toi O	Ref#	EMA2403/03/42
	Monthly EM&A Report	Rev.	01
		Date	Nov 24

### TABLE OF CONTENT

1.	EXECUTIVE SUMMARY	4
2.	INTRODUCTION	6
3.	AIR QUALITY	9
4.	NOISE	7
5.	WATER QUALITY	1
6.	WASTE MANAGEMENT	5
7.	ENVIRONMENTAL SITE INSPECTION AND AUDIT2	6
8.	FUTURE KEY ISSUES	0
9.	CONCLUSION	1
FIGUR	E 2-1 – LAYOUT PLAN OF THE CAPTIONED PROJECT	
FIGUR	E 3-1 PROPOSED AIR QUALITY AND NOISE MONITORING STATIONS LOCATIONS	
FIGUR	E 5-1 LOCATIONS OF WATER QUALITY IMPACT MONITORING STATIONS	
APPEN	NDIX A – PROJECT ORGANIZATION CHART	
APPEN	NDIX B - CONSTRUCTION PROGRAMME	
APPEN	NDIX C – METEORLOGICAL DATA	
APPEN	NDIX D – AIR QUALITY MONITORING EQUIPMENT CALIBRATION CERTIFICATES	
	NDIX E – METHODOLOGY FOR CORRELATION CALCULATION BETWEEN POTABLE LASER DUST	
APPEN	NDIX F – AIR QUALITY AND NOISE IMPACT MONITORING SCHEDULE	
APPEN	NDIX G – AIR QUALITY MONITORING RESULT	
APPEN	NDIX H – EVENT AND ACTION PLAN	
APPEN	NDIX I - NOISE MONITORING EQUIPMENT CALIBRATION CERTIFICATES	
APPEN	NDIX J - NOISE IMPACT MONITORING RESULT	
APPEN	NDIX K – WATER QUALITY MONITORING SCHEDULE	
APPEN	NDIX L – WATER QUALITY MONITORING RESULTS	
APPEN	NDIX M – CALIBRATION CERTIFICATE OF WATER QUALITY MONITORING EQUIPMENT	
APPEN	NDIX N – MONTHLY SUMMARY OF WASTE FLOW	
APPEN	NDIX O - IMPLEMENTATION SCHEDULE OF RECOMMENDED MITIGATION MEASURES	
APPEN	NDIX P - RECOMMENDED MITIGATION MEASURES AND PROACTIVE ENVIRONMENTAL PROTECT	ION PROFORMA



#### 1. EXECUTIVE SUMMARY

- 1.1 The proposed sewerage works in Po Toi O (hereafter as "the Project") is an environmental enhancement project that aims to improve environmental hygiene of the Po Toi O area. The Environmental Impact Assessment (EIA) Report for the Project (Register No: AEIAR-206/2017) was approved on 27 January 2017. The Environmental Permit (EP) (Permit No.: EP-516/2016) was issued on 27 January 2017 and is the current permit for the Project.
- 1.2 Société Générale de Surveillance (SGS) Hong Kong Limited has been appointed by Drainage Services Department (DSD) under service contract no. SD 4/2024 as the Environmental Team (ET) to undertake the EM&A programme during construction phase of the Project in accordance with the approved EM&A Manual for the Project.
- 1.3 This is the 44<sup>th</sup> monthly Environmental Monitoring & Audit (EM&A) Report prepared by SGS for the Project. This report summarized the monitoring results and audits findings of the EM&A programme under the EP and the EM&A Manual of the Project during the reporting period of 1 October 2024 to 31 October 2024.

#### Key Construction Works During the Reporting Period

- 1.4 The main works undertaken during the reporting period are as follows:
  - Major activities in the reporting month:
  - a) Construction of village sewer;
  - b) Excavation works and construction of ELS for Po Toi O Sewage Treatment Plant;
  - c) Enlargement of HDD and Pipe Installation

#### Summary of Exceedances, Investigation and Follow-up

- 1.5 There was no action or limit level exceedance record of construction noise and air quality was recorded in the reporting month.
- 1.6 In this Reporting Period, twenty-six (26) Action Level and zero (0) Level exceedances of Suspended Solids were recorded. Notification of Exceedances (NOEs) had been issued to relevant parties. Investigation for the cause of exceedance was carried out by ET subsequently.

#### **Complaint Handling, Prosecution and Public Engagement**

- 1.7 No complaints, notification of summons and successful prosecution was received in the reporting period. No public engagement activity was conducted in the reporting month.
- 1.8 No notification of summons and successful prosecution was received in the reporting period. No public engagement activity was conducted in the reporting month.
- 1.9 No air quality, noise and water complaints was received in the reporting month.



#### Reporting Change of EM&A Programme

1.10 No reporting change of the EM&A programme in this reporting month.

#### Future Key Issues

1.11 The main works will be anticipated in the next reporting period are as follows:

-Major activities in the upcoming month:

- Construction of village sewer;
- Construction of Cofferdam;
- Excavation works and construction of ELS for Po Toi O Sewage Treatment Plant;
- Enlargement of HDD and Pipe Installation



#### 2. INTRODUCTION

#### **Project Information**

2.1 Société Générale de Surveillance (SGS) Hong Kong Limited has been appointed by Drainage Services Department (DSD) as the Environmental Team (ET) to undertake the EM&A programme during construction phase of the Project in accordance to the approved EM&A Manual for the proposed sewerage works in Po Toi O (hereafter as "The Project"), an environmental enhancement project that aims to improve environmental hygiene of the Po Toi O area.

#### **Project Background**

- 2.2 Po Toi O is located in the southern part of Sai Kung District, next to Clear Water Bay. There is a small settlement called Po Toi O village around the bay. There is currently no public sewerage system for the village. Sewage and wastewater generated by local residents and local restaurants are treated by septic tanks/ soakaway system (STS).
- 2.3 Sewage works at Po Toi O comprise sewage collection, treatment and disposal facilities at Po Toi O under Port Shelter Sewerage, Stage 3 Sewerage Works at Po Toi O.
- 2.4 The Project in Po Toi O mainly comprises of the following items:
  - a. Provision of village sewerage to the unsewered areas of Po Toi O. The works involve construction of about 800m of gravity sewers and 400m of rising mains;
  - b. Construction of a local sewage treatment plant (STP) with Average Dry Weather Flow (ADWF) of about 139m3/day; and
  - c. Construction of a submarine outfall of about 385m in length.
- 2.5 The Project consists of the following works, which are classified as Designated Projects under Part I, Schedule 2 of the Environmental Impact Assessment Ordinance (EIAO):
  - a. Item Q.1 A sewage treatment plant and portion of sewer alignments in a conservation area;
  - b. Item C.12 (a) (v) and (vii) A dredging operation which is less than 500m from the nearest boundary of an existing fish culture zone and coastal protection area; and
  - c. Item F.6 A submarine sewage outfall.
- 2.6 The Environmental Impact Assessment (EIA) Report "Port Shelter Sewerage, Stage 3 Sewerage Works at Po Toi O" (Register No: AEIAR-206/2017) was approved on 27 January 2017. An Environmental Permit (EP) (Permit No.: EP-516/2016) was issued on 27 January 2017 and is the current permit for the Project. The EM&A programme of the Project shall be implemented in accordance with the requirements and procedures set out in the EM&A Manual and the Environmental Permit (EP) of the Project (Permit No.: EP-516/2016).



2.7 The air quality and noise baseline monitoring works were conducted from 23 December 2020 to 5 January 2021 and the water quality baseline monitoring work was conducted from 17 December 2020 to 12 January 2021. A Baseline Monitoring Report had been submitted to EPD on 10 March 2021.

#### Scope of Report

2.8 This is the 44<sup>th</sup> EM&A Report prepared by SGS for the Port Shelter Sewerage, Stage 3 – Sewerage Works at Po Toi O. This report summarized the monitoring results and audits findings of the EM&A programme under the EP of the Project and in accordance with the EM&A Manual during the reporting period of 1 October 2024 to 31 October 2024.

#### **Project Organisation**

2.9 The project organization structure is shown in **Appendix A**. The key personnel contact names and numbers are summarized in **Table 2-1**.

Position	Party	Name	Telephone
Project Proponent	Drainage Services Department (DSD)	Mr. Gary Chung	2594 7227
Senior Resident Engineer (SRE)	Binnies Hong Kong Limited (Binnies)	Mr. Eugene Chan	6392 3809
Independent Environmental Checker (IEC)	Acuity Sustainability Consulting Limited (ASC)	Dr. F.C. Tsang	2698 8060
Environmental Team (ET)	Société Générale de Surveillance (SGS) Hong Kong Limited	Mr. Johnathan Ho	9236 5528
Environmental Officer	China Geo-engineering Corporation (CGC)	Mr. Alex Chow	5918 9179

#### Table 2-1 Contact information of key personnel



#### **Construction Programme and Activities**

2.10 The main works undertaken in the reporting period are as follows:

Major activities in the reporting month:

- 1. Construction of village sewer;
- 2. Excavation works and construction of ELS for Po Toi O Sewage Treatment Plant;
- 3. Enlargement of HDD and Pipe Installation

The Construction Programme is shown in **Appendix B**. The general layout plan of the Project is shown in **Figure 2-1**.



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage		9
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report		01
	Date	Nov 24

### 3. AIR QUALITY

#### **Monitoring Requirements**

3.1 In accordance with the EM&A Manual, impact air quality monitoring shall be carried out throughout the construction period at all approved air quality monitoring locations (AMSs). 24- hours total suspended particles (TSP) monitoring shall be conducted at least once every 6 days. Meanwhile, 1-hour TSP monitoring shall be conducted at least 3 times every 6 days when the highest dust impact takes place. The Action and Limit levels for 1-hour and 24-hours TSP level are provided in Table 3-1 and Table 3-2.

#### Table 3-1 Action and Limit Levels for 1-hour-TSP

Parameter	Air Quality Monitoring Station (AMSs)	Action Level (μg/m³)	Limit Level (μg/m³)
	AMS1N	319	
	AMS2N1	279	
1-hr TSP (μg/m³)	AMS3N	303	500μg/m³
	AMS4N	278	

#### Table 3-2 Action and Limit Levels for 24-hour-TSP

Parameter	Air Quality Monitoring Station (AMSs)	Action Level (μg/m³)	Limit Level (μg/m³)
	AMS1N	153	
24-hr TSP (μg/m³)	AMS2N1	179	
	AMS3N	158	260µg/m³
	AMS4N	144	

SGS	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	10
	Works at Po Toi O	Ref#	EMA2403/03/42
	Monthly EM&A Report	Rev.	01
		Date	Nov 24

## **Monitoring Equipment**

3.2 The 24-hour TSP air quality monitoring was performed using High Volume Air Samplers (HVS) at each of the designated monitoring stations. The HVS are calibrated by a HVS calibrator. Meanwhile 1-hour TSP air quality monitoring was performed using portable TSP monitors. The equipment used for air quality monitoring are given in **Table 3-3**.

Air Quality Monitoring	Brand and Model of Equipment	Serial Number
24-hour TSP*	Graseby GMW High Volume Sampler	1180
	Sampler	1174
		9795
		2483
	Tisch TE-5025A High Volume Sampler Calibrator	4228
1-hour TSP	Sibata LD-3B Portable TSP	014746
	Monitors	155331
		597340
		597227

#### Table 3-3 Equipment Used for Air Quality Monitoring

- 3.3 Meteorological information (such as the humidity, rainfall, air pressure and temperature etc.) were collected from Hong Kong Observatory (HKO)'s Weather Stations.
- 3.4 According to the approved EM&A Manual, wind data monitoring equipment shall be provided and setup for logging wind speed and wind direction near the dust monitoring locations. The equipment installation location shall be proposed by the ET and agreed with the IEC. For installation and operation of wind data monitoring equipment, the following points shall be observed:
  - a. The wind sensors should be installed 10 m above ground so that they are clear of obstructions or turbulence caused by buildings.
  - b. The wind data should be captured by a data logger. The data shall be downloaded for



analysis at least once a month.

- c. The wind data monitoring equipment should be re-calibrated at least once every six months.
- d. Wind direction should be divided into 16 sectors of 22.5 degrees each.
- 3.5 It is noted that after liaison with the Po Toi O resident's representative on 22 December 2020, the resident's representative has rejected the access to the space and power supply for ET to install the wind data monitoring stations. Therefore, ET had proposed the alternative method for wind data collection according to section 3.4.7 of EM&A Manual.
- 3.6 The alternative method for wind data collection was adopt the wind data information collected from the HKO's Waglan Island weather station as the representative wind data. Although there are other closer weather stations, Waglan Island Station was selected as it is the nearest weather station that measures wind data information mentioned above.
- 3.7 The meteorological data from HKO's Weather Station is given in **Appendix C**.

### Monitoring Parameters, Frequency and Duration

3.8 The parameters, duration and frequency for air quality impact monitoring is given in Table 3-4. Monitoring stations AMS1N, AMS2N1, AMS3N and AMS4N were set up in accordance to the requirements for placement of equipment, as set out in section 3.5.3 of the EM&A manual of the Project. Locations of the alternative AMSs are given in **Figure 3-1**.

Identification no.	Location	Type of monitoring	Parameters	Frequency
AMS1N*	Footpath above House No. 28 Po Toi O Chuen Road			
AMS2N1*	Open space Approx. 15 m from Hung Shing Temple	TSP	1-hr TSP	1-hour TSP: At least 3 times for 1- hour with every 6 days
AMS3N*	Vacant land near Temporary Structure (House) Rocky Shore	ISP	24-hr TSP	24-hour TSP: Once every 6 days
AMS4N*	Resting shelter near Seacrest Villas			

Table 3-4 Monitoring Parameters	s for Air Quality Monitoring
---------------------------------	------------------------------



#### Notes:

\*- Due to a number of limitations identified at the air quality monitoring stations in the Approved EM&A Manual for the Project, the monitoring location AMS1 – AMS4 were replaced by alternative monitoring location AMS1N – AMS4N, which were approved by ER and IEC.

#### Monitoring Methodology for 24-hour TSP Monitoring

- 3.9 The HVS was installed in the vicinity of the air quality monitoring stations. The following criteria were considered in the installation of the HVS:
  - a. A horizontal platform with appropriate support to secure the sampler against gusty wind was provided.
  - b. The distance between the HVS and any obstacles, such as buildings, was at least twice the height that the obstacle protrudes above the HVS.
  - c. A minimum of 2 meters separation from walls, parapets and penthouse for rooftop sampler.
  - d. A minimum of 2 meters separation from any supporting structure, measured horizontally.
  - e. No furnace or incinerator flues nearby.
  - f. Airflow around the sampler was unrestricted.
  - g. Permission was obtained to set up the samplers and access to the monitoring stations.
  - h. A secured supply of electricity was obtained to operate the samplers.
  - i. The sampler was located more than 20 meters from any dripline.
  - j. Any wire fence and gate, required to protect the sampler, did not obstruct the monitoring process.
  - k. Flow control accuracy was kept within  $\pm 2.5\%$  deviation over 24-hour sampling period.
- 3.10 The following procedures to be followed for the preparation of filter papers of the HVS:
  - a. Glass fibre filters, G810 were labelled and sufficient filters that were clean and without pinholes were selected.
  - b. All filters were equilibrated in the conditioning environment for 24 hours before weighing. The conditioning environment temperature was around 25 °C and not variable by more than ±3 °C; the relative humidity (RH) was < 50% and not variable by more than ±5%. A convenient working RH was 40%.</p>
  - c. All filter papers were prepared and analysed by a HOKLAS accredited laboratory and has comprehensive quality assurance and quality control programmes.



3.11 The following procedures are followed throughout air quality monitoring works:

a. The power supply was checked to ensure the HVS works properly.

b. The filter holder and the area surrounding the filter were cleaned.

c. The filter holder was removed by loosening the four bolts and a new filter, with stamped number upward, on a supporting screen was aligned carefully.

d. The filter was properly aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter.

e. The swing bolts were fastened to hold the filter holder down to the frame. The pressure applied was sufficient to avoid air leakage at the edges.

f. Then the shelter lid was closed and was secured with the aluminum strip.

g. The HVS was warmed-up for about 5 minutes to establish run-temperature conditions.

h. A new flow rate record sheet was set into the flow recorder.

i. On site temperature and atmospheric pressure readings were taken and the flow rate of the HVS was checked and adjusted at around 1.1 m3 /min and complied with the range specified in the updated EM&A Manual (i.e., 0.6-1.7 m3 /min).

j. The programmable digital timer was set for a sampling period of 24 hrs, and the starting time, weather condition and the filter number were recorded.

k. The initial elapsed time was recorded.

I. At the end of sampling, on site temperature and atmospheric pressure readings were taken and the final flow rate of the HVS was checked and recorded.

m. The final elapsed time was recorded.

n. The sampled filter was removed carefully and folded in half-length so that only surfaces with collected particulate matter were in contact.

o. It was then placed in a clean plastic envelope and sealed.

p. All monitoring information was recorded on a standard data sheet.

3.12 The following procedures are followed for the maintenance and calibration of HVS:

- a. The HVS and its accessories were maintained in good working condition, such as replacing motor brushes routinely and checking electrical wiring to ensure a continuous power supply.
- b. 5-point calibration of the HVS was conducted using TE-5025A Calibration Kit prior to the commencement of monitoring. Bi-monthly 5-point calibration of the HVS will be carried out



during impact monitoring. The details for HVS calibration against the TE-5025A Calibration Kit is given in **Appendix D**.

#### Monitoring Methodology for 24-hour TSP Monitoring by Direct Reading Dust Meters

- 3.13 Since power supply for HVS for 24-hour TSP monitoring at alternative monitoring locations (i.e., AMS1N to AMS4N) were rejected, the use of direct reading dust meters is adopted to measure both 1-hour and 24-hour average TSP levels for the reporting month.
- 3.14 In accordance to Condition 3.1 of the Project's EP and Section 3.3 of the Project's EM&A Manual, the proposal for alternative monitoring equipment (i.e., direct reading dust meter) for TSP monitoring was approved by IEC and ER.
- 3.15 The measuring procedures of the direct reading dust meters are given in Section 3.5.10.
- 3.16 24 consecutive 1-hour TSP concentration measurement results is adopted for the evaluation of 24-hour TSP concentration. Results are manually logged daily, during daily maintenance of the dust meter. Calculation of the value of 24-hour TSP concentration is given by the average of 24 calculated 1-hour TSP concentration, where the calculated 1-hr TSP concentration is given by the product of the direct reading and the K-factor based on the correlation results between the direct reading meter and HVS. Details for the correlation methodology and correlation record are given in Appendix D and Appendix E.
- 3.17 HVS for 24-hr TSP monitoring will be adopted once secured supply of electricity becomes available for any agreed TSP monitoring locations.

#### Monitoring Methodology for 1-Hour TSP Monitoring

- 3.18 The measuring procedures of the direct reading dust meters were in accordance with the Manufacturer's Instruction Manual as follows:
  - a. Turn the power on.
  - b. Close the air collecting opening cover.
  - c. Push the "TIME SETTING" switch to [BG].
  - d. Push "START/STOP" switch to perform background measurement for 6 seconds.
  - e. Turn the knob at SENSI ADJ position to insert the light scattering plate.
  - f. Leave the equipment for 1 minute upon "SPAN CHECK" is indicated in the display.
  - g. Push "START/STOP" switch to perform automatic sensitivity adjustment. This measurement takes 1 minute.
  - h. Pull out the knob and return it to MEASURE position.



- i. Push the "TIME SETTING" switch the time set in the display to 3 hours.
- j. Lower down the air collection opening cover.
- k. Push "START/STOP" switch to start measurement.
- 3.19 The following procedures are followed for the maintenance and calibration of direct reading dust meters:
  - a. The 1-hour TSP meter was calibrated at 1-year intervals against with high volume sampler.
  - b. Calibration certificates of the Laser Dust Monitors are provided in **Appendix D**. 1-hour validation checking of the TSP meter against HVS is carried out yearly at the air quality monitoring locations.

#### **Monitoring Results and Observations**

- 3.20 The schedule for environmental monitoring in the reporting period is provided in Appendix F.
- 3.21 The air quality monitoring results for 1-hour and 24-hour air quality monitoring are summarized in **Table 3-6** and **Table 3-7**. Air quality monitoring data and graphical presentation of the data are provided in **Appendix G**.

#### Table 3-6 1-hour Air Quality Monitoring Results in the Reporting Period

Parameter	Monitoring Station	Average (μg/m³)	Range (µg/m³)
	AMS1N	47.5	35 – 53
1-hr TSP in μg/m³	AMS2N1	52.6	41 – 64
	AMS3N	46.9	39 – 60
	AMS4N	41.2	32 - 46

#### Table 3-7 24-hour Air Quality Monitoring Results in the Reporting Period

Parameter	Monitoring Station	Average (μg/m³)	Range (µg/m³)
	AMS1N	34.4	32 – 36
24-hr TSP in $\mu$ g/m <sup>3</sup>	AMS2N1	46.4	44 - 49
	AMS3N	38.0	36 - 41

Works at Po Toi O     Ref#     EMA2403/03/42       Monthly EM&A Report     Rev.     01       Date     Nov 24	000	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		16
Monthly EM&A Report				EMA2403/03/42
	<b>JUJ</b>	Monthly FM&A Report	Rev.	01
			Date	Nov 24

AMS4N	38.4	37 - 40
-------	------	---------

3.22 No Action or Limit Level exceedances of air quality were recorded in the reporting month. No air quality complaints between 0700 – 1900 hours on normal weekdays (i.e., Mondays to Saturdays) were received in the reporting month.

#### Other Influencing Factors of the Monitoring Results

- 3.23 Major emission sources during air quality monitoring in the reporting period were mainly vehicle emission from Po Toi O Chuen Road and nearby residents' activities.
- 3.24 The event and action plan for air quality monitoring are given in **Appendix H**.



#### 4. NOISE

#### **Monitoring Requirements**

4.1 In accordance with the EM&A Manual, noise impact monitoring was conducted during daytime construction work on normal weekdays (0700-1900 hours between Monday to Saturday), 1 set of 30-min measurement shall be carried out at approved noise monitoring stations (NMSs) every week based on the measurement procedures under EPD's" Technical Memorandum for the Assessment of Noise from Places Other Than Domestic Premises, Public Places or Construction Sites". The Action and Limit levels for construction noise monitoring is provided in **Table 4-1**.

#### Table 4-1 Action and Limit Levels for Construction Noise

NMSs ID	Noise Sensitive Receivers	Descriptions	Action Level	Limit Level
NMS1N	PTO_N1	Footpath Above House No. 28 Po Toi O Chuen Road		
NMS2N1	PTO_N2	Open Space Approx. 15 m from Hung Shing Temple	When one documented complaint	
NMS3N	PTO_N3	Vacant Land Near Temporary Structure (House) Rocky Shore	is received from any one of the noise sensitive receivers	75 dB(A)*
NMS4N	PTO_N4	Resting Shelter Near Seacrest Villas		

#### **Monitoring Equipment**

4.2 Noise monitoring was completed using sound level meters at each NMSs. The sound levels meters deployed comply with the International Electrotechnical Commission Publications (IEC) 651:1979 (Type 1) and 804:1985 (Type 1) specifications. Acoustic calibrator was deployed to calibrate the sound level meters at a given sound pressure level. The equipment used for noise impact monitoring is given in **Table 4-2**.

#### Table 4-2 Noise Monitoring Equipment

Equipment	Brand and Model	Serial No. /Equipment ID
Integrated Sound Level Meter	Rion NL-52	00264519

EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage		Page	18
	Works at Po Toi O	Ref#	EMA2403/03/42
<b>DUD</b>	Monthly EM&A Report	Rev.	01
		Date	Nov 24

Integrated Sound Level Meter	Rion NL-52	00264520
Acoustic Calibrator	NC-73	10196943
Anemometer	AZ Instrument – AZ 8908	1064869

#### **Monitoring Locations**

4.3 Due to the limitation posed by the approved monitoring stations set out by the EM&A manual, alternative monitoring stations NMS1N, NMS2N1, NMS3N and NMS4N were proposed in accordance to Section 4.5.3 of the EM&A Manual of the Project and approved from the ER and the IEC. The locations of the NMSs are given in **Figure 3-1**, and the details of the monitoring stations are illustrated in **Table 4-3**.

#### **Table 4-3 Description of Proposed Noise Monitoring Locations**

NMSs ID	Location	Type of measurement	Type of Monitoring	Duration
NMS1N*	Footpath above House No. 28 Po Toi O Chuen Road			30 mins
NMS2N1*	Open space approximately 15			30 mins
NMS3N*	m from Hung Shing Temple Vacant land near Temporary	Free-Field	Noise	30 mins
	Structure (House) Rocky Shore			
NMS4N*	Resting shelter near Seacrest Villas			30 mins

Notes:

\*For Free-field measurement, a correction of +3dB(A) should be made to the measured results.

\* Due to the limitation posed by the approved monitoring stations set out by the EM&A manual, four alternative representative Noise Quality Monitoring Stations

(NMSs) are proposed. The alternative monitoring Locations were approved by ER and IEC.



#### **Monitoring Parameters and Frequency**

4.4 The monitoring parameters, frequency and duration of impact noise monitoring are summarized in **Table 4-4**.

#### **Table 4-4 Parameters for Noise Impact Monitoring**

Parameter and Duration	Frequency
30-mins measurement at each monitoring station between 0700 and 1900 on normal weekdays. Leq, L10 and L90 would be recorded	At least once per week

#### **Monitoring Methodology**

- 4.5 The measuring procedures of the sound level meter were in accordance with the Manufacturer's Instruction Manual as follows:
  - a. Free-field measurement was made for the noise monitoring stations.
  - b. The sound level meter was set on a tripod at a height of 1.2 m above the ground.
  - c. The battery condition was checked to ensure the correct functioning of the meter.
  - d. Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:
    - i. frequency weighting: A
    - ii. Time weighting: Fast
    - iii. Time measurement: Leq(30-minutes) during non-restricted hours i.e., 07:00 1900 on normal weekdays; Leq(5-minutes) during restricted hours i.e., 19:00 23:00 and 23:00 07:00 of normal weekdays, whole day of Sundays and Public Holidays
  - e. Prior to and after each noise measurement, the meter was calibrated using the acoustic calibrator at a specified sound pressure level at a specified frequency. If the difference in the calibration level before and after measurement was more than 1 dB(A), the measurement would be considered invalid and repeat of noise measurement would be required after re-calibration or repair of the equipment.
  - f. During the monitoring period, the Leq, L10 and L90 were recorded. In addition, site conditions and noise sources were recorded on a standard record sheet.
  - g. Noise measurement was paused during periods of high intrusive noise (e.g., dog barking, helicopter noise) if possible. Observations were recorded when intrusive noise was unavoidable.
  - h. Noise monitoring was cancelled in the presence of fog, rain, wind with a steady speed exceeding 5m/s, or wind with gusts exceeding 10m/s.



- 4.6 The following procedures are followed for the maintenance and calibration of sound level meters:
  - a. The microphone head of the sound level meter was cleaned with soft cloth at regular
  - b. intervals.
  - c. The meter and calibrator were sent to the supplier or HOKLAS laboratory to check
  - d. and calibrate at yearly intervals.
  - e. Calibration certificates of the sound level meters, and acoustic calibrators are provided in **Appendix I.**

#### Monitoring Results and Observations

- 4.7 The schedule for environmental monitoring in the reporting period is provided in **Appendix F**.
- 4.8 The monitoring results for construction noise are summarized in **Table 4-5**. The noise monitoring data graphical presentation of the data is provided in **Appendix J**.

NMSs ID	Construction Noise	Baseline Level, dB(A)	Limit Level, db(A)
	Level,		
	dB(A)*, Leq (30 min)		
NMS1N	60.8 dB(A)	62.7 dB(A)	75
NMS2N1	51.9 dB(A)	61.8 dB(A)	75
NMS3N	56.9 dB(A)	64.6 dB(A)	75
NMS4N	49.1 dB(A)	58.1 dB(A)	75

#### Table 4-5 Summary of Construction Noise Monitoring Results in the Reporting Period

Note:

\*- A correction of +3 dB(A) was made to the free field measurements. Leq (30min) was measured at 0700-1900 hours on normal weekdays.

- 4.9 No Action or Limit Level exceedance of construction noise was recorded in the reporting month.
- 4.10 No noise complaints from between 0700 1900 hours on normal weekdays was received in the reporting month.
- 4.11 The event and action plan are provided in Appendix H.

#### Other Influencing Factors of the Monitoring Results


4.12 Major noise sources during noise monitoring in the reporting period were mainly road traffic noise.



#### 5. WATER QUALITY

#### Monitoring Requirements

- 5.1 With the recommendations of the Project's EIA report, water quality impact monitoring shall be carried out carried out 3 days per week, at mid-flood and mid-ebb tides (within ± 1.75 hour of the predicted time required) at all the approved Water Quality Monitoring Stations (WQMSs) during whole cofferdam installation/extraction work and during dredging works. The interval between two sets of monitoring shall not be less than 36 hours.
- 5.2 Replicate in-situ measurements of Suspended Solids (SS) and in-situ water quality data (temperature, pH, turbidity, water depth, salinity, dissolved oxygen and percentage of saturation) shall be collected.
- 5.3 Other relevant data should also be recorded, including monitoring location/position, time, tidal stages, weather conditions and any special observation or works that may affect the monitoring results in the vicinity.
- 5.4 To ensure sufficient data for robust analysis, duplicate in-situ data shall be collected. In case the difference in the duplicate in-situ measurement results is larger than 25%, the third set of in-situ measurement shall be carried out for result confirmation purpose.
- 5.5 Water samples shall be extracted at 1m below surface, 1m above seabed and the mid-depth level at where the water depth is at least 6m. However, if the water depth is less than 3m, water samples shall only be collected at the mid-depth level. For stations with depth less than 6m, the mid-depth sample can be omitted.
- 5.6 Tidal information was collected from Hong Kong Observatory (HKO)'s Tai Miu Wan Tidal Station, the closest tidal station to the Project. It was utilized to determine the schedule for water quality monitoring during mid-ebb and mid-flood period.
- 5.7 In addition, duplicated water samples for suspended solid analysis shall be collected at all the above stations and delivered to the HOKLAS accredited laboratory for analysis. Results for suspended solids shall be received back from the laboratory within 24-hour of the receipt of the samples.
- 5.8 Water quality impact monitoring shall also be conducted at the same frequency as monitoring throughout the whole cofferdam installation/extraction work and during dredging work. In case of exceedance of Action/Limit Level recorded, the frequency of water quality monitoring shall be increased as per the Event and Action Plan.
- 5.9 The water quality impact monitoring schedule shall be issued to IEC at least one week prior to the commencement of Impact Monitoring. The impact monitoring schedule is provided in **Appendix K**.



## **Monitoring Equipment**

5.10 The water quality monitoring (i.e. pH, salinity, temperature, turbidity and dissolved oxygen (DO)) was measured with Multi-Parameter Water Quality Meter at each of the designated monitoring stations. Water depth detector was used to measure the water depth of each monitoring locations. A global positioning device was used to locate the WMSs. Table 5-1 summarized the equipment used in water quality monitoring.

#### Table 5-1 Equipment Used for Water Quality Monitoring

Water Quality Monitoring Parameters	Brand and Model of Equipment
Multi-Parameter Water Quality Meter	Xylem-YSI ProDSS
Water Sampler	Kemmerer Bottle
Water Depth Detector	Xylem-YSI ProDSS
Global Positioning Device	Garmin eTrex H

### **Monitoring Parameters and Frequency**

5.11 The monitoring parameters, monitoring periods and frequencies of the water quality monitoring are summarized in **Table 5-2**.

Table 5-2 Parameters of Water Quality Monitoring

Parameters	Duration	Frequency
Temperature (°C)	During Construction Phase:	3 Days Per Week
pH (pH Unit)	Throughout Installation	(The Interval Between Two
Turbidity (NTU)	And Extraction Of	Sets of Monitoring Shall Not
Water Depth (m)	Cofferdam; And	Be Less Than 36 Hours.)
Salinity (ppt)	During Dredging	
DO (mg/L and % Of		
Saturation)		
SS (mg/L)		

#### **Monitoring Locations**

5.12 According to section 5.2.6 of the EM&A manual of the project, 6 water quality monitoring stations (WMSs) are proposed at the Po Toi O FCZs, major amphioxus habitats and rocky shores where coral thrives. With reference to the tidal characteristics of Po Toi O Bay, 3 control stations are proposed where fresh marine water is not affected by the cofferdam installation/ extraction works, and 2 impact stations are proposed near the cofferdam under different tidal periods. All water



quality monitoring stations show as **Figure 5-1** and **Table 5-3**.

 Table 5-3 Summary of Water Quality Impact Monitoring Stations

Station	Monitoring period	Description	Easting	Northing
*WMS1N	Mid-Ebb, Mid-Flood	Po Toi O Fish Culture Zone	848416	845209
*WMS2N	Mid-Ebb, Mid-Flood	Po Toi O Fish Culture Zone	848505	815375
WMS3	Mid-Ebb, Mid-Flood	Rocky Shore with Corals	848644	815391
WMS4	Mid-Ebb, Mid-Flood	Rocky Shore with Corals	848774	815602
WMS5	Mid-Ebb, Mid-Flood	Rocky Shore with Corals	848578	815591
WMS6	Mid-Ebb, Mid-Flood	Major Amphioxus Habitat	848639	815523
1	Mid-Flood	Impact monitoring Station	848643	815692
12	Mid-Ebb	Impact monitoring Station	848722	815910
C1	Mid-Flood	Control station	848904	816052
C2	Mid-Ebb	Control station	848529	815373
C3	Mid-Ebb	Control station	848243	815710
WMS1	Mid-Ebb, Mid-Flood	Po Toi O Fish Culture Zone	848387	815201
WMS2	Mid-Ebb, Mid-Flood	Po Toi O Fish Culture Zone	848479	815378

Notes:

\*WMS1N, WMS2N are new proposed alterative monitoring location. As previous EIA proposed monitoring location WMS1, WMS2 are situated in fish barges within the Fish Culture Zone (FCZ), and accesses to WMS1 and WMS2 were subsequently denied by the tenants of the fish barges. The relocation of WMS1 and WMS2 were approved by IEC and the ER of the Project.

#### **Results and Observations**

- 5.13 According to submission of construction works schedule and location plan under the EP of Project, the commencement of construction work with cofferdam installation / extraction work was 6 December 2023. Marine construction and water quality monitoring was commenced starting from 6 December 2023.
- 5.14 In this Reporting Period, a total of 13 sampling days were performed for marine water monitoring at the 11 designated locations. Monitoring results are summarized in **Appendix L.**
- 5.15 A summary of exceedances for the three parameters: Dissolved oxygen (DO), turbidity and suspended solids (SS) are shown in **Table 5-4**.

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	24
<b>CCC</b>	Works at Po Toi O	Ref#	EMA2403/03/42
545	Monthly EM&A Report	Rev.	01
		Date	Nov 24

#### Table 5-4 Summary of Water Quality Exceedance

Station	Тор 8	erage of & Mid- oth)	-	ottom oth)		y (Depth age)	-	Depth rage)	To Exceeda the St	ance for
	AL	LL	AL	LL	AL	LL	AL	LL	AL	LL
WMS1N	0	0	0	0	0	0	3	0	3	0
WMS2N	0	0	0	0	0	0	3	0	3	0
WMS3	0	0	0	0	0	0	6	0	6	0
WMS4	0	0	0	0	0	0	5	0	5	0
WMS5	0	0	0	0	0	0	4	0	4	0
WMS6	0	0	0	0	0	0	2	0	2	0
11	0	0	0	0	0	0	0	0	0	0
12	0	0	0	0	0	0	3	0	3	0
No. of Exceedance	0	0	0	0	0	0	26	0	26	0

- 5.16 In this Reporting Period, twenty-six (26) Action Level and zero (0) Limit Level exceedances of Suspended Solids were recorded. Exceedances of Action level in the monitoring period were found at various sampling stations on each sampling day and no stations were exceeded continuously for consecutive sampling days. Notification of Exceedances (NOEs) had been issued to relevant parties. Investigation for the cause of exceedance was carried out by ET subsequently.
- 5.17 SS exceedance were recorded on 2, 4, 7, 9, 12, 14, 16, 18, 21, 23, 25, 28 & 30 October 2024. Investigation were carried out by ET for these exceedance incidents. Since silt curtain as water quality mitigation measure was properly implemented, no abnormal and turbid discharge made from the construction site and from the seashore was observed during the course of marine water sampling, it was considered that the exceedances of suspended solids recorded in this period were unlikely caused by the Project. Nevertheless, the Contractor was reminded to check the implementation of silt curtain regularly to ensure no seepage of muddy water into the marine water body.
- 5.18 Moreover, refer to Sections 5.2.10 and 5.2.11 of approved EM&A Manual, construction phase site inspection for water quality mitigation measures and check the contractor's work practice on water pollution prevention during construction phase has been conducted during weekly site audit.
- 5.19 During the weekly site audit of this reporting month, no non-conformance water pollution was



identified / observed in the commencement works area.

#### 6. WASTE MANAGEMENT

- 6.1 As advised by the Contractor, 129 m<sup>3</sup> (to be provided at a later stage) of inert C&D material was generated in the reporting month. For C&D wastes, 0 m<sup>3</sup> of general refuse was disposed of at NENT landfill, 0 kg waste were collected by recycling contractors, and 0 kg of chemical wastes was collected by licensed Contractors in the reporting period.
- 6.2 The actual amounts of different types of waste generated by the activities of the Project in the reporting period are shown in **Table 6-1**, the detailed monthly summary of waste flow is detailed in **Appendix N**.

Waste Type	Quantity	Disposal/ Reuse Locations
Inert C&D Waste Disposed as	129 m <sup>3</sup>	Tseung Kwan O Area 137 Fill
Public Fill		Bank (TKO137FB).
C&D Wastes Disposed as General	0 m <sup>3</sup>	North East New Territories
Refuse		(NENT)
Recycle Materials	0 kg	Recycling Facilities
General Refuse	0 kg	North East New Territories
		(NENT)
Chemical Waste	0 kg	Licensed Contractors

#### Table 6-1 Summary of Waste Flow Table

6.3 During regular site auditing, the mitigation measures proposed in the Implementation Schedule of the Environmental Mitigation Measures (EMIS) in the approved EIA report of the Project has been effectively implemented in the commenced works area. No adverse waste impact was observed from the construction works in reporting month.



### 7. ENVIRONMENTAL SITE INSPECTION AND AUDIT

#### **Site Inspection**

- 7.1 Site inspections were carried out by ET on a weekly basis to monitor the implementation of proper environmental pollution control and mitigation measures for the Project. Key observations were recorded in the site inspection checklist and passed to the Contractor together with the appropriate recommended mitigation measures where necessary.
- 7.2 In the reporting period, 5 site inspections were carried out on 3, 10, 17, 24 & 31 October 2024. No noncompliance was recorded during the site inspection. Details of observations recorded during the site inspections are presented in **Table 7-1**.

Parameters	Observations and Recommendations	Action was taken by
		the contractor
-	Observation	Follow up Observation
	Observation 1: Due to the adverse	Item 1:
	weather from Typhoon Yagi, according	(Pending)
	to EP Condition 2.13 Silt Curtain and	
	Cofferdam Deployment Plan Section	
	2.5, the contractor is reminded to check	
	the conditions of the silt curtains at both	
	HDD and cofferdam construction areas	
	and dive inspection is required to ensure	
	the silt curtains are in good condition	
	and functionable after the typhoon.	
	(Repeated)	
Waste	Observation	Follow up Observation
Management	<b>Observation 1</b> : Due to the adverse	Item 1:
	weather from Typhoon Yagi, according	(Pending)
	to EP Condition 2.13 Silt Curtain and	
	Cofferdam Deployment Plan Section	
	2.5, the contractor is reminded to check	
	the conditions of the silt curtains at both	
	HDD and cofferdam construction areas	
	and dive inspection is required to ensure	
	- Waste	- Observation Observation 1: Due to the adverse weather from Typhoon Yagi, according to EP Condition 2.13 Silt Curtain and Cofferdam Deployment Plan Section 2.5, the contractor is reminded to check the conditions of the silt curtains at both HDD and cofferdam construction areas and dive inspection is required to ensure the silt curtains are in good condition and functionable after the typhoon. (Repeated) Waste Management Observation 1: Due to the adverse weather from Typhoon Yagi, according to EP Condition 2.13 Silt Curtain and Cofferdam Deployment Plan Section 2.5, the contractor is reminded to check the conditions of the silt curtains at both HDD and cofferdam construction areas

#### Table 7-1 Observations and Recommendations in the Reporting Month



Date Parameters Observa		Observations and Recommendations	Action was taken by
			the contractor
		the silt curtains are in good condition	
		and functionable after the typhoon.	
		Observation 2: Oil containers were	Item 2: The oil
		found at PTO-SPS. The Contractor	containers have been
		should store the chemicals in a drip tray	removed away from the
		or remove the containers from the	construction site location.
		construction site area.	(Item Closed)
17	Waste	Observation	Follow up Observation
October 2024	Management /	<b>Observation 1</b> : Due to the adverse	Item 1:
	Air Quality	weather from Typhoon Yagi, according	(Pending)
		to EP Condition 2.13 Silt Curtain and	
		Cofferdam Deployment Plan Section	
		2.5, the contractor is reminded to check	
		the conditions of the silt curtains at both	
		HDD and cofferdam construction areas	
		and dive inspection is required to ensure	
		the silt curtains are in good condition	
		and functionable after the typhoon.	
		(Repeated)	
		<b>Observation 2</b> : Oil containers were	Item 2: The oil
		found at PTO-SPS. The Contractor	containers have been
		should store the chemicals in a drip tray	removed away from the
		or remove the containers from the	construction site location.
		construction site area.	(Item Closed)
		<b>Observation 3:</b> NRMM label was found	Item 3: The NRMM label
		faded on the mobile generator. The	have been affixed with
		Contractor should replace the NRMM	correct format.
		label.	(Item Closed)
24	Air Quality	Observation	Follow up Observation
October 2024		Observation 1: Due to the adverse	Item 1:
		weather from Typhoon Yagi, according	(Pending)
		to EP Condition 2.13 Silt Curtain and	
		Cofferdam Deployment Plan Section	
		2.5, the contractor is reminded to check	



Date	Parameters	Observations and R	ecommendations	Action was taken by
				the contractor
		the conditions of the s	silt curtains at both	
		HDD and cofferdam c	construction areas	
		and dive inspection is	required to ensure	
		the silt curtains are in	good condition	
		and functionable after	the typhoon.	
		(Repeated)		
		Observation 2: NRM	IM label was found	Item 2: The NRMM label
		faded on the mobile g	enerator. The	have been affixed with
		Contractor should rep	lace a proper	correct format.
		NRMM label with the i	right format.	(Item Closed)
31	Air Quality /	Observation		Follow up Observation
October 2024	Waste	Observation 1: Due	to the adverse	Item 1:
	Management	weather from Typhoor	n Yagi, according	(Pending)
		to EP Condition 2.13	Silt Curtain and	
		Cofferdam Deploymer	nt Plan Section	
		2.5, the contractor is r	eminded to check	
		the conditions of the s	silt curtains at both	
		HDD and cofferdam c	construction areas	
		and dive inspection is	required to ensure	
		the silt curtains are in	good condition	
		and functionable after	the typhoon.	
		(Repeated)		
		Observation 2: NRM	M label was found	Item 2: The NRMM label
		faded on the mobile g	enerator. The	have been affixed with
		Contractor should rep	lace a proper	correct format.
		NRMM label with the r	right format.	(Item Closed)
		Observation 3: Rubb	ish has been	Item 3:
		accumulated at the ou	utfall of the silt	(Pending)
		curtain of PTO-STP. T	The Contractor	
		should clear up the ru	bbish accordingly.	
No adverse observa	ition was identified in	the reporting period.	Noise Impact	1
No adverse observa	tion was identified in	the reporting period.	Ecology	
No adverse observa	tion was identified in	the reporting period.	Fisheries	
No adverse observa	tion was identified in	the reporting period.	Built Heritage	



Date	Parameters	Observations and F	Recommendations	Action was taken by the contractor
No adverse observation was identified in the reporting period.			Landscape and Visu	al Impact
No adverse observation was identified in the reporting period.			Miscellaneous	

#### Status of Environmental Licenses, Notification and Permits

7.3 The environmental licenses and permits for the Project and valid in the reporting period are summarized in **Table 7-2**.

 Table 7-2 Status of Environmental License, Notification and Permit

License/ Notification/ Permit	Reference No.	Valid Period	
		From	То
Environmental Permit	EP-516/2016	27 January 2017	End of Project
Construction Dust Notification	458613	3 August 2020	N/A
Under APCO			
Wastewater Discharge License	WT00038707-	3 November 2021	31 August 2026
	2021		
Chemical Waste Producer	5213-820-	23 September 2020	N/A
Registration	C3510-		
	18		
Billing Account for Disposal of	WFG22785	17 August 2020	N/A
Construction Waste			

#### **Implementation Status on Environmental Protection Requirements**

7.4 The Implementation Schedule of the Environmental Mitigation Measures (EMIS) of the reporting period is summarized in **Appendix O**. The implementation of the key mitigation measures during the reporting period is presented in **Appendix P**.

# Summary of Complaints, Notification of Summons, Successful Prosecutions and Public Engagement Activities

- 7.5 No complaints, notification of summons and successful prosecution was received in the reporting period. No public engagement activities were conducted in the reporting period.
- 7.6 Statistics on complaints, notifications of summons, successful prosecutions and public engagement activities are summarized in **Appendix Q**.



### 8. FUTURE KEY ISSUES

#### CONSTRUCTION PROGRAMME FOR THE UPCOMING REPORTING MONTH

- 8.1 Major activities in the upcoming month:
  - a. Construction of village sewer;
  - b. Excavation works and construction of ELS for Po Toi O Sewage Treatment Plant;
  - c. Construction of Cofferdam;
  - d. Enlargement of HDD and Pipe Installation

#### Reinstatement Works Key Issues for the Upcoming Reporting Month

- 8.2 Potential environmental impacts due to the construction activities, including air quality, noise, water quality, waste, landscape and visual, will be monitored or reviewed. The ET will continue to implement the environmental monitoring & audit programme in accordance with the EM&A Manual and Environmental Permit requirement. The recommended environmental mitigation measures shall be implemented on site and regular inspections as required will be carried out to ensure that the environmental conditions are acceptable.
- 8.3 The anticipated impact of major work activities within the site and the recommended mitigation measures are shown in **Appendix Q**.

#### Monitoring Schedule for the Coming Month

8.4 The tentative schedule for environmental monitoring in November 2024 is provided in AppendixF.



### 9. CONCLUSION

#### General

9.1 This Report Summarized the Monitoring Results and Audits Findings of the EM&A Programme Under the EP of The Project and In Accordance with the EM&A Manual During the Reporting Period of 1 October 2024 to 31 October 2024.

#### **Environmental Impact Monitoring**

- 9.2 No Action or Limit Level exceedance of construction air quality, noise was recorded in the reporting month. No air quality complaints and noise complaints were received in the reporting month.
- 9.3 In this Reporting Period, twenty-six (26) Action Level and zero (0) Level exceedances of Suspended Solids were recorded.

#### **Environmental Site Inspections**

9.4 The environmental site inspections were carried out in the reporting month. Recommendations on remedial actions were given to the contractors for the deficiencies identified during the site inspection. The contractor had been follow-up the recommendations on the remedial action accordingly.

#### **Complaint Log**

9.5 There was no complaint received in relation to the environmental impact during the reporting period.

#### **Reporting Changes**

9.6 No report changes in this reporting period.


#### Notifications of Summons and Successful Prosecutions


9.7 There was no notification of summons and successful prosecution was received in the reporting period.





EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		-
		EMA2403/03/42
Monthly EM&A Report		01
		Nov 24

#### FIGURE 2-1 – LAYOUT PLAN OF THE CAPTIONED PROJECT

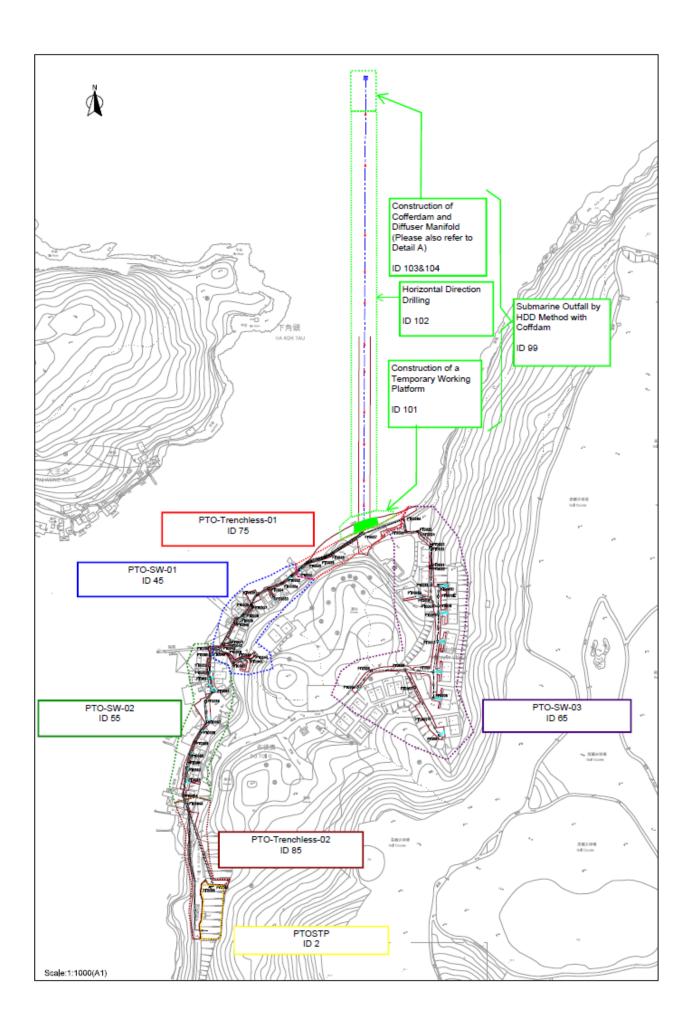

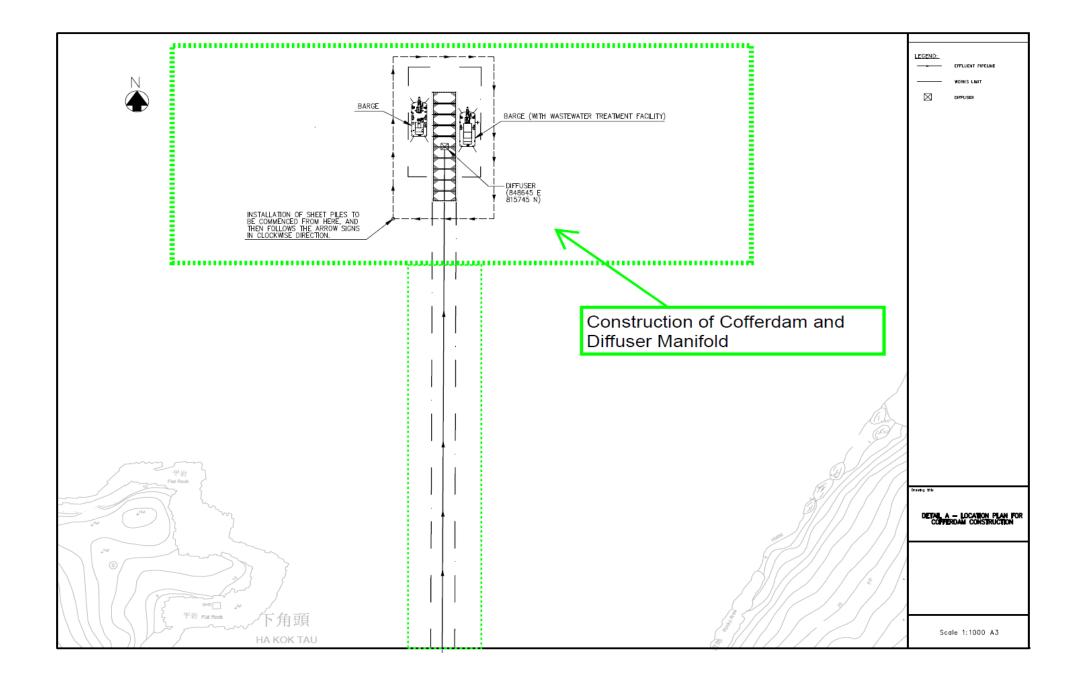


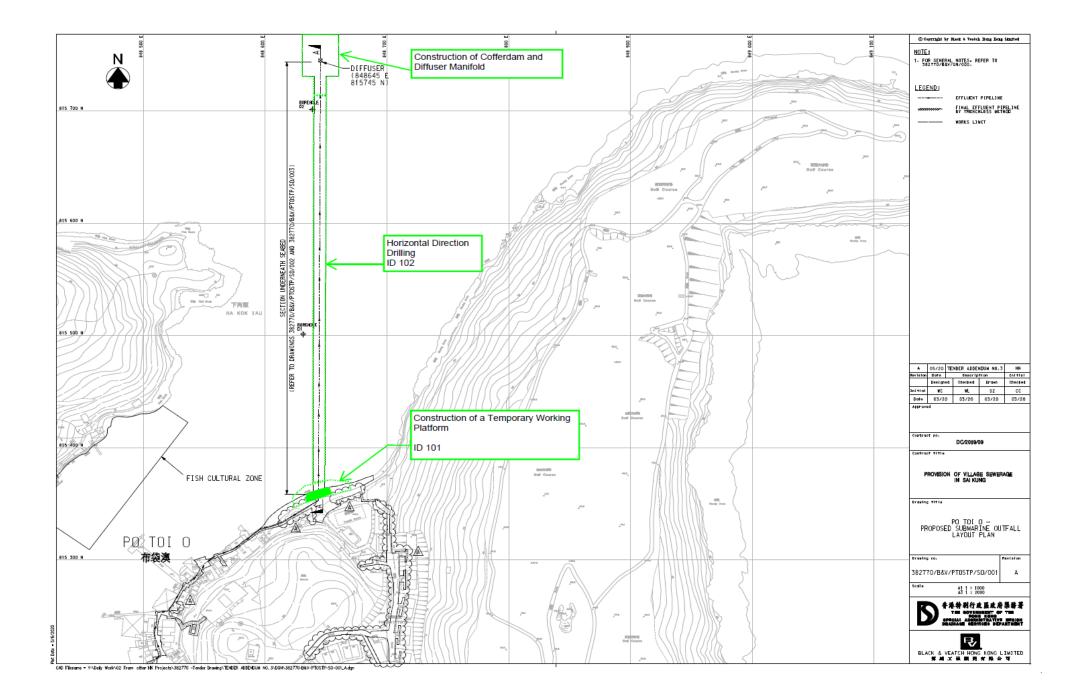

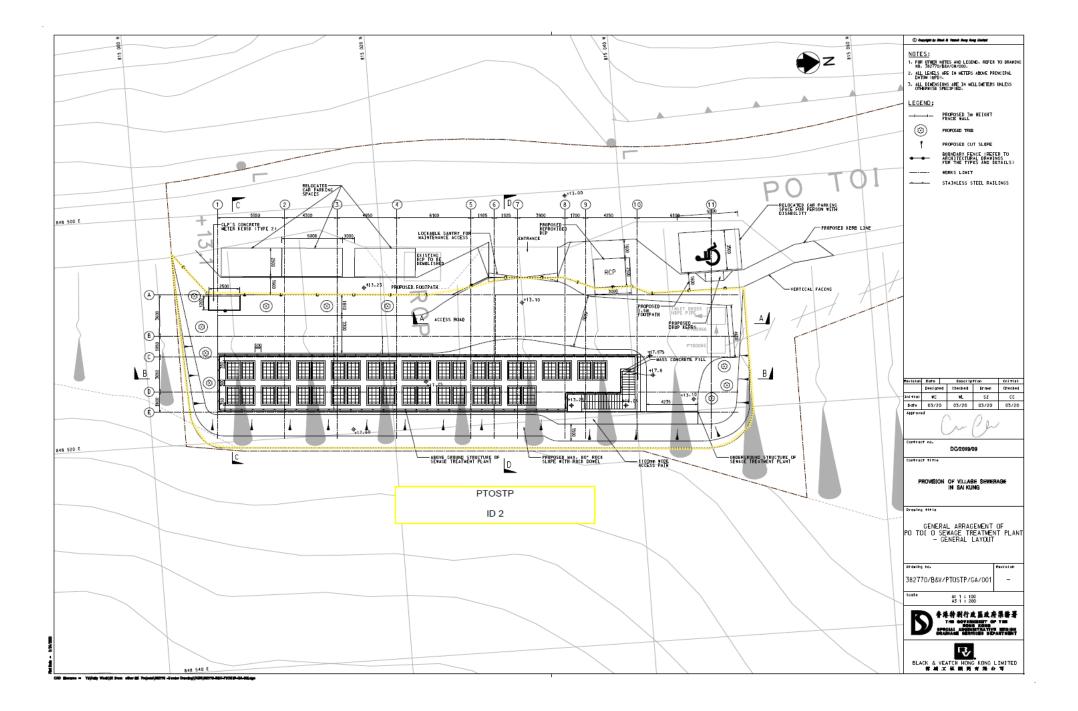




## FIGURE 3-1 PROPOSED AIR QUALITY AND NOISE MONITORING STATIONS LOCATIONS

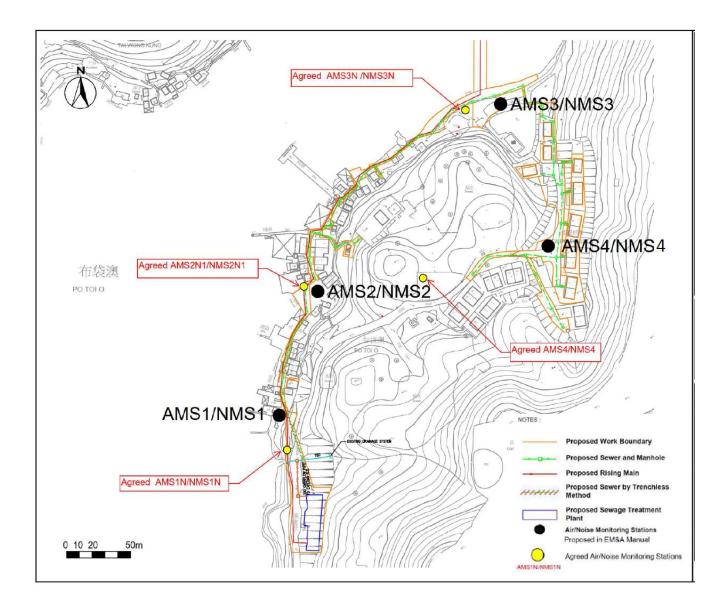




# FIGURE 5–1 LOCATIONS OF WATER QUALITY IMPACT MONITORING STATIONS

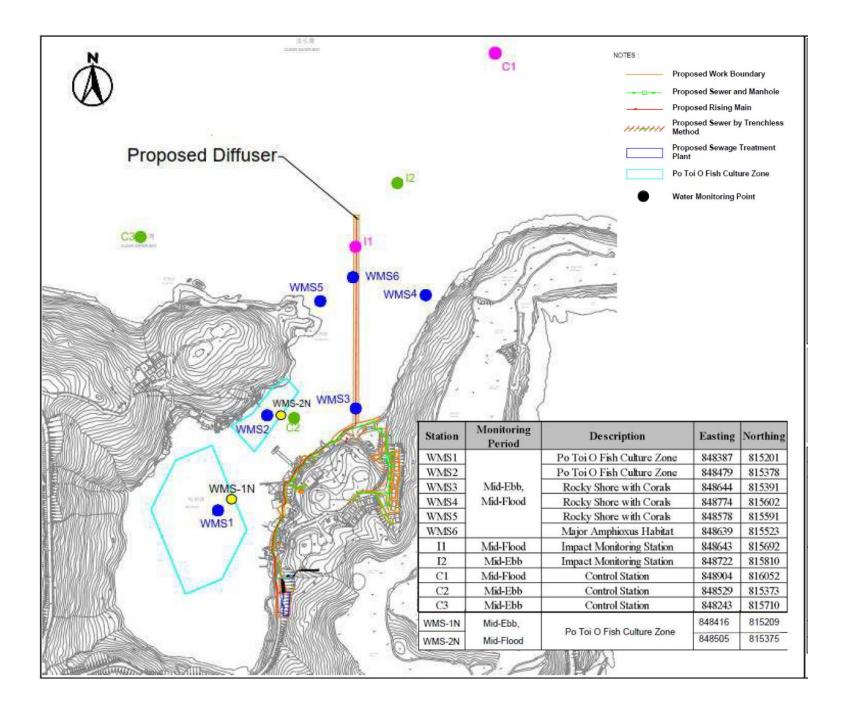



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	A-1
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

## **APPENDIX A – PROJECT ORGANIZATION CHART**

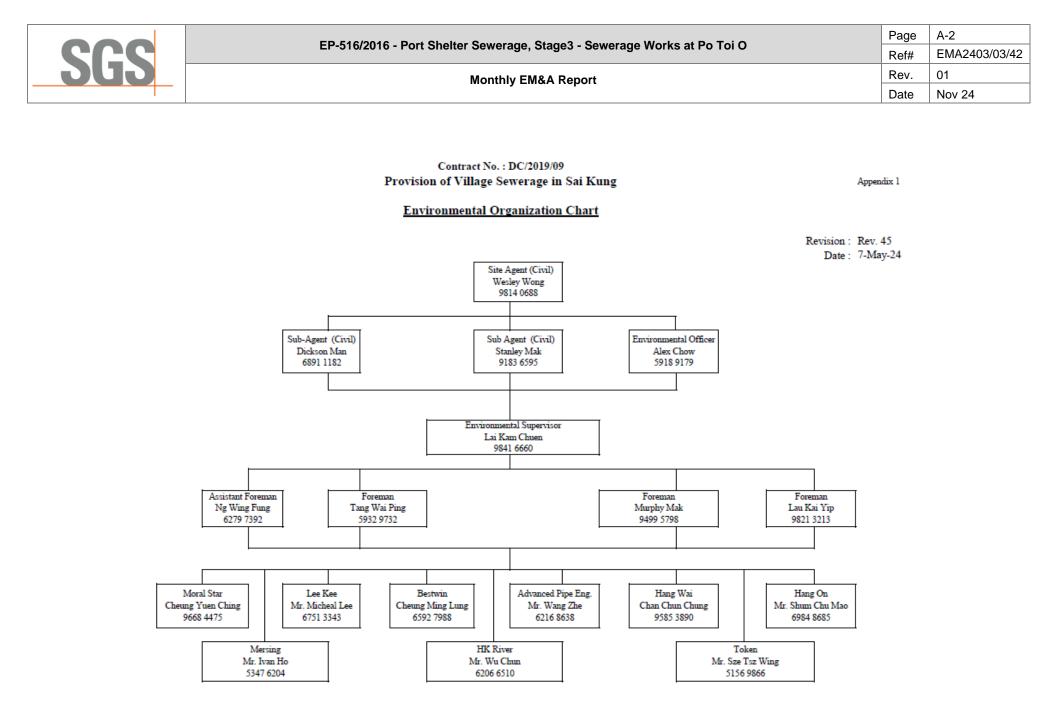



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	B-1
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

## **APPENDIX B – CONSTRUCTION PROGRAMME**

Project	t: Provision of Village Sewerage in	Sai Kung			Provision of V Contr	vices Departn /illage Sewera ract No: DC/2 s Programme	019/09	2 9							Date: Aug
ID	Task Name			Duration			Completion Date	TRAF	Predecessor	TRA	Text10	2024 H1	H2	2025 H1	H2
1	Section 2 - Village Sewerage Works	at Po Toi O and PTOSTP		1545 days	Fri 24/7/20		e 16/9/25								~
2	Po Toi O Sewage Treatment Pla	nt (PTOSTP)		1545 days	Fri 24/7/20	0% Tu	e 16/9/25								
3															
4	Liaise with the village represent	tative works to ensure the possession of construct	ion site	75 days	Fri 24/7/20	0% We	ed 21/10/20								
5	Preperation works (i.e. TMLG slot; Re-provision of existing R	meetings; Application for traffic advice for susper CP, etc.)	sion of existing parking	231 days	Fri 24/7/20	0% Th	u 29/4/21								
6	Environmental submissions			231 days	Fri 24/7/20	0% Th	u 29/4/21								
7	Possession of site (Access Date	: 22nd October 2020)		1 day	Thu 22/10/20	0% Th	u 22/10/20	4	ł						
8	Installation of site hoardings at	PTOSTP		50 days	Fri 23/10/20	0% Mo	on 21/12/20	7	1						
9	Mobilization of plant and equip	oment		10 days	Tue 22/12/20	0% Tu	e 5/1/21	8	3						
10	Site clearance			95 days	Wed 6/1/21	0% Th	u 29/4/21	9	)						
11	Initial survey, UU detection and	d permit-to-dig		95 days	Wed 6/1/21	0% Th	u 29/4/21	9	)						
12															
13	Preparation for geotechnical sul	bmissions		7 days	Fri 30/4/21	0% Sat	8/5/21	1	1,10,5,6						
14															
15	Liaison with PTO VR			18 days	Mon 10/5/21	0% Mo	on 31/5/21	1	3						
16															
17	loosen materials to be removed	olid materials to be removed, i.e. about 4275 m3 l per day, i.e. 4 trips of dumping per day)(installati		148 days	Tue 1/6/21	0% Th	u 25/11/21	1	5						
18	outlet of the box culvert) Installation of rock dowl (incluse	de drilling, rebar installation and grouting, etc.)		35 days	Fri 26/11/21	0% Sat	8/1/22	1	17						
19	Construction of anchorages for	flexible barrier		40 days	Mon 10/1/22	0% Mo	on 28/2/22	1	8						
	I														
roject	t:DC/2019/09 Spli Mik	iect Guide: Critical Task Protect Spectral Spectral Spectral Spectral Protect Spectral Spectr	ogress		Inactiv Manua Durati	ve Milestone ve Summary al Task ion-only			Finisl	n-only nal Tasks	ŝ	* 	Progress Summary	Ŷ	
age 1		nmary Mi	lestone	\$	Manua	al Summary Rol	llup 🔶		Exter	nal Miles	stone				

iame Installation of flexible barriers Installation of sheetpile Excavation from +13.25 Mpd to -1.20 Mpd (Total 2150 m3 solid materials to be removed, i.e. about 3225m3 loosen materials. 23.8m3 loosen materials to be removed per day, i.e. 4 trips of dumping per Plate load test Construction of raft footing Construction of basement (below +13.25 mPD)	Duration 40 days 146 days 60 days 14 days 40 days 50 days		Programme for PTO Procentage Completion Date of Completion O% Wed 20/4/22 O% Sat 23/12/23 O% Sat 23/12/23 O% Tue 26/3/24 O% Tue 26/3/24	TRA Predecessors TRA 19 20 22	A Text10	2024 H1	112	2025 H1	H2
Installation of sheetpile Excavation from +13.25 Mpd to -1.20 Mpd (Total 2150 m3 solid materials to be removed, i.e. about 3225m3 loosen materials. 23.8m3 loosen materials to be removed per day, i.e. 4 trips of dumping per Plate load test Construction of raft footing Construction of basement (below +13.25 mPD)	146 days 60 days 14 days 40 days	Tue 4/7/23 Wed 27/12/23 Mon 11/3/24 Wed 27/3/24	0% Wed 20/4/22 0% Sat 23/12/23 0% Sat 9/3/24 0% Tue 26/3/24	20		HI	H2	H1	H2
Excavation from +13.25 Mpd to -1.20 Mpd (Total 2150 m3 solid materials to be removed, i.e. about 3225m3 loosen materials. 23.8m3 loosen materials to be removed per day, i.e. 4 trips of dumping per Plate load test Construction of raft footing Construction of basement (below +13.25 mPD)	60 days 14 days 40 days	Wed 27/12/23 Mon 11/3/24 Wed 27/3/24	0% Sat 9/3/24 0% Tue 26/3/24						
Excavation from +13.25 Mpd to -1.20 Mpd (Total 2150 m3 solid materials to be removed, i.e. about 3225m3 loosen materials. 23.8m3 loosen materials to be removed per day, i.e. 4 trips of dumping per Plate load test Construction of raft footing Construction of basement (below +13.25 mPD)	60 days 14 days 40 days	Wed 27/12/23 Mon 11/3/24 Wed 27/3/24	0% Sat 9/3/24 0% Tue 26/3/24						
3225m3 loosen materials. 23.8m3 loosen materials to be removed per day, i.e. 4 trips of dumping per Plate load test Construction of raft footing Construction of basement (below +13.25 mPD)	14 days 40 days	Mon 11/3/24 Wed 27/3/24	0% Tue 26/3/24	22					
Plate load test Construction of raft footing Construction of basement (below +13.25 mPD)	40 days	Wed 27/3/24							
Construction of basement (below +13.25 mPD)				23					
	50 days	Sat 18/5/24	0% Fri 17/5/24	24		- X-			
			0% Wed 17/7/24	25					
Construction of R.C. walls at 1st Floor	55 days	Mon 8/4/24	0% Thu 13/6/24				<b></b> h		
Construction of rooftop (below + 17.75 mPD)	55 days	Fri 14/6/24	0% Sat 17/8/24	28			The second secon		
	90 days	Mon 19/8/24	0% Wed 4/12/24	29			l l		
	90 days	Mon 19/8/24	0% Wed 4/12/24						
Landscape works & other associated works	797 days	Thu 31/3/22	0% Wed 4/12/24	13					
	180 days	Thu 18/7/24	0% Tue 18/2/25	26			-		
T&C (Stage 3)	60 days	Wed 9/7/25	0% Tue 16/9/25	35					
nstruction of PTO Village Sewerage	1173 days	Fri 24/7/20	0% Wed 3/7/24						
Liaise with the village representatives	90 days	Fri 24/7/20	0% Mon 9/11/20						
Initial survey and photo-taking	90 days	Wed 26/8/20	0% Fri 11/12/20	40SS+28 daj					
UU Detection and application for permit-to-dig	90 days	Mon 21/9/20	0% Sat 9/1/21	41SS+22 dag	_				
Trial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020)	90 days	Thu 22/10/20	0% Mon 8/2/21	42SS+25 day					
Producing Layout plans showing the loction of terminal manholes, timber box and alignment of sewers	83 days	Tue 17/11/20	0% Sat 27/2/21	44SS+21					
and other associated preparation works				days					
Task Project Summary	$\bigtriangledown$			Manual Sur	nmary	•	Progress		
	< ♦	Inactiv		Start-only			Summary	Ŷ	
019/09 Split Split		Manua	al Task 🔷	Finish-only		-			
Milestone Progress		Durati	on-only	External Ta	sks				
Summary Milestone	•	Manua	al Summary Rollup 🛛 🔶	External Mi	ilestone				
	Construction of rooftop (below + 17.75 mPD) External Finishes Internal Finishes (incl. installation of Door & Window etc) Landscape works & other associated works E&M works T&C (Stage 1) + T&C (Stage 2) T&C (Stage 3)  nstruction of PTO Village Severage Liaise with the village representatives Initial survey and photo-taking UU Detection and application for permit-to-dig Trial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020)  Producing Layout plans showing the loction of terminal manholes, timber box and alignment of sewers and other associated preparation works  Task Project Guide: Critical Task Project Guide: Critical Task Project Guide: Critical Task Project Summary Project Guide: Critical Task Project Summary Proje	Construction of rooftop (below + 17.75 mPD) 55 days External Finishes (incl. installation of Door & Window etc) 90 days Internal Finishes (incl. installation of Door & Window etc) 90 days E&M works 797 days E&M works 180 days E&M works 180 days E&M works (Stage 1) + T&C (Stage 2) 120 days T&C (Stage 1) + T&C (Stage 2) 120 days T&C (Stage 3) 60 days Initial survey and photo-taking 90 days Initial survey and photo-taking 90 days UU Detection and application for permit-to-dig 90 days Trial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days Trial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days Trial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days ITial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days ITial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days ITial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days ITial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days ITial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days ITial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days ITial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days ITial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days ITial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days ITial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days ITial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days ITial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days ITial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days ITial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days ITial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days ITial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days ITial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days ITial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days ITial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 day	Construction of rooftop (below + 17.75 mPD)       55 days       Fri 14/6/24         External Finishes       90 days       Mon 19/8/24         Internal Finishes (incl. installation of Door & Window etc)       90 days       Mon 19/8/24         Landscape works & other associated works       797 days       Thu 31/3/22         E&M works       180 days       Thu 18/7/24         E&M works       180 days       Wed 19/2/25         Go days       Wed 19/2/25       60 days       Wed 19/2/25         FX (Stage 1) + T&C (Stage 2)       60 days       Wed 19/2/25         nstruction of PTO Village Sewerage       1173 days       Fri 24/7/20         Liaise with the village representatives       90 days       Wed 26/8/20         UU Detection and application for permit-to-dig       90 days       Mon 21/9/20         Trial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020)       90 days       Thu 22/10/20         Producing Layout plans showing the loction of terminal manholes, timber box and alignment of sewers and other associated preparation works       83 days       Tue 17/11/20         019/09       Task       Project Summary       Project Summary       Inactin Inactin Inactin Inactin Inaction In	Construction of cooltop (below + 17.75 mPD) 55 days Fri 14/6/24 09/Sat 17/8/24 External Finishes (incl. installation of Door & Window etc) 90 days Mon 19/8/24 07% Wed 4/12/24 Lindscape works & other associated works 977 days Thu 31/3/22 07% Wed 4/12/24 E&M works Tac (Stage 1) + T&C (Stage 2) 120 days Wed 9/7/25 09% Tac 8/7/25 T&C (Stage 3) 60 days Wed 9/7/25 09% Tac 8/7/25 T&C (Stage 3) 60 days Wed 9/7/25 09% Tac 8/7/25 T&C (Stage 3) 60 days Wed 9/7/25 09% Tac 8/7/25 Linisies with the village representatives 90 days Fri 24/7/20 0% Wed 3/7/24 Linisies with the village representatives 90 days Wed 26/8/20 0% Fri 11/12/20 UU Detection and application for permit-to-dig 90 days Mon 21/9/20 0% Sat 9/1/21 Trial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days Thu 22/10/20 0% Kon 8/2/21 Trial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days Tu 22/10/20 0% Kon 8/2/21 Trial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days Tu 22/10/20 0% Kon 8/2/21 Trial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days Tu 22/10/20 0% Kon 8/2/21 Trial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days Tu 22/10/20 0% Kon 8/2/21 Trial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days Tu 22/10/20 0% Kon 8/2/21 Trial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days Tu 22/10/20 0% Kon 8/2/21 Trial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days Tu 22/10/20 0% Kon 8/2/21 Trial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020) 90 days Tu 21/11/20 0% Sat 27/2/21 Manual Task Project Guide: Critical Task Project Summary Project Guide: Critical Task Split Project Guide: Critic	Construction of roofing (bedw + 17.75 mPD)       55 days       Fit 14/62/4       0% (% at 17.8/24       28         External Finishes       90 days       Mon 19/82/4       0% (% ed 41/12/4       29         Internal Finishes (incl. installation of Door & Window etc)       90 days       Mon 19/82/4       0% (% ed 41/12/4       29         Landscape works & other associated works       797 days       Thu 18/7/24       0% (% ed 41/12/4       26         Kack Works       180 days       Thu 18/7/24       0% (% ed 41/12/4       26         Kack Works       180 days       Thu 18/7/24       0% (% ed 41/12/4       26         Kack Works       180 days       Wed 19/225       0% (% Ed 7/725       26 (% Fit 17/72)       0% Tae 16/9/25       35         Kack C(Stage 3)       60 days       Wed 9/7/25       0% (% ed 37/24)       1       1         Stack with the village representatives       90 days       Fit 24/7/20       0% (% Ga 5/7/24)       408Ss-28 day         Initial survey and photo-taking       90 days       Mon 21/9/20       0% (% at 9/1/21)       41SS-22 day         Trial pit excavation (Access Date of PTO-B1-01: 22nd Oct 2020)       90 days       Mon 21/9/20       0% (% at 27/2/1)       42SS+25 day         Producing Layout plans showing the loction of terminal manholes, timber box and alignment	Construction of roof top (below + 17.75 mPD)       55 days       Fit 14/624       0% 54.178.24       28       28         Deteral Finishes (incl. installation of Door & Window etc)       90 days       Mon 198/24       0% Word 4/1224       29       1         Landscape works & other associated works       797 days       Tau 31/322       0% Word 4/1224       13       1         E&M works       797 days       Tau 31/322       0% Word 4/1224       13       1         E&M works & other associated works       190 days       Mon 198/24       0% Word 4/1224       13       1         E&M works       Tak (Stage 2)       120 days       Word 192/25       0% Tue 18/275       34 FS-223 da       1         Tak C (Stage 2)       120 days       Word 192/25       0% Tue 16/925       35       1	Construction of rooting (below + 17.75 mPD)       55 drys       Fit 146/24       0% Skt 178/24       28       Image: Skt 178/24       29       Image: Skt 178/24       28       Image: Skt 178/24       28       Image: Skt 178/24       28       Image: Skt 178/24       28       Image: Skt 188/24       Image: Skt 188/24       Image: Sk	Construction of routing below 11.75 mP2)       55 days       Fri 14/6/24       0% Vol 17/18/24       28       Image: Construction of Door & Window rety       90 days       Mon 19/8/24       0% Wol 1/12/24       29       1         External Finishes (ncl. installation of Door & Window rety)       90 days       Mon 19/8/24       0% Wol 4/12/24       29       1	Construction of routing (below 17.25 mPD) \$3 days Fri 14624 07(3) 40 (7) (7) (7) (7) (7) (7) (7) (7) (7) (7)

			Cont	/illage Sewerage in Sai Kung ract No: DC/2019/09 Programme for PTO	9					June 202
isk Name		Duration		Percentage Completion Date of Completion	TRAPredece	essors TRA Te	xt10 2024 H1	H2	2025 HI H2	
Liaison with PTO VR		77 days	Mon 1/3/21	0% Mon 31/5/21	46					
PTO-SW-01 (Open Tre	nch, 18 nos. manholes (170m), and rising main(CH2+53.81 - CH4+36.66)	316 days	Tue 1/6/21	0% Thu 23/6/22						
Landscape works for P	FO-SW-01	316 days	Tue 1/6/21	0% Thu 23/6/22						
PTO-SW-02 (Open Tre	nch, 16nos. Manhole(145m), and a Section of Rising Main)	263 days	Fri 24/6/22	0% Sat 13/5/23						
Landscape works for P	FO-SW-02	263 days	Fri 24/6/22	0% Sat 13/5/23						
PTO-SW-03 (Open Tre	nch, 25 nos., Length: 360m)	390 days	Fri 24/6/22	0% Sat 14/10/23						
Landscape works for P	FO-SW-03	390 days	Fri 24/6/22	0% Sat 14/10/23						
PTO-Trenchless-01 (Tr	enchless, (Length: 75m) and related Rising Main)	237 days	Fri 24/6/22	0% Wed 12/4/23						
Landscape works for P	FO-Trenchless-01	237 days	Fri 24/6/22	0% Wed 12/4/23						
PTO-Trenchless-02 (Tr	enchless, (Length: 100m) and related Rising Main)	289 days	Thu 13/4/23	0% Mon 1/4/24						
Landscape works for P	FO-Trenchless-02	289 days	Thu 13/4/23	0% Mon 1/4/24						
Testing of PTO Village	Sewerage	75 days	Tue 2/4/24	0% Wed 3/7/24			-			
C/2019/09	Task     Project Summary       Project Guide: Critical Task     Project Guide: Critical Task       Split     Split       Milestone     Progress	A A A A A A A A A A A A A A A A A A A	Inacti Manu	al Task 🔷	S F	Start-only Finish-only	* •	Progress Summary	Ŷ	
	Summary Milestone	\$	Manu				e			
	PTO-SW-01 (Open Tree Landscape works for PT PTO-SW-02 (Open Tree Landscape works for PT PTO-SW-03 (Open Tree Landscape works for PT PTO-Trenchless-01 (Tr Landscape works for PT PTO-Trenchless-02 (Tr Landscape works for PT	PTO-SW-01 (Open Trench, 18 nos. manholes (170m), and rising main(CH2+53.81 - CH4+36.66)         Landscape works for PTO-SW-01         PTO-SW-02 (Open Trench, 16nos. Manhole(145m), and a Section of Rising Main)         Landscape works for PTO-SW-02         PTO-SW-03 (Open Trench, 25 nos., Length: 360m)         Landscape works for PTO-SW-03         PTO-Trenchless-01 (Trenchless, (Length: 75m) and related Rising Main)         Landscape works for PTO-Trenchless-01         PTO-Trenchless-02 (Trenchless, (Length: 100m) and related Rising Main)         Landscape works for PTO-Trenchless-02         Testing of PTO Village Sewerage         C/2019/09       Task         Project Guide: Critical Task         Split       Project Guide: Critical Task         Milestone       Split	PTO-SW-01 (Open Trench, 18 nos. manholes (170m), and rising main(CH2+53.81 - CH4+36.66)       316 days         Landscape works for PTO-SW-01       316 days         PTO-SW-02 (Open Trench, 16 nos. Manhole(145m), and a Section of Rising Main)       263 days         Landscape works for PTO-SW-02       263 days         PTO-SW-03 (Open Trench, 25 nos., Length: 360m)       390 days         Landscape works for PTO-SW-03       390 days         PTO-Trenchless-01 (Trenchless, (Length: 75m) and related Rising Main)       237 days         Landscape works for PTO-Trenchless-01       237 days         PTO-Trenchless-42 (Trenchless, (Length: 100m) and related Rising Main)       289 days         Landscape works for PTO-Trenchless-02       289 days         Landscape works for PTO-Trenchless-02 <td< td=""><td>PTO-SW-01 (Open Trench, 18 nos. manholes (170m), and rising main(C112+53.81 - C114+36.66)       316 days       Tue 1/6/21         Landscape works for PTO-SW-01       316 days       Tue 1/6/21         PTO-SW-02 (Open Trench, 16nos. Manhole(145m), and a Section of Rising Main)       263 days       Fri 24/6/22         Landscape works for PTO-SW-02       263 days       Fri 24/6/22         PTO-SW-03 (Open Trench, 25 nos., Length: 360m)       390 days       Fri 24/6/22         Landscape works for PTO-SW-03       390 days       Fri 24/6/22         PTO-Trenchless-01 (Trenchless, (Length: 75m) and related Rising Main)       237 days       Fri 24/6/22         Landscape works for PTO-Trenchless-01       27 days       Fri 24/6/22         PTO-Trenchless-02 (Trenchless, (Length: 100m) and related Rising Main)       289 days       Thu 13/4/23         Landscape works for PTO-Trenchless-02       299 days       Thu 13/4/23         Landscape works for PTO-Trenchles</td><td>Linison with PTO VR       77 days       Mon 1/3/21       0% Mon 31/5/21         PTO-SW-01 (Open Trench, 18 nos. manholes (170m), and rising maint(CH2+53.81 - CH4+36.60)       316 days       Ter 1/6/21       0% The 23/6/22         Landscape works for PTO-SW-01       316 days       Ter 1/6/21       0% The 23/6/22         PTO-SW-02 (Open Trench, 16 nos. Manhole(145m), and a Section of Rising Main)       263 days       Fri 24/6/22       0% Sat 13/5/23         Landscape works for PTO-SW-02       263 days       Fri 24/6/22       0% Sat 13/5/23         PTO-SW-03 (Open Trench, 16 nos. Manhole(145m), and a Section of Rising Main)       263 days       Fri 24/6/22       0% Sat 13/5/23         Landscape works for PTO-SW-02       263 days       Fri 24/6/22       0% Sat 14/10/23         PTO-SW-03 (Open Trench, 25 nos., Length: 360m)       390 days       Fri 24/6/22       0% Sat 14/10/23         Landscape works for PTO-SW-03       390 days       Fri 24/6/22       0% Sat 14/10/23         PTO-Trenchless-01 (Trenchless, (Length: 75m) and related Rising Main)       27 days       Fri 24/6/22       0% Wed 12/4/23         PTO-Trenchless-02 (Trenchless, (Length: 100m) and related Rising Main)       29 days       Thu 13/4/23       0% Mon 1/4/24         PTO-Trenchless-02 (Trenchless, (Length: 100m) and related Rising Main)       29 days       Thu 13/4/23       0% Mon 1/4/24         <td< td=""><td>Lision with PTO VR       77 days       Mon 1/321       0% Mon 31/521       4         PTO-SW-01 (Open Trench, 18 nos. manholes (170m), and rising main(CH2+53.81 - CH4+56.60)       316 days       Tar 1/621       0% Tan 23/622       5         Landscape works for PTO-SW-01       16 days       Tar 1/621       0% Tan 23/622       6         PTO-SW-02 (Open Trench, 16 nos. Manhole(145m), and a Section of Rising Main)       263 days       Fri 24/622       0% Sat 13/523       1         PTO-SW-02 (Open Trench, 16 nos. Manhole(145m), and a Section of Rising Main)       263 days       Fri 24/622       0% Sat 13/523       1         PTO-SW-02 (Open Trench, 16 nos. Manhole(145m), and a Section of Rising Main)       390 days       Fri 24/622       0% Sat 14/1023       1         Iandscape works for PTO-SW-02       263 days       Fri 24/622       0% Sat 14/1023       1       1         PTO-SW-03 (Open Trench, 25 ms., Lengh: 360m)       390 days       Fri 24/622       0% Sat 14/1023       1       1         Iandscape works for PTO-Trenchless-01       237 days       Fri 24/622       0% Wed 12/423       1       1         PTO-Trenchless-02 (Trenchless-01       237 days       Fri 24/622       0% Wed 12/423       1       1         PTO-Trenchless-02 (Trenchless-01       280 days       Thu 13/423       0% Mon 1/4/24       1</td><td>Laison with PTO VR       72 days       Man 1/321       0% Mon 31/521       0       1       1</td><td>Lansen with PTD VR       77 days       Men 1/3/21       0       Men 3/3/21       6       1&lt;</td><td>Laisen with PTD V.       71 days       Net       1/2       1</td><td><math display="block"> \begin{tabular}{ c                                   </math></td></td<></td></td<>	PTO-SW-01 (Open Trench, 18 nos. manholes (170m), and rising main(C112+53.81 - C114+36.66)       316 days       Tue 1/6/21         Landscape works for PTO-SW-01       316 days       Tue 1/6/21         PTO-SW-02 (Open Trench, 16nos. Manhole(145m), and a Section of Rising Main)       263 days       Fri 24/6/22         Landscape works for PTO-SW-02       263 days       Fri 24/6/22         PTO-SW-03 (Open Trench, 25 nos., Length: 360m)       390 days       Fri 24/6/22         Landscape works for PTO-SW-03       390 days       Fri 24/6/22         PTO-Trenchless-01 (Trenchless, (Length: 75m) and related Rising Main)       237 days       Fri 24/6/22         Landscape works for PTO-Trenchless-01       27 days       Fri 24/6/22         PTO-Trenchless-02 (Trenchless, (Length: 100m) and related Rising Main)       289 days       Thu 13/4/23         Landscape works for PTO-Trenchless-02       299 days       Thu 13/4/23         Landscape works for PTO-Trenchles	Linison with PTO VR       77 days       Mon 1/3/21       0% Mon 31/5/21         PTO-SW-01 (Open Trench, 18 nos. manholes (170m), and rising maint(CH2+53.81 - CH4+36.60)       316 days       Ter 1/6/21       0% The 23/6/22         Landscape works for PTO-SW-01       316 days       Ter 1/6/21       0% The 23/6/22         PTO-SW-02 (Open Trench, 16 nos. Manhole(145m), and a Section of Rising Main)       263 days       Fri 24/6/22       0% Sat 13/5/23         Landscape works for PTO-SW-02       263 days       Fri 24/6/22       0% Sat 13/5/23         PTO-SW-03 (Open Trench, 16 nos. Manhole(145m), and a Section of Rising Main)       263 days       Fri 24/6/22       0% Sat 13/5/23         Landscape works for PTO-SW-02       263 days       Fri 24/6/22       0% Sat 14/10/23         PTO-SW-03 (Open Trench, 25 nos., Length: 360m)       390 days       Fri 24/6/22       0% Sat 14/10/23         Landscape works for PTO-SW-03       390 days       Fri 24/6/22       0% Sat 14/10/23         PTO-Trenchless-01 (Trenchless, (Length: 75m) and related Rising Main)       27 days       Fri 24/6/22       0% Wed 12/4/23         PTO-Trenchless-02 (Trenchless, (Length: 100m) and related Rising Main)       29 days       Thu 13/4/23       0% Mon 1/4/24         PTO-Trenchless-02 (Trenchless, (Length: 100m) and related Rising Main)       29 days       Thu 13/4/23       0% Mon 1/4/24 <td< td=""><td>Lision with PTO VR       77 days       Mon 1/321       0% Mon 31/521       4         PTO-SW-01 (Open Trench, 18 nos. manholes (170m), and rising main(CH2+53.81 - CH4+56.60)       316 days       Tar 1/621       0% Tan 23/622       5         Landscape works for PTO-SW-01       16 days       Tar 1/621       0% Tan 23/622       6         PTO-SW-02 (Open Trench, 16 nos. Manhole(145m), and a Section of Rising Main)       263 days       Fri 24/622       0% Sat 13/523       1         PTO-SW-02 (Open Trench, 16 nos. Manhole(145m), and a Section of Rising Main)       263 days       Fri 24/622       0% Sat 13/523       1         PTO-SW-02 (Open Trench, 16 nos. Manhole(145m), and a Section of Rising Main)       390 days       Fri 24/622       0% Sat 14/1023       1         Iandscape works for PTO-SW-02       263 days       Fri 24/622       0% Sat 14/1023       1       1         PTO-SW-03 (Open Trench, 25 ms., Lengh: 360m)       390 days       Fri 24/622       0% Sat 14/1023       1       1         Iandscape works for PTO-Trenchless-01       237 days       Fri 24/622       0% Wed 12/423       1       1         PTO-Trenchless-02 (Trenchless-01       237 days       Fri 24/622       0% Wed 12/423       1       1         PTO-Trenchless-02 (Trenchless-01       280 days       Thu 13/423       0% Mon 1/4/24       1</td><td>Laison with PTO VR       72 days       Man 1/321       0% Mon 31/521       0       1       1</td><td>Lansen with PTD VR       77 days       Men 1/3/21       0       Men 3/3/21       6       1&lt;</td><td>Laisen with PTD V.       71 days       Net       1/2       1</td><td><math display="block"> \begin{tabular}{ c                                   </math></td></td<>	Lision with PTO VR       77 days       Mon 1/321       0% Mon 31/521       4         PTO-SW-01 (Open Trench, 18 nos. manholes (170m), and rising main(CH2+53.81 - CH4+56.60)       316 days       Tar 1/621       0% Tan 23/622       5         Landscape works for PTO-SW-01       16 days       Tar 1/621       0% Tan 23/622       6         PTO-SW-02 (Open Trench, 16 nos. Manhole(145m), and a Section of Rising Main)       263 days       Fri 24/622       0% Sat 13/523       1         PTO-SW-02 (Open Trench, 16 nos. Manhole(145m), and a Section of Rising Main)       263 days       Fri 24/622       0% Sat 13/523       1         PTO-SW-02 (Open Trench, 16 nos. Manhole(145m), and a Section of Rising Main)       390 days       Fri 24/622       0% Sat 14/1023       1         Iandscape works for PTO-SW-02       263 days       Fri 24/622       0% Sat 14/1023       1       1         PTO-SW-03 (Open Trench, 25 ms., Lengh: 360m)       390 days       Fri 24/622       0% Sat 14/1023       1       1         Iandscape works for PTO-Trenchless-01       237 days       Fri 24/622       0% Wed 12/423       1       1         PTO-Trenchless-02 (Trenchless-01       237 days       Fri 24/622       0% Wed 12/423       1       1         PTO-Trenchless-02 (Trenchless-01       280 days       Thu 13/423       0% Mon 1/4/24       1	Laison with PTO VR       72 days       Man 1/321       0% Mon 31/521       0       1       1	Lansen with PTD VR       77 days       Men 1/3/21       0       Men 3/3/21       6       1<	Laisen with PTD V.       71 days       Net       1/2       1	$ \begin{tabular}{ c                                   $

Projec	t: Provision of Village Sewera	age in Sai Kung		Provision of \ Cont	rvices Department of HK /illage Sewerage in Sai I tract No: DC/2019/09 s Programme for PTO	SAR Kung						Date: June 2
ID	Task Name		Duration		Percentage Completion I of Completion	Date TRAPr	edecessors	TRA Tex	110 2024 H1	H2	2025 H1	H2
102					compicator					112		112
03												
104	Submarine Outfall by HD	D Method with Cofferdam	639 days	Mon 12/12/22	0% Tue 4/2/25							
105												
06	Construction of temporar	ry working platform	111 days	Mon 12/12/22	0% Tue 2/5/23	23	FS+60 day					
07	Preparation of MDN		99 days	Mon 5/6/23	0% Fri 29/9/23	10	6			$\neg$		
108	Construction of Cofferda	ım	308 days	Wed 6/12/23	0% Tue 17/12/24	10	6FS+24 di					
109	Pilot Drilling of HDD		40 days	Thu 18/4/24	0% Wed 5/6/24	10	7			*		
10	Enlargement of HDD and	d Pipe Installation	52 days	Fri 19/7/24	0% Tue 17/9/24	10	9			<b>*</b>		
11	Construction of difuser n	nanifold	74 days	Thu 19/9/24	0% Mon 16/12/24	11	0			*		
112	Removal of cofferdam at removal of cofferdam)	t both the manifold and the entry pit (including removal of silt	curtain after 30 days	Wed 1/1/25	0% Tue 4/2/25							
114	Testing of Submaine O	utfall	75 days	Sat 18/5/24	0% Thu 15/8/24					<b>~~~~</b> ,		
116												
117	Completion of Section 2		0 days	Thu 15/8/24	0% Thu 15/8/24	11	5					
		Task Project S Project Guide: Critical Task Project G	ummary		ve Milestone			l Summary nly	•	Progress Summary	÷	
rojec	t:DC/2019/09	Split Split Milestone Progress		Manu Durat	al Task $\diamond$		Finish- Externa	only al Tasks	<b>*</b>	•	-	
		Summary Mileston	• •	Manu	al Summary Rollup 🛛 🔶		Entomo	al Milestone				



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	C-1
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

## APPENDIX C – METEORLOGICAL DATA




EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	C-2
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

				Hong Kong	Observatory		· · ·		King's Park	Waglan	Island^
Day	Mean Pressure (hPa)	A Absolute Daily Max (deg. C)	ir Temperatu Mean (deg. C)	re Absolute Daily Min (deg. C)	Mean Dew Point (deg. C)	Mean Relative Humidity (%)	Mean Amount of Cloud (%)	Total Rainfall (mm)	Total Bright Sunshine (hours)	Prevailing Wind Direction (degrees)	Mean Wind Speed (km/h)
1	1005.2	34.2	30.9	27.8	21.6	58	78	0	***	***	***
2	1009.9	30.8	27.4	25.5	17.3	54	75	0	***	***	***
3	1013.2	29.4	26.1	23.3	14.6	49	74	0	***	***	***
4	1014.4	30.9	27	24.6	15.8	50	69	0	***	***	***
5	1013.3	31.5	27.9	25.5	20	63	80	0	***	***	***
6	1013.7	33.3	29.2	26.7	23	70	42	0	***	***	***
7	1014.4	32.9	29.3	27.3	22.2	66	60	0	***	***	***
8	1014.2	31.7	28.2	26.2	20.1	62	35	0	***	***	***
9	1013.5	27.4	26.4	25.2	20.1	68	83	Trace	***	***	***
10	1013	30.6	27	24.5	20.4	68	58	Trace	***	***	***
1	1013.7	27.5	25.3	23.2	21.3	79	84	8.7	***	***	***
2	1015.1	29.7	27	25.6	20.2	67	31	0	***	***	***
3	1014.5	30.2	27.5	25.9	22.2	73	65	0	***	***	***
4	1013.5	31	28	26.3	23	75	34	0	***	***	***
5	1013.6	30.9	28.1	26.6	23.3	75	77	0	***	***	***
6	1014.5	31.1	28.2	27.4	23	74	88	Trace	***	***	***
7	1013.9	29.7	27.8	27.1	23.3	77	85	Trace	***	***	***
8	1013.2	30.7	28.3	27.1	24	78	85	Trace	***	***	***
19	1014.1	33.7	29.2	26.4	23.9	74	43	0	***	***	***
20	1016.5	29.7	27.9	26.9	23.1	75	82	1.9	***	***	***
21	1015	31.5	27.8	26.4	22.9	75	69	Trace	***	***	***
22	1013.7	32.3	28.3	26	20.5	64	52	0	***	***	***
23	1012.4	28.4	25.7	23.4	16.4	57	81	0	***	***	***
24	1009.2	28.5	24.8	22	10.6	42	84	0	***	***	***
25	1006.7	29.4	26	22.9	13.2	45	78	0	***	***	***
26	1006.6	28.5	26.6	25.3	19.8	67	88	0.7	***	***	***
27	1009.3	29.2	27.3	25.9	22	73	77	Trace	***	***	***
28	1010.1	27.2	25.8	24.6	19.2	67	83	Trace	***	***	***
29	1011.1	26.7	25.3	23.7	19.1	69	86	Trace	***	***	***
30	1010.3	29.3	26.2	24.3	18.7	64	70	0	***	***	***
31	1006	30.6	27.1	24.1	16.4	52	41	0	***	***	***
ı∕Total	1012.2	30.3	27.3	25.4	20	65	69	11.3	***	***	***
Climatologic al Normal?	1014	28.1	25.7	23.9	20.2	73	58	120.3	197.8	80	26.3


Source: Daily Extract | Hong Kong Observatory(HKO) | Climate Information Service





# APPENDIX D – AIR QUALITY MONITORING EQUIPMENT CALIBRATION CERTIFICATES

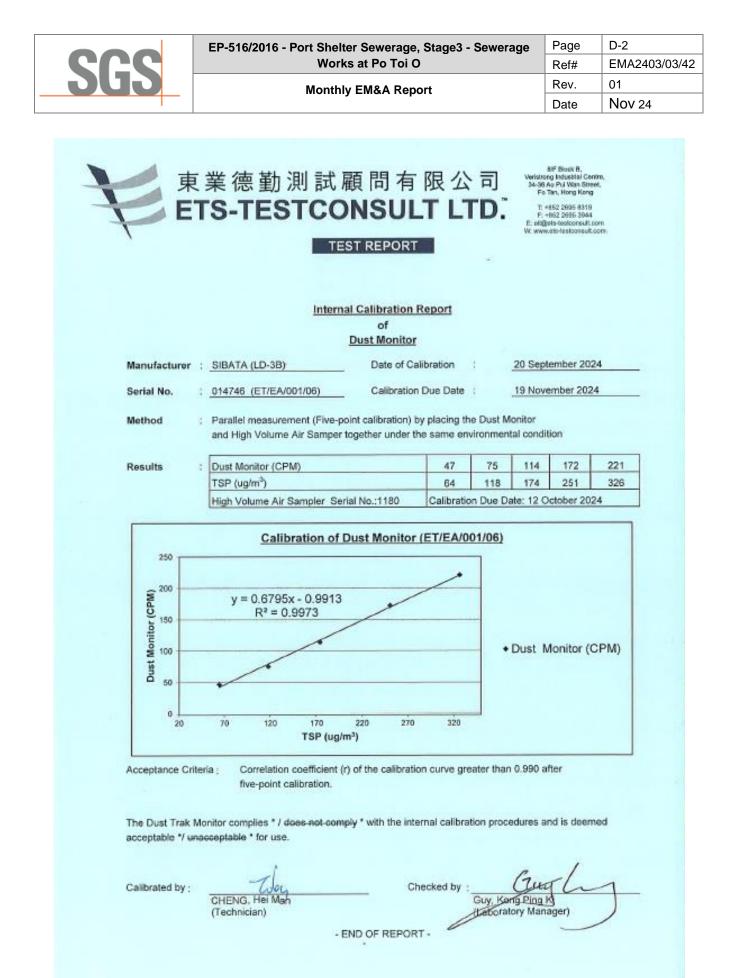

000	EP-516/2016 - Port Shelter Sewerage,	Stage3 - S	ewerage	e P	age	D-3
212	Works at Po Toi O			R	ef#	EMA2403/03/42
	Monthly EM&A Repo	rt		R	ev.	01
ļ				D	ate	Nov 24
			D. (	Antering Ind 34-34 Au P. Fo Tan, I Fo Tan, I F	took 8, Institut Cervito 4 Wan Street, Hong Kong 2866 5014 astoonsult.com softworkell, com softworkell, com softworkell, com mber 202 mber 202	24
Method	Parallel measurement (Five-point calibration) by and High Volume Air Samper together under the					
Results	: Dust Monitor (CPM)	60	112	161	223	279
	TSP (ug/m <sup>3</sup> )	71	123	192	249	316
	High Volume Air Sampler Serial No.: 9795	Calibratio	on Due Dat	te: 11 O	ctober 20	24
300 250 200 150 150 50 0 200	Calibration of Dust Monitor (E y = 0.8898x - 2.2399 R <sup>2</sup> = 0.9968	<u></u>	+ Dus	st Mor	nitor (CF	PM)
acceptable */ u Calibrated by :	Iteria : Correlation coefficient (r) of the calibration calibration Monitor complies * / does not comply * with the intern nacceptable * for use, CHENG, Hei Man (Technician) - END OF REPORT	nal calibration Chec	procedure ked by :	es and is		

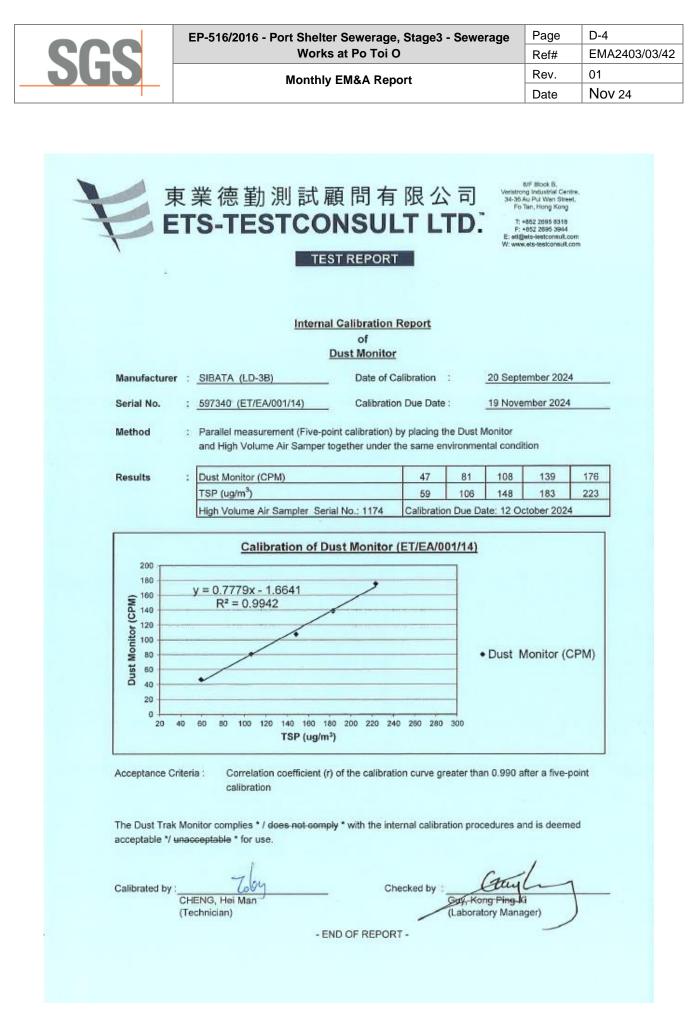

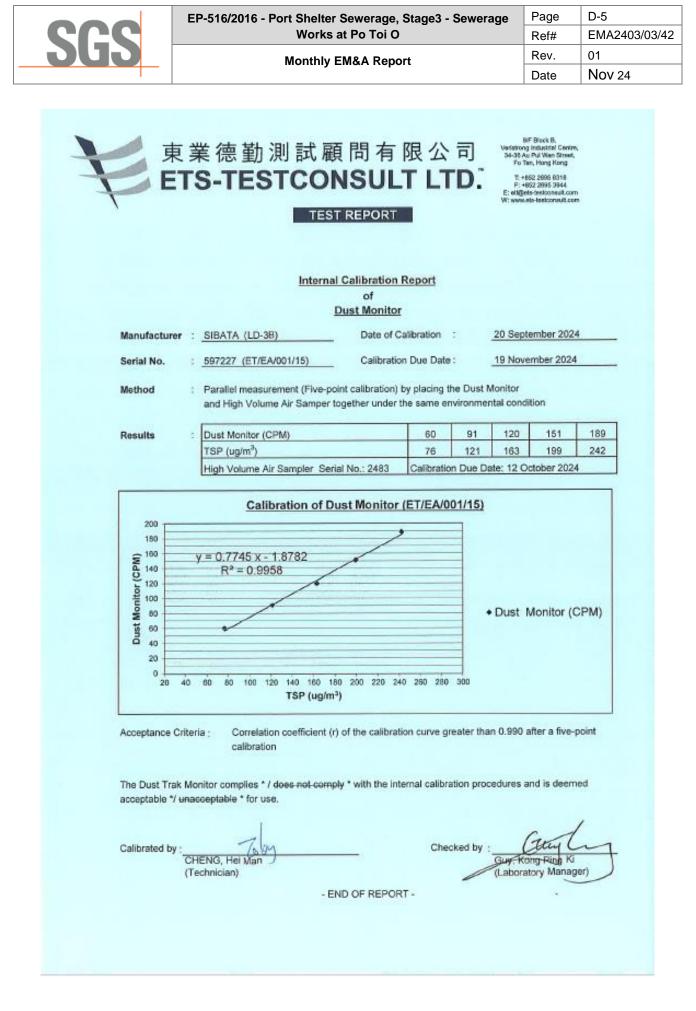

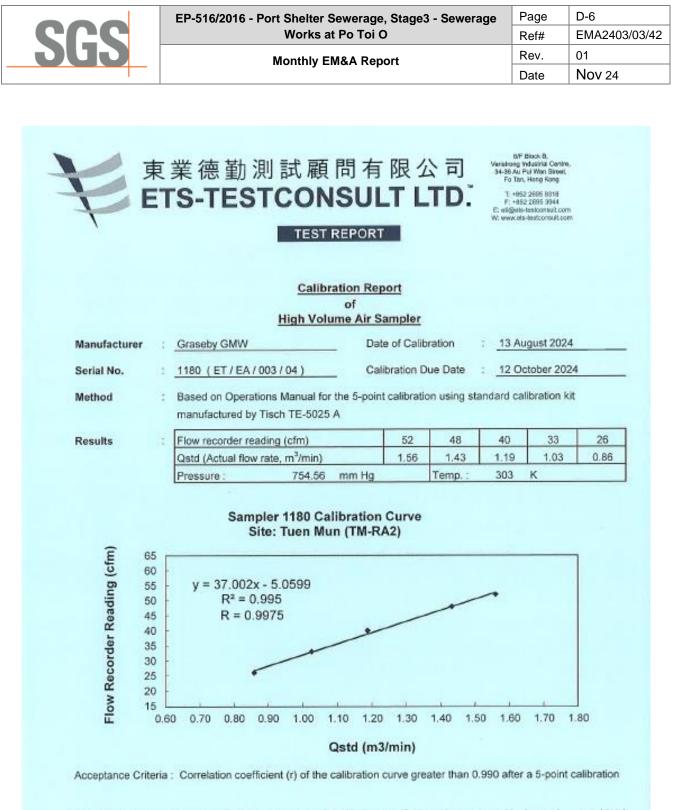


The high volume sampler complies\* / does not comply\* with the specified requirements and is deemed acceptable\* / unacceptable \* for use.

Calibrated by : Wai MAK, Kei Wai

(Assistant Supervisor)

Checked by :

LAU, Chi Leung (Environmental Team Leader)

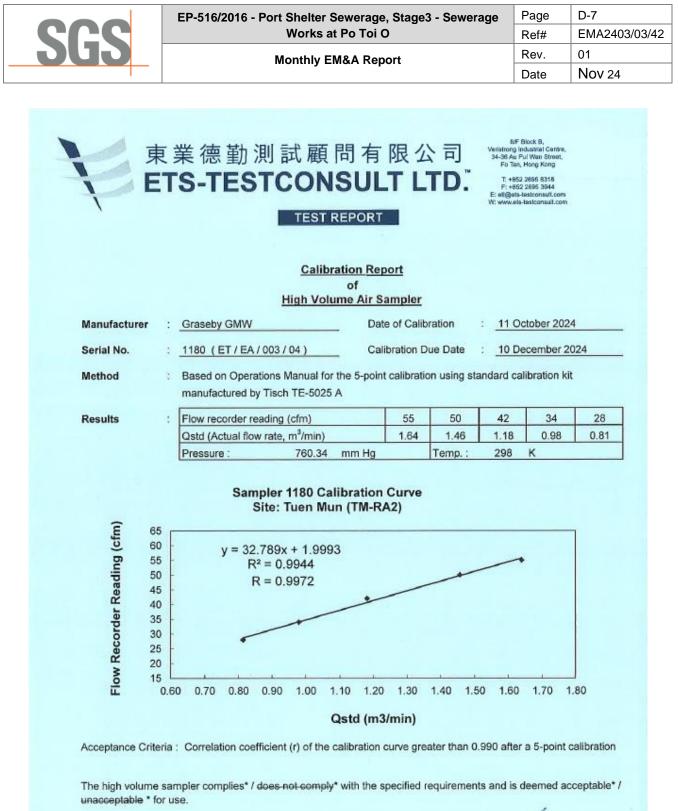

Calibrated by : <u>Mak</u> <u>Yu</u> <u>Wan</u> MAK, Kei Wai (Assistant Supervisor)

Checked by LAU, Chi Leung (Environmental Team Leader)

	EP-516/2016 - Port Shelter Sewerag	e, Stage3	3 - Sewerag	je Pa	ge	D-8
<b>QLQ</b>	Works at Po Toi	0		Ret	f#	EMA2403/03/4
<b>JUJ</b>	Monthly EM&A Re	port		Re	v.	01
				Dat	te	Nov 24
	業德勤測試顧問有 TS-TESTCONSU TEST REPOR	LTL		0/F Bio Verletong Indu 34-36 Au Pul Fo Tan, Ho F: +652 20 F: +652 20 F: +652 20 F: +652 20 F: edi@etn-fes W: www.ets-fee	istrial Centre, Wan Street, ong Kong 195 8318 595 3944 dconsult.com	
	<u>Calibration R</u> of <u>High Volume Air</u>	na n	<u>ər</u>			
Manufacturer	: Graseby GMW Da	ate of Calib	ration :	13 Augus	st 2024	
Serial No.	: <u>1174 (ET / EA / 003 / 08)</u> Ca	alibration D	ue Date :	12 Octob	er 2024	
Method	: Five-point calibration by using standard cal Manual	ibration kit	Tisch TE-502	5A refer to	the Oper	rations
Results	Flow recorder reading (cfm)	53	47	42	33	27
	Qstd (Actual flow rate, m <sup>3</sup> /min)	1.56	1.42	1.23	1.02	0.87
	Pressure : 754.56 mi	m Hg	Temp. :	303 K		
Reading (cfm) 0 2 2 2 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	Sampler 1174 Cal Site: Tuen Mun ( y = 37.395x - 5.2472 R <sup>2</sup> = 0.9954 R = 0.9977				•	
Flow Recorder Reading (cfm) 52 05 05 05 05 05 05 05 05 05 05 05 05 05	70 0.80 0.90 1.00 1.10 1		.0 1.40	1.50	1.60	1.70


Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a 5-point calibration.

Qstd (m3/min)

The high volume sampler complies\* / does not comply\* with the specified requirements and is deemed acceptable\* / unacceptable\* for use.

Calibrated by : <u>Mark Vei 1</u> MAK, Kei Wai (Assistant Supervisor) Ver War

Checked by : LAU, Chi Leung (Environmental Team Leader)

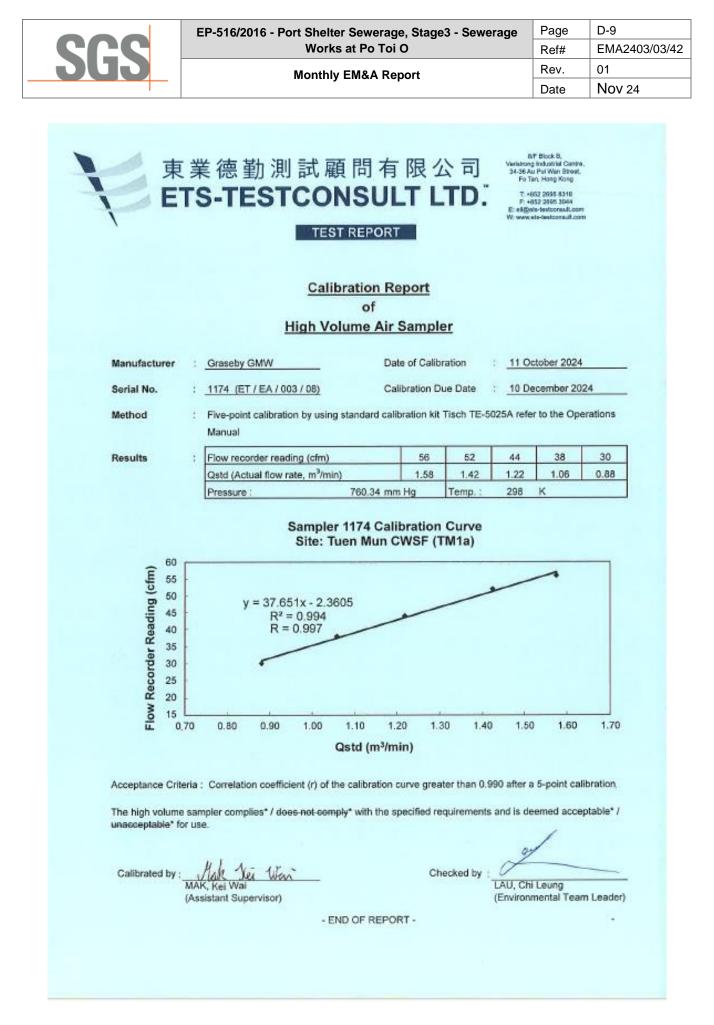





#### **Calibration Report**

of


#### High Volume Air Sampler

Manufacturer	:	Graseby 105	Date of Calibration	:	12 August 2024
Serial No.	:	9795 (ET/EA/003/18)	Calibration Due Date	:	_11 October 2024
Method	;	Five-point calibration by using star Operations Manual	ndard calibration kit Tisch T	E-50	25A refer to the

Results

Flow recorder rea	ading (cfm)	50	44	38	33	25
Qstd (Actual flow rate, m <sup>3</sup> /min)		1.54	1.42	1.23	1.07	0.85
Pressure :	753.14 mm H	łg	Temp.: 302 K			

#### Sampler 9795 Calibration Curve Site: Tseung Kwan O 137 (TKO-A1)



Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a 5-point calibration


The high volume sampler complies\* / does not comply\* with the specified requirements and is deemed acceptable\*/ unacceptable\* for use.

Calibrated by :

Checked by : LAU, Chi Leung (Environmental Team Leader)

MAK, Kei Wai (Assistant Supervisor)

Wai



	業德勤測試顧 TS-TESTCON TEST			Verisiron 34-35 A Fo T T: + F: + E: etil@r	M <sup>®</sup> Block B, Ig Industrial Cent w Pui Wan Stree an, Hong Kong 852 2695 8318 852 2695 3944 ets-testconsuit c .ets-testconsuit c	om
		ration Report of ume Air Sampler				
Manufacturer	: Graseby 105	Date of Calibra	ation	: <u>09 Oc</u>	tober 2024	
Serial No.	: 9795 (ET/EA/003/18)	Calibration Du	e Date	: 08 De	cember 20	24
Method	: Five-point calibration by using st Operations Manual	tandard calibration kit	Tisch TE-	5025A ref	er to the	
Results	Flow recorder reading (cfm)	46	42	34	30	24
	Qstd (Actual flow rate, m <sup>3</sup> /min)	1.64	1.47	1.24	1.08	0.83

760.19 mm Hg


Pressure :

#### Sampler 9795 Calibration Curve Site: Tseung Kwan O 137 (TKO-A1)

Temp. :

299

K



Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a 5-point calibration

The high volume sampler complies\* / does not comply\* with the specified requirements and is deemed acceptable\*/ unacceptable\* for use.

Calibrated by :

Checked by : LAU, Chi Leung

(Environmental Team Leader)


- END OF REPORT -

Wai

les

MAK, Kei Wai


(Assistant Supervisor)

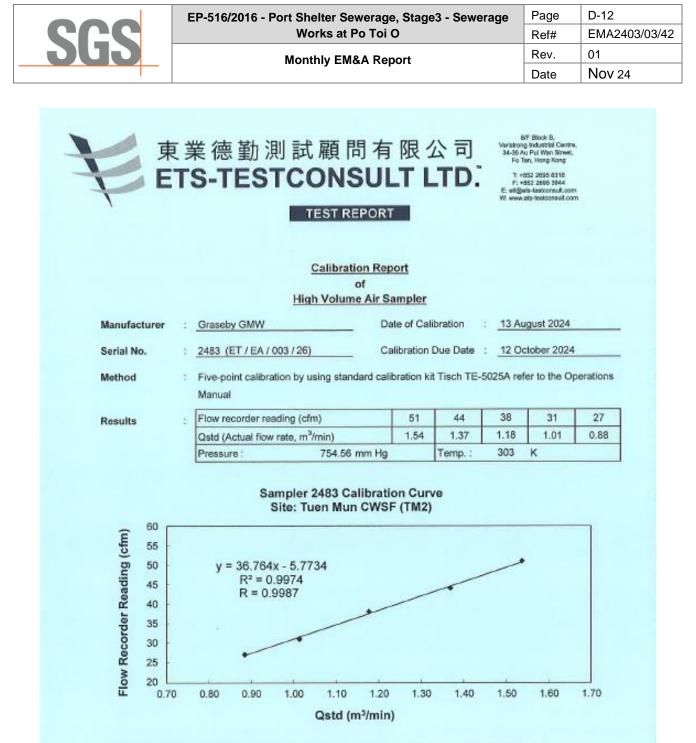

Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a 5-point calibration

The high volume sampler complies\* / does not comply\* with the specified requirements and is deemed acceptable\*/ unacceptable\* for use.

Checked by : 1,14 Calibrated by LAU, Chi Leung MAK, Kei Wai (Assistant Supervisor) (Environmental Team Leader)

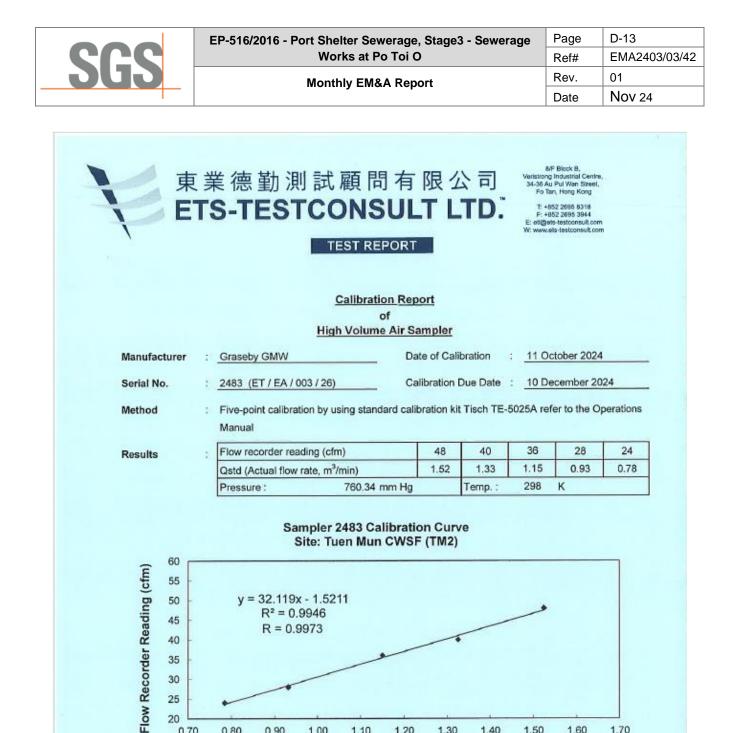

Qstd (m<sup>3</sup>/min)

1.20

1.30

1.40

1.10

1.00

Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a 5-point calibration

The high volume sampler complies\* / does not comply\* with the specified requirements and is deemed acceptable\*/ unacceptable\* for use.

War Calibrated by MAK, Kei Wai (Assistant Supervisor)

0.80

0.90

30 25 20

0.70

Checked by : LAU, Chi Leung

(Environmental Team Leader)

1.60

1.50

1.70

EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	D-14
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24



Tisch Environmental, Inc.

145 South Miami Avenue

Village of Cleves, OH 45002

www.tisch-env.com TOLL FREE: (877)263-7610 FAX: (513)467-9009



# APPENDIX E – METHODOLOGY FOR CORRELATION CALCULATION BETWEEN POTABLE LASER DUST METER AND HIGH-VOLUME SAMPLER



### Correlation between Portable laser dusty meter and High-volume Sampler Methodology

Correlation results between the direct reading meter and High-Volume Sampler

High – Volume Sampler Calibration

The specification, a sample of calibration certificate and certificate of comparison check with High volume sampler of the proposed air quality monitoring equipment listed in Table 2.1 are attached in appendix.

The High-Volume air sampler calibration procedure based on the requirement of manufacturer is shown below.

- a. Disconnect the sampler motor from the mass flow controller and connect the motor to a stable AC power source.
- b. Mount the calibrator orifice and top loading adapter plate to the sampler. A sampling filter is generally not used during this procedure. Tighten the top loading adapter hold down nuts securely to ensure that no air leaks are present.
- c. Allow the sampler motor to warm up to its normal operating temperature (approximately 10-15 minutes).
- d. Conduct a leak test by covering the hole(s) on top of the orifice and pressure tap on the orifice with your hands. Listen for a high-pitched squealing sound made by escaping air. If this sound is heard, a leak is present and the top loading adapter hold-down nuts need to be re-tightened. If the sound is lower, the leak is near one of the other gaskets in the system. Avoid running the sampler for longer than 30 seconds at a time with the orifice blocked to avoid overheating the motor. Do not perform this leak test procedure with a manometer connected to the side tap on the calibration orifice or the blower motor. Liquid from the manometer could be drawn into the system and cause motor damage
- e. Connect one side of a water manometer to the pressure tap on the side of the orifice with a rubber vacuum tube. Leave the opposite side of the manometer open to the atmosphere. Note: Both valves on the manometer have to be open for the liquid to flow freely. One side of the 'U' tube goes up the other goes down; add together for the "H2O reading.
- f. A manometer must be held vertically to ensure accurate readings. Tapping the backside of the continuous flow recorder will help to center the pen and provide accurate readings. When using a variable orifice, five flow rates are achieved in this step by adjusting the knob on the variable orifice to five different positions and taking five different reading.



- g. Record the ambient air temperature, the ambient barometric pressure, the sampler serial number, the orifice s/n, the orifice slope and intercept with date last certified, today's date, site location and the operators initial on the attached blank calibration sheet.
- h. An example of a Lead (or TSP) Sampler Calibration Data Sheet has been attached with data filled in from a typical calibration. This includes the transfer standard orifice calibration relationship which was taken from the Orifice Calibration Worksheet that accompanies the calibrator orifice.

Disconnect the sampler motor from its power source and remove the orifice and top loading adapter plate. Re-connect the sampler motor to the electronic mass flow controller.

Since this calibration is for a TSP sampler, the slope and intercept for this orifice uses standard flows rather than actual flows and is taken from the Q standard section of the Orifice Calibration Worksheet. The Q actual flows are only used when calibrating a PM-10 sampler.

The five orifice manometer readings taken during the calibration have been recorded in the column on the data worksheet titled Orifice "H2O. The five continuous flow recorder readings taken during the calibration have been recorded under the column titled I chart.

The orifice manometer readings need to be converted to the standard air flows they represent using the following equation:

 $Qstd = 1/m[Sqrt((H_20)(Pa/760)(298/Ta))-b]$ 

where:


Qstd = actual flow rate as indicated by the calibrator orifice,  $m^3/min$  H<sub>2</sub>O = orifice manometer reading during calibration, "H<sub>2</sub>O

- Ta = ambient temperature during calibration, K ( $K = 273 + ^{\circ}C$ )
- 298 = standard temperature, a constant that never changes, K

Pa = ambient barometric pressure during calibration, mm Hg

- 760 = standard barometric pressure, a constant that never changes, mm Hg
- m = *Qstandard slope of orifice* calibration relationship

b = *Qstandard intercept of orifice* calibration relationship.



Once these standard flow rates have been determined for each of the five run points, they are recorded in the column titled Qstd and are represented in cubic meters per minute.

The continuous flow recorder readings taken during the calibration need to be corrected to the current meteorological conditions using the following equation:

IC = I[Sqrt((Pa/760)(298/Ta))]

where:
IC = continuous flow recorder readings corrected to current Ta and Pa
I = continuous flow recorder readings during calibration
Pa = ambient barometric pressure during calibration, mm Hg.
760 = standard barometric pressure, a constant that never changes, mm Hg
Ta = ambient temperature during calibration, K (K = 273 + °C)
298 = standard temperature, a constant that never changes, K

After each of the continuous flow recorder readings have been corrected, they are recorded in the column titled IC (corrected).


Using Qstd and IC (or FLOW (corrected)) as the x and y axis respectively, a slope, intercept, and correlation coefficient can be calculated using the least squares regression method. The correlation coefficient should never be less than 0.990 after a five-point calibration. A coefficient below .990 indicates a calibration that is not linear, and the calibration should be performed again. If this occurs, it is most likely the result of an air leak during the calibration or high wind speed during the calibration procedure.

The equations for determining the slope (m) and intercept (b) are as follows:

m=
$$\frac{\frac{(\sum x)(\sum y)}{\sum xy - n}}{\frac{(\sum x)^2}{\sum x^2 - n}}; \quad b = \overline{y} - m\overline{x}$$

The equation for the coefficient of correlation (r) is as follows:

202	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page Ref#	E-5 EMA2403/03/42
<b>DUD</b>	Monthly EM&A Report	Rev.	01
		Date	Nov 24



where: n = number of observations $\sum = sum of$ 

The acceptable operating flow range of a TSP sampler is 1.1 to 1.7 m3/min (39 to 60 CFM). Looking at the worksheet column Qstd(see page 38), the flow rates that are within this range can be identified along with the chart reading (I) that represents them. For instance, if you wanted to set this sampler at 1.265 m3/min (44.67 CFM) (Make sure the mass flow controller is plugged in and a filter is in place) you would turn the Flow Adjustment screw until the continuous flow recorder read 37 on the chart. By making sure that the sampler is operating at a chart reading (or manometer reading) that is within the acceptable range, it can be assumed that valid TSP data is being collected.

A calibration that has a correlation coefficient of less than .990 is not considered linear and should be re-calibrated. Therefore, if r < 0.990, return all the points or only the point with the greatest deviation and the recalculate.

The 24-hour TSP levels to be measured by direct reading methods, utilising portable Laser Particle Photometer Monitors (Sibata Model LD-3B), in place of High-Volume Sampler (HVS) if HVS experience difficulties in operation during monitoring. It is demonstrated by the previous project experiences, that 24-hour TSP monitoring results collected by direct reading method are comparable to those produced by the high-volume sampling method, to indicate short event impacts. The projects utilising the collection of 24-hour TSP levels data by direct reading methods are shown below.

## Project Reference for utilising the collection of 24-hour TSP levels data by direct reading methods

Project Contract Number	Location	Status
NDO 03/2018	Road Widening and Retrofitting Noise Barriers on	On-going
	Tai Po Road (Sha Tin Section)	



NDO 14/2018	Advance and First Stage Works of Kwu Tung North	On-going
	and Fanling North New Development Areas	

Calculation of the value of 24-hour TSP concentration is given by the average of 24 calculated 1-hour TSP concentration, where the calculated 1-hr TSP concentration is given by the product of the direct reading and the K-factor based on the correlation results between the direct reading meter and High-Volume Sampler.

The correlation results between the direct reading meter and High-Volume Sampler shall be review with bimonthly internal calibration. To maintain the correlation with two sets of data (monitoring data from HVS and monitoring data from Portable Laser Particle Photometer Monitors) bimonthly internal calculated are strongly linked together two sets of data.

To protect the dust meter from being damaged and to operate without disturbances or nuisance, temporary barriers shall be erected around the monitoring equipment during the monitoring period. Temporary barriers will be placed approx. 0.5m away from the dust meter.

## Maintenance/ Calibration for the High-Volume Sampler (HVS) being correlation

The HVS shall be calibrated bimonthly in accordance to the specification in the manufacturer's manual. The calibration certificates shall be available to the IEC for checking upon request. The validity and accuracy of the HVS shall also be tested against the result by the TE-5025A Calibration Kit periodically, Details of Calibration Cert and Specification for HVS – Graseby GMW and HVS- Calibration Kit TE-5025A are given in Appendix 2-1 and Appendix 2-3.

Graseby GMW is chosen as the HVS for 24-hour TSP monitoring and Tisch TE – 5025A is chosen as the HVS Calibration-Kit for HVS calibration.



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	F-1
Works at Po Toi O		EMA2403/03/42
Monthly EM&A Report		01
		Nov 24

# APPENDIX F – AIR QUALITY AND NOISE IMPACT MONITORING SCHEDULE



## 2024 October Air Quality and Noise Impact Monitoring Schedule

Sunday	Monday	Tuesday	Wednesday	Thuraday	Friday	Saturday
29-Sep		1-Oct		3-Oct		5-Oct
	1 hr TSP x 3 24 hr TSP Noise (30 mins)				1 hr TSP x 3 24 hr TSP	
6-Oct	7-0d	8-Oct	9-Oct	10-Oct	11-Oct	12-0d
				1 hr TSP x 3 24 hr TSP Noise (30 mins)		
13-Oct	14-Oct	15-Oct	16-Oct	17-Oct	18-Oct	19-Oct
			1 hr TSP x 3 24 hr TSP Noise (30 mins)			
20-Oct	21-Oct	22-Oct	23-Oct	24-Oct	25-Oct	26-Oct
		1 hr TSP x 3 24 hr TSP Noise (30 mins)				
27-Oct	28-Oct	29-Oct	30-Oct	31-Oct	1-Nov	2-Nov
	1 hr TSP x 3 24 hr TSP Noise (30 mins)				1 hr TSP x 3 24 hr TSP	



## 2024 November Air Quality and Noise Impact Monitoring Schedule

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	8-aturday
27-Oct	28-Oct	29-Oct	30-Oct	31-Oct	1-Nov	2-Nov
	1 hr TSP x 3 24 hr TSP Noise (30 mins)				1 hr TSP x 3 24 hr TSP	
2.000	4-Nov	5-Nov	6-Nov	7-Nov	8-Nov	9-Nov
3-Nov	- HOV	5-1407	6-NOV	1 hr TSP x 3 24 hr TSP Noise (30 mins)	8-1407	-107
10-Nov	11-Nov	12-Nov	13-Nov	14-Nov	15-Nov	16-Nov
			1 hr TSP x 3 24 hr TSP Noise (30 mins)			
17-Nov	18-Nov	19-Nov 1 hr TSP x 3 24 hr TSP Nolse (30 mins)	20-Nov	21-Nov	22-Nov	23-Nov
24-Nov	25-Nov 1 hr TSP x 3 24 hr TSP Noise (30 mins)	26-Nov	27-Nov	28-Nov	29-Nov 1 hr TSP x 3 24 hr TSP	30-Nov

SGS	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	G-1
	Works at Po Toi O	Ref#	EMA2403/03/42
	Monthly EM&A Report	Rev.	01
		Date	Nov 24

## APPENDIX G – AIR QUALITY MONITORING RESULT

SGS	ED 516/2016 Dart Shaltar Sawarana Stance Sowarana Warka at Da Tai O	Page	G-2
	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Ref#	EMA2403/03/42
	Monthly EM&A Report		01
		Date	Nov 24

## 2024 October 1-hour Monitoring Data

## Monitoring Location: AMS1N

				1-hour TSP Monitoring			
Date	Weather		Start Time	Concentration (µg/m³)	Average Concentration (µg/m <sup>3</sup> )		
		1st hr	13:00	52.0			
4- October -24	Fine	2nd hr	14:00	53.0	52.7		
		3rd hr	15:00	53.0			
		1st hr	10:30	50.0			
10- October -24	Sunny	2nd hr	13:30	49.0	50.0		
		3rd hr	14:32	51.0			
	Sunny	1st hr	10:15	47.0			
16- October -24		2nd hr	13:15	49.0	48.7		
		3rd hr	14:15	50.0			
		1st hr	10:30	46.0			
22- October -24	Sunny	2nd hr	13:10	49.0	48.3		
		3rd hr	14:10	50.0			
		1st hr	10:45	35.0			
28- October -24	Sunny	2nd hr	13:46	36.0	37.7		
	•	3rd hr	14:48	42.0			
				Average:	47.5		
				Action Level:	319		
				Limit Level:	500		

SGS	ED 516/2016 Dert Shelter Sewerere Stare? Sewerere Werke at De Tei O	Page	G-3
	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Ref#	EMA2403/03/42
	Monthly EM&A Report	Rev.	01
		Date	Nov 24

## 2024 October 1-hour Monitoring Data

## Monitoring Location: AMS2N1

			1-hour TSP Monitoring				
Date	Weather		Start Time	Concentration (µg/m³)	Average Concentration (µg/m³)		
		1st hr	13:05	53.0			
4- October -24	Fine	2nd hr	14:05	50.0	51.0		
		3rd hr	15:05	50.0			
		1st hr	10:40	54.0			
10- October -24	Sunny	2nd hr	13:17	50.0	56.0		
	·	3rd hr	14:20	64.0			
	Sunny	1st hr	10:25	55.0			
16- October -24		2nd hr	13:25	51.0	56.3		
		3rd hr	14:25	63.0			
	Sunny	1st hr	10:35	55.0			
22- October -24		2nd hr	13:15	50.0	56.3		
		3rd hr	14:15	64.0			
		1st hr	10:40	41.0			
28- October -24	Sunny	2nd hr	13:41	44.0	43.3		
		3rd hr	14:41	45.0			
				Average:	52.6		
				Action Level:	279		
				Limit Level:	500		

SGS	ED 516/2016 Dest Shelter Severage Stage? Severage Werke at De Tei O	Page	G-4
	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Ref#	EMA2403/03/42
	Monthly EM&A Report	Rev.	01
		Date	Nov 24

## 2024 October 1-hour Monitoring Data

## Monitoring Location: AMS3N

			1-hour TSP Monitoring				
Date	Weather		Start Time	Concentration (µg/m <sup>3</sup> )	Average Concentration (µg/m³)		
		1st hr	13:15	43.0			
4- October -24	Fine	2nd hr	14:15	46.0	43.7		
		3rd hr	15:15	42.0			
		1st hr	10:50	51.0			
10- October -24	Sunny	2nd hr	13:08	43.0	47.7		
		3rd hr	14:10	49.0			
	Sunny	1st hr	13:30	51.0			
16- October -24		2nd hr	14:30	45.0	52.0		
		3rd hr	15:30	60.0			
	Sunny	1st hr	13:35	52.0			
22- October -24		2nd hr	14:35	43.0	51.7		
		3rd hr	15:35	60.0			
		1st hr	10:35	41.0			
28- October -24	Sunny	2nd hr	13:35	39.0	39.7		
	-	3rd hr	14:35	39.0			
		·		Average:	46.9		
				Action Level:	303		
				Limit Level:	500		


SGS	ED 516/2016 Dart Shaltar Sawarana Stana3 Sawarana Warka at Da Tai O	Page	G-5
	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Ref#	EMA2403/03/42
	Monthly EM&A Report	Rev.	01
		Date	Nov 24

## 2024 October 1-hour Monitoring Data

## Monitoring Location: AMS4N


			1-hour TSP Monitoring		
Date	Weather		Start Time	Concentration (µg/m <sup>3</sup> )	Average Concentration (µg/m <sup>3</sup> )
		1st hr	13:25	41.0	
4- October -24	Fine	2nd hr	14:25	40.0	41.3
		3rd hr	15:25	43.0	
		1st hr	11:00	38.0	
10- October -24	Sunny	2nd hr	13:00	32.0	38.7
	·	3rd hr	14:00	46.0	
	Sunny	1st hr	14:45	44.0	
16- October -24		2nd hr	15;45	43.0	44.3
		3rd hr	16:45	46.0	
	Sunny	1st hr	13:40	43.0	
22- October -24		2nd hr	14:40	41.0	43.3
		3rd hr	15:40	46.0	
		1st hr	10:26	38.0	
28- October -24	Sunny	2nd hr	13:37	40.0	38.3
	- 	3rd hr	14:28	37.0	
				Average:	41.2
				Action Level:	278
				Limit Level:	500

SGS	ED 516/2016 Dest Shelter Severage Stage? Severage Werke at De Tei O	Page	G-6
	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Ref#	EMA2403/03/42
	Monthly EM&A Report	Rev.	01
		Date	Nov 24

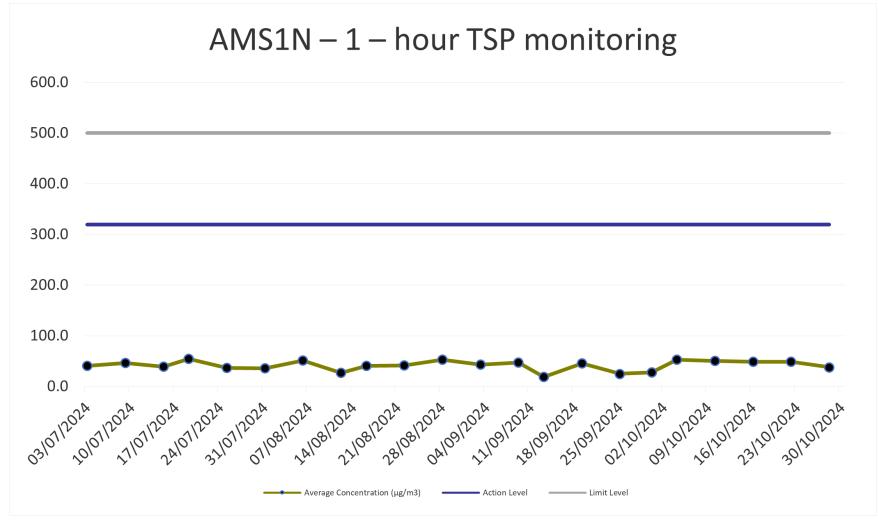


G-6


	ED 516/2016 Dert Shelter Sewerere Stare? Sewerere Werke at De Tei O	Page	G-7
CCC	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		EMA2403/03/42
<u> </u>	Monthly EM&A Report	Rev.	01
		Date	Nov 24

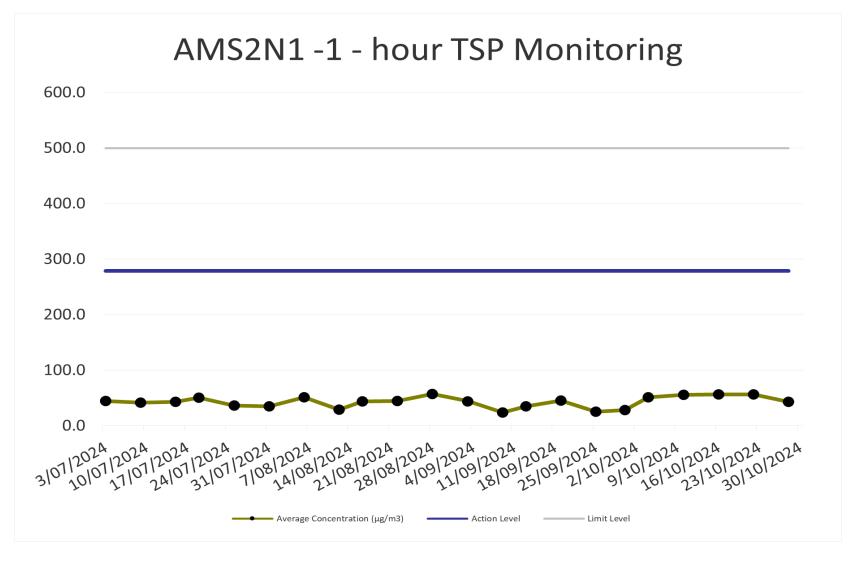

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-8
		Ref#	EMA2403/03/42
<u> </u>	Monthly EM&A Report	Rev.	01
		Date	Nov 24

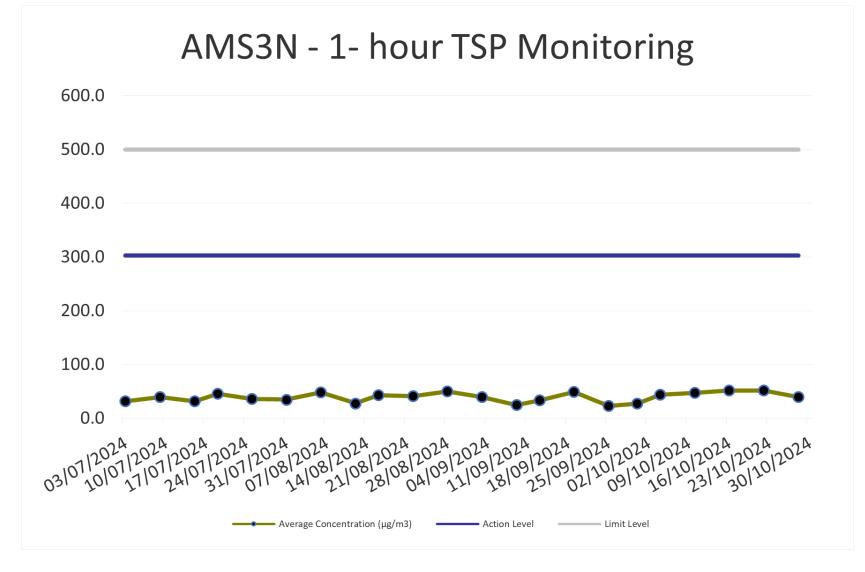

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-9
		Ref#	EMA2403/03/42
<u> </u>	Monthly EM&A Report	Rev.	01
		Date	Nov 24

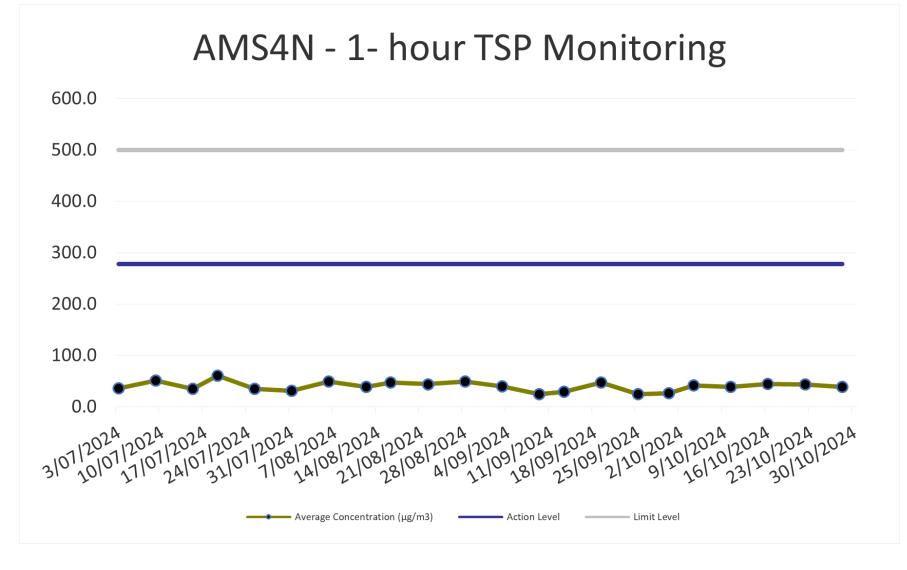

000	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po	Page	G-10
SGS	Τοί Ο	Ref#	EMA2403/03/42
	Monthly EM&A Report	Rev.	01
		Date	Nov 24

## 2024 Ocotober 24-hour Monitoring Data

## Monitoring Location: AMS1N

Hour	4- October -24	10- October -24	16- October -24	22- October -24	28- October -24
1	26	24	26	22	29
2	23	22	27	23	31
3	24	34	35	35	29
4	30	32	33	31	28
5	28	33	33	38	31
6	25	31	37	36	29
7	27	27	26	27	30
8	25	21	27	28	28
9	35	31	30	30	29
10	23	27	29	28	25
11	20	28	30	29	32
12	21	28	27	27	31
13	26	26	27	26	29
14	27	32	37	31	27
15	25	23	25	29	29
16	27	33	35	35	31
17	31	33	36	36	29
18	24	22	25	26	28
19	26	25	26	25	30
20	29	31	30	31	28
21	27	22	23	22	27
22	24	28	27	28	31
23	29	28	28	27	33
24	28	23	32	23	26
Average:	26	28	30	29	29
24-hr TSP					
(µg/m³; with					
correlation(x)	32	34	36	35	35
Action Level:	153		•	•	•
Limit Level:	260				

SGS	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po	Page	G-11
	Toi O	Ref#	EMA2403/03/42
	Monthly EM&A Report	Rev.	01
		Date	Nov 24

## 2024 Ocotober 24-hour Monitoring Data

## Monitoring Location: AMS2N1

Hour	4- October -24	10- October -24	16- October -24	22- October -24	28- October -24
1	37	39	38	38	32
2	39	31	33	34	33
3	42	33	38	38	35
4	44	37	37	37	30
5	39	33	32	28	33
6	35	28	38	29	31
7	37	31	37	32	30
8	34	32	36	33	35
9	31	35	36	37	33
10	35	36	37	36	30
11	30	36	38	37	36
12	33	38	35	38	28
13	32	35	39	39	32
14	37	34	35	34	33
15	33	35	37	36	34
16	38	25	33	28	31
17	40	33	34	35	33
18	35	34	37	35	33
19	37	32	36	30	31
20	34	35	33	36	36
21	30	33	38	36	32
22	32	25	34	34	33
23	36	27	35	25	34
24	35	26	36	27	31
Average:	36	33	36	34	32
24-hr TSP					
(µg/m³; with					
correlation(x)	48	45	49	46	44
Action Level:	179				
Limit Level:	260				

SGS	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po	Page	G-12
	Toi O	Ref#	EMA2403/03/42
	Monthly EM&A Report		01
		Date	Nov 24

## 2024 Ocotober 24-hour Monitoring Data

## Monitoring Location: AMS3N


Hour	4- October -24	10- October -24	16- October -24	22- October -24	28- October -24
1	24	30	32	32	30
2	31	28	27	26	31
3	28	27	27	27	28
4	30	23	26	25	31
5	26	29	29	29	33
6	26	29	31	30	29
7	25	27	26	21	26
8	22	25	28	21	33
9	30	32	31	20	28
10	35	27	25	23	32
11	30	25	26	24	33
12	33	27	27	26	26
13	31	26	24	23	31
14	28	34	33	32	30
15	28	30	32	30	27
16	32	32	38	35	34
17	20	24	33	30	28
18	20	23	23	23	26
19	30	26	23	24	30
20	33	25	25	23	31
21	31	22	27	26	30
22	25	30	24	23	28
23	27	28	29	29	30
24	31	28	28	27	32
Average:	28	27	28	26	30
24-hr TSP					
(µg/m³; with					
correlation(x)	38	37	38	36	41
Action Level:	158				
Limit Level:	260				

SGS	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po	Page	G-13
	Toi O	Ref#	EMA2403/03/42
	Monthly EM&A Report	Rev.	01
		Date	Nov 24


## 2024 Ocotober 24-hour Monitoring Data

## Monitoring Location: AMS4N


Hour	4- October -24	10- October -24	16- October -24	22- October -24	28- October -24
1	20	28	29	28	23
2	32	26	25	24	24
3	27	28	26	26	25
4	25	26	27	25	26
5	26	24	25	23	24
6	22	29	28	28	22
7	22	24	23	20	26
8	20	27	29	29	22
9	25	23	28	29	26
10	27	28	28	28	24
11	21	25	26	25	23
12	23	26	28	26	24
13	29	27	26	27	23
14	26	22	23	21	25
15	21	21	24	24	25
16	30	24	26	26	20
17	28	24	25	25	23
18	31	29	23	20	28
19	23	21	22	21	25
20	34	22	27	21	23
21	28	29	29	27	24
22	32	27	28	30	24
23	24	31	27	28	24
24	23	20	30	20	23
Average:	26	25	26	25	24
24-hr TSP					
(µg/m³; with					
correlation(x)	39	38	40	38	37
Action Level:	144		1	1	1
Limit Level:	260				




# AMS1N - 24-hour TSP monitoring

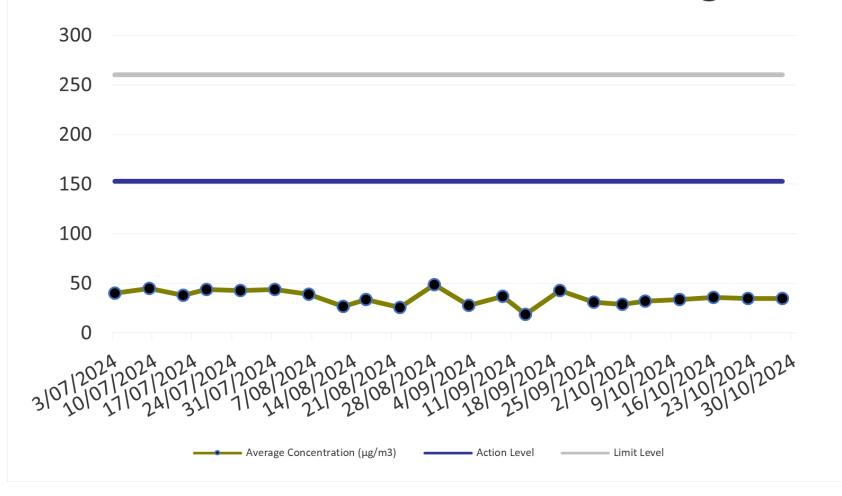


	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-15
SGS	EF-516/2016 - Port Shelter Sewerage, Stages - Sewerage works at Portor O	Ref#	EMA2403/03/42
	Monthly EM&A Report		01
	······································	Date	Nov 24

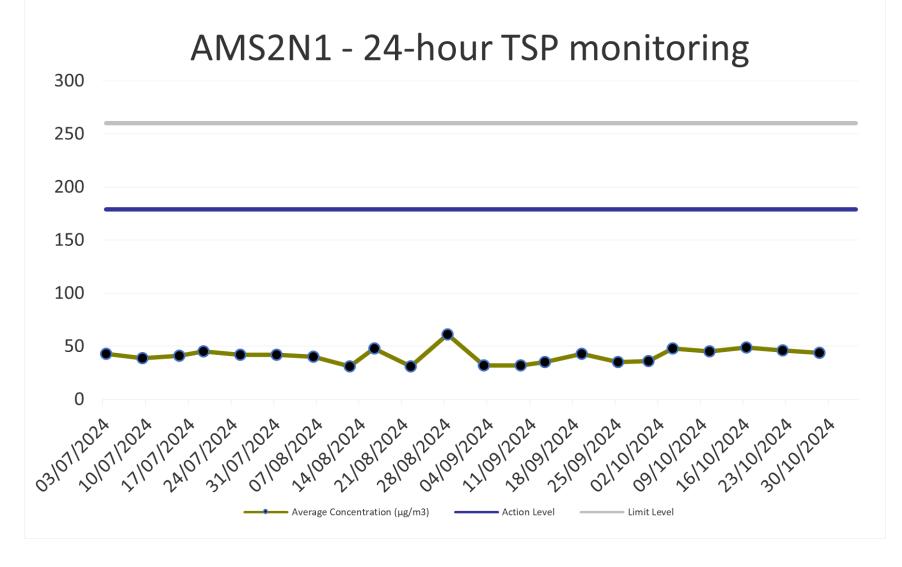




# AMS3N - 24-hour TSP monitoring

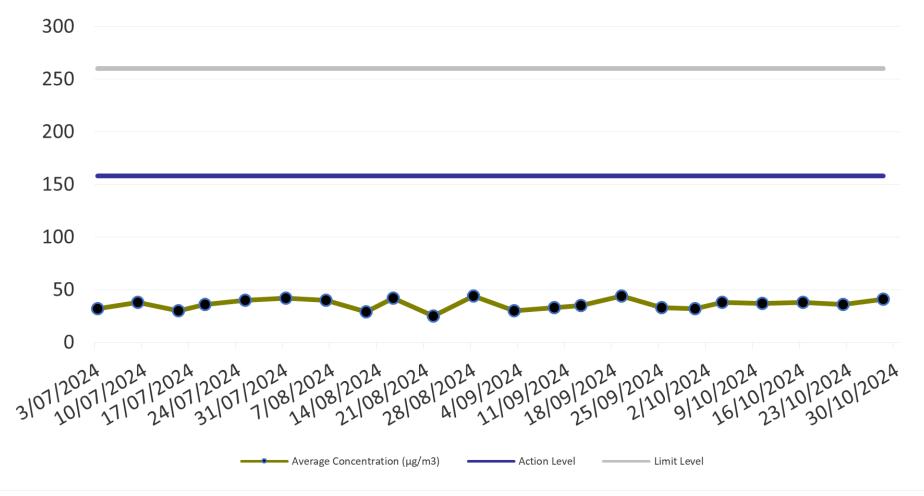

SGS	ED 516/2016 Dart Shelter Severage Stage? Severage Works of De Tei O	Page	G-17
	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Ref#	EMA2403/03/42
	Monthly EM&A Report	Rev.	01
	······································	Date	Nov 24

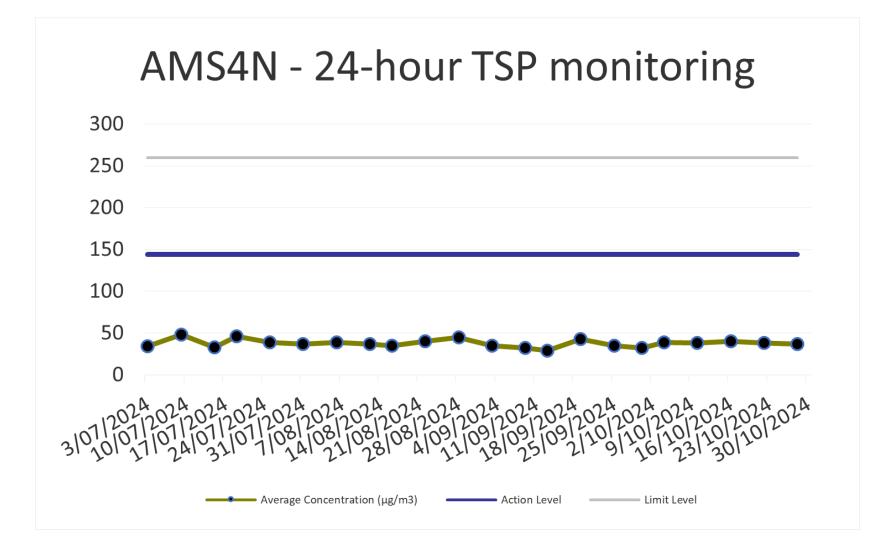



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage		H-1
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

## **APPENDIX H – EVENT AND ACTION PLAN**



## AIR QUALITY MONITORING

EVENT		ACTION						
EVENT	ET	IEC	ER	CONTRACTOR				
ACTION LEVEL								
Exceedance for one sample	<ol> <li>Repeat measurement to confirm findings;</li> <li>If exceedance is confirmed, inform the Contractor, IEC and ER;</li> <li>Identify source(s), investigate the causes of exceedance and propose remedial measures; and</li> <li>Increase monitoring frequency.</li> </ol>	<ol> <li>Check monitoring data submitted by the ET;</li> <li>Check Contractor's working method; and</li> <li>Discuss with ET, ER and Contractor on possible remedial measures</li> <li>Review and advise the ET and ER on the effectiveness of the proposed remedial measures.</li> </ol>	<ol> <li>Confirm receipt of notification of exceedance in writing.</li> </ol>	<ol> <li>Identify source(s), investigate the causes of exceedance and propose remedial measures;</li> <li>Implement remedial measures; and</li> <li>Amend working methods agreed with the ER as appropriate.</li> </ol>				
Exceedance for two or more consecutive samples	<ol> <li>Repeat measurements to confirm findings;</li> <li>If exceedance is confirmed, inform Contractor, IEC and ER;</li> <li>Identify source(s), investigate the causes of exceedance and propose remedial measures;</li> <li>Increase monitoring frequency to daily;</li> <li>Advise the Contractor and ER on the effectiveness of the proposed remedial measures;</li> <li>Discuss with IEC and Contractor on remedial actions required;</li> </ol>	<ol> <li>Check monitoring data submitted by the ET;</li> <li>Check Contractor's working method; and</li> <li>Discuss with ET, ER and Contractor on possible remedial measures;</li> <li>Review and advise the ET and ER on the effectiveness of the proposed remedial measures; and</li> <li>Supervise Implementation of remedial measures.</li> </ol>	<ol> <li>Confirm receipt of notification of exceedance in writing;</li> <li>In consultation with the ET and IEC agree with the Contractor on the remedial measures to be implemented; and</li> <li>Supervise implementation of remedial measures</li> </ol>	<ol> <li>Identify source(s) and investigate the causes of exceedance;</li> <li>Submit proposals for remedial measures to the ER, ET and IEC within three working days of notification for agreement;</li> <li>Implement the agreed proposals; and</li> <li>Amend proposal as appropriate.</li> </ol>				



H-3

01

Nov 24

EMA2403/03/42

EVENT		A	CTION	
EVENT	ET 7. If exceedance continues, arrange meeting with Contractor, IEC and ER to discuss the remedial measures to be taken; and 8. If exceedance stops, cease additional monitoring.	IEC	ER	CONTRACTOR
LIMIT LEVEL Exceedance for one sample	<ol> <li>Repeat measurement to confirm findings;</li> <li>If exceedance is confirmed, inform the Contractor, IEC, EPD and ER;</li> <li>Identify source(s), investigate the causes of exceedance and propose remedial;</li> <li>Increase monitoring frequency to daily; and</li> <li>Discuss with the ER, IEC and Contractor on the remedial measures and assess effectiveness.</li> </ol>	<ol> <li>Check monitoring data submitted by the ET;</li> <li>Check Contractor's working method;</li> <li>Discuss with the ET, ER and Contractor on possible remedial measures;</li> <li>Review and advise the ET and ER on the effectiveness of the proposed remedial measures; and</li> <li>Supervise implementation of remedial measures.</li> </ol>	<ol> <li>Confirm receipt of notification of exceedance in writing;</li> <li>Review and agree on the remedial measures proposed by the Contractor; and</li> <li>Ensure remedial measures properly implemented.</li> </ol>	<ol> <li>Identify source(s) and investigate the causes of exceedance;</li> <li>Take immediate action to avoid further exceedance;</li> <li>Submit proposals for remedial measures to ER, ET and IEC within three working days of notification for agreement;</li> <li>Implement the agreed proposals; and</li> <li>Amend proposal if appropriate.</li> </ol>
Exceedance for two or more consecutive samples	<ol> <li>Repeat measurement to confirm findings;</li> <li>If exceedance is confirmed, inform IEC, ER, Contractor and EPD;</li> <li>Identify source(s), investigate the causes of</li> </ol>	<ol> <li>Check monitoring data submitted by the ET;</li> <li>Discuss amongst ER, ET, and Contractor on the potential remedial actions;</li> </ol>	<ol> <li>Confirm receipt of notification of exceedance in writing;</li> <li>In consultation with the ET and IEC, agree with the Contractor on the remedial measures to be implemented;</li> </ol>	<ol> <li>Identify source(s) and investigate the causes of exceedance;</li> <li>Take immediate action to avoid further exceedance;</li> <li>Submit proposals for remedial measures to the</li> </ol>



Monthly EM&A Report

EVENT		Α	ACTION					
EVENT	<ul> <li>ET</li> <li>exceedance and propose remedial measures;</li> <li>Increase monitoring frequency to daily;</li> <li>Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented;</li> <li>Arrange meeting with IEC and ER to discuss the remedial actions to be taken;</li> <li>Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; and</li> <li>If exceedance stops, cease additional monitoring.</li> </ul>	A IEC 3. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; and 4. Supervise the implementation of remedial measures.	<ul> <li>ER</li> <li>Supervise the implementation of remedial measures; and</li> <li>If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.</li> </ul>	<ul> <li>CONTRACTOR</li> <li>ER, IEC and ET within three working days of notification for agreement;</li> <li>Implement the agreed proposals;</li> <li>Revise and resubmit proposals if problem still not under control; and</li> <li>Stop the relevant portion of works as determined by the ER until the exceedance is abated.</li> </ul>				

Note: ET – Environmental Team; ER – Engineer's Representative; IEC – Independent Environmental Checker



## NOISE IMPACT MONITORING

Event	Action					
	ET	IEC	ER	CONTRACTOR		
Action Level	1. Notify IEC, ER and Contractor of	1. Review the analysed results	1. Confirm receipt of notification of	1. Submit noise mitigation proposals to		
	exceedance;	submitted by the ET;	failure in writing;	ER with copy to ET and IEC;		
	2. Identify source	2. Review the proposed remedial	2. Notify Contractor;	Implement noise mitigation proposals.		
	3. Investigate the causes of	measures by the Contractor and advise	3. Require Contractor to propose			
	exceedance and propose remedial	the ER accordingly;	remedial measures for the analysed			
	measures;	3. Supervise the implementation of	noise problem;			
	4. Report the results of investigation to	remedial measures.	4. Ensure remedial measures are			
	the IEC, ER and Contractor;		properly implemented			
	5. Discuss with the IEC, ER and					
	Contractor and formulate remedial					
	measures;					
	6. Increase monitoring frequency to					
	check mitigation effectiveness					



Monthly EM&A Report

Event	Action			
	ET	IEC	ER	CONTRACTOR
Limit Level				
	1. Inform IEC, ER, EPD and Contractor;	1. Discuss amongst ER, ET, and	1. Confirm receipt of notification of failure in	1. Take immediate action to avoid further
	2. Identify source;	Contractor on the potential remedial	writing;	exceedance;
	3. Repeat measurements to confirm findings;	actions;	2. Notify Contractor;	2. Submit proposals for remedial actions to ER
	4. Increase monitoring frequency;	2. Review Contractor's remedial	3. Require Contractor to propose remedial	with copy to ET and IEC within 3 working days of
	5. Carry out analysis of Contractor's working	actions whenever necessary to	measures for the analyzed noise problem;	notification;
	procedures to determine possible mitigation to	assure their effectiveness and advise	4. Ensure remedial measures are properly	3. Implement the agreed proposals;
	be implemented;	the ER accordingly;	implemented;	4. Resubmit proposals if problem still not under
	6. Inform IEC, ER and EPD the causes and	3. Supervise the implementation of	5. If exceedance continues, investigate what	control;
	actions taken for the exceedances;	remedial measures.	portion of the work is responsible and instruct	5. Terminate the relevant portion of works as
	7. Assess effectiveness of Contractor's remedial		the Contractor to terminate that portion of	determined by the ER until the exceedance
	actions and keep IEC, EPD and ER informed		work until the exceedance ceases.	ceases.
	of the results;			
	8. If exceedance stops, cease additional			
	monitoring.			



## Water Quality Monitoring

Event	Action					
	ET	IEC	ER	CONTRACTOR		
Action Level being exceeded	1. Repeat in situ measurement on next day	1. Check monitoring data submitted by	1. Confirm receipt of notification of non-	1. Inform the ER and confirm notification of the		
by one sampling day	of exceedance to confirm findings;	ET and Contractor's working methods.	conpliance in writing;	non-compliance in writing;		
	2. Identify source(s) of impact;	2. Discuss with ET and Contractor on	2. Notify Contractor;	2. Rectify unacceptable practice;		
	3. Inform IEC, contractor and ER;	possible remedial actions.	3. Discuss with IEC on possible	3. Check all plant and equipment and consider		
	4. Check monitoring data, all plant,	3. Review the proposed mitigation	remedial actions;	changes of working methods;		
	equipment and Contractor's working	measures submitted by Contractor and	4. Make agreement on the mitigation	4. Submit proposal of mitigation measures to		
	methods.	advise the ER accordingly.	measures to be implemented.	ER within 3 working days of notification and		
	5. Discuss mitigation measures with IEC			discuss with ET, IEC and ER.		
	and Contractor.			5. Implement the agreed mitigation measures.		
Action Level being exceeded	1. Repeat measurement on next day of	1. Check monitoring data submitted by	1. Discuss with IEC on the proposed	1. Inform the ER and confirm notification of the		
by more than one consecutive	exceedance to confirm findings;	ET and Contractor's working method;	mitigation measures;	non-compliance in writing;		
sampling days	2. Identify source(s) of impact;	2. Discuss with ET and Contractor on	2. Make agreement on the mitigation	2. Rectify unacceptable practice;		
	3. Inform IEC, contractor and ER and EPD;	possible remedial actions.	measures to be implemented;	3. Check all plant and equipment and consider		
	4. Check monitoring data, all plant,	3. Review the proposed mitigation	3. Ensure mitigation measures are	changes of working methods;		
	equipment and Contractor's working	measures submitted by Contractor and	properly implemented by the	4. Submit proposal of mitigation measures to		
	methods.	advise the ER accordingly;	Contractor;	ER within 3 working days of notification and		
	5. Discuss mitigation measures with IEC	4. Supervise the implementation of	4. Assess the effectiveness of the	discuss with ET, IEC and ER.		
	and Contractor;	mitigation measures.	implemented mitigation measures.	5. Implement the agreed mitigation measures.		
	6. Ensure mitigation measures are					
	implemented;					
	7. Increase the monitoring frequency to					
	daily until no exceedance of Action level.					

SGS	ED 516/2016 Dort Sholtor Sowerage Stage? Sowerage Works at Do Toi O	Page	H-8
	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Ref#	EMA2403/03/42
	Monthly EM&A Report	Rev.	01
		Date	Nov 24

Event	Action					
	ET	IEC	ER	CONTRACTOR		
Limit Level being exceeded by	1. Repeat measurement on next day of	1. Check monitoring data submitted by	1. Confirm receipt of notification of non-	1. Inform the ER and confirm notification of the		
one sampling day	exceedance to confirm findings;	ET and Contractor's working method;	conpliance in writing;	non-compliance in writing;		
	2. Identify source(s) of impact;	2. Discuss with ET and Contractor on	2. Discuss with IEC, ET and Contractor	2. Rectify unacceptable practice;		
	3. Inform IEC, contractor and ER;	possible remedial actions.	on the proposed mitigation measures;	3. Check all plant and equipment and consider		
	4. Check monitoring data, all plant,	3. Review the proposed mitigation	3. Request Contractor to review the	changes of working methods;		
	equipment and Contractor's working	measures submitted by Contractor and	working methods.	4. Submit proposal of mitigation measures to		
	methods.	advise the ER accordingly.		ER within 3 working days of notification and		
	5. Discuss mitigation measures with IEC			discuss with ET, IEC and ER.		
	and Contractor.					


SGS	ED 516/2016 Dart Sheltar Sawaraga Stage? Sawaraga Warks at De Tei O	Page	H-8
	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Ref#	EMA2403/03/42
	Monthly EM&A Report	Rev.	01
		Date	Nov 24

Limit Level being exceeded by	1. Repeat measurement on next day of	1. Check monitoring data submitted by	1. Discuss with IEC, ET and Contractor	1. Inform the ER and confirm notification of the
more than one consecutive	exceedance to confirm findings;	ET and Contractor's working method;	on the proposed mitigation measures;	non-compliance in writing;
sampling days	2. Identify source(s) of impact;	2. Discuss with ET and Contractor on	2. Request Contractor to critically	2. Take immediate action to avoid further
sumpling days	3. Inform IEC, contractor and ER and	possible remedial actions.	review the working methods;	exceedance;
	EPD:	3. Review the Contractor's mitigation	3. Make agreement on the mitigation	3. Check all plant and equipment and consider
		ů –	с с	
	4. Check monitoring data, all plant,	measures whenever necessary to	measures to be implemented;	changes of working methods;
	equipment and Contractor's working	assure their effectiveness and advise	4. Ensure mitigation measures are	4. Submit proposal of mitigation measures to
	methods.	the ER accordingly;	properly implemented;	ER within 3 working days of notification and
	5. Discuss mitigation measures with IEC	4. Supervise the implementation of	5. Consider and instruct, if necessary,	discuss with ET, IEC and ER.
	and Contractor;	mitigation measures.	the Contractor to slow down or stop all	5. Implement the agreed mitigation measures;
	6. Ensure mitigation measures are		or part of the construction activities until	6. Resubmit proposals of mitigation measures
	implemented;		no exceedance of Limit Level.	if problem still not under control;
	7. Increase the monitoring frequency to			7. As directed by the Supervising Officer, to
	daily until no exceedance of Limit level for			slow down or stop all or part of the
	two consecutive days.			construction activities until no exceedance of
				Limit Level



## APPENDIX I - NOISE MONITORING EQUIPMENT CALIBRATION CERTIFICATES









T: +852 2695 8318 F: +852 2695 3944 E: eti@ets-testconsult.com W: www.ets-testconsult.com



Form Q/AS/C/02 Issue 1(1/4) [02/22]

### **Calibration Certificate**

Page

Certificate No. : CSA38446

: 1 of 2

#### Information Provided by Customer : ETS - Testconsult Limited

Customer Address

: 8/F., Block B, Veristrong Industrial Centre, 34 - 36 Au Pui Wan Street, Fotan, Shatin, Hong Kong

Procedure

Sampling

Date of Receipt

Relative Humidity

Calibration Location

#### Information of Unit-under-test (UUT)

Description	:	Sound Level Calibrator
Manufacturer	÷	RION
Туре	:	NC-73

Equipment I.D. : ET/EN/002/01 : 10196943 Serial No.

: CQS/002/A

: 15-Nov-2023

: (50±20) %

: As received

: Calibration Laboratory

Laboratory Information

## Lab. Ref. No. ; Q/CAL/23/9463/I Date of Calibration ; 23-Nov-2023

: 24-Nov-2023 Date of Issue

#### **Calibration Condition**

Ambient Temperature : (20 ± 3) °C : 30 minutes Stabilizing Time : (1000 ± 50) hPa Ambient Pressure

#### Reference equipment

- Multi-function sound calibrator, ET/2801/01
- Measuring Amplifier, ET/2702/01/01
- Signal generator, ET/2503/01
- Reference Oscilloscope, ET/2502/01

#### Calibration specification

- To perform the calibration of sound level calibrator.

#### Calibration result

- The results are detailed on the subsequent pages.

#### Remarks

- The calibration results apply to the particular unit-under-test only.
- The values given in this calibration certificate only to the values measureed at the time of test & any uncertainties quoted will not include allowance for the equipment long term drift, varifications with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement

Calibrated By :

Tony MA (Technician)

Approved By: CHAN Chi Wai

The results shown in this certificate are traceable to the International System of Units (SI) or recognised measurement standards. This report shall not be reproduced unless with prior written approval from this laboratory.





ets-testconsult.com



### **Calibration Certificate**

Certificate No. : CSA38446

Form Q/AS/C/02 Is

Page: 2 of 2

### Calibration Result:

1. Measured Sound Pressure Level:

Nominal Frequency	Nominal Output	Measured Output (dB)	Expanded	Coverage
(Hz)	Sound Pressure (dB)		Uncertatiny (dB)	Factor
1000	94.0	93,9	0.13	2.0

2. Actual Output Frequency:

,	Nominal Frequency (Hz)	Nominal Output Sound Pressure (dB)	Measured Output (Hz)	Expanded Uncertatiny (Hz)	Coverage Factor
	1000	94.0	980.763	0.057	2.0

Remark:

- The uncertainty quoted is based on 95 % confidence level.

- Measured output are mean of three measurements.

\*\*\*End of certificate\*\*\*





8/F Block B,

T: +852 2695 8318 F: +852 2695 3944 E: et@ets-testconsult.com W: www.ets-testconsult.com



Form Q/AS/C/01 Issue 1(1/7) (09/21)

3

### **Calibration Certificate**

Certificate No.	: CSA44621
Page	1 of

; CQS/001/A

: 25-Jun-2024

; (50 ± 20) %

: As received

: Calibration Laboratory

Information Provided by Customer

Customer Address

### : ETS - Testconsult Limited

8/F., Block B, Veristrong Industrial Centre, 34 - 36 Au Pui Wan Street, Fotan, Shatin, Hong Kong

Procedure

Sampling

Date of Receipt

Calibration Location

Relative Humidity

#### Information of Unit-under-test (UUT)

	Sound Level Meter	Microphone	Pre-amplifier	Sound Calibrator
Manufacturer	RION	RION	RION	N/A
Туре	NL-52	UC-59	NH-25	*
Equipment I.D. no.	ET/EN/003/17			
Serial No,	00264519	03558	64644	,
Adaptors used			•	-
Resolution	0.1 d8			

Laboratory Information Lab. Ref. No. Q/CAL/24/5138/I Date of Calibration 16-Jul-2024 Date of Issue 18-Jul-2024

#### **Calibration Condition**

Ambient Temperature : (20 ± 3) °C Stabilizing Time : 30 minutes : (1000 ± 50) hPa Ambient Pressure

#### Reference equipment

- Multi-function sound calibrator, ET/2801/01
- Signal generator, ET/2503/01

#### Calibration specification

To perform the calibration of linearity and frequency response by multi-function sound calibrator.

#### Calibration result

The results are detailed on the subsequent pages.

#### Remarks

- The calibration results apply to the particular unit-under-test only.
- The values given in this calibration certificate only to the values measureed at the time of test & any uncertainties quoted will not include allowance for the equipment long term drift, varifications with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement

Calibrated By :

Tommy TAM (Technician) Approved By: CHAN Chi Wai

The results shown in this certificate are traceable to the international System of Units (SI) or recognised measurement standards This report shall not be reproduced unless with prior written approval from this laboratory,





8/F Block B, Veristrong Industrial Centre, 34-35 Au Pui Wan Street, Fo Tan, Hong Kong

T: +852 2685 8318 F: +852 2695 3944 E: atl@ats-lestconsuit.com W: www.ets-lestconsuit.com



Calibration Certificate

#### Certificate No. : CSA44621

Page : 2 of 3

#### Calibration Result:

1 Reference Sound Pressure Level : (Unit in: dB)

Ra	nge / Mode		Reference Level	REF Frequency (kHz)	UUT Reading	Deviation	Expanded Uncertatiny	Coverage Factor
	Self-cal	-	94.0		93,9	-0.1	0.13	2.0
	Range	30 to 130	104.0	1 1	103.9	-0.1	0.13	2.0
Mode	Mode	Fast	114.0	1 1	113.9	-0.1	0.13	2.0
A-Weighting	Self-cal		94.0		\$3,8	-0.2	0.13	2.0
	Range	30 to 130	104.0	1 1	103.9	-0.1	0.13	2.0
	Mode	Slow	114.0		113.9	-0.1	0.13	2.0
Mode Fast	94.0		93.8	-0.2	0,13	2.0		
	Range	30 to 130	104.0	1	103.9	-0.1	0,15	2.0
	Mode	Fast	114.0		113.8	-0.2	0.13	2.0
C-Weighting	Self-cal		94,0		93.8	-0.2	0.13	2.0
	Range	30 to 130	104.0		103.9	-0.1	0.15	2.0
1	Mode	Slow	114.0	1 1	113.9	-0.1	0,13	2.0
	Self-cal		94.D		93.8	-0.2	0.13	2,0
1	Range	30 to 130	104.0	1 1	103.9	-0.1	0,13	2.0
	Mode	Fast	114.0		113,9	-0.1	0.13	2.0
Z-Weighting	Self-cal		94.0		93.8	-0.2	0.13	2.0
	Range	30 to 130	104.0	1 1	103.9	-0.1	0.13	2.0
	Mode	Slow	114.0	1	113.9	-0.1	0.13	2.0

Remark:

- The uncertainty quoted is based on 95 % confidence level.

- UUT reading are mean of three measurements.

- Deviation = UUT Reading - Reference Level







B/F Block B, Varistrang Industrial Centre, 34-35 Au Pul Wan Street, Fo Tan, Hong Kong

T: +852 2695 6318 F: +852 2695 3944 E: eti@ets-testconsuit.com W: www.ets-testconsuit.com



#### **Calibration Certificate**

Certificate No. : CSA44621

Page : 3 of 3

Calibration Result:

#### Acoustic Sensitivity and Frequency Response:

2 Frequency Response A-Weighting (Unit in: dB)

Range	Mode	Applied Level	Frequency (Hz)	Reference Level	UUT Reading	Deviation	Expanded Uncertainty	Coverage Factor
		31.5	54,6	32.2	-22.4	0.15	2.0	
			63	67.8	50.0	-17.8	0.13	2.0
		l t	125	77.9	65.5	-12.4	0.13	2,0
			250	85.4	78.1	-7.3	0.12	2.0
		500	90.8	87.8	-3.0	0.14	2.0	
30 to 130	Fast	94	1000 (Ref.)	94,0	93.8	-0.2	0.13	2.0
		l i	2000	95.1	95.0	-0.1	0.13	2.0
			4000	94.9	93.5	-1.4	0.13	2.0
			8000	92.9	89.6	-3,3	0.14	2.0
		12500	89.7	83,4	-6.3	0.14	2.0	
		-	16000	87.5	79.6	-8.0	0.14	2.0

#### 3 Frequency Response C-Weighting (Unit in: dB)

Range	Mode	Applied Level	Frequency (Hz)	Reference Level	UUT Reading	Deviation	Expanded Uncertainty	Coverage Factor
			31.5	91.0	67.6	-23.4	0.15	2.0
			63	93.2	76.4	-17.8	0.15	2.0
			125	93.8	81.6	-12.2	0.15	2.0
			250	\$4.0	86,8	-7.2	0.12	2.0
	l t	500	94.0	91.2	-2.8	0.12	2.0	
30 to 130	Fast	94	1000 (Ref.)	94.0	93.6	-0.2	0.13	2.0
1000000000			2000	93.7	93.6	-0.1	0.13	2.0
			4000	93.1	91.7	-1.4	0.13	2.0
		I 1	8000	91.0	87.7	-3,3	0.14	2.0
			12500	87.8	81.5	-6.3	0.14	2,0
			16000	85.6	77.6	-8.1	0.14	2.0

#### 4 Frequency Response Z-Weighting (Unit in: dB)

Range	Mode	Applied Level	Frequency (Hz)	Reference Lovel	UUT Reading	Deviation	Expanded Uncertainty	Coverage Factor	
			31.5	94.0	70.6	-23.4	0.14	2.0	
		1 1	63	94.0	76.3	-17.7	0,15	2,0	
			125	94.0	81.8	-12.2	0.15	2,0	
				250	94.0	88.8	-7.2	0.14	2.0
		st 94	500	94,0	91.1	-2.9	0.12	2.0	
30 to 130	Fast		1000 (Ref.)	94.0	93.8	-0.2	0.13	2.0	
22222	100000		2000	94.0	93.8	-0.2	0.13	2.0	
			4000	84.0	92,5	-1.5	0.13	2,0	
			8000	94.0	90,6	-3.4	0,14	2,0	
			12500	94.0	88,0	-6,0	0.14	2.0	
			16000	94.0	87.2	-6.8	0.14	2.0	

Remark:

Signal level at 1000 Hz is set as indication of reference sound pressure level.

- The uncertainty quoted is based on 95 % confidence level with coverage factor k=2.0.

- UUT reading are mean of three measurements;

- Deviation = UUT Reading - Reference Level

\*\*\*End of certificate\*\*\*





Date

T: +852 2696 8318 F: +852 2695 3944 E: eli@ets-testconsult.com W: www.els-testconsult.com Ww



Nov 24

Form Q/AS/C/01 Issue 1(1/7) [09/21]

### **Calibration Certificate**

Certificate No.	: (	CSA4	4105	
Page	÷	1	of	3

: CQS/001/A

: 4-Jun-2024

: (50 ± 20) %

; As received

: Calibration Laboratory

Information Provided by Customer

Customer Address

: ETS - TESTCONSULT LIMITED

8/F., Block B, Veristrong Industrial Centre, 34 - 36 Au Pul Wan Street, Fotan, Shatin, Hong Kong

Procedure

Sampling

Date of Receipt

Calibration Location

Relative Humidity

#### Information of Unit-under-test (UUT)

	Sound Level Meter	Microphone	Pre-amplifier	Sound Calibrator
Manufacturer	RION	RION	1	N/A
Туре	NL-52	UC-59	NH-25	
Equipment LD. no.	ET/EN/003/18	•	•	
Serial No.	00264520	09668	64646	
Adaptors used		e. 6	· · · ·	-
Resolution	0.1 dB	•		

#### Laboratory Information

Lab. Ref. No. ; Q/CAL/24/4583/I : 6-Jun-2024 Date of Calibration : 7-Jun-2024 Date of Issue

#### **Calibration Condition**

Ambient Temperature : (20 ± 3) °C Stabilizing Time : 30 minutes Ambient Pressure : (1000 ± 50) hPa Ambient Pressure

#### Reference equipment

- Multi-function sound calibrator, ET/2801/01
- Signal generator, ET/2503/01

#### Calibration specification

To perform the calibration of linearity and frequency response by multi-function sound calibrator.

#### Calibration result

- The results are detailed on the subsequent pages.

#### Remarks

- The calibration results apply to the particular unit-under-test only.
- The values given in this calibration certificate only to the values measureed at the time of test & any uncertainties quoted will not include allowance for the equipment long term drift, varifications with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement


Calibrated By :

Tommy TAM (Technician)

Approved By: CHAN Chi Wai

The results shown in this certificate are traceable to the international System of Units (SI) or recognised measurement standards. This report shall not be reproduced unlass with prior written approval from this laboratory.







T: +852 2695 8318 F: +852 2695 3944 E: otiĝets-testconsult.com W: www.ots-testconsult.com



**Calibration Certificate** 

Certificate No. : CSA44105

Page: 2 of 3

#### Calibration Result:

1 Reference Sound Pressure Level : (Unit in: dB)

Range / Mode			Reference Level	REF Frequency (kHz)	UUT Reading	Deviation	Expanded Uncertatiny	Coverage Factor
	Self-cal		94.0		94,1	0.1	0.13	2.0
	Range	30 to 130	104.0	1	104.1	0,1	0,13	2.0
Mode	Mode	Fast	114.0		114.1	0.1	0.13	2.0
A-Weighting	Self-cal		94.0		94,1	0.1	0.13	2.0
1	Range	30 to 130	104.0	1	104.1	0.1	0.13	2.0
-	Mode	Slow	114.0		114.1	0.1	0.13	2.0
-	Self-cal		94.0		94.1	0,1	0,13	2.0
	Range	30 to 130	104.0	1	104.1	0.1	0.13	2.0
C. Mariabella a	Mode	Fast	114.0		114.1	0,1	0.13	2.0
C-Weighting	Self-cal		94.0	1	94.1	0.1	0.13	2.0
	Range	30 to 130	104.0		104.1	0,1	0.13	2.0
	Mode	Slow	114.0		114.1	0.1	0.13	2.0
	Self-cal	-	94.0		94.1	0.1	0.13	2.0
	Range	30 to 130	104.0	1	104.1	0.1	0.13	2.0
The state of the s	Mode	Fast	114.0		114.1	0.1	0.13	2.0
Z-Weighting	Self-cal		94.0		94.1	0,1	0.13	2.0
	Range 30 to 130 104.0	1	104.1	0.1	0.13	2.0		
	Mode	Slow	114.0	1	114.1	0.1	0.13	2.0

Remark:

- The uncertainty quoted is based on 95 % confidence level.

- UUT reading are mean of three measurements.

- Deviation = UUT Reading - Reference Level





B/F Block B, Veristrong Industrial Centre 34-36 Au Pul Wan Street, Fe Tan, Hong Kong



**Calibration Certificate** 

Certificate No.	÷5	CSA44105		
Page	50	3 of 3		

Form GAS/CI01 Issue 1(3/7) [06(21]

Calibration Result:

Acoustic Sensitivity and Frequency Response:

2 Frequency Response A-Weighting (Unit in: d3)

Range	Mode	Applied Level	Frequency (Hz)	Reference Level	UUT Reading	Deviation	EC 61672-1-2002 class 1 Specification		
-	o 130 Fast 94		31.5	54.6	54.P	0,3	-39.4 +/- 2.0		
			63	67.8	06.0	0.2	-28.2 +/- 1.6		
			125	77.9	78.1	0.2	-18.1 1/- 1.5		
					250	85.4	85.5	0.1	-8.6 +/- 1.4
			500	90,8	90.9	0.1	-3.2 16 1.4		
30 to 130		94	1000 (Ref.)	94.0	94,1	0.1	0+/-1.1		
			2000	25.1	95.2	0.1	+1.2 +/- 1.6		
			4000	94.9	95,1	0.2	+1.0+/-1.0		
			8000	82.9	92.6	-0.3	+1.1 (+2.1 ; - 3.1)		
			12600	89.7	87,0	-2.7	-4.3 (+3.0 ; -6.0)		
			16000	87.5	82.0	-5.5	-8.8 (+3.5; -17.0)		

#### 3 Frequency Response C-Weighting : (Unit in: dB)

Range	Mode	Applied Level	Frequency (Hz)	Reference Level	UUT Reading	Deviation	IEC 61672-1:2002 class 1 Specification
-		31.5	91.0	91.1	0.1	-3.0 +/- 2.0	
			63	93.2	93,4	0.2	-0.8 +/- 1.5
			125	83.8	94.0	0.2	-0.2 +/- 1.5
			250	84.0	94.2	0.2	0.0 +/- 1.4
				500	94.0	94.1	0.1
30 to 120	Feat	Feet 04	1000 (Ref.)	84.0	94.1	0.1	0+/-1.1
			2000	93.7	93.8	0.1	-0.2 +/- 1.6
			4000	93.1	93.3	0.2	-0.8 +/- 1.8
			8000	91.0	90.B	-0.2	-3.0 (+2.1 : -3.1)
			12500	67.6	85.1	-2.7	-6.2 (+3.0 ; -6.0)
			16000	85.6	80.1	-5.5	-8.5 (+3.5 ; -17.0)

#### 4 Frequency Response Z-Weighting : (Unit in: dB)

Ranpe	Made	Applied Level	Frequency (Hz)	Reference Level	UUT Reading	Deviation	IEC 61672-1:2002 class 1 Specification
	1	31.5	94.0	94.0	0.0	0.0 +/- 2.0	
			63	94.0	94.2	0.2	0.0+/-1.5
			125	94.0	94.2	0.2	0.0 +/- 1.5
		Fast 94	250	94.0	94.2	0.2	0.0 +/- 1.4
			500	94.0	94,1	0.1	0.0 +/- 1.4
30 to 130	to 130 Fast		1000 (Ref.)	94.0	04.1	0.1	0+/- 1.1
1000000			2000	94.0	94.0	0.0	0.0 +/- 1.6
			4000	94.0	94.0	0.0	0.0 +/- 1.8
24			8000	94.0	93.6	-0.4	0.0 (+2.1 ; -3.1)
			12500	94.0	91.6	-2.4	0.0 (+3.0 ; -8.0)
			16000	94.0	88.7	-43	0.0 (+3.5 ; -17.0)

#### Expanded upcartainty of my

	Range (Hz)	(dB)	Range (Hz)	(dB)
	31.5	0.20	2000	0.13
	83	0.15	4000	0.13
	125	0.13	8000	0.14
94 dB	250	0.14	12500	0.14
	500	0.12	16000	0.14
	1000	0.13		

Remark:

- Signal level at 1000 Hz is set as indication of reference sound pressure level

IEC 61672 class 1 - The uncertainty quoted is based on 95 % confidence lavel with coverage factor k=2.0.

- UUT reading are mean of three measurements

- Manufacturer apecification:

- Deviation = UUT Reading - Reference Lavel

\*\*\*End of certificate\*\*\*



And a	東業德勤測試顧問有限公司
1	ETS-TESTCONSULT LTD.

	Calibration record of Anemometer							
Equipment Ref. N	o. :ET/EN/0	001/05 Manu	facturer :	AZ Instrument				
Model No.	:AZ 89	908 Serial	No.	1064869				
Date of Check	:27-Oct-	-2023 Due [	Date :	26-Oct-2024				
Method								
<ul> <li>2 A fan with vario</li> <li>3 Adjust the spee</li> <li>4 Ose the reference</li> <li>5 Record the indi</li> <li>6 Apply the corre</li> </ul>	us speed control had ed and direction of the cated value of both ar cted value in the refer	ength about 1m was us set in on end of the pip fan to achieve the targ me unit unitier test to d nemometer rence anemometer and Id not over ±5% of the	pe get wind speeds neck the wind speed in I calculate the correcte					
Reference Ane	mometer							
Equipment Ref. N	o. :ET/121	15/01 Calib	ration Due Date :	15-Aug-2024				
Deeulte								
	Reference Ane	emometer (m/s)	Unit Under	r Test (m/s)				
Applied Range (m/s)	Reference Ane Indicated Value	emometer (m/s) Corrected Value	Unit Under Indicated Value	r Test (m/s) Corrected Value				
Applied Range								
Applied Range (m/s)	Indicated Value	Corrected Value	Indicated Value	Corrected Value				
Applied Range (m/s) 0	Indicated Value 0.00	Corrected Value 0.00	Indicated Value 0.0	Corrected Value 0.0				
Applied Range (m/s) 0 2 - 3	Indicated Value 0.00 2.38	Corrected Value 0.00 2.43 5.68 10.3	Indicated Value 0.0 2.1	Corrected Value 0.0 +0.3 -0.5 -0.4				
(m/s) 0 2 - 3 4 - 6 9 - 11 14 - 16	Indicated Value 0.00 2.38 5.74 9.7 15.3	Corrected Value 0.00 2.43 5.68 10.3 15.1	Indicated Value 0.0 2.1 6.2 10.7 15.4	Corrected Value 0.0 +0.3 -0.5 -0.4 -0.3				
Applied Range (m/s) 0 2 - 3 4 - 6 9 - 11	Indicated Value 0.00 2.38 5.74 9.7	Corrected Value 0.00 2.43 5.68 10.3	Indicated Value 0.0 2.1 6.2 10.7	Corrected Value 0.0 +0.3 -0.5 -0.4				
Applied Range (m/s) 0 2 - 3 4 - 6 9 - 11 14 - 16	Indicated Value 0.00 2.38 5.74 9.7 15.3 19.4 iteria	Corrected Value 0.00 2.43 5.68 10.3 15.1	Indicated Value 0.0 2.1 6.2 10.7 15.4	Corrected Value 0.0 +0.3 -0.5 -0.4 -0.3				
Applied Range (m/s) 0 2 - 3 4 - 6 9 - 11 14 - 16 18 - 20 Acceptance Cri Correction value s	Indicated Value           0.00           2.38           5.74           9.7           15.3           19.4           iteria           should < ±5% FS	Corrected Value 0.00 2.43 5.68 10.3 15.1 19.7 s not-comply * with t	Indicated Value 0.0 2.1 6.2 10.7 15.4 19.3	Corrected Value 0.0 +0.3 -0.5 -0.4 -0.3 +0.4				



#### 来樂德勤測試顧問有限公司 ETS-TESTCONSULT LTD.

Calibration record of Anemometer						
Equipment Ref. No	. : ET/EN/0	01/05 Manu	facturer	AZ Instrument		
Model No.	: AZ 89	08 Seria	No. :	1064869		
Date of Check	:25-Oct-2	2024 Due	Date :	24-Oct-2025		
Method						
2 A fan with variou 3 Adjust the speed 4 Adjust the speed 5 Record the indic 6 Apply the correct	ated value of both an	tet in on end of the pi fan to achieve the tar enometer ence anemometer an	pe get wind speeds neuk une wind speed t d calculate the correct			
Reference Anen	nometer					
Equipment Ref. No	). : ET/121	5/01 Calib	ration Due Date :	2-Sep-2026		
Ambient Temperat <b>Results</b>	ure :26.0	) Rela	ive Humidity :	45%		
Applied Range	Reference Ane	mometer (m/s)	Unit Unde	er Test (m/s)		
(m/s)	Indicated Value	Corrected Value	Indicated Value	Corrected Value		
0	0.00	0.00	0.0	0.0		
2-3	2.59	2.65	2.4	+0.3		
4-6	5.68	5.54	5.9	-0.4		
9-11	9.4	9.8	10.1	-0.3		
14 - 16	14.9	15.4	15.2	+0.2		
18 - 20	18.6	18.8	19.3	-0.5		
Acceptance Crit						
	ble * / unacceptabl		the specified requir	ements and is		
Checked by	: _ Tole	<b>)</b>	Approved by :	6		



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		J-1
		EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

# APPENDIX J - NOISE IMPACT MONITORING RESULT

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		J-2
666			EMA2403/03/42
<u> </u>	Monthly EM&A Report	Rev.	01
		Date	Nov 24

2024 October Noise Monitoring Data

Monitoring Location: NMS1N

Date	Noise Monitoring (30min)							
Dale	Weather	Start Time	Leq dB(A)	L10 dB(A)	L90 dB(A)			
10- October -24	Sunny	10:20	64.8	66.9	59.6			
16- October -24	Sunny	10:05	62.4	65.3	55.4			
22- October -24	Sunny	10:30	42.0	44.2	38.7			
28- October -24	Sunny	13:06	41.3	45.3	39.3			
Average		60.8						
Action Level:	When one valid documented complaint is received							
Limit Level:			75.0 dB(A)					

SGS	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		J-3
			EMA2403/03/42
	Monthly EM&A Report		01
		Date	Nov 24

2024 October Noise Monitoring Data

Monitoring Location: NMS2N1

Date	Noise Monitoring (30min)							
Dale	Weather	Start Time	Leq dB(A)	L10 dB(A)	L90 dB(A)			
10- October -24	Sunny	10:53	49.0	51.1	46.3			
16- October -24	Sunny	10:40	48.7	51.6	45.8			
22- October -24	Sunny	13:05	54.0	56.8	46.8			
28- October -24	Sunny	10:58	53.4	56.2	45.5			
Average			51.9		·			
Action Level:	When one valid documented complaint is received							
Limit Level:			75.0 dB(A)					

	ED 540/2040 Dart Chalder Courseans Stars 2 Courseans Wester at Da Tai O	Page	J-4
CCC	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		EMA2403/03/42
<u> </u>	Monthly EM&A Report		01
I		Date	Nov 24

#### 2024 October Noise Monitoring Data

#### Monitoring Location: NMS3N

Dete	Noise Monitoring (30min)							
Date	Weather	Start Time	Leq dB(A)	L10 dB(A)	L90 dB(A)			
10- October -24	Sunny	11:28	53.7	54.3	48.6			
16- October -24	Sunny	11:20	54.4	55.2	48.9			
22- October -24	Sunny	13:40	58.3	60.9	49.2			
28- October -24	Sunny	13:41	58.8	63.2	51.5			
Average			56.9		·			
Action Level:	When one valid documented complaint is received							
Limit Level:			75.0 dB(A)					


	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	J-5
CCC	F-510/2010 - Fort Sheller Sewerage, Stages - Sewerage Works at F0 1010		EMA2403/03/42
<b>JUJ</b>	Monthly EM&A Report		01
			Nov 24

2024 October Noise Monitoring Data

Monitoring Location: NMS4N


Date	Noise Monitoring (30min)							
Date	Weather	Start Time	Leq dB(A)	L10 dB(A)	L90 dB(A)			
10- October -24	Sunny	13:06	51.2	51.9	48.2			
16- October -24	Sunny	13:05	49.9	52.2	46.6			
22- October -24	Sunny	14:15	47.0	49.0	44.8			
28- October -24	Sunny	14:15	47.0	49.1	45.0			
Average		49.1						
Action Level:		When one valid documented complaint is received						
Limit Level:			75.0 dB(A)					

	ED 546/2046 Dart Chalter Courseans Stars 2 Courseans Wester at Da Tai O	Page	J-6
666	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		EMA2403/03/42
<u> </u>	Monthly EM&A Report		01
			Nov 24

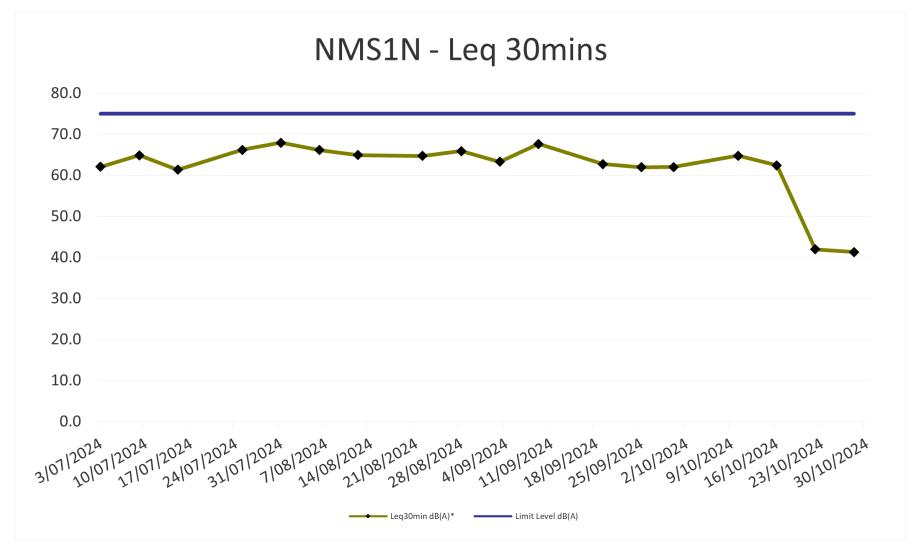


J-6

	ED 540/2040 Dart Chalter Courseans Stars 2 Courseans Wester at Da Tai O	Page	J-7
CCC	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		EMA2403/03/42
<u> </u>	Monthly EM&A Report	Rev.	01
	Monthly EM&A Report		Nov 24

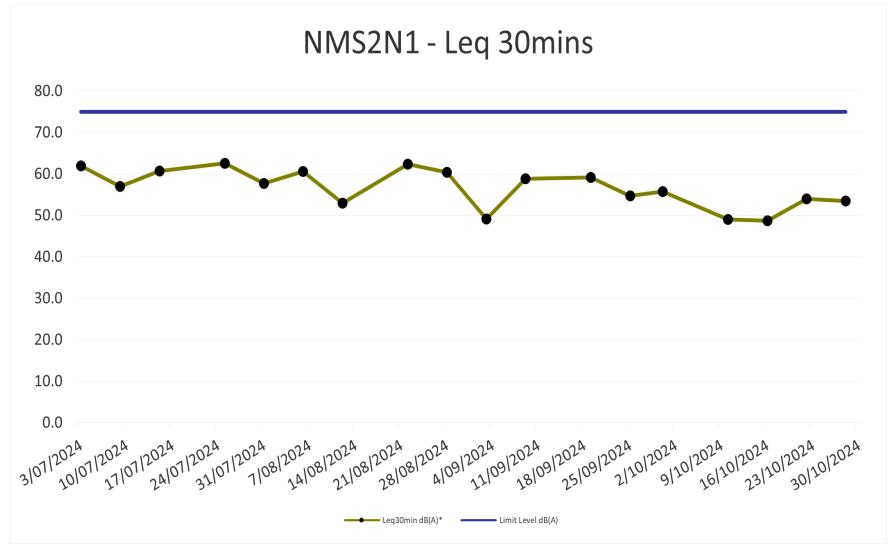

#### J-7


	ED 516/2016 Dart Shaltar Sawarana Stana? Sawarana Warka at Da Tai O	Page	J-8
CCC	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		EMA2403/03/42
<b>JUJ</b>	Monthly EM&A Report	Rev.	01
	Monthly EM&A Report		Nov 24

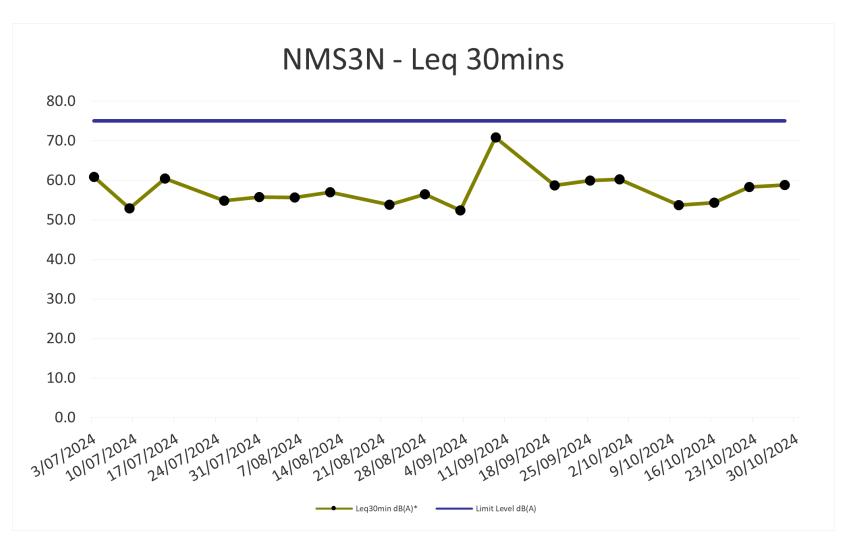

J-8

	ED 516/2016 Dart Shaltar Sawarana Stana? Sawarana Warka at Da Tai O	Page	J-9
CCC	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		EMA2403/03/42
<b>JUJ</b>	Monthly EM&A Report	Rev.	01
	Monthly EM&A Report		Nov 24



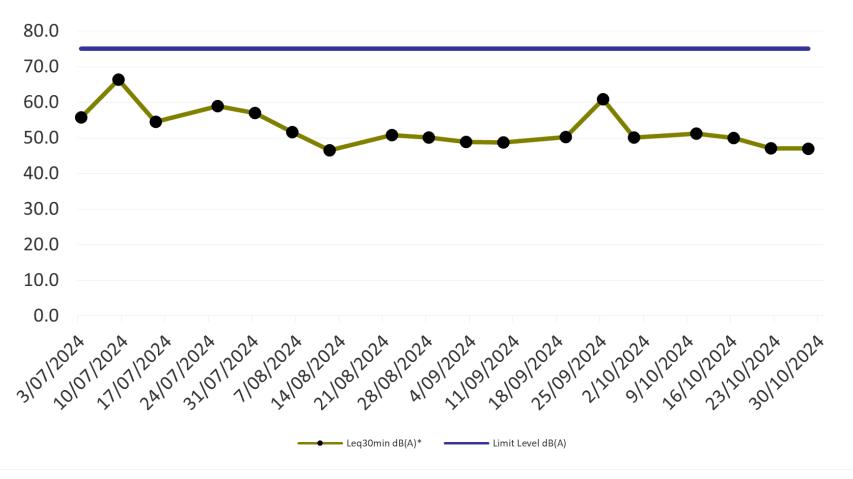



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	K-1
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

## APPENDIX K – WATER QUALITY MONITORING SCHEDULE



# October 2024

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		1 National Day	2	3	4	5
			Malan		I	
			Water Quality Monitoring		Water Quality Monitoring	
			Ebb: 10:15 - 13:45		Ebb: 11:15 - 14:4	_
			Flood: 16:15 - 19:45		Flood: 16:45 - 20:1	
6	7	8	9	10	11 Chung Yeung Festiva	
	Water		Water			Water
	Quality Monitoring		Quality Monitoring			Quality Monitoring
	Ebb: 12:45 - 16:15	5	Ebb: 02:45 - 06:15			Ebb: 06:15 - 09:45
	Flood: 07:15 - 10:45	5	Flood: 14:15 - 17:45			Flood: 14:45 - 18:15
13	14	15	16	17	18	19
	Water	Ī	Water		Water	
	Quality Monitoring		Quality Monitoring		Quality Monitoring	
	Ebb: 08:15 - 11:45	5	Ebb: 09:15 - 12:45		Ebb: 10:45 - 14:1	5
	Flood: 15:15 - 18:45		Flood: 15:15 - 18:45		Flood: 16:15 - 19:4	
20	21	22	23	24	25	26
	Water		Water		Water	
	Quality Monitoring Ebb: 12:45 - 16:15	_	Quality Monitoring		Quality Monitoring	-
	Ebb: 12:45 - 16:15 Flood: 08:15 - 11:45		Ebb: 03:15 - 06:45 Flood: 14:15 - 17:45		Ebb: 5:15 - 8:4 Flood: 14:15 - 17:4	
27	28	29	30	31	1000: 14:15 - 17:4	
21	20	29	50	51		
	Water		Water		I I	
	Quality Monitoring		Quality Monitoring			
	Ebb: 08:15 - 11:45	5	Ebb: 09:15 - 12:45			
	Flood: 14:15 - 17:45		Flood: 14:45 - 18:15			
		Notes				tes by Vertex42.com ex42.com/calendars/
		1 Water sampling will be conduct	ed +/- 1.75 hour of the predicted tides	time		2 LLC. Free to print.
		2. Predicted tides time were refere	-	anno.	G EVEL VOICAN	c cost too to print
		(Tai Miu Wan Station).	in the second seco			
		· · · · · ·			2024 Calendars	2025 Calendars



# November 2024

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
					1	2
					Water	
					Quality Monitoring	
					Ebb: 10:15 - 13:4	5
					Flood: 15:15 - 18:49	
3	4	5	6	7	8	9
	Water	1	Water	1	Water	1
	Quality Monitoring		Quality Monitoring		Quality Monitoring	
	Ebb: 12:15 - 15:4		Ebb: 13:15 - 16:45		Ebb: 03:15 - 06:49	
	Flood: 16:15 - 19:4		Flood: 17:15 - 20:45		Flood: 14:15 - 17:4	
10	11	12	13	14	15	16
	Water	[	Water	1	Water	I
	Quality Monitoring		Quality Monitoring		Quality Monitoring	
	Ebb: 06:15 - 09:4		Ebb: 08:15 - 11:45		Ebb: 09:45 - 13:15	
	Flood: 13:15 - 16:4		Flood: 14:15 - 17:45		Flood: 14:45 - 18:15	
17	18	19	20	21	22	23
			ļ		ļ	
	Water		Water		Water	
	Quality Monitoring Ebb: 11:45 - 15:1!	-	Quality Monitoring Ebb: 12:45 - 16:15		Quality Monitoring Ebb: 3:15 - 6:4!	-
	Ebb: 11:45 - 15:15 Flood: 16:15 - 19:45		Ebb: 12:45 - 16:15 Flood: 17:15 - 20:45		Ebb: 3:15 - 6:4 Flood: 13:15 - 16:4	
24	25	26	27	28	29	30
24	20	20	£1	20	23	00
	Water		Water		Water	
	Quality Monitoring		Quality Monitoring		Quality Monitoring	
	Ebb: 06:15 - 09:4	5	Ebb: 08:15 - 11:45		Ebb: 09:15 - 12:49	5
	Flood: 13:15 - 16:4	5	Flood: 13:45 - 17:15		Flood: 14:15 - 17:49	5
		Notes			Calendar Templat	es by Vertex42.com
					https://www.verte	ex42.com/calendars/
		1. Water sampling will be conducte	ed +/- 1.75 hour of the predicted tide:	s time.	© 2022 Vertex42	LLC. Free to print.
		2. Predicted tides time were refere	nce from Hong Kong Observatory			
		(Tai Miu Wan Station).				
		<u> </u>			2024 Calendars	2025 Calendars



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-1
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

# **APPENDIX L – WATER QUALITY MONITORING RESULTS**



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-2
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	Mode				Water									In-situ Me	asurement						Lab	ooratory Anal	lysis						
Date	Tidal Me	Monitoring Location	Weather	Time	Depth (m)	Monitoring Level	Monitoring Level (m)	Replicate	р	Н	Salinity	y (ppt)	Tempera	ature (°C)	DO Satu	ation (%)	DO (	mg/L)	Turbidi	ty (NTU)		ended solids o 105 (°C), mg/							
	F								Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value		Ave.						
/2/2024		WMS-1N				S		1	8.40	0.40	35.30	05.00	28.7	00.7	112.4		7.88	7.00	1.09	4.00	6.63	6.63	0.00						
		WMS-1N				S	1	2	8.40	8.40	35.30	35.30	28.7	28.7	112.3	112.4	7.89	7.89	1.09	1.09	6.68	6.68	6.66						
	Ebb	WMS-1N		40.00	-	М		1	8.40	0.40	35.44	25.44	28.7	00.7	109.6	400.7	7.80	7.04	1.09	4.00	5.48	5.48	5 50						
	Mid-Ebb	WMS-1N	SUNNY	12:00	7	М	3	2	8.40	8.40	35.44	35.44	28.7	28.7	109.7	109.7	7.81	7.81	1.09	1.09	5.52	5.52	5.50						
		WMS-1N				В	6	1	8.40	8.40	35.60	35.60	28.5	28.5	107.8	107.9	7.70	7.71	1.05	1.06	7.61	7.61	7.62						
		WMS-1N				В	0	2	8.40	0.40	35.60	35.60	28.5	26.5	107.9	107.9	7.71	7.71	1.06	1.06	7.63	7.63	7.02						
		WMS-2N				S	1	1	8.42	8.42	35.52	35.52	28.7	28.7	108.3	108.3	7.74	7.75	0.80	0.81	7.04	7.04	7.02						
		WMS-2N				S		2	8.42	0.42	35.52	35.52	28.7	20.7	108.2	106.5	7.75	1.15	0.81	0.81	7.02	7.02	7.03						
	Ebb	WMS-2N	CLININIV/	44.45		М	NA	1	NA	NIA	NA	NIA	NA	NIA	NA	NIA	NA	NA	NA	NA	NA	NA	NIA						
	Mid-Ebb	WMS-2N	SUNNY	11:45	4	М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA						
		WMS-2N				В		1	8.42	0.40	35.60	25.00	28.7	00.7	105.1	405.0	7.65	7.66	0.40	0.40	6.69	6.69	0.70						
		WMS-2N				В	3	2	8.42	8.42	35.60	35.60	28.7	28.7	105.2	105.2	7.66	7.66	0.40	0.40	6.70	6.70	6.70						
		WMS3				S	NA	1	NA	NIA	NA	NIA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA						
		WMS3				S	NA	2	NA	NA	NA	NA	NA	NA	NA	INA	NA	NA	NA	INA	NA	NA	INA						
	Mid-Ebb	WMS3	CLININIV/	11.15	0.7	М	1.5	1	8.46	8.46	35.54	35.54	28.7	28.7	109.0	109.0	7.77	7.78	0.32	0.32	5.23	5.23	5.05						
	Mid-	WMS3	SUNNY	11:15	2.7	М	1.5	2	8.46	0.40	35.54	35.54	28.7	20.7	108.9	109.0	7.78	1.10	0.32	0.32	5.26	5.26	5.25						
		WMS3				В	NA	1	NA	NA	NA	NA	NA	NIA	NA	NA	NA	NA	NA	NA	NA	NA	NA						
		WMS3				В	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA						
		WMS4						-	-	-		S	1	1	8.45	8.45	35.81	35.81	28.9	28.9	110.8	110.9	7.85	7.85	0.27	0.27	4.86	4.86	4.07
		WMS4				S		2	8.45	8.45	35.81	35.81	28.9	28.9	110.9	110.9	7.84	7.85	0.27	0.27	4.88	4.88	4.87						
	Ebb	WMS4		10.20		М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA						
	Mid-Ebb	WMS4	SUNNY	10:30	3.6	М	NA	2	NA	NA NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA						
		WMS4				В	3	1	8.45	8.45	35.85	35.85	28.9	28.9	108.3	108.3	7.77	7 77	0.37	0.27	3.78	3.78	2.01						
		WMS4				В	3	2	8.45	0.40	35.85	33.65	28.9	20.9	108.2	106.5	7.76	7.77	0.37	0.37	3.83	3.83	3.81						
		WMS5				S	1	1	8.47	0.47	35.95	25.05	29.1	20.1	109.0	109.0	7.78	7.79	0.52	0.52	7.42	7.42	7.44						
		WMS5				S	1	2	8.47	8.47	35.95	35.95	29.1	29.1	108.9	109.0	7.79	1.19	0.52	0.52	7.39	7.39	7.41						
	Mid-Ebb	WMS5	SUNNY	10:45	4.5	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA						
	Mid	WMS5	SUNNT	10.45	4.5	М		2	NA		NA	INA	NA		NA	INA	NA		NA		NA	NA							
		WMS5				В	4	1	8.48	8.48	35.93	35.93	29.1	29.1	105.9	106.0	7.70	7.70	0.47	0.47	6.98	6.98	7.01						
		WMS5				В	4	2	8.48	0.40	35.93	55.55	29.1	23.1	106.0	100.0	7.69	1.10	0.47	0.47	7.04	7.04	7.01						
		WMS6				S	1	1	8.47	8.47	35.99	35.99	29.1	29.1	106.3	106.3	7.70	7.71	0.54	0.55	5.68	5.68	5.66						
		WMS6				S	1	2	8.47	0.47	35.99	55.55	29.1	23.1	106.2	100.5	7.71	1.11	0.55	0.55	5.64	5.64	5.00						
	Mid-Ebb	WMS6	SUNNY	11:00	4.5	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA						
	Mid-	WMS6	JUNNT	11.00	4.0	М		2	NA		NA		NA		NA	IN/A	NA	11/1	NA		NA	NA							
		WMS6				В	4	1	8.48	8.48	35.97	35.97	29.1	29.1	104.6	104.6	7.65	7.66	0.50	0.50	4.75	4.75	4.77						
		WMS6				В	4	2	8.48	0.40	35.97	55.87	29.1	23.1	104.5	104.0	7.66	1.00	0.49	0.50	4.78	4.78	4.77						
Γ	Mid - Ebb	12	SUNNY	10:00	14	S	1	1	8.47	8.47	36.09	36.09	29.2	29.2	115.4	115.5	7.93	7.93	0.60	0.60	8.56	8.56	8.57						



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-3
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	12				s		2	8.47		36.09		29.2		115.5		7.92		0.59	l	8.57	8.57	
	12				М		1	8.45		36.01		29.1		110.2		7.80		0.57		10.98	10.98	
	12				м	7	2	8.45	8.45	36.01	36.01	29.1	29.1	110.3	110.3	7.81	7.81	0.56	0.57	10.92	10.92	10.95
	12				В		1	8.43		36.22		29.3		108.8		7.73		0.37		9.23	9.23	
	12				В	13	2	8.43	8.43	36.22	36.22	29.3	29.3	108.7	108.8	7.74	7.74	0.38	0.38	9.21	9.21	9.22
	C2				S		1	8.42		35.58		28.7		108.0		7.74		0.79		12.59	12.59	
	C2				S	1	2	8.42	8.42	35.58	35.58	28.7	28.7	108.1	108.1	7.75	7.75	0.78	0.79	12.66	12.66	12.63
qq	C2				М		1	NA		NA		NA		NA		NA		NA		NA	NA	
Mid-Ebb	C2	SUNNY	11:30	3.9	М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
2	C2				В		1	8.42		35.67		28.7		104.9		7.65		0.41		12.73	12.73	
	C2				В	3	2	8.42	8.42	35.65	35.66	28.7	28.7	105.0	105.0	7.64	7.65	0.42	0.42	12.72	12.72	12.73
	C3				S		1	8.45		35.98		29.1		111.9		7.86		0.53		9.98	9.98	
	C3				S	1	2	8.45	8.45	35.98	35.98	29.1	29.1	112.0	112.0	7.87	7.87	0.53	0.53	10.03	10.03	10.01
qq	C3				М		1	8.44		35.98		29.1		109.7		7.77		0.54		11.02	11.02	
Mid-Ebb	C3	SUNNY	10:15	13	М	6	2	8.44	8.44	35.98	35.98	29.1	29.1	109.8	109.8	7.78	7.78	0.54	0.54	11.05	11.05	11.04
2	C3				В		1	8.42		36.12		29.3		107.9		7.70		0.33		11.26	11.26	
	C3				В	12	2	8.42	8.42	36.12	36.12	29.3	29.3	107.8	107.9	7.71	7.71	0.33	0.33	11.22	11.22	11.24
	WMS-1N				S		1	8.34		35.20		28.8		110.8		7.83		1.08		4.86	4.86	
	WMS-1N				S	1	2	8.34	8.34	35.18	35.19	28.8	28.8	110.9	110.9	7.84	7.84	1.09	1.09	4.89	4.89	4.88
Mid-Flood	WMS-1N				М		1	8.34		35.33		28.8		108.0		7.75		1.07		5.02	5.02	
Пd-F	WMS-1N	SUNNY	15:45	7.4	М	3	2	8.34	8.34	35.33	35.33	28.8	28.8	108.1	108.1	7.76	7.76	1.08	1.08	5.10	5.10	5.06
≥	WMS-1N				В		1	8.34		35.52		28.6		106.2		7.65		1.07		7.36	7.36	
	WMS-1N				В	6	2	8.34	8.34	35.50	35.51	28.6	28.6	106.3	106.3	7.66	7.66	1.06	1.07	7.33	7.33	7.35
	WMS-2N				S		1	8.36		35.40		28.8		109.2		7.77		0.79		6.24	6.24	
	WMS-2N				S	1	2	8.36	8.36	35.40	35.40	28.8	28.8	109.1	109.2	7.78	7.78	0.78	0.79	6.25	6.25	6.25
lood	WMS-2N	<b>.</b>			М		1	NA		NA		NA		NA		NA		NA		NA	NA	
Mid-Flood	WMS-2N	SUNNY	15:30	4.2	М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
2	WMS-2N				В		1	8.36	0.00	35.49	05.40	28.8	00.0	106.1	400.4	7.68	7.00	0.39	0.00	5.76	5.76	5.74
	WMS-2N				В	3	2	8.36	8.36	35.49	35.49	28.8	28.8	106.0	106.1	7.69	7.69	0.33	0.36	5.71	5.71	5.74
	WMS3				S	NIA	1	NA	NIA	NA	NIA	NA	NIA	NA	NIA	NA	NIA	NA	NIA	NA	NA	NIA
-	WMS3				S	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	WMS3	CLININIX	15.15	2	М	1.5	1	8.40	8.40	35.43	35.44	28.8	28.8	107.3	107.4	7.72	7.73	0.35	0.36	6.03	6.03	6.03
Mid-Flood	WMS3	SUNNY	15:15	3	М	1.5	2	8.40	0.40	35.44	55.44	28.8	20.0	107.4	107.4	7.73	1.15	0.36	0.30	6.03	6.03	0.03
2	WMS3				В	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	WMS3				В	IN/A	2	NA	NA	NA	INA	NA	INA	NA	INA	NA	INA	NA	INA	NA	NA	INA
	WMS4				S	1	1	8.39	8.39	35.70	35.70	29.0	29.0	112.0	112.1	7.88	7.88	0.30	0.29	9.96	9.96	9.93
7	WMS4				S	1	2	8.39	0.59	35.70	55.70	29.0	29.0	112.1	112.1	7.87	7.00	0.28	0.29	9.90	9.90	9.95
	WMS4	SUNNY	14:30	4	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
Mid-Flood	WMS4	CONNT	14.50	-	М		2	NA		NA	DIA .	NA		NA	DIA .	NA	na	NA	11/1	NA	NA	
-	WMS4				В	3	1	8.39	8.39	35.74	35.74	29.0	29.0	109.5	109.5	7.80	7.80	0.39	0.39	7.51	7.51	7.50
	WMS4				В		2	8.39	0.00	35.74	00.14	29.0	20.0	109.4	100.0	7.79	7.00	0.38	0.03	7.49	7.49	1.50
Mid- Flood	WMS5	SUNNY	14:45	5	S	1	1	8.41	8.41	35.84	35.84	29.2	29.2	110.0	110.1	7.81	7.82	0.56	0.56	5.45	5.45	5.45
ΣĔ	WMS5	001111	UF.F		S		2	8.41	0.71	35.84	00.04	29.2	20.2	110.1		7.82	1.02	0.55	0.00	5.44	5.44	5.40

SGS	

EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-4
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	WMS5				М		1	NA		NA		NA		NA		NA		NA		NA	NA	
	WMS5				М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	WMS5				В		1	8.42	0.40	35.81	05.04	29.2	00.0	106.9	407.0	7.73	7 70	0.48	0.40	5.12	5.12	
	WMS5				В	4	2	8.42	8.42	35.81	35.81	29.2	29.2	107.0	107.0	7.72	7.73	0.48	0.48	5.09	5.09	5.11
	WMS6				S	4	1	8.41	0.44	35.86	25.00	29.2	00.0	107.3	407.4	7.73	7.74	0.59	0.50	6.61	6.61	0.50
	WMS6				S	1	2	8.41	8.41	35.86	35.86	29.2	29.2	107.4	107.4	7.74	7.74	0.58	0.59	6.56	6.56	6.59
Mid-Flood	WMS6		45.00	_	М		1	NA		NA		NA		NA		NA		NA		NA	NA	
Aid-F	WMS6	SUNNY	15:00	5	М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
2	WMS6				В		1	8.42	0.40	35.83	05.00	29.2	00.0	105.5	405.0	7.68	7.00	0.50	0.50	5.86	5.86	5.07
	WMS6				В	4	2	8.42	8.42	35.83	35.83	29.2	29.2	105.6	105.6	7.69	7.69	0.50	0.50	5.87	5.87	5.87
	11				S		1	8.39	0.00	35.88	05.00	29.2		110.5		7.82	7.00	0.55	0.55	4.31	4.31	
	11				S	1	2	8.39	8.39	35.88	35.88	29.2	29.2	110.6	110.6	7.83	7.83	0.54	0.55	4.28	4.28	4.30
Mid-Flood	11		44.45		М	7	1	8.37	0.00	35.87	05.00	29.2	00.0	108.2	100.0	7.73	7 70	0.56	0.57	6.02	6.02	0.01
Aid-F	11	SUNNY	14:15	14	М	/	2	8.38	8.38	35.88	35.88	29.2	29.2	108.1	108.2	7.72	7.73	0.57	0.57	6.00	6.00	6.01
2	11				В	40	1	8.36	0.00	36.01	00.00	29.4	00.4	106.1	400.4	7.65	7.00	0.35	0.00	7.33	7.33	7.00
	1				В	13	2	8.36	8.36	36.02	36.02	29.4	29.4	106.0	106.1	7.66	7.66	0.36	0.36	7.32	7.32	7.33
	C1				S		1	8.41	0.44	36.00	00.00	29.2	00.0	113.8	440.0	7.89	7.00	0.63	0.00	12.56	12.56	40.54
	C1				S	1	2	8.41	8.41	36.00	36.00	29.2	29.2	113.9	113.9	7.88	7.89	0.62	0.63	12.51	12.51	12.54
Mid-Flood	C1		14.00	45	М	0	1	8.39	0.00	35.92	25.00	29.2	20.0	108.6	400.7	7.76	7 77	0.59	0.00	12.34	12.34	40.00
Aid-F	C1	SUNNY	14:00	15	М	8	2	8.39	8.39	35.92	35.92	29.2	29.2	108.7	108.7	7.77	7.77	0.60	0.60	12.31	12.31	12.33
2	C1				В		1	8.37	0.07	36.12	20.40	29.4	20.4	107.1	407.0	7.70	7 70	0.40	0.40	12.18	12.18	10.10
	C1				В	14	2	8.37	8.37	36.12	36.12	29.4	29.4	107.2	107.2	7.69	7.70	0.39	0.40	12.20	12.20	12.19



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-5
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
Monthly EMAA Report	Date	Nov 24

	Mode				Water									In-situ Me	asurement						Lab	poratory Anal	lysis					
Date	Tidal Mc	Monitoring Location	Weather	Time	Depth (m)	Monitoring Level	Monitoring Level (m)	Replicate	р	н	Salinity	y (ppt)	Tempera	iture (°C)	DO Satur	ration (%)	DO (I	mg/L)	Turbidit	ty (NTU)		ended solids o 105 (°C), mg						
									Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value		Ave.					
0/4/2024		WMS-1N				S		1	8.40		35.62		26.9		110.4		7.85		0.03		8.05	8.05						
		WMS-1N				S	1	2	8.40	8.40	35.62	35.62	26.9	26.9	110.5	110.5	7.86	7.86	0.04	0.04	8.02	8.02	8.04					
	Ebb	WMS-1N				М	_	1	8.40		35.63		26.9		107.2		7.74		0.14		7.77	7.77						
	Mid-Ebb	WMS-1N	SUNNY	11:00	7.5	М	3	2	8.40	8.40	35.63	35.63	26.9	26.9	107.3	107.3	7.75	7.75	0.13	0.14	7.69	7.69	7.73					
	_	WMS-1N				В	_	1	8.40	0.40	35.83	05.00	27.0	07.0	104.0	101.0	7.62	7.00	0.64	0.05	7.11	7.11						
		WMS-1N				В	7	2	8.40	8.40	35.83	35.83	27.0	27.0	103.9	104.0	7.63	7.63	0.65	0.65	7.16	7.16	7.14					
		WMS-2N				S		1	8.40	0.40	35.66	05.00	26.9		107.6	107.7	7.73	4	0.09	0.00	6.36	6.36	0.07					
		WMS-2N				S	1	2	8.40	8.40	35.66	35.66	26.9	26.9	107.7	107.7	7.74	7.74	0.08	0.09	6.37	6.37	6.37					
	Ebb	WMS-2N	<b></b>			М		1	NA		NA		NA		NA		NA		NA		NA	NA						
	Mid-Ebb	WMS-2N	SUNNY	10:45	4.3	М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA					
	_	WMS-2N				В	_	1	8.41		36.07	00.07	27.4	07.4	104.5	101.0	7.64	7.04	0.26	0.07	10.92	10.92	40.00					
		WMS-2N				В	3	2	8.41	8.41	36.07	36.07	27.4	27.4	104.6	104.6	7.63	7.64	0.27	0.27	10.86	10.86	10.89					
		WMS3				S		1	NA		NA		NA		NA		NA		NA		NA	NA						
		WMS3				S	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA					
	Ebb	WMS3		40.45		М	4.5	1	8.42	0.40	36.28	20.00	27.8	07.0	105.9	405.0	7.67	7.00	0.24	0.05	4.23	1.00	0.00					
	Mid-Ebb	WMS3	SUNNY	10:15	3	М	1.5	2	8.42	8.42	36.29	36.29	27.8	27.8	105.8	105.9	7.68	7.68	0.25	0.25	4.26	4.26	2.63					
	_	WMS3			-	В	NIA	1	NA		NA		NA	<b>N</b> 14	NA	<b>N</b> 10	NA		NA		NA	NA						
		WMS3				В	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA					
		WMS4									S		1	8.43	0.40	36.31	20.24	28.2	00.0	111.3	110.0	7.84	7.05	0.01	0.01	5.12	5.12	E 40
		WMS4				S	1	2	8.43	8.43	36.31	36.31	28.2	28.2	114.4	112.9	7.85	7.85	0.01	0.01	5.07	5.07	5.10					
	Mid-Ebb	WMS4		0.00	4.0	М	NIA	1	NA		NA		NA	<b>N</b> 14	NA	<b>N</b> 10	NA		NA		NA	NA						
	Mid-	WMS4	SUNNY	9:30	4.2	М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA					
		WMS4				В	2	1	8.43	0.40	36.31	20.24	28.2	00.0	108.8	108.9	7.77	7.78	0.18	0.40	4.78	4.78	4.77					
		WMS4				В	3	2	8.43	8.43	36.31	36.31	28.2	28.2	108.9	106.9	7.78	1.10	0.19	0.19	4.75	4.75	4.77					
		WMS5				S	1	1	8.42	8.42	36.36	36.36	28.3	28.3	109.3	109.4	7.79	7.80	0.08	0.08	7.32	7.32	7.32					
		WMS5				S	I	2	8.42	0.42	36.36	30.30	28.3	20.3	109.4	109.4	7.80	7.00	0.07	0.06	7.32	7.32	1.52					
	Mid-Ebb	WMS5	CLININIX	0.45	4.6	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA					
	Mid-	WMS5	SUNNY	9:45	4.6	М	NA	2	NA	NA	NA	INA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA					
		WMS5				В		1	8.42	8.42	36.36	36.36	28.3	28.3	106.4	106.4	7.76	7.77	0.11	0.12	5.71	5.71	5.73					
		WMS5				В	4	2	8.42	0.42	36.36	30.30	28.3	20.3	106.3	100.4	7.77	1.11	0.12	0.12	5.74	5.74	5.75					
		WMS6				S	1	1	8.42	0.40	36.38	26.20	28.3	20.2	106.6	106 7	7.73	7 72	0.10	0.11	7.03	7.03	7.04					
		WMS6				S	1	2	8.42	8.42	36.38	36.38	28.3	28.3	106.7	106.7	7.72	7.73	0.11	0.11	7.04	7.04	7.04					
	Mid-Ebb	WMS6	SUNNY	10:00	4.6	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA					
	Mid-	WMS6	SUNNT	10.00	4.0	М		2	NA		NA	INA	NA	INA	NA	INA	NA		NA		NA	NA						
		WMS6				В	л	1	8.42	8.42	36.38	36.38	28.3	28.3	104.8	104.9	7.68	7.68	0.15	0.14	6.64	6.64	6.66					
		WMS6				В	4	2	8.42	0.42	36.38	30.30	28.3	20.3	104.9	104.9	7.67	1.00	0.13	0.14	6.67	6.67	0.00					
	Mid - Ebb	12	SUNNY	9:00	17	S	1	1	8.40	8.40	36.34	36.34	28.4	28.4	112.1	112.2	7.88	7.89	0.30	0.30	8.68	8.68	8.71					

SGS	

EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-6
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	12				S		2	8.40		36.34		28.4		112.3		7.89		0.29		8.73	8.73	
	12				М		1	8.39		36.34		28.4		109.1		7.76		0.24		8.49	8.49	
	12				M	8	2	8.39	8.39	36.34	36.34	28.4	28.4	109.2	109.2	7.77	7.77	0.25	0.25	8.48	8.48	8.49
	12				В		1	8.38		36.31		28.4		105.9		7.64		1.12		9.01	9.01	
	12				В	16	2	8.38	8.38	36.13	36.22	28.4	28.4	106.0	106.0	7.65	7.65	1.11	1.12	8.97	8.97	8.99
	C2				S		1	8.40		35.70		27.0		107.8		7.75		0.12		15.32	15.32	
	C2				s	1	2	8.40	8.40	35.70	35.70	27.0	27.0	107.9	107.9	7.74	7.75	0.12	0.12	15.36	15.36	15.34
q	C2				M		1	NA		NA NA		NA		NA		NA		NA		NA	NA	
Mid-Ebb	C2 C2	SUNNY	10:30	4.2	M	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
Σ	C2 C2				B		1	8.40		36.12		27.4		105.1		7.65		0.28		15.18	15.18	
						3			8.40		36.12		27.4		105.2		7.66		0.29			15.20
	C2				В		2	8.40		36.12		27.4		105.2		7.66		0.29		15.22	15.22	
	C3				S	1	1	8.42	8.42	36.30	36.30	28.3	28.3	111.2	111.3	7.86	7.86	0.39	0.40	11.87	11.87	11.88
Ą	C3				S		2	8.42		36.30		28.3		111.3		7.85		0.40		11.88	11.88	
Mid-Ebb	C3	SUNNY	9:15	14.5	M	7	1	8.41	8.41	36.30	36.30	28.2	28.2	108.1	108.1	7.71	7.72	0.29	0.30	13.69	13.69	13.76
Mi	C3				M		2	8.41		36.30		28.2		108.0		7.72		0.30		13.82	13.82	
	C3				В	14	1	8.41	8.41	36.28	36.28	28.2	28.2	104.8	104.9	7.62	7.63	1.17	1.18	12.37	12.37	12.30
	C3				В		2	8.41		36.28		28.2		104.9		7.63		1.18		12.23	12.23	
	WMS-1N				S	1	1	8.34	8.34	35.50	35.50	27.0	27.0	109.5	109.6	7.81	7.82	0.05	0.06	6.86	6.86	6.84
p	WMS-1N				S		2	8.34		35.50		27.0		109.6		7.82		0.06		6.81	6.81	
Mid-Flood	WMS-1N	SUNNY	15:45	8	М	3	1	8.35	8.35	35.52	35.52	27.0	27.0	106.3	106.4	7.70	7.71	0.16	0.17	5.55	5.55	5.58
Mid	WMS-1N				М		2	8.35		35.52		27.0		106.4		7.71		0.17		5.60	5.60	
	WMS-1N				В	7	1	8.34	8.34	35.71	35.71	27.1	27.1	103.0	103.1	7.58	7.59	0.67	0.68	7.46	7.46	7.44
	WMS-1N				В		2	8.34		35.71		27.1		103.1		7.59		0.68		7.42	7.42	
	WMS-2N				S	1	1	8.34	8.34	35.54	35.55	27.1	27.1	106.7	106.8	7.69	7.70	0.11	0.12	6.61	6.61	6.60
σ	WMS-2N				S		2	8.34		35.55	00.00	27.1		106.8		7.71		0.12		6.59	6.59	
Mid-Flood	WMS-2N	SUNNY	15:30	4.7	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
Mid-	WMS-2N				М		2	NA		NA		NA		NA		NA		NA		NA	NA	
	WMS-2N				В	4	1	8.33	8.33	35.95	35.95	27.5	27.5	103.5	103.6	7.60	7.61	0.23	0.23	7.04	7.04	7.07
	WMS-2N				В		2	8.33	0.00	35.95	00.00	27.5	21.0	103.6	100.0	7.61	1.01	0.22	0.20	7.09	7.09	
	WMS3				S	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
σ	WMS3				S		2	NA		NA	INA.	NA		NA	INA.	NA	NA	NA		NA	NA	
	WMS3	SUNNY	15:15	3.2	М	1.5	1	8.36	8.36	36.18	36.18	27.9	27.9	105.0	105.0	7.63	7.64	0.30	0.30	7.52	7.52	7.51
Mid-Flood	WMS3	JOININT	10.10	5.2	М	1.0	2	8.36	0.00	36.18	50.10	27.9	21.3	104.9	103.0	7.64	7.04	0.29	0.50	7.49	7.49	7.31
~	WMS3				В	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	WMS3				В		2	NA	AI	NA	INA	NA		NA	INA	NA		NA		NA	NA	
	WMS4				S	4	1	8.37	0.07	36.20	26.00	28.3	28.3	110.5	110.6	7.8	7.00	0.03	0.04	6.16	6.16	6.15
-	WMS4				S	1	2	8.37	8.37	36.20	36.20	28.3	20.3	110.6	0.011	7.8	7.83	0.04	0.04	6.13	6.13	0.15
Mid-Flood	WMS4	OLD IN INV	44.00	4.5	М	NIA	1	NA	NIA	NA	NA	NA	NIA	NA	NIA	NA	NIA	NA	NIA	NA	NA	NIA
Aid-F	WMS4	SUNNY	14:30	4.5	М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
2	WMS4				В		1	8.36	0.00	36.22	00.05	28.2	<u> </u>	107.9	400.5	7.7		0.19		5.41	5.41	
	WMS4				В	4	2	8.36	8.36	36.22	36.22	28.2	28.2	108.0	108.0	7.8	7.75	0.20	0.20	5.41	5.41	5.41
4 p	WMS5				S		1	8.36		36.25		28.4		108.5		7.8		0.09		3.85	3.85	
Mic Floc	WMS5	SUNNY	14:45	5	S	1	2	8.36	8.36	36.25	36.25	28.4	28.4	108.6	108.6	7.8	7.77	0.08	0.09	3.82	3.82	3.84
Mid- Flood		SUNNY	14:45	5		1			8.36	36.25	36.25		28.4		108.6		7.77		0.09			

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-7
CCC	Works at Po Toi O	Ref#	EMA2403/03/42
202	Monthly EM&A Report	Rev.	01
		Date	Nov 24

	WMS5				м		1	NA		NA		28.4	00.4	NA		NA	N10	NA		NA	NA	
	WMS5				М	NA	2	NA	NA	NA	NA	28.4	28.4	NA	NA	NA	NA	NA	NA	NA	NA	NA
	WMS5				В		1	8.36	0.00	36.26	00.00	28.4	00.4	105.5	405.5	7.7	7 74	0.13	0.40	7.01	7.01	0.00
	WMS5				В	4	2	8.36	8.36	36.26	36.26	28.4	28.4	105.4	105.5	7.7	7.74	0.12	0.13	6.96	6.96	6.99
	WMS6				S	4	1	8.36	0.00	36.29	20.00	28.4	00.4	105.7	405.0	7.7	7 70	0.12	0.40	10.64	10.64	40.04
-	WMS6				S	1	2	8.36	8.36	36.29	36.29	28.4	28.4	105.8	105.8	7.7	7.70	0.11	0.12	10.58	10.58	10.61
Mid-Flood	WMS6	SUNNY	15:00	-	М	NA	1	NA	NA	NA	NA	28.4	28.4	NA	NA	NA	NA	NA	NA	NA	NA	NA
Aid-F	WMS6	SUNINT	15.00	5	М	NA	2	NA	NA	NA	INA	28.4	20.4	NA	NA	NA	NA	NA	NA	NA	NA	NA
2	WMS6				В	4	1	8.36	8.36	36.28	36.28	28.4	28.4	103.9	104.0	7.6	7.65	0.16	0.16	7.27	7.27	7.24
	WMS6				В	4	2	8.36	0.30	36.28	30.20	28.4	20.4	104.0	104.0	7.7	7.05	0.15	0.16	7.21	7.21	7.24
	l1				S	1	1	8.35	8.35	36.19	36.20	28.4	28.4	110.4	110.4	7.8	7.82	0.42	0.43	6.96	6.96	7.00
75	l1				S	I	2	8.35	0.33	36.20	30.20	28.4	20.4	110.3	110.4	7.8	1.02	0.43	0.43	7.03	7.03	7.00
Mid-Flood	l1	SUNNY	14:15	15.5	М	7	1	8.35	8.35	36.19	36.19	107.2	107.2	107.2	107.2	7.7	7.68	0.32	0.32	8.54	8.54	8.53
Mid-F	l1	SUMME	14.15	15.5	М	1	2	8.35	0.55	36.19	30.19	107.1	107.2	107.1	107.2	7.7	7.00	0.31	0.32	8.51	8.51	0.00
-	l1				В	13	1	8.33	8.33	36.15	36.15	104.0	104.0	104.0	104.0	7.6	7.59	1.16	1.16	9.12	9.12	9.10
	l1				В	15	2	8.33	0.55	36.15	50.15	103.9	104.0	103.9	104.0	7.6	1.55	1.15	1.10	9.08	9.08	9.10
	C1				S	1	1	8.34	8.34	36.25	36.25	111.2	111.3	111.2	111.3	7.8	7.85	0.31	0.32	14.05	14.05	14.00
<del>a</del>	C1				S	1	2	8.34	0.54	36.25	50.25	111.3	111.5	111.3	111.5	7.9	7.00	0.32	0.52	13.94	13.94	14.00
Floo	C1	SUNNY	14:00	18	М	8	1	8.33	8.33	36.23	36.23	108.2	108.3	108.2	108.3	7.7	7.73	0.26	0.27	12.27	12.27	12.31
Mid-Flood	C1	CONNT	14.00	10	М	0	2	8.33	0.00	36.23	00.20	108.3	100.0	108.3	100.0	7.7	1.10	0.27	0.27	12.34	12.34	12.01
_	C1				В	17	1	8.32	8.32	36.18	36.18	105.0	105.1	105.0	105.1	7.6	7.62	1.13	1.13	11.11	11.11	11.14
	C1				В	.,	2	8.32	0.02	36.18	00.10	105.1	100.1	105.1	100.1	7.6	1.02	1.12	1.10	11.17	11.17	11.17



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-8
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	Mode				Water									In-situ Me	asurement						Lab	oratory Anal	lysis
Date	Tidal Mo	Monitoring Location	Weather	Time	Depth (m)	Monitoring Level	Monitoring Level (m)	Replicate	p	н	Salinity	y (ppt)	Tempera	ture (ºC)	DO Satu	ration (%)	DO (I	mg/L)	Turbidit	ty (NTU)		ended solids o 105 (ºC), mg/	
									Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value		Ave.
/7/2024		WMS-1N				S		1	8.37		35.66		28.3		111.7		7.86		0.37		4.51	4.51	
		WMS-1N				S	1	2	8.37	8.37	35.66	35.66	28.3	28.3	111.8	111.8	7.87	7.87	0.37	0.37	4.48	4.48	4.50
	Ebb	WMS-1N				М	_	1	8.39		36.01		28.5		108.5		7.76		0.23		6.16	6.16	
	Mid-Ebb	WMS-1N	SUNNY	16:00	6.7	М	3	2	8.39	8.39	36.01	36.01	28.5	28.5	108.6	108.6	7.75	7.76	0.24	0.24	6.13	6.13	6.15
	-	WMS-1N				В		1	8.32	0.00	36.32		28.4		105.3	405.4	7.63	7.04	1.08	4.00	5.27	5.27	
		WMS-1N				В	6	2	8.32	8.32	36.32	36.32	28.4	28.4	105.4	105.4	7.64	7.64	1.09	1.09	5.23	5.23	5.25
		WMS-2N				S		1	8.38		36.05	00.05	28.6		108.8	400.0	7.74		0.23	0.00	6.23	6.23	0.05
		WMS-2N				S	1	2	8.38	8.38	36.05	36.05	28.6	28.6	108.9	108.9	7.75	7.75	0.23	0.23	6.26	6.26	6.25
	Ebb	WMS-2N	0. n n n /			М		1	NA		NA		NA		NA		NA		NA		NA	NA	
	Mid-Ebb	WMS-2N	SUNNY	15:45	3.6	М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	-	WMS-2N				В		1	8.39		36.08		28.6		105.6		7.65		0.39		5.55	5.55	
		WMS-2N				В	3	2	8.39	8.39	36.08	36.08	28.6	28.6	105.7	105.7	7.66	7.66	0.39	0.39	5.54	5.54	5.55
		WMS3				S		1	NA		NA		NA		NA		NA		NA		NA	NA	
		WMS3				S	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	ad II	WMS3	<b></b>			М	4.5	1	8.40	0.40	36.12	00.40	28.7	00 <b>7</b>	107.3	407.0	7.68	7.00	0.20	0.00	4.78	4.78	4.77
	Mid-Ebb	WMS3	SUNNY	15:15	2.6	М	1.5	2	8.40	8.40	36.12	36.12	28.7	28.7	107.2	107.3	7.69	7.69	0.20	0.20	4.75	4.75	4.77
	-	WMS3				В		1	NA		NA		NA		NA		NA		NA		NA	NA	
		WMS3				В	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
		WMS4				S		1	8.39		36.23		28.7		112.7		7.87		0.55		6.17	6.17	
		WMS4				S	1	2	8.39	8.39	36.23	36.23	28.7	28.7	112.6	112.7	7.88	7.88	0.55	0.55	6.18	6.18	6.18
	qq	WMS4	0. n. n. n. /			М		1	NA		NA		NA		NA		NA		NA		NA	NA	
	Mid-Ebb	WMS4	SUNNY	14:30	4	М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	-	WMS4				В		1	8.39	0.00	36.30		28.7	00.7	110.2		7.79	7.00	0.54		4.32	4.32	
		WMS4				В	3	2	8.39	8.39	36.30	36.30	28.7	28.7	110.3	110.3	7.80	7.80	0.54	0.54	4.30	4.30	4.31
		WMS5				S		1	8.40		36.19		28.8		110.6		7.82		0.69		7.04	7.04	
		WMS5				S	1	2	8.40	8.40	36.19	36.19	28.8	28.8	110.7	110.7	7.81	7.82	0.68	0.69	7.05	7.05	7.05
	pp	WMS5				М		1	NA		NA		NA		NA		NA		NA		NA	NA	
	Mid-Ebb	WMS5	SUNNY	14:45	3.7	М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	-	WMS5				В	_	1	8.41		36.30		28.7		107.5		7.78		0.22		6.68	6.68	
		WMS5				В	3	2	8.41	8.41	36.30	36.30	28.7	28.7	107.4	107.5	7.79	7.79	0.22	0.22	6.73	6.73	6.71
		WMS6				S		1	8.41		36.22		28.8		108.0		7.74		0.70		5.74	5.74	
		WMS6				S	1	2	8.41	8.41	36.22	36.22	28.7	28.8	107.9	108.0	7.75	7.75	0.71	0.71	5.71	5.71	5.73
	Ebb	WMS6				М		1	NA		NA		NA		NA		NA		NA		NA	NA	
	Mid-Ebb	WMS6	SUNNY	15:00	3.7	М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	4	WMS6				В		1	8.41		36.33		28.7		106.2		7.69		0.21		3.36	3.36	
		WMS6				В	3	2	8.41	8.41	36.33	36.33	28.7	28.7	106.3	106.3	7.70	7.70	0.21	0.21	3.38	3.38	3.37
F	Mid - Ebb	12	SUNNY	14:00	16	S	1	1	8.37	8.37	36.32	36.32	28.7	28.7	113.4	113.5	7.89	7.90	0.56	0.56	11.75	11.75	11.74



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-9
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	12				S		2	8.37		36.32		28.7		113.5		7.90		0.56		11.73	11.73	
	12				М		1	8.35		36.44		28.4		110.5		7.77		0.41		7.98	7.98	
	12				м	8	2	8.35	8.35	36.44	36.44	28.4	28.4	110.4	110.5	7.78	7.78	0.41	0.41	8.02	8.02	8.00
	12				В		1	8.34		36.54		28.3		107.2		7.65		1.10		8.24	8.24	
	12				В	15	2	8.34	8.34	36.54	36.54	28.3	28.3	107.3	107.3	7.66	7.66	1.11	1.11	8.23	8.23	8.24
	C2				S		1	8.38		36.12		28.6		109.2		7.75		0.25		14.79	14.79	+
	C2				s	1	2	8.38	8.38	36.12	36.12	28.6	28.6	109.1	109.2	7.76	7.76	0.26	0.26	14.75	14.75	14.77
qq	C2				M		1	NA		NA		NA		NA		NA		NA		NA	NA	
Mid-Ebb	C2	SUNNY	15:30	3.5	M	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
Σ	C2				В		1	8.38		36.16		28.6		106.0		7.66		0.41		14.40	14.40	
					В	3	2	8.38	8.38		36.16	28.6	28.6	105.9	106.0	7.67	7.67	0.41	0.42	14.40		14.41
	C2						2			36.16											14.42	
	C3				S	1	1	8.39	8.39	36.31	36.31	28.7	28.7	112.6	112.7	7.87	7.87	0.46	0.46	15.12	15.12	15.13
م	C3				S		2	8.39		36.31		28.7		112.7		7.86		0.46		15.13	15.13	
Mid-Ebb	C3	SUNNY	14:15	14	M	7	1	8.36	8.36	36.46	36.46	28.3	28.3	109.4	109.4	7.72	7.73	0.22	0.22	15.34	15.34	15.37
Ξ	C3				M		2	8.36		36.46		28.3		109.3		7.73		0.22		15.39	15.39	
	C3				В	13	1	8.35	8.35	36.52	36.52	28.3	28.3	106.1	106.2	7.63	7.64	0.15	0.15	13.41	13.41	13.37
	C3				В		2	8.35		36.52		28.3		106.2		7.64		0.15		13.33	13.33	<u> </u>
	WMS-1N				S	1	1	8.31	8.31	35.52	35.52	28.2	28.2	110.5	110.6	7.83	7.84	0.39	0.39	7.77	7.77	7.76
g	WMS-1N				S		2	8.31		35.52		28.2		110.6		7.84		0.38		7.75	7.75	
Mid-Flood	WMS-1N	SUNNY	10:45	7.2	M	3	1	8.33	8.33	35.88	35.88	28.4	28.4	107.3	107.3	7.73	7.73	0.26	0.26	8.24	8.24	8.27
Mid	WMS-1N				M		2	8.33		35.88		28.4		107.2		7.72		0.25		8.29	8.29	
	WMS-1N				В	6	1	8.26	8.26	36.21	36.21	28.3	28.3	104.1	104.1	7.61	7.61	1.09	1.10	9.16	9.16	9.15
	WMS-1N				В		2	8.26		36.21		28.3		104.0		7.60		1.10		9.13	9.13	<u> </u>
	WMS-2N				S	1	1	8.32	8.32	35.92	35.92	28.5	28.5	107.9	108.0	7.71	7.72	0.27	0.26	6.76	6.76	6.74
g	WMS-2N				S		2	8.32		35.92		28.5		108.0		7.72		0.25		6.72	6.72	
Mid-Flood	WMS-2N	SUNNY	10:30	4	M	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
Mid	WMS-2N				M		2	NA		NA		NA		NA		NA		NA		NA	NA	<u> </u>
	WMS-2N				В	3	1	8.33	8.33	35.95	35.95	28.5	28.5	104.7	104.8	7.62	7.63	0.41	0.41	5.59	5.59	5.60
	WMS-2N				В		2	8.33		35.95		28.5		104.8		7.63		0.40		5.60	5.60	<u> </u>
	WMS3				S	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
σ	WMS3				S		2	NA		NA		NA		NA		NA		NA		NA	NA	
Mid-Flood	WMS3	SUNNY	10:15	2.8	М	1.5	1	8.34	8.34	36.01	36.01	28.6	28.6	106.0	106.1	7.66	7.66	0.23	0.23	5.78	5.78	5.76
Mid-	WMS3				М		2	8.34		36.01		28.6		106.1		7.65		0.22		5.73	5.73	
	WMS3				В	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	WMS3				В		2	NA		NA		NA		NA		NA		NA		NA	NA	
	WMS4				S	- 1	1	8.33	8.33	36.11	36.11	28.6	28.6	111.8	111.9	7.84	7.85	0.59	0.59	9.85	9.85	9.82
<del></del>	WMS4				S		2	8.33	0.00	36.11	00.11	28.6	20.0	111.9		7.85	7.00	0.58	0.00	9.79	9.79	0.02
Mid-Flood	WMS4	SUNNY	9:30	4.5	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
Mid-I	WMS4	SCININI	3.50	7.0	М		2	NA	11/1	NA		NA		NA		NA		NA	11/4	NA	NA	
	WMS4				В	4	1	8.33	8.33	36.18	36.18	28.6	28.6	109.3	109.4	7.76	7.77	0.52	0.52	7.23	7.23	7.23
	WMS4				В	4	2	8.33	0.33	36.18	30.10	28.6	20.0	109.4	109.4	7.77	1.11	0.52	0.52	7.22	7.22	1.23
Mid- Flood	WMS5		0.45	4.2	S	4	1	8.34	0.04	36.05	26.05	28.7	29.7	109.8	100.0	7.79	7 70	0.72	0.70	5.95	5.95	5.04
Flo	WMS5	SUNNY	9:45	4.2	S	1	2	8.34	8.34	36.05	36.05	28.7	28.7	109.9	109.9	7.78	7.79	0.71	0.72	5.92	5.92	5.94

SGS	

EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-10
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

		WMS5				М		1	NA		NA		NA		NA		NA		NA		NA	NA	
		WMS5				М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
		WMS5				В		1	8.34	0.04	36.18	00.40	28.6		106.7	400.7	7.75	7 70	0.25	0.00	7.04	7.04	7.00
		WMS5				В	3	2	8.34	8.34	36.18	36.18	28.6	28.6	106.6	106.7	7.76	7.76	0.26	0.26	7.02	7.02	7.03
		WMS6				S		1	8.35	0.05	36.10	00.40	28.6		106.9	407.0	7.71	7 70	0.73	0.74	5.63	5.63	5.00
		WMS6				S	1	2	8.35	8.35	36.10	36.10	28.6	28.6	107.0	107.0	7.72	7.72	0.74	0.74	5.60	5.60	5.62
	lood	WMS6	<b></b>			М		1	NA		NA		NA		NA		NA		NA		NA	NA	
	Mid-Flood	WMS6	SUNNY	10:00	4.2	М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	2	WMS6				В		1	8.35		36.21		28.6		105.3		7.66		0.23		4.75	4.75	. = 0
		WMS6				В	3	2	8.35	8.35	36.21	36.21	28.6	28.6	105.4	105.4	7.67	7.67	0.24	0.24	4.80	4.80	4.78
		l1				S	_	1	8.33		36.18		28.6		111.3		7.84		0.48		8.56	8.56	
		l1				S	1	2	8.33	8.33	36.18	36.18	28.6	28.6	111.4	111.4	7.83	7.84	0.47	0.48	8.59	8.59	8.58
	Mid-Flood	l1				М	_	1	8.30		36.33		28.2		108.1		7.69		0.23		7.87	7.87	
	1id-F	l1	SUNNY	9:15	15	М	7	2	8.30	8.30	36.33	36.33	28.2	28.2	108.2	108.2	7.70	7.70	0.24	0.24	7.84	7.84	7.86
	2	l1				В		1	8.30		36.40		28.2		105.0		7.60		0.18		9.91	9.91	
		11				В	14	2	8.29	8.30	36.40	36.40	28.2	28.2	104.9	105.0	7.61	7.61	0.17	0.18	9.96	9.96	9.94
		C1				S		1	8.31		36.20		28.6		112.2		7.87		0.58		13.24	13.24	
		C1				S	1	2	8.31	8.31	36.20	36.20	28.6	28.6	112.3	112.3	7.86	7.87	0.59	0.59	13.29	13.29	13.27
	C1 C1 C1 C1 C1	C1				М		1	8.28		36.32		28.3		109.3		7.74		0.40		13.89	13.89	
		SUNNY	9:00	17	М	8	2	8.28	8.28	36.32	36.32	28.3	28.3	109.2	109.3	7.75	7.75	0.39	0.40	13.92	13.92	13.91	
	2	C1				В		1	8.30		36.43		28.2		106.0		7.62		1.08		15.52	15.52	
		C1				В	16	2	8.30	8.30	36.43	36.43	28.2	28.2	106.1	106.1	7.63	7.63	1.09	1.09	15.54	15.54	15.53



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-11
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	ode				Water									In-situ Me	asurement						Lab	oratory Anal	lysis
Date	Tidal Mode	Monitoring Location	Weather	Time	Depth (m)	Monitoring Level	Monitoring Level (m)	Replicate	р	Н	Salinity	y (ppt)	Tempera	ature (°C)	DO Satu	ration (%)	DO (I	mg/L)	Turbidit	ty (NTU)		ended solids o 105 (ºC), mg/	
	·								Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value		Ave.
10/9/2024		WMS-1N				S		1	8.34	0.04	36.17	00.47	28.2		110.0	110.0	7.80	7.04	0.45	0.45	6.61	6.61	0.50
		WMS-1N				S		2	8.34	8.34	36.17	36.17	28.2	28.2	109.9	110.0	7.81	7.81	0.45	0.45	6.56	6.56	6.59
	Ebb	WMS-1N		44.00		М		1	8.35	0.05	36.20	00.00	28.4	00.4	107.2	107.0	7.74	7.74	0.29	0.00	7.37	7.37	7.00
	Mid-Ebb	WMS-1N	CLOUDY	11:00	6.6	М	3	2	8.35	8.35	36.20	36.20	28.4	28.4	107.3	107.3	7.73	7.74	0.29	0.29	7.35	7.35	7.36
		WMS-1N				В	6	1	8.35	0.05	36.51	20 54	28.6	00.0	105.5	405 F	7.63	7.04	0.10	0.40	7.04	7.04	7.04
		WMS-1N				В	6	2	8.35	8.35	36.51	36.51	28.6	28.6	105.4	105.5	7.64	7.64	0.10	0.10	7.03	7.03	7.04
		WMS-2N				S		1	8.35	0.05	36.27	00.07	28.1	00.4	108.7	100.0	7.75	7 70	0.24	0.04	8.24	8.24	0.00
		WMS-2N				S	1	2	8.35	8.35	36.27	36.27	28.1	28.1	108.8	108.8	7.76	7.76	0.24	0.24	8.21	8.21	8.23
	Ebb	WMS-2N				М		1	NA		NA		NA		NA		NA		NA		NA	NA	
	Mid-Ebb	WMS-2N	CLOUDY	10:45	3.5	М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	_	WMS-2N				В		1	8.36	0.00	36.31	00.04	28.1	00.4	105.2	105.0	7.66	7.07	0.08	0.00	7.79	7.79	7 70
		WMS-2N				В	3	2	8.36	8.36	36.31	36.31	28.1	28.1	105.3	105.3	7.67	7.67	0.08	0.08	7.76	7.76	7.78
		WMS3				S		1	NA		NA		NA		NA	NIA	NA		NA	NIA	NA	NA	
		WMS3				S	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid-Ebb	WMS3		10:15	2.4	М	1 5	1	8.36	8.36	36.23	36.23	28.1	28.1	106.7	106.7	7.70	7.70	0.14	0.14	7.23	7.23	7.04
	Mid-	WMS3	CLOUDY	10:15	2.4	М	1.5	2	8.36	0.30	36.23	30.23	28.1	20.1	106.6	100.7	7.69	1.70	0.14	0.14	7.18	7.18	7.21
		WMS3				В	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
		WMS3				В	NA	2	NA	INA	NA	INA	NA	NA NA	NA	NA	NA	NA NA	NA	NA NA	NA	NA	INA
		WMS4				S	1	1	8.38	8.38	36.47	36.47	28.3	28.3	111.2	111.3	7.85	7.86	0.70	0.70	5.26	5.26	5.27
		WMS4				S		2	8.38	0.30	36.47	30.47	28.3	20.3	111.3	111.3	7.86	7.00	0.70	0.70	5.27	5.27	5.27
	Mid-Ebb	WMS4		0.20	2.0	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	- NA
	Mid-	WMS4	CLOUDY	9:30	3.6	М	NA	2	NA	NA NA	NA	INA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
		WMS4				В	2	1	8.38	0.00	36.47	00.47	28.3	00.0	108.9	100.0	7.78	7 70	0.63	0.04	9.67	9.67	0.05
		WMS4				В	3	2	8.38	8.38	36.47	36.47	28.3	28.3	109.0	109.0	7.79	7.79	0.64	0.64	9.63	9.63	9.65
		WMS5				S	4	1	8.40	9.40	36.57	26.57	28.5	20.5	109.6	100.6	7.80	7.04	0.70	0.70	4.96	4.96	4.09
		WMS5				S	1	2	8.40	8.40	36.57	36.57	28.5	28.5	109.5	109.6	7.81	7.81	0.70	0.70	5.00	5.00	4.98
	Mid-Ebb	WMS5	CLOUDY	9:45	4	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid-	WMS5	CLOUDT	9.45	4	М	INA	2	NA	INA.	NA	INA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA .
		WMS5				В	3	1	8.40	8.40	36.56	36.56	28.5	28.5	106.2	106.2	7.71	7.71	0.71	0.71	5.32	5.32	5.31
		WMS5				В	5	2	8.40	0.40	36.56	30.00	28.5	20.0	106.2	100.2	7.70	1.11	0.71	0.71	5.29	5.29	5.51
Ī		WMS6				S	1	1	8.40	8.40	36.60	36.61	28.5	28.5	106.9	107.0	7.72	7.72	0.75	0.75	4.62	4.62	4.63
		WMS6				S	1	2	8.40	0.40	36.61	30.01	28.5	20.0	107.0	107.0	7.71	1.12	0.74	0.75	4.63	4.63	4.03
	Mid-Ebb	WMS6	CLOUDY	10.00	A	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid-	WMS6	CLOUDY	10:00	4	М	NA	2	NA		NA	INA	NA		NA	INA	NA		NA		NA	NA	INA
		WMS6				В	3	1	8.40	8.40	36.59	36.59	28.5	28.5	105.1	105.2	7.68	7.68	0.72	0.72	6.04	6.04	6.03
		WMS6				В		2	8.40	0.40	36.59	30.39	28.5	20.0	105.2	103.2	7.67	1.00	0.71	0.72	6.02	6.02	0.03
Γ	Mid - Ebb	12	CLOUDY	9:00	15	S	1	1	8.41	8.41	36.58	36.58	28.5	28.5	111.8	111.9	7.82	7.83	0.87	0.84	8.78	8.78	8.76



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-12
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	12				s		2	8.41		36.58		28.5		111.9		7.83		0.80		8.73	8.73	
	12				M		1	8.46		36.58		28.5		108.1		7.74		0.80		9.42	9.42	
	12				М	7	2	8.46	8.46	36.58	36.58	28.5	28.5	108.2	108.2	7.75	7.75	0.80	0.80	9.45	9.45	9.44
	12				В		1	8.36		36.76		28.4		106.7		7.68		0.34		7.65	7.65	
	12				B	14	2	8.36	8.36	36.76	36.76	28.4	28.4	106.8	106.8	7.67	7.68	0.34	0.34	7.56	7.56	7.61
	C2				S		1	8.36		36.33		28.1		109.0		7.76		0.26		18.68	18.68	
	C2				s	1	2	8.36	8.36	36.33	36.33	28.1	28.1	109.0	109.1	7.77	7.77	0.20	0.27	18.73	18.73	18.71
q							1	NA		NA								NA		NA		
Mid-Ebb	C2	CLOUDY	10:30	3.4	M	NA	-		NA		NA	NA	NA	NA	NA	NA	NA		NA		NA	NA
Σ	C2				M		2	NA		NA 20.07		NA 20.4		NA 105.0		NA Z 65		NA		NA 17.00	NA 17.00	
	C2				В	3	1	8.36	8.36	36.37	36.37	28.1	28.1	105.0	105.0	7.65	7.66	0.10	0.11	17.88	17.88	17.87
	C2				В		2	8.36		36.37		28.1		105.0		7.66		0.11		17.85	17.85	
	C3				S	1	1	8.41	8.41	36.58	36.58	28.5	28.5	109.7	109.8	7.80	7.81	0.70	0.70	20.03	20.03	20.05
٩	C3				S		2	8.41		36.58		28.5		109.8		7.81		0.70		20.06	20.06	
Mid-Ebb	C3	CLOUDY	9:15	13	M	6	1	8.40	8.40	36.58	36.58	28.5	28.5	107.5	107.6	7.70	7.71	0.77	0.77	16.12	16.12	16.11
Mic	C3				М		2	8.40		36.58		28.5		107.6		7.71		0.77		16.09	16.09	
	C3				В	12	1	8.32	8.32	36.63	36.63	28.4	28.4	105.3	105.4	7.63	7.64	1.20	1.20	18.71	18.71	18.69
	C3				В		2	8.32		36.63		28.4		105.4		7.64		1.20		18.67	18.67	
	WMS-1N				S	1	1	8.22	8.22	36.05	36.05	28.3	28.3	109.0	109.1	7.77	7.78	0.47	0.47	7.71	7.71	7.73
σ	WMS-1N				S		2	8.22		36.05		28.3		109.1		7.78		0.47		7.75	7.75	
Floo	WMS-1N	CLOUDY	15:45	7	М	3	1	8.29	8.29	36.07	36.07	28.5	28.5	106.5	106.5	7.72	7.72	0.31	0.31	6.89	6.89	6.87
Mid-Flood	WMS-1N				М	-	2	8.29		36.07		28.5		106.4		7.71		0.30		6.85	6.85	
	WMS-1N				В	6	1	8.28	8.28	36.37	36.37	28.7	28.7	104.7	104.8	7.61	7.62	0.12	0.13	8.81	8.81	8.84
	WMS-1N				В	Ŭ	2	8.28	0.20	36.37	00.07	28.7	20.7	104.8	104.0	7.62	1.02	0.13	0.10	8.86	8.86	0.04
	WMS-2N				S	1	1	8.30	8.30	36.15	36.15	28.2	28.2	107.6	107.7	7.72	7.73	0.30	0.29	4.75	4.75	4.74
	WMS-2N				S	1	2	8.30	0.50	36.15	30.15	28.2	20.2	107.7	107.7	7.73	1.15	0.28	0.29	4.72	4.72	4.74
Mid-Flood	WMS-2N		15:20	2.0	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
Aid-F	WMS-2N	CLOUDY	15:30	3.8	М	INA	2	NA	NA	NA	INA	NA	INA	NA	INA	NA	INA	NA	IN/A	NA	NA	NA
2	WMS-2N				В	2	1	8.30	0.20	36.19	26.40	28.2	20.2	104.3	104.4	7.63	7.64	0.05	0.05	5.15	5.15	E 10
	WMS-2N				В	3	2	8.30	8.30	36.18	36.19	28.2	28.2	104.4	104.4	7.64	7.64	0.04	0.05	5.11	5.11	5.13
	WMS3				S	NIA	1	NA	NIA	NA	NIA	NA	NIA	NA	NIA	NA	NIA	NA	NIA	NA	NA	NIA
-	WMS3				S	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	WMS3		45.45		М	4.5	1	8.30	0.00	36.30	20.20	28.3	00.0	105.6	405.0	7.67	7.07	0.16	0.47	11.86	11.86	44.04
Mid-Flood	WMS3	CLOUDY	15:15	2.8	М	1.5	2	8.30	8.30	36.30	36.30	28.3	28.3	105.5	105.6	7.66	7.67	0.17	0.17	11.82	11.82	11.84
2	WMS3				В		1	NA		NA		NA		NA		NA		NA		NA	NA	
	WMS3				В	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	WMS4				S		1	8.31		36.35		28.4		110.5		7.83		0.67		6.61	6.61	
	WMS4				S	1	2	8.31	8.31	36.35	36.35	28.4	28.4	110.6	110.6	7.82	7.83	0.68	0.68	6.58	6.58	6.60
Mid-Flood	WMS4				М		1	NA		NA		NA		NA		NA		NA		NA	NA	
lid-F	WMS4	CLOUDY	14:30	4	М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
Σ	WMS4				В		1	8.31		36.35		28.4		108.1		7.75		0.61		5.86	5.86	
	WMS4				В	3	2	8.31	8.31	36.35	36.35	28.4	28.4	108.2	108.2	7.76	7.76	0.62	0.62	5.83	5.83	5.85
<u>– A</u>	WMS5				S		1	8.34		36.45		28.6		108.5		7.78		0.68		4.21	4.21	
Mid- Flood	WMS5	CLOUDY	14:45	4.5	S	1	2	8.34	8.34	36.45	36.45	28.6	28.6	108.4	108.5	7.77	7.78	0.69	0.69	4.22	4.22	4.22
		L							I		I		I						1			I

SGS	

EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-13
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	WMS5				М		1	NA		NA		NA		NA		NA		NA		NA	NA	
	WMS5				М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	WMS5				В		1	8.34	0.04	36.43	00.40	28.6	00.0	105.3	405.4	7.68	7.00	0.65	0.00	4.68	4.68	4.74
	WMS5				В	4	2	8.34	8.34	36.43	36.43	28.6	28.6	105.4	105.4	7.67	7.68	0.66	0.66	4.73	4.73	4.71
	WMS6				S		1	8.34	0.04	36.49	00.40	28.6		105.9	100.0	7.69	7.00	0.73	0.74	7.14	7.14	7.40
	WMS6				S	1	2	8.34	8.34	36.49	36.49	28.6	28.6	106.0	106.0	7.68	7.69	0.74	0.74	7.12	7.12	7.13
lood	WMS6				М		1	NA		NA		NA		NA		NA		NA		NA	NA	
Mid-Flood	WMS6	CLOUDY	15:00	4.5	М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
2	WMS6				В	_	1	8.34		36.47		28.6		104.1		7.64		0.77		6.83	6.83	
	WMS6				В	4	2	8.34	8.34	36.47	36.47	28.6	28.6	104.2	104.2	7.65	7.65	0.78	0.78	6.82	6.82	6.83
	l1				S		1	8.35		36.45		28.7		109.0		7.78		0.68		9.45	9.45	
	l1				S	1	2	8.35	8.35	36.45	36.45	28.7	28.7	108.9	109.0	7.79	7.79	0.67	0.68	9.42	9.42	9.44
Mid-Flood	11				М	_	1	8.33		36.46		28.7		106.7		7.68		0.71		8.78	8.78	
1id-F	11	CLOUDY	14:15	14	М	7	2	8.33	8.33	36.45	36.46	28.7	28.7	106.8	106.8	7.69	7.69	0.73	0.72	8.79	8.79	8.79
2	11				В		1	8.26		36.51		28.6		104.5		7.60		1.17		8.86	8.86	
	11				В	13	2	8.26	8.26	36.51	36.51	28.6	28.6	104.6	104.6	7.61	7.61	1.16	1.17	8.82	8.82	8.84
	C1				S		1	8.34		36.45		28.7		110.5		7.78		0.90		15.32	15.32	
	C1				S	1	2	8.34	8.34	36.45	36.45	28.7	28.7	110.6	110.6	7.79	7.79	0.91	0.91	15.37	15.37	15.35
pool	C1				М		1	8.40		36.45		28.7		107.3		7.71		0.89		13.20	13.20	
Mid-Flood	C1	CLOUDY	14:00	16	М	8	2	8.40	8.40	36.45	36.45	28.7	28.7	107.2	107.3	7.72	7.72	0.88	0.89	13.16	13.16	13.18
Σ	C1				В		1	8.28		36.63		28.6		105.8		7.65		0.37		15.47	15.47	
	C1				В	15	2	8.28	8.28	36.63	36.63	28.6	28.6	105.9	105.9	7.64	7.65	0.39	0.38	15.44	15.44	15.46



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-14
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	ode				Water									In-situ Me	easurement						Lab	oratory Anal	ysis
Date	Tidal Mode	Monitoring Location	Weather	Time	Depth (m)	Monitoring Level	Monitoring Level (m)	Replicate	р	Н	Salinit	ty (ppt)	Tempera	ature (°C)	DO Satu	ation (%)	DO (r	mg/L)	Turbidit	ty (NTU)		spended solids 3 - 105 (°C), m	
									Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value		Ave.
10/12/2024		WMS-1N				S	4	1	8.05	0.05	31.79	04.70	28.0		107.8	407.0	7.74	7 75	0.70	0.70	9.21	9.21	0.40
		WMS-1N				S	1	2	8.05	8.05	31.79	31.79	28.0	28.0	107.9	107.9	7.75	7.75	0.70	0.70	9.17	9.17	9.19
	Ebb	WMS-1N	0. n n n /			М		1	8.09	0.00	32.07	00.07	28.2		106.0	100.0	7.65	7.00	1.08	4.00	8.46	8.46	0.40
	Mid-Ebb	WMS-1N	SUNNY	11:00	6.4	М	3	2	8.09	8.09	32.07	32.07	28.2	28.2	105.9	106.0	7.66	7.66	1.09	1.09	8.49	8.49	8.48
		WMS-1N				В	-	1	8.09	0.00	32.22	00.00	28.2	00.0	104.3	404.4	7.59	7.00	1.08	4.00	9.56	9.56	0.54
		WMS-1N				В	5	2	8.09	8.09	32.22	32.22	28.2	28.2	104.4	104.4	7.60	7.60	1.09	1.09	9.51	9.51	9.54
		WMS-2N				S		1	8.07	0.07	32.07	00.07	28.2		107.6	107.0	7.71	4	1.48		7.45	7.45	
		WMS-2N				S	1	2	8.07	8.07	32.07	32.07	28.2	28.2	107.5	107.6	7.70	7.71	1.48	1.48	7.39	7.39	7.42
	Ebb	WMS-2N	0. n n n /			М		1	NA		NA		NA		NA		NA		NA		NA	NA	
	Mid-Ebb	WMS-2N	SUNNY	10:45	4	М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	_	WMS-2N				В		1	8.08	0.00	32.16	00.40	28.2		105.9	100.0	7.66	7.07	1.56	4.57	6.93	6.93	
		WMS-2N				В	3	2	8.08	8.08	32.16	32.16	28.2	28.2	106.0	106.0	7.67	7.67	1.57	1.57	6.88	6.88	6.91
		WMS3				S	N14	1	NA		NA		NA	NA	NA	N14	NA		NA		NA	NA	
		WMS3				S	NA	2	NA	NA	NA	NA	NA		NA	NA	NA	NA	NA	NA	NA	NA	NA
	Ebb	WMS3		10.15		М	4.5	1	8.10	0.40	32.09	22.00	27.8	07.0	105.5	405.0	7.64	7.05	1.20	4.04	5.63	5.63	5.00
	Mid-Ebb	WMS3	SUNNY	10:15	2.6	М	1.5	2	8.10	8.10	32.09	32.09	27.8	27.8	105.6	105.6	7.65	7.65	1.22	1.21	5.56	5.56	5.60
		WMS3				В	NIA	1	NA	NIA	NA	NA	NA	NA	NA	NIA	NA	NIA	NA	NIA	NA	NA	NA
		WMS3				В	NA	2	NA	NA	NA	NA NA	NA		NA	NA	NA	NA	NA	NA	NA	NA	NA
		WMS4				S	4	1	8.12	0.40	32.31	22.24	28.0	20.0	109.7	400.7	7.86	7.07	0.82	0.00	7.15	7.15	7.40
		WMS4				S	1	2	8.12	8.12	32.31	32.31	28.0	28.0	109.6	109.7	7.87	7.87	0.82	0.82	7.10	7.10	7.13
	Ebb	WMS4		0.20	0.7	М	NA	1	NA	NIA	NA	NIA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid-Ebb	WMS4	SUNNY	9:30	3.7	М	NA	2	NA	NA	NA	NA	NA		NA	NA	NA	INA	NA	NA	NA	NA	NA
		WMS4				В	0	1	8.12	0.40	32.31	00.04	28.0	00.0	108.4	100 5	7.79	7 70	0.70	0.70	6.36	6.36	0.05
		WMS4				В	3	2	8.12	8.12	32.31	32.31	28.0	28.0	108.5	108.5	7.78	7.79	0.70	0.70	6.33	6.33	6.35
		WMS5				S	4	1	8.08	0.00	32.13	22.42	27.9	27.9	108.3	109.4	7.79	7 70	0.81	0.91	11.67	11.67	11.64
		WMS5				S	1	2	8.08	8.08	32.13	32.13	27.9	27.9	108.4	108.4	7.78	7.79	0.81	0.81	11.61	11.61	11.04
	Ebb	WMS5	CLININIX	0.45	2.4	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid-Ebb	WMS5	SUNNY	9:45	3.4	М	NA	2	NA	NA NA	NA	NA NA	NA	NA	NA	INA	NA	INA	NA	INA	NA	NA	NA
		WMS5				В	2	1	8.11	0.11	32.27	22.07	28.0	28.0	107.5	107 E	7.75	7.75	0.83	0.92	4.86	4.86	4.87
		WMS5				В	3	2	8.11	8.11	32.27	32.27	28.0	28.0	107.4	107.5	7.74	7.75	0.83	0.83	4.88	4.88	4.07
		WMS6				S	4	1	8.09	0.00	32.17	20.47	27.9	27.9	107.6	107.6	7.76	7.76	0.79	0.70	7.02	7.02	7.00
		WMS6				S	1	2	8.09	8.09	32.17	32.17	27.9	27.9	107.5	107.6	7.75	1.10	0.78	0.79	6.97	6.97	7.00
	Ebb	WMS6	CLININIX	10-00	2.4	М	NIA	1	NA	NIA	NA	NIA	NA	NIA	NA	NIA	NA	NIA	NA	NIA	NA	NA	NIA
	Mid-Ebb	WMS6	SUNNY	10:00	3.4	М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
		WMS6				В	0	1	8.13	0.40	32.30	20.00	28.0		106.7	106.0	7.71	7 70	0.84	0.04	4.63	4.63	4.60
		WMS6				В	3	2	8.13	8.13	32.30	32.30	28.0	28.0	106.8	106.8	7.72	7.72	0.83	0.84	4.69	4.69	4.66
	Mid - Ebb	12	SUNNY	9:00	15	S	1	1	8.13	8.13	32.72	32.72	28.1	28.1	109.3	109.4	7.82	7.83	0.98	0.99	9.23	9.23	9.21



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-15
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

ŀ					S		2	8.13		32.72		28.1		109.4		7.83		0.99		9.19	9.19	
	12				М		1	8.15		32.72		28.1		107.1		7.70		1.03		7.69	7.69	
F	12				М	7	2	8.15	8.15	32.72	32.72	28.1	28.1	107.2	107.2	7.71	7.71	1.04	1.04	7.66	7.66	7.68
-	12				В		1	8.18		32.72		28.1		105.7		7.66		1.09		8.46	8.46	
F	12				В	14	2	8.18	8.18	32.72	32.72	28.1	28.1	105.8	105.8	7.67	7.67	1.10	1.10	8.43	8.43	8.45
	C2				S		1	8.08		32.10		28.2		107.1		7.71		1.49		27.11	27.11	<u> </u>
F	C2				s	1	2	8.08	8.08	32.10	32.10	28.2	28.2	107.1	107.2	7.72	7.72	1.50	1.50	27.08	27.08	27.10
q	C2				M		1	NA		NA		NA		NA		NA		NA		NA	NA	<u> </u>
Mid-Et	C2	SUNNY	10:30	3.9	M	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
Σ	C2				В		1	8.08		32.20		28.2		106.2		7.67		1.58		27.20	27.20	<u> </u>
F	C2				В	3	2	8.08	8.08	32.20	32.20	28.2	28.2	106.3	106.3	7.68	7.68	1.59	1.59	27.20	27.20	27.21
							2											-				<u> </u>
-	C3				S	1	1	8.09	8.09	32.26	32.26	28.0	28.0	108.8	108.9	7.79	7.80	1.10	1.10	28.24	28.24	28.28
qq	C3				S		2	8.09		32.26		28.0		108.9		7.80		1.10		28.31	28.31	<u> </u>
Mid-Eb	C3	SUNNY	9:15	13	M	6	1	8.09	8.09	32.26	32.26	28.0	28.0	106.5	106.5	7.68	7.69	1.00	1.00	28.51	28.51	28.53
ž.	C3				M		2	8.09		32.26		28.0		106.5		7.69		1.00		28.55	28.55	<u> </u>
F	C3				В	12	1	8.09	8.09	32.26	32.26	28.0	28.0	105.1	105.2	7.63	7.64	1.45	1.46	24.28	24.28	24.24
	C3				В		2	8.09		32.26		28.0		105.2		7.64		1.46		24.19	24.19	<u> </u>
-	WMS-1N				S	1	1	8.12	8.12	31.92	31.92	28.1	28.1	108.6	108.7	7.77	7.78	0.79	0.80	4.67	4.67	4.68
- g	WMS-1N				S		2	8.12		31.92		28.1		108.7		7.78		0.80		4.69	4.69	<u> </u>
Flood	WMS-1N	SUNNY	15:45	6.8	М	3	1	8.16	8.16	32.19	32.19	28.3	28.3	106.7	106.8	7.68	7.69	1.10	1.10	11.31	11.31	11.29
Mid-	WMS-1N				М		2	8.16		32.19		28.3		106.8		7.69		1.09		11.27	11.27	<b></b>
-	WMS-1N				В	6	1	8.16	8.16	32.34	32.35	28.3	28.3	105.2	105.2	7.63	7.64	1.09	1.09	7.62	7.62	7.58
	WMS-1N				В		2	8.16		32.35		28.3		105.1		7.64		1.09		7.53	7.53	
	WMS-2N				S	1	1	8.13	8.13	32.20	32.20	28.3	28.3	108.4	108.5	7.74	7.74	1.47	1.47	5.26	5.26	5.25
<del>.</del> -	WMS-2N				S		2	8.13	0.10	32.20	02.20	28.3	20.0	108.5	100.0	7.73		1.46		5.24	5.24	0.20
	WMS-2N	SUNNY	15:30	4.5	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
Mid-Flood	WMS-2N	CONT	10.00	4.0	М		2	NA		NA	101	NA		NA		NA		NA		NA	NA	
_	WMS-2N				В	3	1	8.15	8.15	32.28	32.28	28.3	28.3	106.9	107.0	7.69	7.70	1.57	1.58	4.78	4.78	4.76
	WMS-2N				В	5	2	8.15	0.10	32.28	02.20	28.3	20.0	107.0	107.0	7.70	1.10	1.58	1.00	4.73	4.73	4.70
	WMS3				S	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
73	WMS3				S		2	NA		NA	INA	NA		NA	INA	NA	NA .	NA		NA	NA	
	WMS3	SUNNY	15:15	3	М	1.5	1	8.18	8.18	32.22	32.22	27.9	27.9	106.4	106.4	7.67	7.68	1.23	1.24	3.78	3.78	3.81
Mid-Flood	WMS3	SUNNT	15.15	5	М	1.5	2	8.18	0.10	32.22	32.22	27.9	21.5	106.3	100.4	7.68	7.00	1.25	1.24	3.83	3.83	3.01
2	WMS3				В	NIA	1	NA	NIA	NA	NIA	NA		NA	NIA	NA	NIA	NA	NIA	NA	NA	NIA
F	WMS3				В	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	WMS4				S	4	1	8.18	0.40	32.42	20.40	28.1	00.4	110.7	140.0	7.90	7.00	0.83	0.04	4.23	4.23	4.04
_ [	WMS4				S	1	2	8.18	8.18	32.42	32.42	28.1	28.1	110.8	110.8	7.89	7.90	0.84	0.84	4.24	4.24	4.24
	WMS4	OLDANY	44.00		М	NIA	1	NA	NIA	NA	NIA	28.1	00.4	NA	NIA	NA	NIA	NA	NIA	NA	NA	NI A
Mid-Flood	WMS4	SUNNY	14:30	4	М	NA	2	NA	NA	NA	NA	28.1	28.1	NA	NA	NA	NA	NA	NA	NA	NA	NA
2	WMS4				В	-	1	8.18	0.45	32.42	00.45	28.1		108.9	400.5	7.81		0.75	0.75	6.32	6.32	
F	WMS4				В	3	2	8.18	8.18	32.42	32.42	28.1	28.1	109.0	109.0	7.80	7.81	0.76	0.76	6.29	6.29	6.31
Mid- Flood	WMS5				S		1	8.14		32.25	a	28.0		109.1		7.82	<b>_</b>	0.82		5.43	5.43	
iĭĭŏ	WMS5	SUNNY	14:45	3.8	S	1	2	8.14	8.14	32.25	32.25	28.0	28.0	109.2	109.2	7.81	7.82	0.83	0.83	5.46	5.46	5.45

SGS	

EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-16
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	WMS5				м		1	NA		NA		NA		NA		NA		NA		NA	NA	
	WMS5				М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	WMS5				В		1	8.18	0.40	32.38	00.00	28.1		108.2	400.0	7.78	7 70	0.85	0.00	3.98	3.98	4.00
	WMS5				В	3	2	8.18	8.18	32.38	32.38	28.1	28.1	108.3	108.3	7.77	7.78	0.87	0.86	4.01	4.01	4.00
	WMS6				S		1	8.15	0.45	32.29	00.00	28.0	00.0	108.5	400.5	7.79	7 70	0.81	0.00	7.25	7.25	7.07
	WMS6				S		2	8.15	8.15	32.29	32.29	28.0	28.0	108.4	108.5	7.78	7.79	0.82	0.82	7.28	7.28	7.27
pool	WMS6		45.00		М		1	NA		NA		NA		NA		NA		NA		NA	NA	N 10
Mid-Floo	WMS6	SUNNY	15:00	3.8	М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
2	WMS6				В		1	8.20		32.43		28.1		107.5		7.74		0.86		7.63	7.63	
	WMS6				В	3	2	8.20	8.20	32.43	32.43	28.1	28.1	107.6	107.6	7.75	7.75	0.87	0.87	7.67	7.67	7.65
	1				S		1	8.16	0.40	32.35	00.05	28.2	00.0	109.7	400.0	7.83	7.04	1.15	4.40	8.42	8.42	0.40
	11				S		2	8.16	8.16	32.35	32.35	28.2	28.2	109.8	109.8	7.84	7.84	1.16	1.16	8.49	8.49	8.46
pool	1		11.15		М	-	1	8.16	0.40	32.35	00.05	28.2	00.0	107.3	407.4	7.71	7 70	1.05	4.00	10.53	10.53	10.50
Mid-Floo	1	SUNNY	14:15	14	М	7	2	8.16	8.16	32.35	32.35	28.2	28.2	107.4	107.4	7.72	7.72	1.06	1.06	10.52	10.52	10.53
2	1				В	10	1	8.16	0.40	32.35	00.05	28.2		105.9	400.0	7.67	7.00	1.47	4.40	9.67	9.67	0.04
	1				В	13	2	8.16	8.16	32.35	32.35	28.2	28.2	106.0	106.0	7.68	7.68	1.48	1.48	9.61	9.61	9.64
	C1				S		1	8.21	0.04	32.80	00.00	28.2		110.5	440.0	7.87	7.07	0.99	4.00	23.13	23.13	00.40
	C1				S		2	8.21	8.21	32.80	32.80	28.2	28.2	110.6	110.6	7.86	7.87	1.00	1.00	23.18	23.18	23.16
pool	C1	0.000	44.00		М		1	8.21	0.04	32.80	00.00	28.2	00.0	107.4	407.5	7.72	7 70	1.05	4.00	20.18	20.18	00.00
Mid-Floo	C1	SUNNY	14:00	16	М	8	2	8.21	8.21	32.80	32.80	28.2	28.2	107.5	107.5	7.71	7.72	1.06	1.06	20.26	20.26	20.22
2	C1				В		1	8.25	0.05	32.80	00.00	28.2		105.9	400.0	7.66	7.07	1.08	4.00	23.09	23.09	00.00
	C1				В	15	2	8.25	8.25	32.80	32.80	28.2	28.2	106.0	106.0	7.67	7.67	1.09	1.09	23.06	23.06	23.08



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-17
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	abo				Water									In-situ Me	asurement						Lab	oratory Anal	ysis
Date	Tidal Mode	Monitoring Location	Weather	Time	Water Depth (m)	Monitoring Level	Monitoring Level (m)	Replicate	p	н	Salinit	ty (ppt)	Tempera	ature (°C)	DO Satur	ation (%)	DO (r	mg/L)	Turbidit	ty (NTU)	Total sus 103	spended solid 3 - 105 (ºC), m	s dried at ng/L
	·								Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value		Ave.
10/14/2024		WMS-1N				S		1	8.07		31.59		27.9		110.9		7.86		0.68		5.86	5.86	
		WMS-1N				S	1	2	8.07	8.07	31.59	31.59	27.9	27.9	111.0	111.0	7.87	7.87	0.68	0.68	5.81	5.81	5.84
	Ebb	WMS-1N		44.00		М		1	8.09	0.00	32.25	00.05	28.1	00.4	107.9	407.0	7.77	7 70	1.07	4.00	6.25	6.25	0.04
	Mid-Ebb	WMS-1N	SUNNY	11:00	6.7	М	3	2	8.09	8.09	32.25	32.25	28.1	28.1	107.8	107.9	7.78	7.78	1.08	1.08	6.23	6.23	6.24
	_	WMS-1N				В		1	8.08	0.00	32.25	00.05	27.9	07.0	104.8	404.0	7.68	7.00	1.09	4.00	7.04	7.04	7.00
		WMS-1N				В	6	2	8.08	8.08	32.25	32.25	27.9	27.9	104.7	104.8	7.67	7.68	1.08	1.09	7.01	7.01	7.03
		WMS-2N				S		1	8.07	0.07	31.94	24.04	27.9	07.0	107.2	407.0	7.77	7 77	0.69	0.70	6.64	6.64	0.00
		WMS-2N				S	1	2	8.07	8.07	31.94	31.94	27.9	27.9	107.3	107.3	7.76	7.77	0.70	0.70	6.61	6.61	6.63
	Ebb	WMS-2N	SUNNY	10:45	2.4	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid-Ebb	WMS-2N	SUNNY	10.45	3.4	М	INA	2	NA	INA	NA	INA	NA	NA NA	NA	INA	NA	INA	NA	INA	NA	NA	NA
		WMS-2N				В	3	1	8.08	8.08	32.10	32.10	28.1	28.1	104.7	104.8	7.67	7.68	1.40	1.40	4.85	4.85	4.87
		WMS-2N				В	3	2	8.08	0.00	32.10	52.10	28.1	20.1	104.8	104.0	7.68	7.00	1.40	1.40	4.88	4.88	4.07
		WMS3				S	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
		WMS3				S	INA	2	NA	INA	NA	INA	NA	NA NA	NA	INA	NA	INA	NA	INA	NA	NA	NA
	Ebb	WMS3	SUNNY	10:15	2.6	М	1.5	1	8.09	8.09	32.02	32.02	27.8	27.8	105.6	105.7	7.72	7.72	0.33	0.33	7.47	7.47	7.48
	Mid-Ebb	WMS3	SUNNT	10.15	2.0	М	1.5	2	8.09	8.09	32.02	32.02	27.8	27.0	105.7	105.7	7.71	1.12	0.33	0.55	7.49	7.49	7.40
		WMS3				В	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
		WMS3				В	INA.	2	NA	112	NA		NA		NA	INA	NA	INA.	NA		NA	NA	
		WMS4				S	1	1	8.11	8.11	32.30	32.30	28.0	28.0	110.7	110.8	7.86	7.86	0.56	0.56	6.65	6.65	6.63
		WMS4				S	1	2	8.11	0.11	32.30	52.50	28.0	20.0	110.8	110.0	7.85	7.00	0.56	0.50	6.61	6.61	0.05
	Mid-Ebb	WMS4	SUNNY	9:30	3.9	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid-	WMS4	SONNT	3.50	5.5	М		2	NA		NA		NA		NA	IN/A	NA		NA		NA	NA	
		WMS4	4			В	3	1	8.11	8.11	32.30	32.30	28.0	28.0	107.3	107.4	7.77	7.78	0.43	0.43	9.25	9.25	9.24
		WMS4				В	5	2	8.11	0.11	32.30	52.50	28.0	20.0	107.4	107.4	7.78	1.10	0.43	0.43	9.23	9.23	9.24
		WMS5	4			S	1	1	8.09	8.09	32.11	32.11	28.0	28.0	107.9	108.0	7.80	7.80	0.60	0.60	5.35	5.35	5.34
	_	WMS5	-			S		2	8.09	0.00	32.11	02.11	28.0	20.0	108.0	100.0	7.79	1.00	0.60	0.00	5.32	5.32	0.04
	Mid-Ebb	WMS5	SUNNY	9:45	4	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid	WMS5	CONT	0.40	-	М		2	NA		NA		NA		NA		NA		NA		NA	NA	
		WMS5	-			В	3	1	8.12	8.12	32.24	32.24	28.0	28.0	105.4	105.5	7.73	7.73	0.50	0.50	4.89	4.89	4.88
		WMS5				В	Ŭ	2	8.12	0.12	32.24	02.21	28.0	20.0	105.5	100.0	7.72	1.10	0.50	0.00	4.87	4.87	
		WMS6				S	1	1	8.10	8.10	32.15	32.15	28.0	28.0	107.0	107.0	7.76	7.77	0.63	0.64	6.64	6.64	6.63
	-	WMS6				S		2	8.10	0.10	32.15	02.10	28.0	20.0	106.9	107.0	7.77		0.64	0.01	6.62	6.62	0.00
	Mid-Ebb	WMS6	SUNNY	10:00	4	4 M M	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid	WMS6		10.00				2	NA		NA		NA		NA		NA		NA		NA	NA	
		WMS6	-			В	3	1	8.12	8.12	32.29	32.29	28.0	28.0	104.3	104.4	7.69	7.69	0.52	0.53	5.52	5.52	5.55
		WMS6				В		2	8.12	0.12	32.29	52.25	28.0	20.0	104.4	.04.7	7.69	7.00	0.53	0.00	5.58	5.58	0.00
	Mid - Ebb	12	SUNNY	9:00	14	S	1	1	8.15	8.15	32.33	32.33	28.0	28.0	112.1	112.2	7.91	7.91	0.57	0.57	7.17	7.17	7.15



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-18
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

1	12				s		2	8.15		32.33		28.0		112.2		7.90		0.57		7.12	7.12	
	12				М		1	8.13		32.32		28.0		109.0		7.82		0.59		8.23	8.23	
	12				М	7	2	8.13	8.13	32.32	32.32	28.0	28.0	109.1	109.1	7.81	7.82	0.60	0.60	8.18	8.18	8.21
	12				В		1	8.12		32.32		28.0		105.8		7.71		0.55		6.97	6.97	
	12				В	13	2	8.12	8.12	32.32	32.32	28.0	28.0	105.9	105.9	7.72	7.72	0.55	0.55	6.96	6.96	6.97
	C2				S		1	8.08		31.98		28.0		107.5		7.77		0.73		14.86	14.86	
	C2				s	1	2	8.08	8.08	31.98	31.98	28.0	28.0	107.6	107.6	7.78	7.78	0.73	0.73	14.95	14.95	14.91
qq	C2				M		1	NA		NA		NA		NA		NA		NA		NA	NA	
Mid-Ebb	C2	SUNNY	10:30	3.3	M	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
Σ	C2				В		1	8.08		32.12		28.2		104.9		7.69		1.37		15.52	15.52	
	C2				В	3	2	8.08	8.08	32.12	32.12	28.2	28.2	104.9	105.0	7.69	7.69	1.37	1.38	15.39	15.39	15.46
							2															
	C3				S	1	1	8.11	8.11	32.26	32.26	28.0	28.0	111.1	111.2	7.88	7.88	0.54	0.54	17.64	17.64	17.61
ą	C3				S		2	8.11		32.26		28.0		111.2		7.87		0.54		17.57	17.57	
Mid-Ebb	C3	SUNNY	9:15	13	M	6	1	8.10	8.10	32.25	32.25	28.0	28.0	108.0	108.0	7.79	7.79	0.64	0.64	15.87	15.87	15.93
Ā	C3				M		2	8.10		32.25		28.0		107.9		7.78		0.64		15.99	15.99	
	C3				В	12	1	8.09	8.09	32.25	32.25	28.0	28.0	104.8	104.8	7.69	7.70	0.57	0.57	20.64	20.64	20.65
	C3				В		2	8.09		32.25		28.0		104.7		7.70		0.57		20.65	20.65	
	WMS-1N				S	1	1	8.13	8.13	31.70	31.71	28.0	28.0	109.8	109.9	7.83	7.84	0.70	0.70	7.02	7.02	7.05
g	WMS-1N				S		2	8.13		31.71		28.0		109.9		7.84		0.69		7.08	7.08	
Mid-Flood	WMS-1N	SUNNY	15:45	7.2	M	3	1	8.15	8.15	32.36	32.36	28.2	28.2	106.7	106.8	7.74	7.75	1.05	1.06	5.96	5.96	5.98
Mid	WMS-1N				M		2	8.15		32.36		28.2		106.8		7.75		1.06		5.99	5.99	
	WMS-1N				В	6	1	8.14	8.14	32.36	32.36	28.1	28.1	103.5	103.6	7.64	7.64	1.08	1.08	6.64	6.64	6.63
	WMS-1N				В		2	8.14		32.36		28.1		103.6		7.63		1.07		6.62	6.62	
	WMS-2N				S	1	1	8.14	8.14	32.08	32.08	28.1	28.1	106.3	106.4	7.74	7.74	0.72	0.72	12.00	12.00	11.95
g	WMS-2N				S		2	8.14		32.08		28.1		106.4		7.73		0.71		11.90	11.90	
Mid-Flood	WMS-2N	SUNNY	15:30	3.8	M	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
Mid	WMS-2N				M		2	NA		NA		NA		NA		NA		NA		NA	NA	
	WMS-2N				В	3	1	8.15	8.15	32.22	32.22	28.3	28.3	103.8	103.9	7.64	7.65	1.43	1.43	6.12	6.12	6.10
	WMS-2N				В		2	8.15		32.22	_	28.3		103.9		7.65		1.42		6.07	6.07	
	WMS3				S	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
σ	WMS3				S		2	NA		NA		NA		NA		NA		NA		NA	NA	
Mid-Flood	WMS3	SUNNY	15:15	3	М	1.5	1	8.16	8.16	32.14	32.14	27.9	27.9	104.5	104.6	7.69	7.69	0.37	0.38	3.78	3.78	3.83
Mid-	WMS3				М		2	8.16		32.14		27.9		104.6		7.68		0.38		3.88	3.88	
	WMS3				В	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	WMS3				В		2	NA		NA		NA		NA		NA		NA		NA	NA	
	WMS4				S	1	1	8.18	8.18	32.42	32.42	28.1	28.1	109.0	109.0	7.83	7.83	0.58	0.59	4.25	4.25	4.26
-	WMS4				S	'	2	8.18	0.10	32.42	02.72	28.1	20.1	108.9	100.0	7.82	7.00	0.59	0.03	4.26	4.26	7.20
Mid-Flood	WMS4	SUNNY	14:30	4.2	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
Mid-I	WMS4	CONNE	17.00	7.2	М	177	2	NA		NA		NA	11/1	NA	197	NA		NA	1.7.1	NA	NA	
	WMS4				В	3	1	8.18	8.18	32.42	32.42	28.1	28.1	106.5	106.6	7.74	7.75	0.41	0.42	5.15	5.15	5.14
	WMS4				В	5	2	8.18	0.10	32.42	52.42	28.1	20.1	106.6	100.0	7.75	1.10	0.42	0.42	5.12	5.12	5.14
<sup>p</sup> d	WMS5		14.45	4.5	S	4	1	8.16	0.46	32.22	22.00	28.1	20.4	107.0	107.1	7.77	7 77	0.62	0.62	7.45	7.45	7 4 4
Mid- Flood	WMS5	SUNNY	14:45	4.5	S	1	2	8.16	8.16	32.22	32.22	28.1	28.1	107.1	107.1	7.76	7.77	0.61	0.62	7.43	7.43	7.44

SGS	

EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-19
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	WMS5				м		1	NA		NA	NA	NA	NA	NA		NA		NA		NA	NA	
	WMS5				М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	WMS5				В		1	8.18	0.40	32.33	00.04	28.1	00.4	104.5	404.0	7.70	7 70	0.53	0.54	6.86	6.86	0.05
	WMS5				В	3	2	8.18	8.18	32.35	32.34	28.1	28.1	104.6	104.6	7.69	7.70	0.54	0.54	6.83	6.83	6.85
	WMS6				S		1	8.17	0.47	32.27	00.07	28.1	00.4	106.0	400.0	7.73	7.74	0.65	0.00	3.15	3.15	0.47
_	WMS6				S		2	8.17	8.17	32.27	32.27	28.1	28.1	105.9	106.0	7.74	7.74	0.66	0.66	3.18	3.18	3.17
pool	WMS6	0.000	45.00		М		1	NA		NA		NA		NA		NA		NA		NA	NA	
Mid-Floc	WMS6	SUNNY	15:00	4.5	М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
2	WMS6				В		1	8.18		32.41		28.1		103.4		7.65		0.54		4.23	4.23	
	WMS6				В	3	2	8.18	8.18	32.41	32.41	28.1	28.1	103.5	103.5	7.66	7.66	0.56	0.55	4.22	4.22	4.23
	l1				S		1	8.18		32.35		28.1		109.9		7.85		0.58		5.65	5.65	
	l1				S	1	2	8.18	8.18	32.35	32.35	28.1	28.1	110.0	110.0	7.84	7.85	0.57	0.58	5.61	5.61	5.63
pool	l1				М	_	1	8.16		32.33		28.1		106.7		7.76		0.67		4.86	4.86	
Mid-Floo	l1	SUNNY	14:15	14	М	7	2	8.16	8.16	32.33	32.33	28.1	28.1	106.8	106.8	7.75	7.76	0.68	0.68	4.87	4.87	4.87
2	l1				В		1	8.15		32.33		28.1		103.5		7.66		0.59		6.21	6.21	
	l1				В	13	2	8.15	8.15	32.33	32.33	28.1	28.1	103.6	103.6	7.67	7.67	0.60	0.60	6.18	6.18	6.20
	C1				S		1	8.21		32.41		28.1		110.9		7.88		0.61		16.03	16.03	
	C1				S	1	2	8.21	8.21	32.41	32.41	28.1	28.1	110.8	110.9	7.87	7.88	0.60	0.61	16.01	16.01	16.02
pool	C1				М		1	8.19		32.40		28.1		107.8		7.79		0.57		16.87	16.87	
Mid-F	C1	SUNNY	14:00	15	М	7	2	8.19	8.19	32.40	32.40	28.1	28.1	107.9	107.9	7.78	7.79	0.56	0.57	16.92	16.92	16.90
2	C1				В		1	8.17		32.40		28.1		104.6		7.68		0.52		16.52	16.52	
	C1				В	14	2	8.17	8.17	32.40	32.40	28.1	28.1	104.7	104.7	7.69	7.69	0.51	0.52	16.47	16.47	16.50



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-20
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	de													In-situ Me	asurement						Lab	oratory Anal	lysis
Date	Tidal Mode	Monitorin g Location	Weather	Time	Water Depth (m)	Monitorin g Level	Monitorin g Level (m)	Replicate	pH	ł	Salinit	ty (ppt)	Tempera	ture (⁰C)	DO Satur	ation (%)	DO (I	mg/L)	Turbidity	/ (NTU)		spended solid 3 - 105 (°C), m	
									Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value		Ave.
10/16/202		WMS-1N				S		1	8.08	0.00	31.99	04.00	28.3		107.5	407.0	7.73		0.83		5.63	5.63	<b>-</b> 00
4		WMS-1N				S	1	2	8.08	8.08	31.99	31.99	28.3	28.3	107.6	107.6	7.74	7.74	0.83	0.83	5.61	5.61	5.62
	Ebb	WMS-1N		44.45	7.0	М		1	8.09	0.00	32.17	00.47	28.3	28.3	105.0	405.4	7.65	7.00	1.09	1.00	4.76	4.76	4.70
	Mid-Ebb	WMS-1N	CLOUDY	11:15	7.2	М	3	2	8.09	8.09	32.17	32.17	28.3	28.3	105.1	105.1	7.66	7.66	1.08	1.09	4.79	4.79	4.78
		WMS-1N				В	6	1	8.07	8.07	32.22	32.22	28.3	28.3	102.7	102.8	7.58	7.59	1.08	1.08	6.61	6.61	6.59
		WMS-1N				В	0	2	8.07	6.07	32.22	32.22	28.3	20.3	102.8	102.0	7.59	7.59	1.07	1.06	6.57	6.57	0.59
		WMS-2N				S	1	1	8.08	8.08	32.15	32.15	28.3	28.3	105.9	105.9	7.67	7.68	1.22	1.22	7.25	7.25	7.24
		WMS-2N				S	I	2	8.08	0.00	32.15	32.10	28.3	20.3	105.8	105.9	7.68	7.00	1.22	1.22	7.22	7.22	1.24
	Ebb	WMS-2N	CLOUDY	11:00	4	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid-Ebb	WMS-2N	CLOUDY	11.00	4	М	NA	2	NA	NA	NA	NA NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
		WMS-2N				В	2	1	8.09	8.09	32.19	32.19	28.2	20.0	103.9	102.0	7.61	7.61	1.52	1.53	6.86	6.86	6.84
		WMS-2N				В	3	2	8.09	6.09	32.19	32.19	28.2	28.2	103.8	103.9	7.60	7.01	1.53	1.55	6.81	6.81	6.84
Γ		WMS3				S	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
		WMS3				S	INA	2	NA	NA	NA	INA	NA	NA	NA	INA	NA	INA	NA	INA	NA	NA	INA
	Mid-Ebb	WMS3	CLOUDY	10:30	3	М	1.5	1	8.13	8.13	32.24	32.24	28.2	28.2	104.7	104.8	7.63	7.64	0.35	0.35	7.41	7.41	7.39
	Mid-	WMS3	CLOUDT	10.50	5	М	1.5	2	8.13	0.15	32.24	32.24	28.2	20.2	104.8	104.0	7.64	7.04	0.35	0.55	7.36	7.36	7.59
		WMS3				В	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
		WMS3				В	110	2	NA	NA	NA		NA	INA.	NA	INA.	NA		NA	INA.	NA	NA	
		WMS4				S	1	1	8.14	8.14	32.26	32.26	28.2	28.2	110.5	110.6	7.82	7.83	0.43	0.43	5.62	5.62	5.63
		WMS4				S	I	2	8.14	0.14	32.26	52.20	28.2	20.2	110.6	110.0	7.83	7.05	0.43	0.43	5.63	5.63	5.05
	Mid-Ebb	WMS4	CLOUDY	9:45	4.3	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid	WMS4	CLOODI	3.45	4.5	М	IN/A	2	NA	NA	NA	IN/A	NA	na	NA	IN/A	NA		NA	INA.	NA	NA	
		WMS4				В	3	1	8.14	8.14	32.26	32.26	28.2	28.2	108.0	108.1	7.76	7.77	0.38	0.38	4.89	4.89	4.88
_		WMS4				В		2	8.14	0.14	32.26	52.20	28.2	20.2	108.1	100.1	7.77	1.11	0.38	0.00	4.86	4.86	4.00
		WMS5				S	1	1	8.11	8.11	32.26	32.26	28.2	28.2	107.8	107.8	7.74	7.75	0.28	0.28	11.53	11.53	11.50
	-	WMS5				S		2	8.11	0.11	32.26	02.20	28.2	20.2	107.7	101.0	7.75	1.10	0.28	0.20	11.47	11.47	
	Mid-Ebb	WMS5	CLOUDY	10:00	4.4	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid	WMS5	020001	10.00		М		2	NA		NA		NA		NA		NA		NA		NA	NA	
		WMS5				В	3	1	8.12	8.12	32.26	32.26	28.2	28.2	105.4	105.5	7.67	7.68	0.40	0.40	5.63	5.63	5.65
		WMS5				В	Ŭ	2	8.12	0.12	32.26	02.20	28.2	20.2	105.5	100.0	7.68	1.00	0.40	0.10	5.66	5.66	0.00
		WMS6				S	1	1	8.12	8.12	32.26	32.26	28.2	28.2	106.5	106.6	7.71	7.72	0.30	0.30	4.89	4.89	4.92
	~	WMS6				S		2	8.12	0.12	32.26		28.2	-9.2	106.7		7.72		0.30	0.00	4.95	4.95	
	Mid-Ebb	WMS6	CLOUDY	10:15	4.4	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid	WMS6	010001	.0.10		М		2	NA		NA		NA		NA		NA		NA		NA	NA	
		WMS6				В	3	1	8.12	8.12	32.26	32.26	28.2	28.2	104.3	104.3	7.63	7.64	0.38	0.38	5.48	5.48	5.46
	<u> </u>	WMS6				В		2	8.12	0.12	32.26	52.20	28.2	20.2	104.2	.04.0	7.64	7.04	0.38	0.00	5.44	5.44	0.40
	Mid-Ebb	12	CLOUDY	9:15	16	S	1	1	8.17	8.17	32.32	32.32	28.3	28.3	110.9	111.0	7.85	7.85	0.70	0.70	7.56	7.56	7.58
	Mid	12		5.15	10	S	·	2	8.17	0.17	32.32	02.02	28.3	20.0	111.0	111.0	7.84	1.00	0.69	0.70	7.59	7.59	1.00



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-21
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	12				м		1	8.17		32.32		28.3		108.3		7.76		0.55		8.20	8.20	1
	12				М	8	2	8.17	8.17	32.32	32.32	28.3	28.3	108.4	108.4	7.77	7.77	0.54	0.55	8.26	8.26	8.23
	12				В		1	8.17		32.32		28.3		105.7		7.68		0.63		7.99	7.99	
	12				В	15	2	8.17	8.17	32.32	32.32	28.3	28.3	105.8	105.8	7.69	7.69	0.64	0.64	7.95	7.95	7.97
	C2				S		1	8.08		32.17		28.3		106.0		7.68		1.27		13.26	13.26	<u> </u>
	C2				S	1	2	8.08	8.08	32.17	32.17	28.3	28.3	106.1	106.1	7.67	7.68	1.29	1.28	13.29	13.29	13.28
qq	C2				M		1	NA		NA		NA		NA		NA		NA		NA	NA	
Mid-Ebb	C2	CLOUDY	10:45	3.9	M	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
Σ	C2 C2				В		1	8.08		32.20		28.2		104.2		7.60		1.55		13.67	13.67	
					В	3	2	8.08	8.08	32.20	32.20	28.2	28.2	104.2	104.2	7.61	7.61	1.58	1.57	13.70	13.70	13.69
	C2																					
	C3				S	1	1	8.13	8.13	32.25	32.25	28.2	28.2	109.3	109.3	7.74	7.74	0.61	0.61	14.03	14.03	14.02
Q	C3				S		2	8.13		32.25		28.2		109.2		7.73		0.61		14.00	14.00	<b> </b>
Mid-Eb	C3	CLOUDY	9:30	14	M	7	1	8.13	8.13	32.25	32.25	28.2	28.2	106.8	106.9	7.70	7.70	0.58	0.58	12.74	12.74	12.72
Ř	C3				M		2	8.13		32.25		28.2		106.9		7.69		0.58		12.69	12.69	<b> </b>
	C3				В	13	1	8.13	8.13	32.25	32.25	28.2	28.2	104.3	104.4	7.64	7.65	0.60	0.60	13.80	13.80	13.77
	C3				В		2	8.13		32.25		28.2		104.4		7.65		0.60		13.74	13.74	<b> </b>
	WMS-1N				S	1	1	8.02	8.02	31.88	31.88	28.4	28.4	108.3	108.4	7.76	7.77	0.87	0.88	5.86	5.86	5.85
ō	WMS-1N				S		2	8.02		31.88		28.4		108.4		7.77		0.88		5.83	5.83	<b> </b>
Floo	WMS-1N	CLOUDY	17:00	7.5	М	3	1	8.03	8.03	32.08	32.08	28.4	28.4	105.8	105.9	7.68	7.68	1.08	1.09	7.45	7.45	7.47
Mid-Floo	WMS-1N				М		2	8.03		32.08		28.4		105.9		7.68		1.09		7.48	7.48	L
	WMS-1N				В	7	1	8.01	8.01	32.12	32.12	28.4	28.4	103.7	103.8	7.61	7.62	1.06	1.07	8.25	8.25	8.24
	WMS-1N				В		2	8.01	0.01	32.12	02.12	28.4	20.4	103.8	100.0	7.62	1.02	1.07	1.07	8.22	8.22	0.24
	WMS-2N				S	1	1	8.01	8.02	32.03	32.03	28.4	28.4	106.9	107.0	7.70	7.71	1.29	1.30	776	776	7.77
	WMS-2N				S	I	2	8.02	0.02	32.03	32.03	28.4	20.4	107.0	107.0	7.71	7.71	1.30	1.50	7.77	7.77	1.11
	WMS-2N		40.45	4.5	М	NIA	1	NA	NA	NA	NIA	NA	NIA	NA	NIA	NA	NA	NA	NIA	NA	NA	NIA
Mid-Floo	WMS-2N	CLOUDY	16:45	4.5	М	NA	2	NA	NA NA	NA	NA	NA	NA	NA	NA	NA	INA	NA	NA	NA	NA	NA
~	WMS-2N				В	4	1	8.03	0.00	32.07	00.07	28.3	00.0	104.7	404.0	7.63	7.04	1.55	4.50	6.66	6.66	0.00
	WMS-2N				В	4	2	8.03	8.03	32.07	32.07	28.3	28.3	104.8	104.8	7.64	7.64	1.56	1.56	6.66	6.66	6.66
	WMS3				S		1	NA		NA		NA		NA		NA		NA		NA	NA	
	WMS3				S	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
-Flood	WMS3				М		1	8.07		32.12		28.3		105.8		7.66		0.37		10.26	10.26	
Mid-F	WMS3	CLOUDY	16:30	3.2	М	1.5	2	8.07	8.07	32.12	32.12	28.3	28.3	105.9	105.9	7.67	7.67	0.38	0.38	10.20	10.20	10.23
2	WMS3				В		1	NA		NA		NA		NA		NA		NA		NA	NA	
	WMS3				В	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	WMS4				S		1	8.08		32.14		28.3		111.4		7.85		0.47		8.02	8.02	
	WMS4				S	1	2	8.08	8.08	32.14	32.14	28.3	28.3	111.3	111.4	7.86	7.86	0.46	0.47	7.96	7.96	7.99
poo	WMS4				м		1	NA		NA		NA		NA		NA		NA		NA	NA	
Mid-Flood	WMS4	CLOUDY	15:45	4.5	М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
Σ	WMS4				В		1	8.08		32.14		28.3		109.0		7.78		0.37		5.59	5.59	
	WMS4				В	4	2	8.08	8.08	32.14	32.14	28.3	28.3	109.1	109.1	7.79	7.79	0.37	0.37	5.58	5.58	5.59
σ	WMS5				S		1	8.05		32.14		28.3		108.8		7.78		0.35		4.78	4.78	
Flood		CLOUDY	16:00	5	S S	1	2	8.05	8.05	32.14	32.14	28.3	28.3	108.9	108.9	7.77	7.78	0.36	0.36	4.73	4.73	4.76
Mid-F	WMS5		10.00	5	M	NA	1	NA NA	NA	NA	NA	28.3 NA	NA	NA	NA	NA	NA	0.36 NA	NA	4.73 NA	4.73 NA	NA
2	CONING				IVI	INA		INA	INA	INA	INA	INA	INA	INA	INA	INA	INA	INA	INA	INA	INA	INA



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-22
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	WMS5				м		2	NA		NA		NA		NA		NA		NA		NA	NA	
	WMS5				В		1	8.06	0.00	32.14	22.4.4	28.3	00.0	106.3	400.4	7.70	7.74	0.41	0.40	6.02	6.02	6.04
	WMS5				В	4	2	8.06	8.06	32.14	32.14	28.3	28.3	106.4	106.4	7.71	7.71	0.42	0.42	6.00	6.00	6.01
	WMS6				S		1	8.06	0.00	32.14	32.14	28.3	28.3	107.7	107.7	7.74	7 75	0.38	0.00	7.23	7.23	7.40
_	WMS6				S		2	8.06	8.06	32.14	32.14	28.3	28.3	107.6	107.7	7.75	7.75	0.34	0.36	7.15	7.15	7.19
	WMS6		40.45	_	М	NA	1	NA	NIA	NA	NA	NA	NIA	NA	NIA	NA	NIA	NA	NIA	NA	NA	NA
Mid-Flood	WMS6	CLOUDY	16:15	5	М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
~	WMS6				В		1	8.06	0.00	32.13	22.42	28.3	00.0	105.1	405.0	7.66	7.07	0.37	0.07	6.42	6.42	6.40
	WMS6				В	4	2	8.06	8.06	32.13	32.13	28.3	28.3	105.2	105.2	7.67	7.67	0.37	0.37	6.38	6.38	6.40
	l1				S		1	8.11	0.44	32.23	22.22	28.4	00.4	110.0	110.1	7.77	7 77	0.73	0.70	9.68	9.68	0.00
_	l1				S		2	8.11	8.11	32.23	32.23	28.4	28.4	110.1	110.1	7.76	7.77	0.72	0.73	9.63	9.63	9.66
Mid-Flood	11		45.00	45	М	7	1	8.11	8.11	32.23	32.23	28.4	28.4	107.6	107.7	7.72	7.73	0.56	0.57	8.68	8.68	8.71
Aid-F	11	CLOUDY	15:30	15	М		2	8.11	0.11	32.23	32.23	28.4	20.4	107.7	107.7	7.73	1.13	0.57	0.57	8.74	8.74	0.71
~	l1				В	11	1	8.11	0.44	32.23	22.22	28.4	00.4	105.2	405.2	7.67	7.00	0.67	0.07	9.26	9.26	0.00
	11				В	14	2	8.11	8.11	32.23	32.23	28.4	28.4	105.3	105.3	7.68	7.68	0.66	0.67	9.25	9.25	9.26
	C1				S	1	1	8.07	0.07	32.16	32.16	28.3	28.3	111.8	111.0	7.88	7.00	0.63	0.04	15.10	15.10	45.07
_	C1				S		2	8.07	8.07	32.16	32.16	28.3	28.3	111.9	111.9	7.87	7.88	0.64	0.64	15.03	15.03	15.07
	C1		45.45	47	М	0	1	8.07	9.07	32.16	22.46	28.3	20.2	109.2	100.2	7.80	7.90	0.59	0.60	11.94	11.94	11.06
Mid-Flood	C1	CLOUDY	15:15	17	М	8	2	8.07	8.07	32.16	32.16	28.3	28.3	109.3	109.3	7.79	7.80	0.60	0.60	11.98	11.98	11.96
	C1	]			В	16	1	8.07	9.07	32.16	22.46	28.4	29.4	106.6	106.6	7.71	7.72	0.62	0.64	16.00	16.00	15.07
	C1			B 16	2	8.07	8.07	32.16	32.16	28.4	28.4	106.5	106.6	7.72	1.12	0.65	0.64	15.93	15.93	15.97		



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-23
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	ode				Water									In-situ Me	asurement						Lab	oratory Anal	ysis
Date	Tidal Mode	Monitoring Location	Weather	Time	Depth (m)	Monitoring Level	Monitoring Level (m)	Replicate	p	Н	Salinit	y (ppt)	Tempera	ature (°C)	DO Satur	ration (%)	DO (r	mg/L)	Turbidit	ty (NTU)		pended solids - 105 (°C), m	
	I								Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value		Ave.
10/18/2024		WMS-1N				S	1	1	8.08	8.08	31.98	31.98	28.0	28.0	111.0	111.0	7.85	7.86	1.09	1.09	7.42	7.42	7.43
		WMS-1N				S	I	2	8.08	0.00	31.98	31.90	28.0	20.0	110.9	111.0	7.86	7.00	1.08	1.09	7.44	7.44	7.43
	Ebb	WMS-1N		11.00	7	М	3	1	8.10	8.10	32.15	32.15	28.0	28.0	108.4	108.5	7.76	7.76	0.84	0.84	11.87	11.87	11.05
	Mid-Ebb	WMS-1N	SUNNY	11:00		М	3	2	8.10	0.10	32.15	32.15	28.0	20.0	108.5	106.5	7.75	7.70	0.84	0.64	11.83	11.83	11.85
		WMS-1N				В	6	1	8.10	8.10	32.19	32.19	28.0	28.0	105.0	105.1	7.63	7.64	1.08	1.08	6.65	6.65	6.64
		WMS-1N				В	0	2	8.10	0.10	32.19	52.19	28.0	20.0	105.1	105.1	7.64	7.04	1.08	1.00	6.63	6.63	0.04
		WMS-2N				S	1	1	8.11	8.11	32.12	32.12	28.0	28.0	108.6	108.7	7.73	7.74	1.38	1.38	5.63	5.63	5.65
		WMS-2N				S	I	2	8.11	0.11	32.12	32.12	28.0	20.0	108.7	100.7	7.74	7.74	1.38	1.50	5.66	5.66	5.05
	Ebb	WMS-2N	SUNNY	10:45	4	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid-Ebb	WMS-2N	SUNNT	10.45	4	М	NА	2	NA	INA.	NA	INA.	NA	INA.	NA	INA	NA	INA	NA	INA	NA	NA	NA .
		WMS-2N				В	3	1	8.12	8.12	32.24	32.24	28.0	28.0	105.3	105.4	7.64	7.65	1.31	1.31	4.86	4.86	4.87
		WMS-2N				В	5	2	8.12	0.12	32.24	32.24	28.0	20.0	105.4	105.4	7.65	7.05	1.31	1.51	4.88	4.88	4.07
		WMS3				S	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
		WMS3				S	INA	2	NA	INA .	NA	INA.	NA	INA.	NA	INA	NA	INA	NA	INA	NA	NA	NA .
	Mid-Ebb	WMS3	SUNNY	10:15	2.8	М	1.5	1	8.16	8.16	32.27	32.27	28.1	28.1	107.0	107.1	7.69	7.69	0.25	0.25	7.89	7.89	7.93
	Mid-	WMS3	SONNT	10.15	2.0	М	1.0	2	8.16	0.10	32.27	52.21	28.1	20.1	107.1	107.1	7.68	7.00	0.25	0.20	7.96	7.96	1.55
		WMS3				В	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
		WMS3				В	IN/A	2	NA		NA		NA		NA	INA.	NA		NA		NA	NA	
		WMS4				S	1	1	8.13	8.13	32.26	32.26	28.1	28.1	112.3	112.4	7.86	7.87	0.48	0.48	6.96	6.96	6.99
		WMS4				S	1	2	8.13	0.10	32.26	52.20	28.1	20.1	112.4	112.4	7.87	1.01	0.48	0.40	7.01	7.01	0.00
	Mid-Ebb	WMS4	SUNNY	9:30	4.2	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid	WMS4	CONNT	5.50	7.2	М	IN/A	2	NA	11/4	NA	11/3	NA	11/4	NA	IN/A	NA	11/2	NA	11/4	NA	NA	
		WMS4				В	3	1	8.13	8.13	32.26	32.26	28.1	28.1	109.8	109.8	7.79	7.79	0.58	0.58	5.23	5.23	5.23
		WMS4				В	0	2	8.13	0.10	32.26	02.20	28.1	20.1	109.7	100.0	7.78	1.10	0.58	0.00	5.22	5.22	0.20
		WMS5				S	1	1	8.14	8.14	32.27	32.27	28.1	28.1	110.3	110.4	7.81	7.81	0.46	0.46	7.04	7.04	7.06
	~	WMS5	4			S	•	2	8.14		32.27		28.1		110.4		7.80		0.46		7.08	7.08	
	Mid-Ebb	WMS5	SUNNY	9:45	4.5	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid	WMS5	-	0110		М		2	NA		NA		NA		NA		NA		NA		NA	NA	ļ
		WMS5				В	4	1	8.14	8.14	32.27	32.27	28.1	28.1	107.3	107.4	7.76	7.77	0.48	0.48	5.59	5.59	5.61
		WMS5				В	-	2	8.14		32.27		28.1		107.4		7.77		0.48		5.63	5.63	
		WMS6	4			S	1	1	8.14	8.14	32.27	32.27	28.2	28.2	107.6	107.7	7.73	7.74	0.49	0.49	7.22	7.22	7.20
	0	WMS6	4			S	-	2	8.14		32.27		28.2		107.7		7.74		0.49		7.17	7.17	
	Mid-Ebb	WMS6	SUNNY	10:00	4.5	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mia	WMS6				М		2	NA		NA		NA		NA		NA		NA		NA	NA	<b> </b>
		WMS6	4			В	4	1	8.14	8.14	32.27	32.27	28.2	28.2	106.1	106.2	7.69	7.69	0.52	0.52	6.86	6.86	6.90
		WMS6				В	-	2	8.14		32.27		28.2		106.2		7.68		0.52		6.93	6.93	
	Mid - Ebb	12	SUNNY	9:00	16	S	1	1	8.14	8.14	32.30	32.30	28.1	28.1	112.3	112.4	7.87	7.87	0.49	0.49	8.58	8.58	8.55



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-24
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

N         N		12				s		2	8.14		32.30		28.1		112.4		7.86		0.48		8.51	8.51	'
i         i																							
Image: border in the start in the							8			8.14		32.30		28.1		110.2		7.78		0.44			8.43
n         n								1															
Q         Q							15	2		8.12		32.28		28.1		107.3		7.66		0.88			8.85
							1			8.12		32.12		28.0		108.9		7.75		1.33			15.28
Image: cond biase in the section of the sec	ą																						
Image: cond biase in the section of the sec			SUNNY	10:30	3.9		NA			NA		NA		NA		NA		NA		NA			NA
i c c c c c c c c c c c c c c c c c c c	Σ																						
0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0							3			8.12		32.24		28.0		105.6		7.66		1.28			17.23
C1         C2         C1         C2         C1         C2         C1         C2         C2 <thc< th="">         C2         <thc2< th="">         C2<td></td><td></td><td></td><td></td><td></td><td></td><td></td><td>2</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></thc2<></thc<>								2															
Image: regr							1	1		8.11		32.24		28.1		111.7		7.85		0.45			16.67
No. 2         SUMP         9:5         1/4         M         7         2         8:1         0:1         2:2:4         2:2:4         2:1         0:1         0:2:3         0:2:4         0	ą																						
2         2 </td <td></td> <td></td> <td>SUNNY</td> <td>9:15</td> <td>14</td> <td></td> <td>7</td> <td></td> <td></td> <td>8.11</td> <td></td> <td>32.24</td> <td></td> <td>28.1</td> <td></td> <td>109.3</td> <td></td> <td>7.73</td> <td></td> <td>0.42</td> <td></td> <td></td> <td>13.41</td>			SUNNY	9:15	14		7			8.11		32.24		28.1		109.3		7.73		0.42			13.41
Image: constraint of	Ä																		-				<u> </u>
VMS-1N VMS-1N VMS-1N VMS-1N         VMS-1N VMS-N VMS-N         VMS-1N VMS-N         VMS-N VMS-N         VMS-N VMS-N </td <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>13</td> <td></td> <td></td> <td>8.10</td> <td></td> <td>32.23</td> <td></td> <td>28.1</td> <td></td> <td>106.1</td> <td></td> <td>7.64</td> <td></td> <td>0.84</td> <td></td> <td></td> <td>17.05</td>							13			8.10		32.23		28.1		106.1		7.64		0.84			17.05
VMS-1N (VMS-1N) (VMS-1N) (VMS-1N)         VMS-1N (VMS-1N) (VMS-1N)         VMS-1N (VMS-1N) (VMS-1N)         VMS-1N (VMS-1N) (VMS-1N)         VMS-1N (VMS-1N) (VMS-1N)         VMS-1N (VMS-1N) (VMS-1N)         VMS-1N (VMS-1N)         VMS-1N (VMS-2N)         VMS-1N (VMS-2N)        VMS-1N (VMS-2N								2															
MMS-1N WKS-1N WKS-1N WKS-1N         VMS-N WKS-1N         VMS-N WKS-1N         VMS-N WKS-1N         VMS-N WKS-1N         VMS-N WKS-1N         VMS-N WKS-1N         VMS-N WKS-1N         VMS-N WKS-1N         MMS-N WKS-1N         MMS-N WKS-1N        MMS-N WKS-1N <th< td=""><td></td><td></td><td></td><td></td><td></td><td></td><td>1</td><td>1</td><td></td><td>8.14</td><td></td><td>32.10</td><td></td><td>28.1</td><td></td><td>110.6</td><td></td><td>7.84</td><td></td><td>1.08</td><td></td><td></td><td>8.99</td></th<>							1	1		8.14		32.10		28.1		110.6		7.84		1.08			8.99
WMS-IN         WMS-IN         ID         B         C         B         C         B         C         B         C         B         C         B         C         B         C         B         C         B         C         B         C         B         C         B         C         B         C         B         C <thc< th="">         C         <thc< th="">         C         <thc< th="">        C         C         <thc< <="" td=""><td>pg</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></thc<></thc<></thc<></thc<>	pg																						
WMS-IN         WMS-IN         ID         B         C         B         C         B         C         B         C         B         C         B         C         B         C         B         C         B         C         B         C         B         C         B         C         B         C         B         C <thc< th="">         C         <thc< th="">         C         <thc< th="">        C         C         <thc< <="" td=""><td>- Floo</td><td></td><td>SUNNY</td><td>15:45</td><td>7.4</td><td></td><td>3</td><td></td><td></td><td>8.16</td><td></td><td>32.27</td><td></td><td>28.1</td><td></td><td>108.1</td><td></td><td>7.77</td><td></td><td>0.89</td><td></td><td></td><td>9.53</td></thc<></thc<></thc<></thc<>	- Floo		SUNNY	15:45	7.4		3			8.16		32.27		28.1		108.1		7.77		0.89			9.53
$ \begin{array}{                                    $	Mid							2															<u> </u>
WMS-N         M         A         NA							6	1		8.16		32.30		28.1		105.4		7.65		1.08			11.77
$ \begin{array}{ c c c c c c c c c c c c c c c c c c c$								2	8.16		32.30		28.1		105.4		7.65				11.77	11.77	ļ'
VMMS-2N         VMMS-2N <t< td=""><td></td><td>WMS-2N</td><td></td><td></td><td></td><td>S</td><td>1</td><td>1</td><td>8.17</td><td>8.17</td><td>32.24</td><td>32.24</td><td>28.1</td><td>28.1</td><td>109.8</td><td>109.8</td><td>7.76</td><td>7.77</td><td>1.30</td><td>1.30</td><td>7.47</td><td>7.47</td><td>7.45</td></t<>		WMS-2N				S	1	1	8.17	8.17	32.24	32.24	28.1	28.1	109.8	109.8	7.76	7.77	1.30	1.30	7.47	7.47	7.45
WMS-2H         WMS-2H         WMS-2H         WMS-2H         WMS-2H         WMS-2H         WMS-2H         WMS-2H         B         A         B	σ	WMS-2N				S		2	8.17		32.24		28.1	-	109.7		7.77		1.30		7.43	7.43	
WMS-2H         WMS-2H         WMS-2H         WMS-2H         WMS-2H         WMS-2H         WMS-2H         WMS-2H         B         A         B	Floo	WMS-2N	SUNNY	15:30	4.5	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
WMS2N         WMS2N         Image: Constraint of the state s	Mid-	WMS-2N			_	M		2	NA		NA		NA		NA		NA				NA	NA	
VMS2N         V         C         B         C         C         B         C         C         B         C <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>4</td> <td>1</td> <td></td> <td>8.18</td> <td></td> <td>32.35</td> <td></td> <td>28.1</td> <td></td> <td>106.5</td> <td></td> <td>7.68</td> <td></td> <td>1.26</td> <td></td> <td></td> <td>6.87</td>							4	1		8.18		32.35		28.1		106.5		7.68		1.26			6.87
$ \begin{array}{ c c c c c c c c c c c c c c c c c c c$		WMS-2N				В		2	8.18		32.35		28.1		106.5		7.68		1.26		6.88	6.88	
$ \begin{array}{ c c c c c c c c c c c c c c c c c c c$		WMS3				S	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
$ \begin{array}{ c c c c c c c c c c c c c c c c c c c$	σ	WMS3				S		2	NA		NA		NA	10.	NA		NA		NA		NA	NA	
$ \begin{array}{ c c c c c c c c c c c c c c c c c c c$	Floo	WMS3	SUNNY	15.15	3	М	1.5	1	8.22	8.22	32.38	32.38	28.2	28.2	107.9	108.0	7.72	7 72	0.29	0.29	7.54	7.54	7 53
$ \begin{array}{ c c c c c c c c c c c c c c c c c c c$	Mid-	WMS3	001111	10.10		М		2	8.22	0.22	32.38	02.00	28.2	20.2	108.0	100.0	7.71		0.28	0.20	7.51	7.51	1.00
VMNS3         V         V         B         2         NA         NA<		WMS3				В	ΝΔ	1	NA	NΔ	NA	NΔ	NA	ΝΔ	NA	NΔ	NA	ΝΔ	NA	ΝΔ	NA	NA	ΝΔ
$ \begin{array}{ c c c c c c c c c c c c c c c c c c c$		WMS3				В		2	NA		NA	na.	NA		NA		NA	11/2	NA		NA	NA	
$ \begin{array}{ c c c c c c c c c c c c c c c c c c c$		WMS4				S	1	1	8.19	8 10	32.38	32.39	28.2	28.2	113.4	113.5	7.89	7 85	0.50	0.50	5.86	5.86	5 00
$ \begin{array}{ c c c c c c c c c c c c c c c c c c c$		WMS4				S		2	8.19	0.19	32.38	52.50	28.2	20.2	113.5	113.5	7.80	1.00	0.50	0.50	5.93	5.93	5.30
$ \begin{array}{ c c c c c c c c c c c c c c c c c c c$		WMS4		14.20	15	М	ΝΑ	1	NA	ΝΔ	NA	NA	NA	NA	NA	NA	NA	ΝΔ	NA	ΝΑ	NA	NA	ΝΑ
$ \begin{array}{ c c c c c c c c c c c c c c c c c c c$	Mid-F	WMS4	SUIVINT	14.30	4.0	М		2	NA	IN/A	NA	11/4	NA	11/1	NA		NA		NA		NA	NA	
WMS4     B     2     8.19     32.38     28.2     111.0     7.82     0.60     6.21     6.21       Umber of boot     WMS5     SUNNY     14:45     5     1     8.20     32.38     28.2     111.0     7.82     0.60     6.21     6.21       Umber of boot     WMS5     SUNNY     14:45     5     1     1     8.20     32.38     28.2     111.4     111.5     7.84     0.48     0.48     2.59     2.60		WMS4				В		1	8.19	0 10	32.38	20.00	28.2	20.0	110.9	111.0	7.81	7 00	0.59	0.60	6.24	6.24	6.00
l ≅ ŏ SUNNY   14:45   5 1		WMS4				В	4	2	8.19	8.19	32.38	32.38	28.2	28.2	111.0	111.0	7.82	1.82	0.60	0.00	6.21	6.21	0.23
$\Xi_{\mu}^{O}$ WMS5 SUINIX 14:45 5 5 1 2 8:20 32.38 32.38 28.2 111.5 7.83 7.84 0.48 2.60 2.60 2.60	-p po	WMS5	OLININ'N	14.45	-	S		1	8.20	0.00	32.38	20.00	28.2	00.0	111.4	444 5	7.84	7.04	0.48	0.40	2.59	2.59	0.00
	FIO	WMS5	SUNNY	14:45	5	S		2	8.20	8.20	32.38	32.38	28.2	28.2	111.5	111.5	7.83	7.84	0.48	0.48	2.61	2.61	2.60

SGS	

EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-25
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	WMS5				м		1	NA		NA	NA	NA	NA	NA	NA	NA		NA		NA	NA	NIA
	WMS5				М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	WMS5				В		1	8.20	0.00	32.38	00.00	28.2	00.0	108.5	400.0	7.80	7.00	0.52	0.54	3.04	3.04	0.00
	WMS5				В	4	2	8.20	8.20	32.38	32.38	28.2	28.2	108.6	108.6	7.79	7.80	0.50	0.51	3.00	3.00	3.02
	WMS6				S		1	8.20	0.00	32.38	22.20	28.2	00.0	108.7	400.0	7.76	7 77	0.50	0.54	6.53	6.53	0.54
_	WMS6				S		2	8.20	8.20	32.38	32.38	28.2	28.2	108.8	108.8	7.77	7.77	0.51	0.51	6.55	6.55	6.54
lood	WMS6	<u></u>			М		1	NA		NA		NA		NA		NA		NA		NA	NA	
Mid-Floo	WMS6	SUNNY	15:00	5	М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
2	WMS6				В		1	8.20		32.38		28.3		107.2		7.71		0.54		7.77	7.77	
	WMS6				В	4	2	8.20	8.20	32.38	32.38	28.3	28.3	107.3	107.3	7.72	7.72	0.55	0.55	7.75	7.75	7.76
	l1				S		1	8.20		32.42		28.2		113.0		7.88		0.51		8.08	8.08	
	l1				S	1	2	8.20	8.20	32.42	32.42	28.2	28.2	112.9	113.0	7.89	7.89	0.52	0.52	8.11	8.11	8.10
pool	l1				м		1	8.20		32.42		28.2		110.7		7.80		0.45		7.45	7.45	
Mid-Floo	l1	SUNNY	14:15	15	м	7	2	8.20	8.20	32.42	32.42	28.2	28.2	110.8	110.8	7.79	7.80	0.44	0.45	7.53	7.53	7.49
Σ	l1				В		1	8.18		32.40		28.2		107.0		7.66		0.89		7.99	7.99	
	l1				В	14	2	8.18	8.18	32.40	32.40	28.2	28.2	106.9	107.0	7.65	7.66	0.90	0.90	8.02	8.02	8.01
	C1				S		1	8.18		32.35		28.1		113.4		7.90		0.47		19.42	19.42	
	C1				S	1	2	8.18	8.18	32.35	32.35	28.1	28.1	113.5	113.5	7.89	7.90	0.46	0.47	19.53	19.53	19.48
poo	C1				М		1	8.18		32.35		28.2		111.1		7.81		0.43		17.01	17.01	
Mid-Floo	C1	SUNNY	14:00	17	М	8	2	8.18	8.18	32.35	32.35	28.2	28.2	111.2	111.2	7.80	7.81	0.43	0.43	16.96	16.96	16.99
Σ	C1				В		1	8.16		32.35		28.2		108.3		7.69		0.85		17.44	17.44	
	C1				B	16	2	8.16 8.16	32.35	32.35	32.35 28.2 28.2	28.2	108.4	108.4	7.68	7.69	0.86	0.86	17.40	17.40	17.42	



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-26
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	ode				Water			itoring Paplicate									Lab	oratory Anal	ysis				
Date	Tidal Mode	Monitoring Location	Weather	Time	Depth (m)	Monitoring Level	Monitoring Level (m)	Replicate	р	Н	Salinit	y (ppt)	Tempera	ature (°C)	DO Satur	ation (%)	DO (I	mg/L)	Turbidit	ty (NTU)		spended solids 3 - 105 (°C), m	
	F								Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value		Ave.
10/21/2024		WMS-1N				S		1	8.08	0.00	32.07	00.07	28.2		108.9	400.0	7.80	7.04	1.10		7.98	7.98	
		WMS-1N	-			S		2	8.08	8.08	32.07	32.07	28.2	28.2	109.0	109.0	7.81	7.81	1.09	1.10	8.06	8.06	8.02
	Mid-Ebb	WMS-1N		10:00	<u> </u>	М	2	1	8.07	8.07	32.06	32.06	28.0	28.0	105.6	105.7	7.71	7.72	1.09	1.10	8.59	8.59	8.63
	Mid-	WMS-1N	SUNNY	16:00	6.8	М	3	2	8.07	8.07	32.06	32.06	28.0	28.0	105.7	105.7	7.72	1.12	1.10	1.10	8.66	8.66	8.63
		WMS-1N				В	6	1	8.08	8.08	32.09	32.09	28.0	28.0	102.4	102.5	7.60	7.61	1.07	1.08	9.14	9.14	9.13
		WMS-1N				В	0	2	8.08	0.00	32.09	32.09	28.0	20.0	102.5	102.5	7.61	7.01	1.08	1.00	9.11	9.11	9.13
		WMS-2N				S	1	1	8.08	8.08	32.15	32.15	28.2	28.2	106.3	106.4	7.72	7.73	1.00	1.00	8.42	8.42	8.43
		WMS-2N				S	I	2	8.08	0.00	32.15	52.15	28.2	20.2	106.4	100.4	7.73	1.15	1.00	1.00	8.44	8.44	0.43
	Mid-Ebb	WMS-2N	SUNNY	15:45	2.0	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid-	WMS-2N	SUNNY	15.45	3.8	М	INA	2	NA	NA NA	NA	INA	NA	NA NA	NA	INA	NA	INA	NA	INA	NA	NA	NA
		WMS-2N				В	3	1	8.08	8.08	32.15	32.15	28.1	28.1	103.7	103.8	7.64	7.65	1.57	1.57	8.56	8.56	8.55
		WMS-2N				В	5	2	8.08	0.00	32.15	52.15	28.1	20.1	103.8	103.0	7.65	7.05	1.57	1.57	8.53	8.53	6.55
		WMS3				S	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
		WMS3				S	NA	2	NA	NA	NA	NA	NA	NA NA	NA	INA	NA	NA NA	NA	NA	NA	NA	NA
	Ebb	WMS3		45.45		М	1 5	1	8.14	8.14	32.22	32.22	28.3	28.3	103.8	103.9	7.67	7.67	0.92	0.92	11.48	11.48	11.46
	Mid-Ebb	WMS3	SUNNY	15:15	2.3	М	1.5	2	8.14	0.14	32.22	32.22	28.3	20.3	103.9	103.9	7.66	7.07	0.92	0.92	11.44	11.44	11.40
		WMS3	-			В	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
		WMS3				В	NA	2	NA	NA	NA	NA	NA	NA	NA	INA	NA	INA	NA	INA	NA	NA	NA
		WMS4				S	1	1	8.13	8.13	32.21	32.21	28.3	28.3	108.9	108.9	7.80	7.81	0.84	0.84	7.43	7.43	7.44
		WMS4				S	I	2	8.13	0.15	32.21	52.21	28.3	20.5	108.8	100.9	7.81	7.01	0.84	0.04	7.44	7.44	7.44
	Mid-Ebb	WMS4	SUNNY	14:30	3.5	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid-	WMS4	SUNNY	14.30	3.5	М	INA	2	NA	NA	NA	INA	NA	INA	NA	INA	NA	INA	NA	INA	NA	NA	NA .
		WMS4				В	3	1	8.13	8.13	32.21	32.21	28.3	28.3	106.7	106.8	7.74	7.75	0.96	0.96	6.56	6.56	6.60
		WMS4				В	3	2	8.13	0.13	32.21	32.21	28.3	20.3	106.8	100.0	7.75	7.75	0.96	0.90	6.63	6.63	0.00
		WMS5				S	1	1	8.13	8.13	32.22	32.22	28.4	28.4	106.7	106.8	7.75	7.75	1.02	1.02	7.17	7.17	7.15
		WMS5	_			S	1	2	8.13	0.15	32.22	32.22	28.4	20.4	106.8	100.8	7.74	1.15	1.02	1.02	7.13	7.13	7.15
	Mid-Ebb	WMS5	SUNNY	14:45	4	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid-	WMS5	SUNNT	14.45	4	М		2	NA		NA	INA.	NA		NA	INA.	NA		NA		NA	NA	
		WMS5	_			В	3	1	8.12	8.12	32.21	32.21	28.3	28.3	104.4	104.5	7.68	7.68	1.29	1.29	6.98	6.98	6.99
		WMS5				В	5	2	8.12	0.12	32.21	52.21	28.3	20.0	104.5	104.5	7.67	7.00	1.29	1.23	7.00	7.00	0.99
		WMS6				S	1	1	8.12	8.12	32.25	32.25	28.4	28.4	105.6	105.7	7.71	7.72	1.13	1.14	6.28	6.28	6.26
		WMS6				S		2	8.12	0.12	32.25	52.25	28.4	20.4	105.7	103.7	7.72	1.12	1.14	1.14	6.24	6.24	0.20
	Mid-Ebb	WMS6	SUNNY	15:00	4	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid-	WMS6	SUNNT	15.00	4	М		2	NA		NA	11/1	NA		NA	11/1	NA		NA		NA	NA	
		WMS6				В	3	1	8.12	8.12	32.22	32.22	28.3	28.3	103.1	103.2	7.63	7.64	1.30	1.31	7.08	7.08	7.09
		WMS6				В	з 	2	8.12	0.12	32.22	52.22	28.3	20.3	103.2	103.2	7.64	7.04	1.31	1.31	7.09	7.09	1.09
	Mid - Ebb	12	SUNNY	14:00	16	S	1	1	8.11	8.11	32.17	32.17	28.3	28.3	109.7	109.7	7.85	7.85	1.10	1.10	8.49	8.49	8.47



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-27
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	12				s		2	8.11		32.17		28.3		109.6		7.84		1.10		8.44	8.44	
	12				М		1	8.10		32.16		28.3		106.8		7.76		1.09		8.69	8.69	
	12				M	8	2	8.10	8.10	32.16	32.16	28.3	28.3	106.7	106.8	7.75	7.76	1.10	1.10	8.77	8.77	8.73
	12				В		1	8.09		32.14		28.1		103.5		7.65		1.11		8.25	8.25	
	12				В	15	2	8.09	8.09	32.14	32.14	28.1	28.1	103.6	103.6	7.66	7.66	1.12	1.12	8.17	8.17	8.21
	C2				S	1	1	8.08	8.08	32.14	32.14	28.2	28.2	106.0	106.1	7.72	7.73	1.01	1.02	29.53	29.53	29.56
٩	C2				S		2	8.08		32.14		28.2		106.1		7.73		1.02		29.59	29.59	
Mid-Ebb	C2	SUNNY	15:30	3.7	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
Mid	C2				М		2	NA		NA		NA		NA		NA		NA		NA	NA	Į]
	C2				В	3	1	8.08	8.08	32.15	32.15	28.1	28.1	103.5	103.6	7.65	7.65	1.56	1.55	31.25	31.25	31.20
	C2				В	-	2	8.08		32.15		28.1		103.6		7.64		1.54		31.15	31.15	
	C3				S	1	1	8.12	8.12	32.19	32.19	28.3	28.3	108.9	108.9	7.82	7.82	1.12	1.12	22.01	22.01	21.98
	C3				S	1	2	8.12	0.12	32.19	52.15	28.3	20.5	108.8	100.5	7.81	1.02	1.12	1.12	21.94	21.94	21.90
Ebb	C3		4445	40	М	6	1	8.12	0.40	32.19	22.40	28.3	00.0	105.6	405.7	7.72	7 70	1.20	4.00	28.47	28.47	00.50
Mid-Ebb	C3	SUNNY	14:15	13	М	6	2	8.12	8.12	32.19	32.19	28.3	28.3	105.7	105.7	7.73	7.73	1.20	1.20	28.52	28.52	28.50
	C3				В		1	8.11		32.19		28.2		102.7		7.63		1.47		28.82	28.82	
	C3				В	12	2	8.11	8.11	32.19	32.19	28.2	28.2	102.8	102.8	7.64	7.64	1.48	1.48	28.70	28.70	28.76
	WMS-1N				S		1	8.14		32.19		28.1		110.5		7.84		1.10		9.96	9.96	
	WMS-1N				S	1	2	8.14	8.14	32.19	32.19	28.1	28.1	110.4	110.5	7.85	7.85	1.10	1.10	9.95	9.95	9.96
poo	WMS-1N				М		1	8.14		32.18		28.0		107.1		7.75		1.10		9.25	9.25	
Mid-Flood	WMS-1N	SUNNY	10:45	7.2	М	3	2	8.14	8.14	32.18	32.18	28.0	28.0	107.2	107.2	7.76	7.76	1.09	1.10	9.22	9.22	9.24
Σ	WMS-1N				В		1	8.14		32.21		28.0		104.0		7.64		1.08		9.64	9.64	
	WMS-1N				В	6	2	8.14	8.14	32.21	32.21	28.0	28.0	103.9	104.0	7.65	7.65	1.09	1.09	9.63	9.63	9.64
	WMS-2N				S		1	8.14		32.27		28.1		107.1		7.75		1.02		7.97	7.97	
	WMS-2N				S	1	2	8.14	8.14	32.27	32.27	28.1	28.1	107.2	107.2	7.76	7.76	1.01	1.02	7.99	7.99	7.98
po	WMS-2N				M		1	NA		NA		NA		NA		NA		NA		NA	NA	
Mid-Flood	WMS-2N WMS-2N	SUNNY	10:30	4.2	M	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
Mic							1															
	WMS-2N				В	3		8.14	8.14	32.27	32.27	28.0	28.0	104.7	104.7	7.67	7.68	1.56	1.57	6.96	6.96	6.95
	WMS-2N				В		2	8.14		32.27		28.0		104.6		7.68		1.57		6.93	6.93	<u> </u>
	WMS3				S	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
g	WMS3				S		2	NA		NA		NA		NA		NA		NA		NA	NA	
Mid-Flood	WMS3	SUNNY	10:15	2.8	М	1.5	1	8.20	8.20	32.34	32.34	28.2	28.2	105.4	105.4	7.71	7.71	0.98	0.98	8.48	8.48	8.46
Mid	WMS3				М		2	8.20		32.34		28.2		105.3		7.70		0.97		8.43	8.43	ļ!
	WMS3				В	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	WMS3				В		2	NA		NA		NA		NA		NA		NA		NA	NA	
	WMS4				S	1	1	8.19	8.19	32.33	32.33	28.2	28.2	109.7	109.8	7.83	7.84	0.87	0.88	7.77	7.77	7.74
σ	WMS4				S		2	8.19	0.10	32.33	52.00	28.2	20.2	109.8		7.84	1.07	0.88	0.00	7.71	7.71	,
Mid-Flood	WMS4	SUNNY	9:30	3.8	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
Mid-I	WMS4	CONNT	0.00	0.0	М		2	NA		NA		NA		NA		NA		NA	193	NA	NA	
	WMS4				В	3	1	8.19	8.19	32.33	32.33	28.2	28.2	107.2	107.3	7.75	7.76	0.97	0.98	7.52	7.52	7.54
	WMS4				В	3	2	8.19	0.19	32.33	52.55	28.2	20.2	107.3	107.5	7.76	1.10	0.98	0.96	7.55	7.55	7.04
ъ р	WMS5	OLININ'N	0.45	4.5	S	4	1	8.19	0.40	32.24	20.04	28.3	00.0	107.8	407.0	7.78	7 70	1.05	4.00	6.34	6.34	0.00
Mid- Flood	WMS5	SUNNY	9:45	4.5	S	1	2	8.19	8.19	32.24	32.24	28.3	28.3	107.9	107.9	7.77	7.78	1.06	1.06	6.31	6.31	6.33
	J			I	J	I	1	I	1	1	I	1	1	1	1	1	1	1	1	I		



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-28
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

WMS5 WMS5 WMS5						-	NA	NIA	NA	NIA	NA	NIA	NA	NIA	NA	NIA	NA	NIA	NA	NA	NIA
				М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
WMS5				В		1	8.19	0.40	32.33	00.00	28.2	00.0	105.3	405.4	7.71	7 74	1.31	4.00	7.54	7.54	7.50
				В	4	2	8.19	8.19	32.33	32.33	28.2	28.2	105.4	105.4	7.70	7.71	1.32	1.32	7.52	7.52	7.53
WMS6				S	4	1	8.19	0.40	32.35	20.05	28.3	00.0	106.7	400.0	7.74	7 75	1.15	4.40	5.59	5.59	5.04
WMS6				S	1	2	8.19	8.19	32.35	32.30	28.3	28.3	106.8	106.8	7.75	1.15	1.17	1.16	5.63	5.63	5.61
WMS6	<u></u>	10.00		М		1	NA		NA		NA		NA		NA		NA		NA	NA	
WMS6	SUNNY	10:00	4.5	М	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
WMS6				В		1	8.18		32.34		28.2		104.2		7.66		1.30		6.01	6.01	
WMS6				В	4	2	8.18	8.18	32.34	32.34	28.2	28.2	104.3	104.3	7.67	7.67	1.29	1.30	5.97	5.97	5.99
11				S		1	8.18		32.32		28.2		110.4		7.86		1.15		7.98	7.98	
11				S	1	2	8.18	8.18	32.32	32.32	28.2	28.2	110.3	110.4	7.85	7.86	1.16	1.16	8.05	8.05	8.02
11				М		1	8.18		32.33		28.2		107.1		7.76		1.25		10.23	10.23	
11	SUNNY	9:15	14	М	7	2	8.18	8.18	32.33	32.33	28.2	28.2	107.2	107.2	7.77	7.77	1.26	1.26	10.28	10.28	10.26
l1				В		1	8.17		32.32		28.1		104.2		7.67		1.44		9.14	9.14	
11				В	13	2	8.17	8.17	32.32	32.32	28.1	28.1	104.3	104.3	7.68	7.68	1.45	1.45	9.12	9.12	9.13
C1				S		1	8.17		32.29		28.2		111.1		7.89		1.11		31.25	31.25	
C1					1	2	8.17	8.17	32.29	32.29	28.2	28.2	111.2	111.2	7.88	7.89	1.11	1.11	31.30	31.30	31.28
						1											1.08		24.26		
	SUNNY	9:00	17		8	2		8.16		32.28		28.2		108.3		7.80		1.09			24.23
						1															
					16	2		8.15		32.26		28.1		105.1		7.70		1.12			25.59
	VMS6 VMS6 VMS6 VMS6 I1 I1 I1 I1 I1 I1 I1 C1	VMS6 VMS6 VMS6 VMS6 VMS6 I1 I1 I1 I1 I1 I1 I1 I1 I1 C1 C1 C1 C1 C1 C1 C1 C1 C1 C1 C1 C1 C1	VMS6         SUNNY         10:00           VMS6         SUNNY         10:00           VMS6         VMS6         Provide the second s	VMS6         SUNNY         10:00         4.5           VMS6         VMS6         4.5         4.5           VMS6         VMS6         9:15         14           11         9:15         14           11         9:15         14           11         9:00         17           C1         SUNNY         9:00         17	VMS6         SUNNY         10:00         4.5         S           VMS6         M         M         M           VMS6         M         B         B           VMS6         M         B         B           VMS6         P         P         P           VMS6         M         B         B           I1         P         P         P         P           I1         P         P         P         P         P           I1         P         P         P         P         P         P           I1         P	$ \begin{array}{c ccccccccccccccccccccccccccccccccccc$	$\frac{VMS6}{VMS6} \\ \frac{VMS6}{VMS6} \\ \frac{VMS6}{VMS6$	$\begin{array}{c c c c c c c c c c c c c c c c c c c $	$\begin{array}{c c c c c c c c c c c c c c c c c c c $	$ \begin{array}{ c c c c c c c c } \hline MS6 \\ \hline SUNNY \\ 9:15 \\ \hline 1 \\ 9:15 \\ \hline 1 \\ 1 \\ \hline SUNNY \\ 9:15 \\ \hline 1 \\ 1 \\ \hline 1 \\ 1 \\ \hline MS  \\ \hline SS \\ \hline SS \\ \hline 1 \\ \hline 1 \\ \hline SS \\ \hline 1 \\ \hline 1 \\ \hline SS \\ \hline 1 \\ \hline 1 \\ \hline 1 \\ \hline SUNNY \\ 9:00 \\ \hline 1 \\ 1 \\$	$ \begin{array}{c c c c c c c c c c c c c c c c c c c $	$ \begin{array}{c c c c c c c c c c c c c c c c c c c $	MS6 /MS6 /MS6 /MS6         SUNNY         10:00         S         1         2         8.19         32.35         32.35         28.3         28.3           MMS6 /MS6         M         NA         S2.34         32.34         32.34         32.34         32.34         32.32         28.2         28.2         28.2         28.2         28.2         28.2         <	MS6 MS6 MS6 MS6 MS6         NA         S         1         2         8.19         8.19         32.35         32.35         28.3         106.8           MS6 MS6         MS6         M         M         M         M         M         NA         SA         SA	MS6 MS6 MS6 MS6         J0:00         A.5         S         1         2         8.19         32.35         32.35         28.3         106.8         106.8           MS6 MS6         MS6         M         NA         NA	MS6         MS6         M         1         2         8.19         32.35         28.3         28.3         106.8         106.8         7.75           MS6         MS6         M         M         NA         NA	MS6 MS6 MS6 MS6         SUNNY         4.5         S         1         2         8.19         8.19         32.35         28.3         28.3         106.8         106.8         7.75         7.75           MS6 MS6         M         M         NA         NA <td>MMS6 MMS6         SUNNY         10.00         I</td> <td>MS6         SUNNY         10:00         S         1         2         8.19         23.35         28.3         106.8         106.8         7.75         7.75         1.17         1.16           MS6         MS6         M         M         M         NA         NA</td> <td>MS6         MS6         M         M         M         NA         NA<!--</td--><td>MRS6 IMS6 IMS6 MS6         SUNY         10:00         S         1         2         6.19         8.19         32.35         28.3         106.8         106.8         7.75         7.76         1.17         1.16         5.63         5.63           MMS6 MS6         MM         M         M         MA         MA</td></td>	MMS6 MMS6         SUNNY         10.00         I	MS6         SUNNY         10:00         S         1         2         8.19         23.35         28.3         106.8         106.8         7.75         7.75         1.17         1.16           MS6         MS6         M         M         M         NA         NA	MS6         MS6         M         M         M         NA         NA </td <td>MRS6 IMS6 IMS6 MS6         SUNY         10:00         S         1         2         6.19         8.19         32.35         28.3         106.8         106.8         7.75         7.76         1.17         1.16         5.63         5.63           MMS6 MS6         MM         M         M         MA         MA</td>	MRS6 IMS6 IMS6 MS6         SUNY         10:00         S         1         2         6.19         8.19         32.35         28.3         106.8         106.8         7.75         7.76         1.17         1.16         5.63         5.63           MMS6 MS6         MM         M         M         MA         MA



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-29
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	ode				Water									In-situ Me	asurement						Lab	oratory Anal	ysis
Date	Tidal Mode	Monitoring Location	Weather	Time	Depth (m)	Monitoring Level	Monitoring Level (m)	Replicate	p	н	Salinit	y (ppt)	Tempera	ature (°C)	DO Satur	ration (%)	DO (I	mg/L)	Turbidit	ty (NTU)		pended solids - 105 (ºC), m	
	·								Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value		Ave.
10/23/2024		WMS-1N				S		1	8.09	0.00	32.04	00.04	27.6	07.0	108.5	100 5	7.78		1.10		7.75	7.75	
		WMS-1N				S	1	2	8.09	8.09	32.04	32.04	27.6	27.6	108.4	108.5	7.77	7.78	1.10	1.10	7.72	7.72	7.74
	Ebb	WMS-1N		44.00		М		1	8.09	0.00	32.03	00.00	27.6	07.0	106.2	100.0	7.70	7.74	1.08	1.00	8.48	8.48	0.54
	Mid-Ebb	WMS-1N	SUNNY	11:00	6.5	М	3	2	8.09	8.09	32.03	32.03	27.6	27.6	106.3	106.3	7.71	7.71	1.08	1.08	8.53	8.53	8.51
	_	WMS-1N				В		1	8.09	0.00	32.02		27.4	07.4	104.2	101.0	7.65	7.05	1.09	4.00	6.99	6.99	0.07
		WMS-1N				В	6	2	8.09	8.09	32.02	32.02	27.4	27.4	104.1	104.2	7.64	7.65	1.09	1.09	6.95	6.95	6.97
		WMS-2N				S		1	NA		NA		NA		NA		NA		NA		NA	NA	·
		WMS-2N				S	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	adi	WMS-2N				М		1	8.14		32.21		27.6		105.0		7.66		1.57		11.55	11.55	·
	Mid-Ebb	WMS-2N	SUNNY	10:45	3	М	1.5	2	8.14	8.14	32.21	32.21	27.6	27.6	105.1	105.1	7.65	7.66	1.57	1.57	11.51	11.51	11.53
	2	WMS-2N	-			В		1	NA		NA		NA		NA		NA		NA		NA	NA	
		WMS-2N	-			В	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
		WMS3				S		1	NA		NA		NA		NA		NA		NA		NA	NA	·
		WMS3	-			S	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Ebb	WMS3	-			м		1	8.13		23.18		27.6		105.9		7.70		1.27		7.29	7.29	
	Mid-Ebb	WMS3	SUNNY	10:15	2	м	1.5	2	8.13	8.13	32.18	27.68	27.6	27.6	105.8	105.9	7.69	7.70	1.27	1.27	7.30	7.30	7.30
	2	WMS3	-			В		1	NA		NA		NA		NA		NA		NA		NA	NA	·
		WMS3	-			В	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
		WMS4				S		1	8.16		32.23		28.0		110.2		7.83		1.44		6.86	6.86	
		WMS4				S	1	2	8.16	8.16	32.23	32.23	28.0	28.0	110.3	110.3	7.84	7.84	1.45	1.45	6.84	6.84	6.85
	qq	WMS4				М		1	NA		NA		NA		NA		NA		NA		NA	NA	·
	Mid-Ebb	WMS4	SUNNY	9:30	3.6	м	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	2	WMS4	-			В		1	8.16		32.23		28.0		108.2		7.77		1.45		6.56	6.56	·
		WMS4	-			В	3	2	8.16	8.16	32.23	32.23	28.0	28.0	108.3	108.3	7.78	7.78	1.46	1.46	6.51	6.51	6.54
-		WMS5				S		1	8.16		32.24		28.0		107.4		7.75		1.24		5.86	5.86	·
		WMS5	-			S	1	2	8.16	8.16	32.24	32.24	28.0	28.0	107.5	107.5	7.76	7.76	1.24	1.24	5.91	5.91	5.89
	Ebb	WMS5	-			м		1	NA		NA		NA		NA		NA		NA		NA	NA	
	Mid-Ebb	WMS5	SUNNY	9:45	3.6	м	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	2	WMS5				В		1	8.16		32.24		28.0		105.3		7.68		1.47		6.63	6.63	
		WMS5	-			В	3	2	8.16	8.16	32.24	32.24	28.0	28.0	105.4	105.4	7.69	7.69	1.46	1.47	6.62	6.62	6.63
		WMS6			1	s		1	8.16		32.24		28.0		105.6		7.70		1.32	1	7.45	7.45	
		WMS6	1			s	1	2	8.16	8.16	32.24	32.24	28.0	28.0	105.7	105.7	7.71	7.71	1.33	1.33	7.40	7.40	7.43
	qq	WMS6	1			м		1	NA		NA		NA		NA		NA		NA		NA	NA	
	Mid-Ebb	WMS6	SUNNY	10:00	3.6	м	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	2	WMS6	1			В		1	8.16		32.24		28.0		103.4		7.63		1.36		8.02	8.02	·
		WMS6	1			В	3	2	8.16	8.16	32.24	32.24	28.0	28.0	103.3	103.4	7.64	7.64	1.37	1.37	7.99	7.99	8.01
	qq	12				S		1	8.15		32.20		28.1		109.1		7.80		1.09		7.86	7.86	
	/id-Ebb	12	SUNNY	9:00	15	S	1	2	8.15	8.15	32.20	32.20	28.1	28.1	109.2	109.2	7.81	7.81	1.10	1.10	7.81	7.81	7.84
	Ž	12	l						0.10					1	100.2	l	1	l	1	I		7.51	



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-30
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	12				м		1	8.14		32.20		28.0		107.3		7.76		1.12	1	8.66	8.66	1
	12				м	7	2	8.14	8.14	32.20	32.20	28.0	28.0	107.2	107.3	7.75	7.76	1.13	1.13	8.62	8.62	8.64
	12				В		1	8.14		32.20		28.0		105.5		7.69		1.14	<u> </u>	7.44	7.44	
	12				B	14	2	8.14	8.14	32.20	32.20	28.0	28.0	105.4	105.5	7.70	7.70	1.13	1.14	7.40	7.40	7.42
	C2				S		1	8.14		NA		NA		NA		NA		NA		NA	NA	
	C2				S	NA	2	8.14	8.14	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
ą	C2				м		1	8.14		32.21		27.6		105.2		7.66		1.58	<u> </u>	28.13		<u> </u> !
Mid-Ebb	C2 C2	SUNNY	10:30	2.9	M	1.5		8.14	8.14	32.21	32.21	27.6	27.6	105.2	105.3	7.67	7.67	1.58	1.58	27.85	28.13 27.85	27.99
Σ							2												<u> </u>	1		·'
	C2				В	NA	1	8.14	8.14	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	C2				В		2	8.14		NA		NA		NA		NA		NA	<u> </u>	NA	NA	ļ'
	C3				S	1	1	8.14	8.14	32.21	32.21	28.1	28.1	108.2	108.3	7.79	7.79	1.49	1.50	26.89	26.89	26.95
0	C3				S		2	8.14		32.21		28.1		108.3		7.78		1.50	<u> </u>	27.00	27.00	
Mid-Ebb	C3	SUNNY	9:15	13	M	6	1	8.14	8.14	32.20	32.20	28.0	28.0	106.1	106.2	7.73	7.73	1.47	1.46	27.05	27.05	27.08
Mid	C3				M		2	8.14		32.20		28.0		106.2		7.72		1.45	<u> </u>	27.11	27.11	ļ'
	C3				В	12	1	8.14	8.14	32.20	32.20	28.0	28.0	104.2	104.3	7.67	7.67	1.48	1.49	29.15	29.15	29.05
	C3				В		2	8.14	0.11	32.20	02.20	28.0	20.0	104.3	101.0	7.66	1.01	1.49		28.94	28.94	20.00
	WMS-1N				S	1	1	8.15	8.15	32.15	32.15	27.8	27.8	107.2	107.3	7.73	7.74	1.10	1.10	8.59	8.59	8.59
	WMS-1N				S	I	2	8.15	0.15	32.15	52.15	27.8	27.0	107.3	107.5	7.74	1.14	1.09	1.10	8.58	8.58	0.59
Mid-Flood	WMS-1N		45.45	7	М	2	1	8.15	0.15	32.14	22.14	27.8	07.0	105.0	105 1	7.66	7.67	1.08	1.00	9.26	9.26	0.24
Aid-F	WMS-1N	SUNNY	15:45	7	М	3	2	8.15	8.15	32.14	32.14	27.8	27.8	105.1	105.1	7.67	7.67	1.09	1.09	9.22	9.22	9.24
2	WMS-1N				В		1	8.15	0.45	32.13	00.40	27.5	07.5	102.9	400.0	7.61	7.04	1.09	4.40	8.83	8.83	0.00
	WMS-1N				В	6	2	8.15	8.15	32.13	32.13	27.5	27.5	103.0	103.0	7.60	7.61	1.10	1.10	8.80	8.80	8.82
	WMS-2N				S		1	NA		NA		NA		NA		NA		NA		NA	NA	
	WMS-2N				S	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
pool	WMS-2N				М		1	8.20		32.29		27.8		104.2		7.63		1.58		5.78	5.78	
Mid-Flood	WMS-2N	SUNNY	15:30	3.2	М	1.5	2	8.20	8.20	32.30	32.30	27.8	27.8	104.1	104.2	7.64	7.64	1.59	1.59	5.75	5.75	5.77
Σ	WMS-2N				В		1	NA		NA		NA		NA		NA		NA		NA	NA	
	WMS-2N				В	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	WMS3				S		1	NA		NA		NA		NA		NA		NA	<u> </u>	NA	NA	
	WMS3				S	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
poo	WMS3				M		1	8.19		32.26		27.8		104.7		7.66		1.28	<u> </u>	6.66	6.66	
Mid-Flood	WMS3	SUNNY	15:15	2.5	M	1.5	2	8.19	8.19	32.27	32.27	27.8	27.8	104.6	104.7	7.65	7.66	1.28	1.28	6.64	6.64	6.65
ž	WMS3				В		1	NA		NA		NA		NA		NA		NA		NA	NA	
	WMS3				В	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
							1												<u> </u>			<u> </u> '
	WMS4				S	1		8.22	8.22	32.31	32.31	28.1	28.1	109.3	109.3	7.80	7.81	1.43	1.44	7.47	7.47	7.44
po	WMS4				S		2	8.22		32.31		28.1		109.2		7.81		1.44	<u> </u>	7.41	7.41	<u> </u> '
Mid-Flood	WMS4	SUNNY	14:30	4	M	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
Mia	WMS4				M		2	NA		NA		NA		NA		NA		NA	<u> </u>	NA	NA	<u> </u> '
	WMS4				В	3	1	8.22	8.22	32.31	32.31	28.1	28.1	107.3	107.4	7.74	7.75	1.45	1.45	6.89	6.89	6.91
	WMS4				В		2	8.22		32.31		28.1		107.4		7.75		1.44	<u> </u>	6.92	6.92	<b> </b> '
poo	WMS5				S	1	1	8.22	8.22	32.32	32.32	28.1	28.1	106.7	106.7	7.72	7.73	1.28	1.29	5.25	5.25	5.28
Mid-Flood	WMS5	SUNNY	14:45	4	S		2	8.22		32.32		28.1		106.6		7.73		1.29		5.30	5.30	
Σ	WMS5				М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-31
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	WMS5				М		2	NA		NA		NA		NA		NA		NA		NA	NA	1
	WMS5				В		1	8.22	0.00	32.32	22.22	28.1	00.4	104.4	404.5	7.65	7.00	1.48	1.40	6.46	6.46	0.45
	WMS5				В	3	2	8.22	8.22	32.32	32.32	28.1	28.1	104.5	104.5	7.66	7.66	1.47	1.48	6.43	6.43	6.45
	WMS6				S	1	1	8.22	8.22	32.32	32.32	28.1	28.1	104.7	104.8	7.67	7.68	1.37	1.37	7.45	7.45	7.44
	WMS6				S		2	8.22	0.22	32.32	32.32	28.1	20.1	104.8	104.0	7.68	7.00	1.36	1.37	7.42	7.42	7.44
	WMS6	CLININIX	45.00		М	NA	1	NA	NA	NA	NIA	NA	NIA	NA	NA	NA	NIA	NA	NA	NA	NA	NA
Mid-Flood	WMS6	SUNNY	15:00	4	М	NA	2	NA	NA NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	INA
	WMS6				В	2	1	8.22	0.00	32.32	22.22	28.1	20.4	102.5	102.6	7.60	7.64	1.38	1.00	6.95	6.95	6.04
	WMS6				В	3	2	8.22	8.22	32.32	32.32	28.1	28.1	102.6	102.0	7.61	7.61	1.37	1.38	6.93	6.93	6.94
	11				S	1	1	8.23	8.23	32.29	32.29	28.2	28.2	107.0	107.1	7.74	7.75	1.51	1.51	8.59	8.59	8.63
	l1				S	I	2	8.23	0.23	32.29	52.29	28.2	20.2	107.1	107.1	7.75	1.15	1.50	1.51	8.67	8.67	0.03
pool	l1	SUNNY	14:15	14	М	7	1	8.21	8.21	32.27	32.27	28.1	28.1	104.9	105.0	7.69	7.69	1.52	1.53	9.86	9.86	9.84
Mid-F	l1	SUNNT	14.15	14	М	/	2	8.21	0.21	32.27	52.21	28.1	20.1	105.0	105.0	7.68	7.09	1.53	1.55	9.81	9.81	9.04
	l1				В	13	1	8.21	8.21	32.27	32.27	28.1	28.1	103.0	103.1	7.63	7.63	1.50	1.51	10.54	10.54	10.55
	l1				В	15	2	8.21	0.21	32.27	52.27	28.1	20.1	103.1	103.1	7.62	7.03	1.51	1.51	10.55	10.55	10.55
	C1				S	1	1	8.22	8.22	32.29	32.29	28.2	28.2	107.9	108.0	7.76	7.77	1.11	1.12	26.89	26.89	26.93
	C1				S	I	2	8.22	0.22	32.29	52.29	28.2	20.2	108.0	108.0	7.77	1.11	1.12	1.12	26.97	26.97	20.93
Mid-Flood	C1	SUNNY	14:00	16	М	8	1	8.20	8.20	32.27	32.27	28.1	28.1	106.0	106.1	7.71	7.72	1.13	1.14	25.03	25.03	25.04
Aid-F	C1	SUNNT	14.00	10	М	0	2	8.20	0.20	32.27	52.21	28.1	20.1	106.1	100.1	7.72	1.12	1.14	1.14	25.04	25.04	23.04
	C1				В	15	1	8.20	8.20	32.27	32.27	28.1	28.1	104.2	104.3	7.65	7.66	1.13	1.13	26.11	26.11	26.01
	C1				В	15	2	8.20	0.20	32.27	52.21	28.1	20.1	104.3	104.5	7.66	7.00	1.12	1.15	25.90	25.90	20.01



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-32
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	de				Matar									In-situ Me	asurement						Lab	oratory Anal	ysis
Date	Tidal Mode	Monitoring Location	Weather	Time	Water Depth (m)	Monitoring Level	Monitoring Level (m)	Replicate	p	н	Salinit	ty (ppt)	Tempera	ature (°C)	DO Satur	ration (%)	DO (r	mg/L)	Turbidit	y (NTU)	Total sus 103	spended solid 3 - 105 (ºC), m	s dried at ng/L
	·								Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value		Ave.
10/25/2024		WMS-1N				S		1	8.14		32.34		25.1		107.0		7.72		1.07		3.65	3.65	
		WMS-1N				S	1	2	8.14	8.14	32.34	32.34	25.1	25.1	107.1	107.1	7.73	7.73	1.08	1.08	3.70	3.70	3.68
	Ebb	WMS-1N		44.00	_	М		1	8.14		32.34	00.04	25.0	05.0	104.7	101.0	7.65	7.00	0.99	0.00	5.11	5.11	5.40
	Mid-Ebb	WMS-1N	SUNNY	11:00	7	М	3	2	8.14	8.14	32.34	32.34	25.0	25.0	104.8	104.8	7.66	7.66	0.99	0.99	5.13	5.13	5.12
		WMS-1N	]			В	6	1	8.14	0.14	32.34	22.24	24.8	24.9	102.5	102.6	7.59	7.60	1.09	1.00	5.66	5.66	5.69
		WMS-1N				В	0	2	8.14	8.14	32.34	32.34	24.8	24.8	102.6	102.6	7.60	7.60	1.08	1.09	5.70	5.70	5.68
		WMS-2N				S	1	1	8.15	0.15	32.39	22.20	25.4	25.4	106.5	106.6	7.70	7 70	1.56	1.50	4.68	4.68	4.66
		WMS-2N				S	1	2	8.15	8.15	32.39	32.39	25.4	25.4	106.6	106.6	7.69	7.70	1.55	1.56	4.63	4.63	4.66
	Ebb	WMS-2N	SUNNY	10:45	3.5	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid-Ebb	WMS-2N	SUNNT	10.45	3.5	М	INA	2	NA	INA.	NA	INA.	NA	NA	NA	INA.	NA	INA	NA	NA	NA	NA	INA
		WMS-2N				В	3	1	8.14	8.14	32.38	32.38	25.3	25.3	104.0	104.1	7.63	7.63	1.57	1.58	5.93	5.93	5.92
		WMS-2N				В	5	2	8.14	0.14	32.38	52.50	25.3	20.0	104.1	104.1	7.62	7.05	1.58	1.50	5.91	5.91	5.92
		WMS3				S	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	_	WMS3				S		2	NA	11/4	NA	11/4	NA		NA	11/2	NA		NA		NA	NA	
	Mid-Ebb	WMS3	SUNNY	10:15	2.8	М	1.5	1	8.14	8.14	32.40	32.40	26.2	26.2	104.3	104.3	7.63	7.64	1.27	1.28	5.30	5.30	5.29
	Mid	WMS3		10.10	2.0	М	1.0	2	8.14	0.11	32.40	02.10	26.2	20.2	104.2	101.0	7.64	1.01	1.28	1.20	5.27	5.27	0.20
		WMS3	_			В	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
		WMS3				В		2	NA		NA		NA		NA		NA		NA		NA	NA	
		WMS4	_			S	1	1	8.13	8.13	32.37	32.37	26.8	26.8	109.3	109.4	7.79	7.80	1.45	1.45	4.03	4.03	4.05
	0	WMS4	_			S		2	8.13		32.37		26.8		109.4		7.80		1.45	_	4.06	4.06	ļ
	Mid-Ebb	WMS4	SUNNY	9:30	3.6	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid	WMS4	_			М		2	NA		NA		NA		NA		NA		NA		NA	NA	I
		WMS4	_			В	3	1	8.14	8.14	32.37	32.37	26.8	26.8	107.4	107.5	7.75	7.75	1.45	1.45	5.18	5.18	5.21
-		WMS4				В		2	8.14		32.37		26.8		107.5		7.74		1.44		5.23	5.23	<b> </b>
		WMS5	_			S	1	1	8.14	8.14	32.38	32.38	26.6	26.6	106.5	106.6	7.71	7.72	1.20	1.20	6.69	6.69	6.67
	٩	WMS5	_			S		2	8.14		32.38		26.6		106.6		7.72		1.20		6.64	6.64	l
	Mid-Ebb	WMS5	SUNNY	9:45	4.3	M	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	ž	WMS5	_			M		2	NA		NA		NA		NA		NA		NA		NA	NA	
		WMS5	_			В	3	1	8.14	8.14	32.39	32.39	26.4	26.4	104.4	104.5	7.64	7.65	1.40	1.41	7.33	7.33	7.36
r		WMS5				B		2	8.14		32.39		26.4		104.5		7.65		1.41		7.38	7.38	
		WMS6	-			S	1	1	8.14	8.14	32.38	32.38	26.6	26.6	104.6	104.6	7.67	7.67	1.18	1.19	5.52	5.52	5.50
	ą	WMS6	-			S		2	8.14		32.38		26.6		104.5		7.66		1.19 NA		5.47	5.47	
	Mid-Ebb	WMS6 WMS6	SUNNY	10:00	4.3	M	NA	1	NA	NA	NA	NA	NA NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mi	WMS6	-			M B		2	NA 8.14		NA 32.40				NA		NA 7.60		NA 1.26		NA 10.02	NA	
		WMS6	-			В	3	2	8.14 8.14	8.14	32.40 32.40	32.40	26.4 26.4	26.4	102.6 102.5	102.6	7.60 7.59	7.60	1.36 1.38	1.37	10.02	10.02 10.00	10.01
-	bi dc	12	SUNNY	9:00	16	S	1	2	8.15	8.15	32.40	32.40	20.4	27.0	102.5	107.9	7.59	7 76		1 1 2	6.36		6.25
	Mid - Ebb	IZ	SUININY	9.00	16	3	1		0.10	0.10	32.40	32.40	27.0	21.0	01.8	107.9	1.15	7.76	1.13	1.13	0.30	6.36	6.35



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-33
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	12				s		2	8.15		32.40		27.0		107.9		7.76		1.12		6.33	6.33	
	12				М		1	8.15		32.42		26.8		105.9		7.70		1.09		4.59	4.59	
	12				М	8	2	8.15	8.15	32.42	32.42	26.8	26.8	105.8	105.9	7.71	7.71	1.10	1.10	4.60	4.60	4.60
	12				В		1	8.14		32.42		26.7		103.7		7.64		0.98		5.51	5.51	
	12				В	15	2	8.14	8.14	32.42	32.42	26.7	26.7	103.8	103.8	7.65	7.65	0.97	0.98	5.48	5.48	5.50
	C2				S		1	8.15		32.40		25.4		106.5		7.69		1.56		23.65	23.65	
	C2				S	1	2	8.15	8.15	32.40	32.40	25.4	25.4	106.4	106.5	7.70	7.70	1.57	1.57	23.68	23.68	23.67
qq	C2				M		1	NA		NA		NA		NA		NA		NA		NA	NA	
Mid-Ebb	C2	SUNNY	10:30	3.4	M	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
Σ	C2				В		1	8.15		32.38		25.3		104.0		7.63		1.57		17.05	17.05	
	C2				В	3	2	8.15	8.15	32.38	32.38	25.3	25.3	103.9	104.0	7.64	7.64	1.58	1.58	16.94	16.94	17.00
							2											1.47				
	C3				S	1	1	8.12	8.12	32.34	32.34	26.9	26.9	106.8	106.8	7.73	7.74		1.48	8.69	8.69	8.72
ą	C3				S		2	8.12		32.34		26.9		106.7		7.74		1.48		8.74	8.74	
Mid-Ebb	C3	SUNNY	9:15	14	M	7	1	8.12	8.12	32.35	32.35	26.8	26.8	104.6	104.7	7.68	7.68	1.21	1.21	17.03	17.03	17.02
Mi	C3				M		2	8.12		32.35		26.8		104.7		7.67		1.21		17.01	17.01	
	C3				B	13	1	8.11	8.11	32.35	32.35	26.7	26.7	102.7	102.8	7.61	7.62	0.99	0.99	22.35	22.35	22.33
	C3				В		2	8.11		32.35		26.7		102.8		7.62		0.99		22.30	22.30	<u> </u>
	WMS-1N				S	1	1	8.20	8.20	32.45	32.45	25.2	25.2	108.2	108.2	7.75	7.76	1.06	1.07	7.27	7.27	7.27
g	WMS-1N				S		2	8.20		32.45		25.2		108.1		7.76		1.07		7.26	7.26	<u></u>
Floc	WMS-1N	SUNNY	15:45	7.2	M	3	1	8.20	8.20	32.44	32.44	25.1	25.1	104.9	104.9	7.68	7.69	0.98	0.99	8.42	8.42	8.41
Mid-Floo	WMS-1N				M		2	8.20		32.44		25.1		104.8		7.69		0.99		8.39	8.39	<u> </u>
	WMS-1N				В	6	1	8.20	8.20	32.44	32.44	24.9	24.9	103.6	103.7	7.62	7.63	1.08	1.09	6.63	6.63	6.62
	WMS-1N				В		2	8.20		32.44		24.9		103.7		7.63		1.09		6.60	6.60	<u> </u>
	WMS-2N				S	1	1	8.21	8.21	32.48	32.48	25.6	25.6	107.4	107.5	7.73	7.73	1.55	1.56	7.80	7.80	7.79
σ	WMS-2N				S		2	8.21		32.48		25.6		107.5		7.72		1.56		7.77	7.77	
Floo	WMS-2N	SUNNY	15:30	4	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
Mid-Floo	WMS-2N	001111	10.00	-	М		2	NA		NA		NA		NA		NA		NA		NA	NA	
	WMS-2N				В	3	1	8.20	8.20	32.46	32.46	25.4	25.4	104.9	105.0	7.65	7.66	1.58	1.58	6.65	6.65	6.64
	WMS-2N				В	5	2	8.20	0.20	32.46	52.40	25.4	20.4	105.0	100.0	7.66	7.00	1.57	1.00	6.63	6.63	0.04
	WMS3				S	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
~	WMS3				S		2	NA		NA		NA		NA		NA		NA		NA	NA	
Mid-Flood	WMS3	SUNNY	15:15	3	М	1.5	1	8.20	8.20	32.49	32.50	26.4	26.4	105.4	105.4	7.66	7.67	1.25	1.26	6.29	6.29	6.34
Aid-F	WMS3	SUMINT	15.15	3	М	1.5	2	8.20	0.20	32.50	52.50	26.4	20.4	105.3	105.4	7.67	7.07	1.26	1.20	6.38	6.38	0.34
2	WMS3				В	NIA	1	NA	NIA	NA	NIA	NA		NA	NIA	NA		NA	NIA	NA	NA	NIA
	WMS3				В	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	WMS4				S		1	8.19	0.40	32.46	00.40	26.9	00.0	110.2	440.0	7.82	7.00	1.44	4.45	8.63	8.63	0.00
_	WMS4				S		2	8.19	8.19	32.46	32.46	26.9	26.9	110.3	110.3	7.83	7.83	1.45	1.45	8.62	8.62	8.63
Mid-Flood	WMS4	0.555	44.00		М	N10	1	NA	N1A	NA	N14	26.9	00.0	NA	N1A	NA	N1.6	NA		NA	NA	N I A
1id-F	WMS4	SUNNY	14:30	4	М	NA	2	NA	NA	NA	NA	26.9	26.9	NA	NA	NA	NA	NA	NA	NA	NA	NA
2	WMS4				В		1	8.20		32.46	00 /-	26.9		108.2	100 -	7.77		1.45		5.75	5.75	
	WMS4				В	3	2	8.20	8.20	32.46	32.46	26.9	26.9	108.3	108.3	7.78	7.78	1.45	1.45	5.71	5.71	5.73
4 Q	WMS5				S		1	8.20		32.46		26.7		107.7		7.74		1.22	1	10.45	10.45	
Mid- Flood	WMS5	SUNNY	14:45	4.8	S	1	2	8.20	8.20	32.46	32.46	26.7	26.7	107.6	107.7	7.75	7.75	1.23	1.23	10.39	10.39	10.42
				1	<u> </u>	I	-		1	1		1	1		1	1	1		1			<u> </u>

SGS	

EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-34
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	WMS5				м		1	8.20	0.00	NA	NA	NA	NA	NA		NA	NIA	NA		NA	NA	
	WMS5				М	NA	2	8.20	8.20	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	WMS5				В		1	8.20	0.00	32.48	00.40	26.5	00 F	105.3	405.4	7.67	7.00	1.44		5.63	5.63	5.00
	WMS5				В	4	2	8.20	8.20	32.48	32.48	26.5	26.5	105.4	105.4	7.68	7.68	1.43	1.44	5.62	5.62	5.63
	WMS6				S		1	8.20	0.00	32.46	32.46	26.7	00.7	105.6	405.7	7.70	7 70	1.20	4.04	7.17	7.17	7.45
_	WMS6				S		2	8.20	8.20	32.46	32.40	26.7	26.7	105.7	105.7	7.69	7.70	1.21	1.21	7.13	7.13	7.15
pool	WMS6		45.00	4.0	М		1	8.20	0.00	NA		NA		NA		NA		NA		NA	NA	N 1 A
Mid-Floc	WMS6	SUNNY	15:00	4.8	М	NA	2	8.20	8.20	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
2	WMS6				В		1	8.20		32.48		26.5		103.4		7.63		1.38	1.00	5.16	5.16	- / -
	WMS6				В	4	2	8.20	8.20	32.48	32.48	26.5	26.5	103.5	103.5	7.62	7.63	1.39	1.39	5.20	5.20	5.18
	11				S		1	8.18		32.44		27.0		108.0		7.76		1.47		6.02	6.02	
_	11				S		2	8.18	8.18	32.44	32.44	27.0	27.0	107.9	108.0	7.77	7.77	1.48	1.48	5.96	5.96	5.99
pool	l1		11.15	45	М	-	1	8.18	0.40	32.45	00.45	26.9	00.0	105.8	405.0	7.71	7 74	1.25	4.00	7.71	7.71	7.07
Mid-Floo	l1	SUNNY	14:15	15	М	7	2	8.18	8.18	32.45	32.45	26.9	26.9	105.9	105.9	7.70	7.71	1.26	1.26	7.62	7.62	7.67
2	l1				В		1	8.17	0.47	32.44	00.44	26.8		103.9	101.0	7.64	7.05	1.02	4.00	9.32	9.32	0.00
	l1				В	14	2	8.17	8.17	32.44	32.44	26.8	26.8	104.0	104.0	7.65	7.65	1.03	1.03	9.33	9.33	9.33
	C1				S		1	8.21	0.04	32.50	00.50	27.1	07.4	109.0	400.4	7.78	7 70	1.14		5.88	5.88	5.00
	C1				S		2	8.21	8.21	32.50	32.50	27.1	27.1	109.1	109.1	7.79	7.79	1.13	1.14	5.83	5.83	5.86
pool.	C1				М		1	8.21	0.04	32.52	00.50	26.9		107.1	407.4	7.73	4	1.11		24.12	24.12	04.00
Mid-F	C1	SUNNY	14:00	17	М	8	2	8.21	8.21	32.52	32.52	26.9	26.9	107.0	107.1	7.74	7.74	1.10	1.11	24.06	24.06	24.09
2	C1	1			В		1	8.20		32.52		26.8		104.9		7.63		1.00	1.00	13.02	13.02	
	C1				В	16	2	8.20	8.20	32.52	32.52	26.8	26.8	105.0	105.0	7.68	7.66	0.99	1.00	12.95	12.95	12.99



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-35
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	Mode				Water									In-situ Me	asurement						Lab	oratory Ana	lysis
Date	Tidal Mo	Monitoring Location	Weather	Time	Depth (m)	Monitoring Level	Monitoring Level (m)	Replicate	р	н	Salinit	ty (ppt)	Tempera	ature (°C)	DO Satu	ration (%)	DO (	mg/L)	Turbidit	ty (NTU)	Total sus	spended solid 3 - 105 (°C), r	ds dried at mg/L
	F								Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value		Ave.
28/2024		WMS-1N				S	4	1	8.05	0.05	32.26	22.00	26.0	20.0	107.8	107.0	7.74	7 74	1.09	4.00	6.65	6.65	0.00
		WMS-1N				S		2	8.05	8.05	32.26	32.26	26.0	26.0	107.9	107.9	7.73	7.74	1.08	1.09	6.61	6.61	6.63
	Mid-Ebb	WMS-1N	SUNNY	11:00	6.7	М	3	1	8.05	8.05	32.27	32.27	26.0	26.0	105.7	105.7	7.67	7.68	1.07	1.08	5.39	5.39	5.39
	Mid-	WMS-1N	SUNNT	11.00	0.7	М	3	2	8.05	0.05	32.27	52.21	26.0	20.0	105.6	105.7	7.68	7.00	1.08	1.00	5.38	5.38	5.59
		WMS-1N				В	6	1	8.04	8.04	32.29	32.29	26.0	26.0	103.1	103.1	7.59	7.60	1.09	1.09	7.21	7.21	7.18
		WMS-1N				В	0	2	8.04	0.04	32.29	52.25	26.0	20.0	103.0	105.1	7.60	7.00	1.08	1.03	7.15	7.15	7.10
		WMS-2N				S	1	1	8.06	8.06	32.32	32.32	26.0	26.0	107.3	107.4	7.71	7.72	1.55	1.56	6.39	6.39	6.37
		WMS-2N				S	1	2	8.06	0.00	32.32	52.52	26.0	20.0	107.4	107.4	7.72	1.12	1.56	1.50	6.34	6.34	0.57
	Mid-Ebb	WMS-2N	SUNNY	10:45	3.8	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid-	WMS-2N	SUNNT	10.45	5.0	М		2	NA		NA		NA		NA		NA		NA		NA	NA	
		WMS-2N				В	3	1	8.07	8.07	32.33	32.33	26.0	26.0	105.4	105.5	7.62	7.64	1.57	1.58	5.86	5.86	5.85
		WMS-2N				В	5	2	8.07	0.07	32.33	52.55	26.0	20.0	105.5	105.5	7.66	7.04	1.58	1.50	5.83	5.83	5.05
		WMS3				S	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
		WMS3				S	NA NA	2	NA	INA	NA	NA NA	NA	NA	NA	INA	NA	INA	NA	NA NA	NA	NA	INA
	Ebb	WMS3	SUNNY	10:15	2.5	М	1.5	1	8.08	8.08	32.33	32.33	26.1	26.1	104.6	104.7	7.63	7.64	0.66	0.63	11.78	11.78	11.79
	Mid-Ebb	WMS3	SUNNT	10.15	2.5	М	1.5	2	8.08	0.00	32.33	52.55	26.1	20.1	104.7	104.7	7.64	7.04	0.60	0.05	11.80	11.80	11.73
		WMS3				В	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
		WMS3				В	NA	2	NA	NA	NA	NA	NA	NA	NA	INA	NA	NA	NA	NA	NA	NA	NA
		WMS4				S	1	1	8.09	8.09	32.34	32.34	26.4	26.4	110.6	110.7	7.83	7.84	1.44	1.45	4.87	4.87	4.85
		WMS4				S		2	8.09	8.09	32.34	32.34	26.4	20.4	110.7	110.7	7.84	7.64	1.45	1.45	4.83	4.83	4.00
	Ebb	WMS4	SUNNY	9:30	3.5	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid-Ebb	WMS4	SUNNY	9.30	3.5	М	NA NA	2	NA	NA	NA	NA	NA	NA NA	NA	INA	NA	INA	NA	NA NA	NA	NA	NA
		WMS4				В	3	1	8.09	8.09	32.34	32.34	26.4	26.4	108.3	108.3	7.75	7.76	1.45	1.46	5.25	5.25	- 5.24
		WMS4				В	5	2	8.09	0.09	32.34	52.54	26.4	20.4	108.2	100.5	7.76	7.70	1.46	1.40	5.22	5.22	5.24
		WMS5				S	1	1	8.09	8.09	32.33	32.33	26.6	26.6	107.8	107.9	7.75	7.75	1.47	1.47	4.86	4.86	4.86
		WMS5				S	1	2	8.09	0.09	32.33	52.55	26.6	20.0	107.9	107.9	7.74	1.15	1.46	1.47	4.85	4.85	4.00
	Ebb	WMS5	SUNNY	9:45	3.8	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid-Ebb	WMS5	SUNNT	9.45	5.0	М		2	NA		NA		NA		NA		NA		NA		NA	NA	
		WMS5				В	3	1	8.09	8.09	32.33	32.33	26.6	26.6	105.3	105.4	7.66	7.67	1.48	1.48	6.12	6.12	6.15
		WMS5				В	5	2	8.09	0.03	32.33	52.55	26.6	20.0	105.4	103.4	7.67	7.07	1.47	1.40	6.17	6.17	0.10
		WMS6				S	1	1	8.09	8.09	32.33	32.33	26.6	26.6	106.4	106.4	7.69	7.70	1.38	1.38	5.36	5.36	- 5.37
		WMS6				S		2	8.09	0.09	32.33	32.33	26.6	20.0	106.3	100.4	7.70	1.10	1.38	1.30	5.38	5.38	5.37
	Mid-Ebb	WMS6	SUNNY	10:00	3.8	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid-	WMS6	SUNNT	10.00	3.0	М	INA.	2	NA	NA	NA	NA	NA	NA	NA	INA.	NA	INA	NA	INA.	NA	NA	INA.
		WMS6				В	3	1	8.09	8.09	32.34	32.34	26.6	26.6	103.8	103.9	7.62	7.62	1.37	1.38	6.53	6.53	6.5
		WMS6				В	3	2	8.09	0.09	32.34	32.34	26.6	20.0	103.9	103.9	7.61	1.02	1.38	1.30	6.50	6.50	6.52
Γ		12				S	1	1	8.07	8.07	32.28	32.28	26.5	26.5	110.4	110.5	7.80	7.80	1.13	1.14	7.86	7.86	7.86
	Ebb	12	CLINING	0.00	46	S		2	8.07	0.07	32.28	32.20	26.5	20.0	110.5	110.5	7.79	1.00	1.14	1.14	7.85	7.85	7.86
	Mid-Ebb	12	SUNNY	9:00	16	М	0	1	8.07	9.07	32.27	32.27	26.5	26 F	108.0	100 4	7.71	7 70	1.14	1 1 4	8.02	8.02	0.04
		12				М	8	2	8.07	8.07	32.27	32.21	26.5	26.5	108.1	108.1	7.72	7.72	1.13	1.14	8.05	8.05	8.04



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-36
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	12				В		1	8.07		32.27		26.5		105.5		7.63		1.12		8.15	8.15	
	12				В	15	2	8.07	8.07	32.27	32.27	26.5	26.5	105.6	105.6	7.64	7.64	1.13	1.13	8.11	8.11	8.13
	C2				S		1	8.06		32.33		26.0		107.0		7.70		1.58		13.86	13.86	
	C2				S	1	2	8.06	8.06	32.33	32.33	26.0	26.0	107.1	107.1	7.71	7.71	1.57	1.58	13.81	13.81	13.84
qq	C2				M		1	NA		NA		NA		NA		NA		NA		NA	NA	
Mid-Ebb	C2	SUNNY	10:30	3.7	M	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
≥	C2				В		- 1	8.07		32.33		26.0		105.1		7.64		1.58		15.80	15.80	
	C2				В	3	2	8.07	8.07	32.33	32.33	26.0	26.0	105.2	105.2	7.65	7.65	1.58	1.58	15.81	15.81	15.81
	C3				S		1	8.08		32.33		26.6		109.0		7.76		1.54		14.96	14.96	
	C3				S	1	2	8.08	8.08	32.32	32.32	26.6	26.6	109.0	109.1	7.75	7.76	1.54	1.54	14.90	14.93	14.95
q	C3				M		1	8.08		32.32		26.5		106.6		7.68		1.53		14.53	14.53	
Mid-Ebb	C3	SUNNY	9:15	14	M	7	2	8.08	8.08	32.32	32.32	26.5	26.5	106.7	106.7	7.67	7.68	1.52	1.53	14.59	14.59	14.56
Σ	C3				В		1	8.08		32.32		26.5		104.1		7.60		1.49		16.92	16.92	
	C3				B	13	2	8.08	8.08	32.32	32.32	26.5	26.5	104.1	104.2	7.59	7.60	1.50	1.50	16.95	16.95	16.94
	WMS-1N				S		1			32.32										8.96		
	WMS-1N				S S	1		8.11 8.11	8.11	32.37	32.37	26.1 26.1	26.1	108.9 109.0	109.0	7.76 7.77	7.77	1.10 1.09	1.10	8.87	8.96 8.87	8.92
ро	WMS-1N						2															
Mid-Flood		SUNNY	15:45	7	M	3	1	8.11	8.11	32.38	32.38	26.1	26.1	106.8	106.9	7.70	7.71	1.08	1.08	7.45	7.45	7.47
Mic	WMS-1N				M		2	8.11		32.38		26.1		106.9		7.71		1.07		7.48	7.48	
	WMS-1N				В	6	1	8.10	8.10	23.40	27.90	26.0	26.0	104.3	104.3	7.62	7.63	1.09	1.09	6.98	6.98	6.99
	WMS-1N				В		2	8.10		32.40		26.0		104.2		7.63		1.08		6.99	6.99	
	WMS-2N				S	1	1	8.12	8.12	32.43	32.43	26.2	26.2	108.4	108.5	7.74	7.75	1.53	1.54	5.63	5.63	5.64
b	WMS-2N				S		2	8.12		32.43		26.2		108.5		7.75		1.54		5.64	5.64	
Mid-Flood	WMS-2N	SUNNY	15:30	4.2	M	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
Mid	WMS-2N				M		2	NA		NA		NA		NA		NA		NA		NA	NA	
	WMS-2N				В	3	1	8.13	8.13	32.44	32.44	26.2	26.2	106.3	106.4	7.68	7.69	1.57	1.58	6.24	6.24	6.23
	WMS-2N				В		2	8.13		32.44		26.2		106.4		7.69		1.58		6.21	6.21	
	WMS3				S	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
g	WMS3				S		2	NA		NA		NA		NA		NA		NA		NA	NA	
Mid-Flood	WMS3	SUNNY	15:15	2.8	М	1.5	1	8.14	8.14	32.44	32.44	26.3	26.3	105.7	105.8	7.67	7.67	0.68	0.67	11.53	11.53	11.56
Mid	WMS3				М		2	8.14		32.44		26.3		105.8		7.66		0.65		11.59	11.59	
	WMS3				В	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	WMS3				В		2	NA		NA		NA		NA		NA		NA		NA	NA	<b></b>
	WMS4				S	1	1	8.15	8.15	32.45	32.45	26.5	26.5	111.8	111.9	7.86	7.87	1.40	1.41	7.42	7.42	7.44
ğ	WMS4				S		2	8.15		32.45		26.5		111.9		7.87		1.41		7.45	7.45	<u> </u>
Mid-Flood	WMS4	SUNNY	14:30	3.9	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
Mid-	WMS4				М		2	NA		NA		NA		NA		NA		NA		NA	NA	
	WMS4				В	3	1	8.15	8.15	32.45	32.45	26.5	26.5	109.3	109.4	7.78	7.79	1.43	1.43	7.98	7.98	7.96
	WMS4				В	-	2	8.15		32.45	-	26.5		109.4		7.79	-	1.42		7.93	7.93	
	WMS5				S	1	1	8.15	8.15	32.44	32.44	26.7	26.7	109.0	109.0	7.77	7.78	1.48	1.49	6.65	6.65	6.63
σ	WMS5				S		2	8.15		32.44		26.7		108.9		7.78		1.49		6.61	6.61	
Mid-Flood	WMS5	SUNNY	14:45	4.3	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
Mid-I	WMS5	CONTRA	UT.TU	7.0	М		2	NA		NA		NA		NA		NA		NA		NA	NA	
	WMS5				В	3	1	8.15	8.15	32.44	32.44	26.6	26.6	106.4	106.5	7.70	7.70	1.47	1.48	7.42	7.42	7.40
	WMS5				В	5	2	8.15	0.15	32.44	32.44	26.6	20.0	106.5	100.5	7.69	1.10	1.48	1.40	7.38	7.38	7.40
1																						

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-37
<b>CLC</b>	Works at Po Toi O	Ref#	EMA2403/03/42
	Monthly EM&A Report	Rev.	01
		Date	Nov 24

	WMS6				S		1	8.15	0.45	32.44	00.44	26.7	00.7	107.3	407.0	7.73	7 70	1.37	1.00	6.26	6.26	0.05
-	WMS6				S		2	8.15	8.15	32.44	32.44	26.7	26.7	107.2	107.3	7.72	7.73	1.38	1.38	6.23	6.23	6.25
Flood	WMS6		45.00	4.0	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
Mid-F	WMS6	SUNNY	15:00	4.3	М	INA	2	NA	INA	NA	INA	NA	NA	NA	INA	NA	INA	NA	NA NA	NA	NA	INA
2	WMS6				В	3	1	8.15	8.15	32.44	32.44	26.6	26.6	104.7	104.8	7.65	7.65	1.38	1.39	7.45	7.45	7.45
	WMS6				В	3	2	8.15	0.15	32.44	32.44	26.6	20.0	104.8	104.0	7.64	60.7	1.39	1.39	7.44	7.44	7.45
	l1				S	1	1	8.15	8.15	32.43	32.43	26.6	26.6	110.1	110.2	7.78	7.79	1.53	1.54	8.65	8.65	8.66
75	l1				S	I	2	8.15	0.15	32.43	32.43	26.6	20.0	110.2	110.2	7.79	1.19	1.54	1.54	8.66	8.66	0.00
pool-	l1	SUNNY	14:15	15	М	7	1	8.14	8.14	32.44	32.44	26.6	26.6	107.8	107.8	7.70	7.71	1.52	1.53	9.32	9.32	9.30
Mid-F	l1	SUNNY	14.15	15	М	1	2	8.14	0.14	32.44	32.44	26.6	20.0	107.7	107.0	7.71	7.71	1.53	1.55	9.27	9.27	9.30
2	l1				В	14	1	8.14	8.14	32.44	32.44	26.5	26.5	105.3	105.3	7.62	7.63	1.51	1.52	7.78	7.78	7.76
	l1				В	14	2	8.14	0.14	32.44	52.44	26.5	20.5	105.2	105.5	7.63	7.03	1.52	1.52	7.74	7.74	7.70
	C1				S	1	1	8.13	8.13	32.38	32.38	26.5	26.5	111.5	111.6	7.83	7.83	1.14	1.14	16.53	16.53	16.57
po	C1				S	I	2	8.13	0.13	32.38	32.30	26.5	20.5	111.6	111.0	7.82	7.03	1.13	1.14	16.60	16.60	10.57
Flood	C1	SUNNY	14:00	17	М	8	1	8.13	8.13	32.38	32.38	26.5	26.5	109.1	109.2	7.75	7.75	1.12	1.13	15.89	15.89	15.92
Aid-F	C1	SUNNT	14.00	17	М	0	2	8.13	0.13	32.38	52.50	26.5	20.5	109.2	109.2	7.74	1.15	1.13	1.15	15.94	15.94	13.92
-	C1				В	16	1	8.14	8.14	32.38	32.38	26.5	26.5	106.6	106.7	7.67	7.67	1.13	1.14	15.80	15.80	15.73
	C1				В	10	2	8.14	0.14	32.38	32.30	26.5	20.5	106.7	100.7	7.66	1.01	1.14	1.14	15.66	15.66	10.70



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-38
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

	ode				Water									In-situ Me	asurement						Lab	oratory Anal	ysis
Date	Tidal Mode	Monitoring Location	Weather	Time	Depth (m)	Monitoring Level	Monitoring Level (m)	Replicate	р	н	Salinit	y (ppt)	Tempera	iture (°C)	DO Satur	ation (%)	DO (	mg/L)	Turbidit	ty (NTU)		pended solids - 105 (ºC), m	
	F								Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value	Ave.	Value		Ave.
10/30/2024		WMS-1N				S	4	1	8.06	0.00	32.25	22.05	25.9	05.0	108.7	100.0	7.77	7 70	1.07	4.00	7.45	7.45	7.44
		WMS-1N				S	1	2	8.06	8.06	32.25	32.25	25.9	25.9	108.8	108.8	7.78	7.78	1.08	1.08	7.42	7.42	7.44
	Mid-Ebb	WMS-1N	SUNNY	11:00	7	М	- 3	1	8.07	8.07	32.25	32.25	25.9	25.9	106.2	106.3	7.69	7.70	1.08	1.08	5.86	5.86	5.85
	Mid-	WMS-1N	SUNNY	11.00	· ·	М	3	2	8.07	0.07	32.25	52.25	25.9	20.9	106.3	100.5	7.70	7.70	1.07	1.00	5.84	5.84	5.65
		WMS-1N				В	- 6	1	8.07	8.07	32.28	32.28	25.8	25.8	104.2	104.3	7.62	7.63	1.09	1.10	7.86	7.86	7.84
		WMS-1N				В	0	2	8.07	0.07	32.28	32.20	25.8	23.0	104.3	104.5	7.63	7.03	1.10	1.10	7.81	7.81	7.04
		WMS-2N				S	- 1	1	8.07	8.07	32.28	32.28	26.0	26.0	106.7	106.7	7.69	7.70	1.54	1.54	6.65	6.65	6.66
		WMS-2N				S	I	2	8.07	0.07	32.28	32.20	26.0	20.0	106.6	100.7	7.70	7.70	1.53	1.54	6.66	6.66	0.00
	Mid-Ebb	WMS-2N	SUNNY	10:45	4	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid-	WMS-2N	SUNNY	10.45	4	М	INA	2	NA	NA	NA	NA NA	NA	INA	NA	INA	NA	INA	NA	INA	NA	NA	INA
		WMS-2N				В	- 3	1	8.07	8.07	32.29	32.29	25.9	25.9	104.5	104.6	7.65	7.65	1.57	1.57	7.02	7.02	7.01
		WMS-2N				В	3	2	8.07	0.07	32.29	32.29	25.9	25.9	104.6	104.6	7.64	7.05	1.56	1.57	6.99	6.99	7.01
Γ		WMS3				S	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
		WMS3				S	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid-Ebb	WMS3		10.15		М	1.5	1	8.10	8.10	32.32	32.32	26.0	26.0	106.3	106.4	7.67	7.68	1.27	1.28	8.12	8.12	8.12
	Mid-	WMS3	SUNNY	10:15 3	М	1.5	2	8.10	0.10	32.32	32.32	26.0	20.0	106.4	100.4	7.68	7.00	1.28	1.20	8.11	8.11	0.12	
		WMS3				В	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
		WMS3				В	NA NA	2	NA	NA	NA	INA	NA	NA NA	NA	INA	NA	INA	NA	INA	NA	NA	INA
		WMS4				S	1	1	8.12	8.12	32.35	32.35	26.3	26.3	111.1	111.2	7.85	7.86	1.00	1.00	6.21	6.21	6.20
		WMS4				S		2	8.12	0.12	32.35	32.33	26.3	20.3	111.2	111.2	7.86	7.00	1.00	1.00	6.18	6.18	0.20
	Ebb	WMS4	SUNNY	9:30	4	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid-Ebb	WMS4	SUMME	9.30	4	М	INA	2	NA	NA	NA	NA	NA	NA	NA	INA	NA	INA.	NA	NA	NA	NA	NA.
		WMS4				В	- 3	1	8.11	8.11	32.35	32.35	26.3	26.3	109.0	109.0	7.78	7.79	1.12	1.13	5.45	5.45	5.44
		WMS4				В	5	2	8.11	0.11	32.35	52.55	26.3	20.5	108.9	109.0	7.79	1.19	1.13	1.15	5.43	5.43	5.44
		WMS5				S	- 1	1	8.11	8.11	32.35	32.35	26.4	26.4	108.6	108.7	7.77	7.78	1.47	1.47	5.23	5.23	5.22
		WMS5				S	I	2	8.11	0.11	32.35	52.55	26.4	20.4	108.7	100.7	7.78	1.10	1.46	1.47	5.20	5.20	5.22
	Mid-Ebb	WMS5	SUNNY	9:45	4.7	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid-	WMS5	SUMM	9.45	4.7	М	INA.	2	NA		NA		NA		NA	INA.	NA		NA		NA	NA	
		WMS5				В	4	1	8.11	8.11	32.35	32.35	26.2	26.2	106.0	106.1	7.70	7.71	1.33	1.33	4.76	4.76	4.74
		WMS5				В	4	2	8.11	0.11	32.35	52.55	26.2	20.2	106.1	100.1	7.71	7.71	1.33	1.55	4.72	4.72	4.74
		WMS6				S	- 1	1	8.11	8.11	32.35	32.35	26.4	26.4	107.3	107.4	7.74	7.75	1.37	1.38	5.94	5.94	5.97
		WMS6				S	I	2	8.11	0.11	32.35	52.55	26.4	20.4	107.4	107.4	7.75	1.15	1.38	1.50	5.99	5.99	5.97
	Mid-Ebb	WMS6	SUNNY	10:00	4.7	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	Mid-	WMS6	SUMMI	10.00	4.7	М	NA .	2	NA		NA	INA .	NA	INA	NA	INA	NA	INA	NA	INA	NA	NA	
		WMS6				В	4	1	8.11	8.11	32.35	32.35	26.2	26.2	105.1	105.1	7.66	7.67	1.32	1.32	6.23	6.23	6.23
		WMS6				В		2	8.11	0.11	32.35	52.55	26.2	20.2	105.0	103.1	7.67	1.07	1.31	1.52	6.23	6.23	0.20
I [		12				S	- 1	1	8.09	8.09	32.33	32.33	26.4	26.4	111.6	111.6	7.86	7.87	1.13	1.14	8.53	8.53	8.55
	-Ebb	12	SUNNY	9:00	16	S		2	8.09	0.09	32.33	52.55	26.4	20.4	111.5	111.0	7.87	1.01	1.14	1.14	8.56	8.56	0.00
	Mid-Ebb	12	SUMME	9.00		М	- 8	1	8.08	8.08	32.33	32.33	26.3	26.3	108.8	108.9	7.78	7.79	1.14	1.14	11.21	11.21	11.19
		12				М	0	2	8.08	0.00	32.33	52.55	26.3	20.3	108.9	100.9	7.79	1.19	1.14	1.14	11.17	11.17	11.19




EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-39
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24


	12				В		1	8.07		32.32		26.8		106.3		7.71		1.13		7.96	7.96	1
	12				В	15	2	8.07	8.07	32.32	32.32	26.8	26.8	106.4	106.4	7.70	7.71	1.14	1.14	7.93	7.93	7.95
	C2				S		1	8.07		32.28		26.0		106.5		7.69		1.52		15.78	15.78	
	C2				S	1	2	8.07	8.07	32.28	32.28	26.0	26.0	106.6	106.6	7.70	7.70	1.53	1.53	15.71	15.71	15.75
qq	C2				M		1	NA		NA		NA		NA		NA		NA		NA	NA	
Mid-Ebb	C2	SUNNY	10:30	3.9	M	NA	2	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
≥	C2				В		1	8.07		32.30		26.0		104.2		7.64		1.58		15.01	15.01	
	C2				В	3	2	8.07	8.07	32.30	32.30	26.0	26.0	104.3	104.3	7.65	7.65	1.57	1.58	15.10	15.10	15.06
	C3				S		1	8.10		32.33		26.4		110.2		7.78		1.53		14.02	14.02	
	C3				S	1	2	8.10	8.10	32.33	32.33	26.4	26.4	110.2	110.3	7.77	7.78	1.52	1.53	13.95	13.95	13.99
요	C3				M		1	8.10		32.33		26.3		107.8		7.74		1.47		14.21	14.21	
Mid-Ebb	C3	SUNNY	9:15	13	M	6	2	8.10	8.10	32.33	32.33	26.3	26.3	107.9	107.9	7.73	7.74	1.48	1.48	14.13	14.13	14.17
Σ	C3				В		1	8.10		32.33		26.3		104.8		7.66		1.43		13.55	13.55	
	C3				В	12	2	8.10	8.10	32.33	32.33	26.3	26.3	104.9	104.9	7.67	7.67	1.44	1.44	13.48	13.48	13.52
	WMS-1N				S		1	8.12		32.37		26.0		107.9		7.74		1.09		6.26	6.26	
	WMS-1N WMS-1N				S	1	2	8.12	8.12	32.37	32.37	26.0	26.0	107.8	107.9	7.75	7.75	1.08	1.09	6.16	6.16	6.21
ро	WMS-1N WMS-1N				M		1	8.14		32.37		26.0		107.0		7.66		1.08		7.42	7.42	
Mid-Flood	WMS-1N WMS-1N	SUNNY	15:45	7.5	M	3	2	8.14	8.14	32.37	32.37	26.0	26.0	105.4	105.4	7.67	7.67	1.03	1.08	7.42	7.42	7.42
Mic	WMS-1N WMS-1N				B		1	8.13		32.40		25.9		103.0		7.59		1.07		8.08	8.08	
	WMS-1N WMS-1N				В	7	2	8.13	8.13	32.40	32.40	25.9	25.9	103.0	103.1	7.60	7.60	1.10	1.10	8.13	8.13	8.11
	WMS-2N				S	1	1	8.13	8.13	32.40	32.40	26.1	26.1	105.7	105.8	7.66	7.67	1.55	1.55	6.53	6.53	6.52
po	WMS-2N				S		2	8.13		32.40		26.1		105.8		7.67		1.54		6.50	6.50	
Mid-Flood	WMS-2N	SUNNY	15:30	4.5	M	NA	1	NA	NA	NA NA	NA	NA	NA	NA	NA	NA NA	NA	NA NA	NA	NA	NA	NA
Mic	WMS-2N				M		2	NA 0.42				NA 20.0		NA 102.0						NA 4.07	NA 4.07	
	WMS-2N				B	4	1	8.13	8.13	32.41	32.41	26.0	26.0	103.6	103.7	7.62	7.62	1.58	1.58	4.87	4.87	4.89
	WMS-2N						2	8.13		32.41		26.0		103.7		7.61		1.57		4.90	4.90	
	WMS3				S	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
р	WMS3				S		2	NA		NA 00.44		NA		NA		NA		NA		NA 5.00	NA	
Mid-Flood	WMS3 WMS3	SUNNY	15:15	3.2	M	1.5	1	8.16	8.16	32.44	32.44	26.2 26.2	26.2	105.1	105.2	7.64 7.65	7.65	1.25 1.26	1.26	5.63 5.63	5.63	5.63
Mig							2	8.16		32.44				105.2							5.63	
	WMS3				B	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	WMS3				В		2	NA		NA		NA		NA		NA		NA		NA	NA	
	WMS4 WMS4				S	1	1	8.17	8.17	32.47	32.47	26.4	26.4	110.2	110.2	7.82	7.83	1.12	1.12	9.10	9.10	9.07
р					S		2	8.17		32.47		26.4		110.1		7.83		1.11		9.04	9.04	
Mid-Flood	WMS4	SUNNY	14:30	4.5	M	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
Mic	WMS4				M		2	NA		NA		NA		NA 100.0		NA		NA		NA	NA	
	WMS4				В	4	8.17	32.47	32.47	26.4	26.4	108.0	108.0	7.75	7.76	1.13	1.13	7.41	7.41	7.39		
	WMS4				В		2	8.17		32.47		26.4		107.9		7.76		1.13		7.37	7.37	
	WMS5				S		1	8.17	8.17	32.47	32.47	26.5	26.5	107.7	107.8	7.74	7.75	1.48	1.48	5.32	5.32	5.33
R	WMS5				S		2 8.17	32.47		26.5		107.8		7.75		1.47		5.34	5.34			
Mid-Flood	WMS5	SUNNY	14:45	5.2	M	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
Mid	WMS5				M		2	NA		NA		NA		NA		NA		NA		NA	NA	
	WMS5				В	4	1	8.17	8.17	32.47	32.47	26.3	26.3	105.2	105.2	7.67	7.68	1.37	1.37	4.86	4.86	4.88
	WMS5				В		2	8.17		32.47		26.3		105.1		7.68		1.36		4.89	4.89	

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-40
<b>CCC</b>	Works at Po Toi O	Ref#	EMA2403/03/42
<b>JUJ</b>	Monthly EM&A Report	Rev.	01
		Date	Nov 24


		WMS6				S	4	1	8.17	0.47	32.48	22.40	26.5	00 F	106.5	100.0	7.71	7 70	1.39	1.00	7.11	7.11	7.00				
	_	WMS6				S	1	2	8.17	8.17	32.48	32.48	26.5	26.5	106.6	106.6	7.72	7.72	1.38	1.39	7.07	7.07	7.09				
	pool	WMS6		45.00	5.0	М	NA	1	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA				
	Mid-F	WMS6	SUNNY	15:00	5.2	М	NA	2	NA	INA	NA	INA	NA	NA	NA	INA	NA	INA	NA	INA	NA	NA	INA				
	2	WMS6				В	4	1	8.17	0.17	32.48	32.48	26.3	26.3	104.0	104.0	7.63	7.64	1.35	1.35	6.23	6.23	6.00				
		WMS6				В	4	2	8.17	8.17	32.48	32.40	26.3	20.3	103.9	104.0	7.64	7.64	1.34	1.35	6.21	6.21	6.22				
Γ		l1				S	1	1	8.16	8.16	32.45	32.45	26.5	26.5	109.5	109.6	7.75	7.75	1.50	1.51	4.32	4.32	4.33				
	pool	l1	SUNNY 14:1			S	I	2	8.16	0.10	32.45	32.43	26.5	20.5	109.6	109.6	7.74	7.75	1.51	1.51	4.33	4.33	4.33				
		l1		SUNNY	SUNNY 1	SUNNY 14:15	14.15	14	М	7	1	8.16	0.16	32.45	22.45	26.4	26.4	107.0	107.1	7.71	7.71	1.49	1.49	6.56	6.56	6.54	
	Mid-F	l1			14:15	14:15	14:15	NY 14:15	14	м ′	1	2	8.16	8.16	32.45	32.45	26.4	26.4	107.1	107.1	7.70	7.71	1.48	1.49	6.51	6.51	0.34
	2	l1									1	8.16	0.16	32.45	22.45	26.4	26.4	104.0	104.1	7.63	7.64	1.46	1.46	7.86	7.86	7.04	
		l1				В	13	2	8.16	8.16	32.45	32.45	26.4	26.4	104.1	104.1	7.64	7.64	1.45	1.40	7.82	7.82	7.84				
Γ		C1				S	4	1	8.15	8.15	32.42	32.42	26.5	26.5	110.8	110.8	7.83	7.84	1.12	1.13	13.68	13.68	13.64				
	-	C1				S	I	2	8.15	0.15	32.42	32.42	26.5	20.5	110.7	110.0	7.84	7.04	1.13	1.15	13.60	13.60	13.04				
	pool <sup>-</sup>	C1	SUNNY	14:00	17	М	8	1	8.15	8.15	32.42	32.42	26.4	26.4	108.0	108.1	7.75	7.76	1.13	1.14	12.12	12.12	12.10				
	Mid-F	C1	SUNNT	14.00	17	М	0	2	8.15	0.15	32.42	32.42	26.4	20.4	108.1	100.1	7.76	7.70	1.14	1.14	12.07	12.07	12.10				
		C1						В	16	8.13	8.13	32.40	32.40	26.9	26.9	105.4 105.5	7.67	7.68	1.12	1.13	18.11	18.11	18.10				
		C1				В	10	2	8.13	0.15	32.40	52.40	26.9	20.9	105.5	105.5	7.68	7.00	1.13	1.15	18.08	18.08	10.10				



## WMS1N GRAPHICAL RESULTS

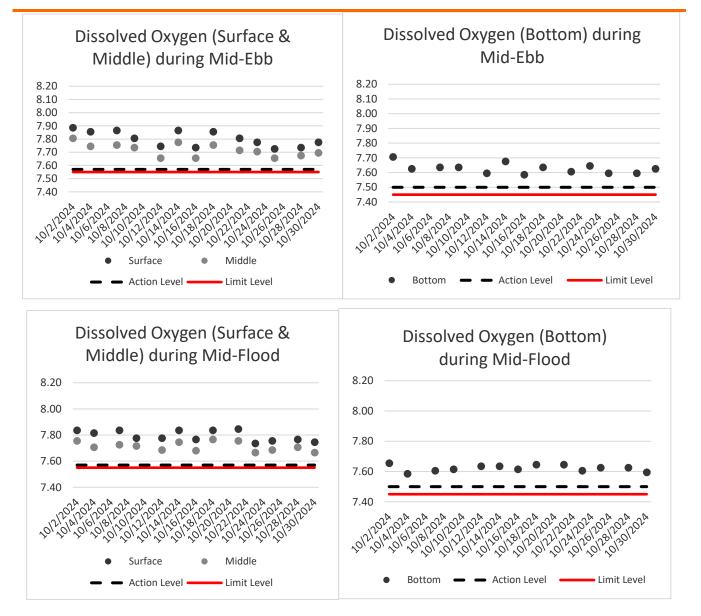





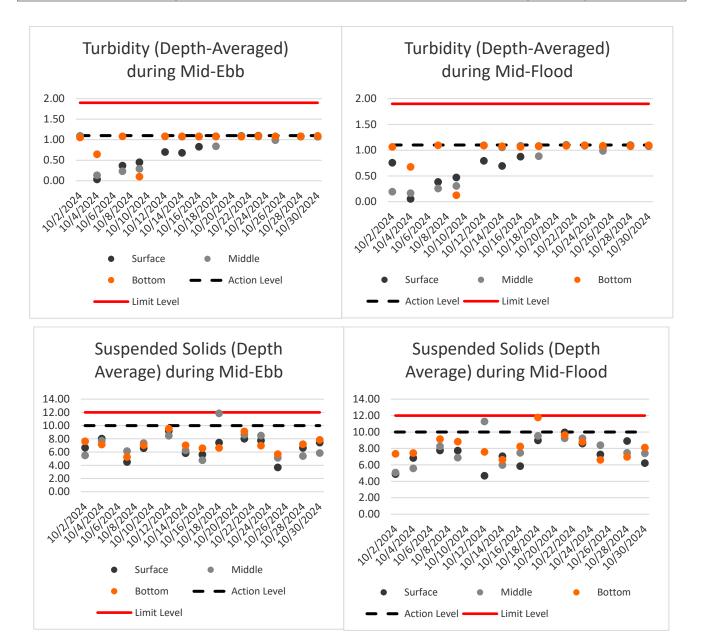


EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-43
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
	Date	Nov 24

### WMS2N Graphical Results

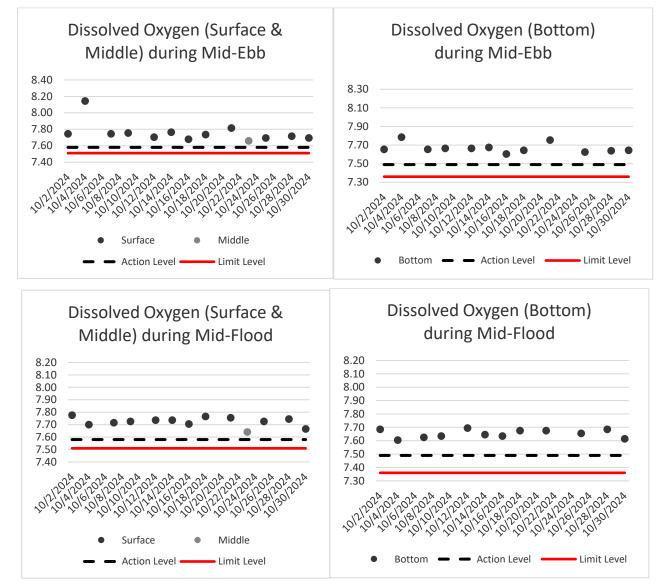



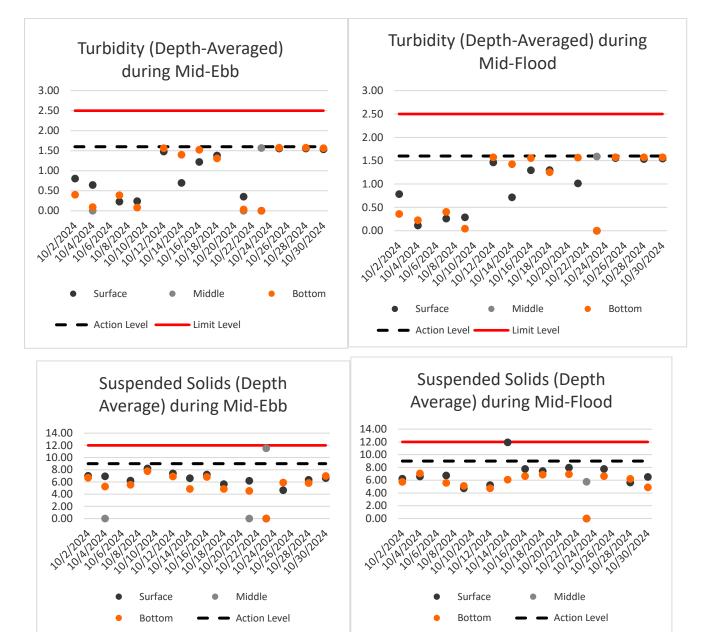



Limit Level


Limit Level

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-45
	Works at Po Toi O	Ref#	EMA2403/03/42
JUD	Monthly EM&A Report	Rev.	01
		Date	Nov 24

## WMS3 Graphical Results

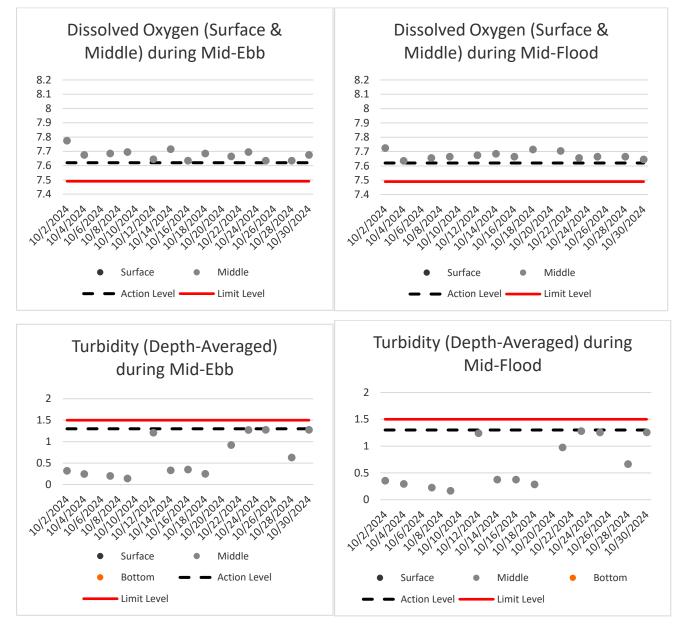




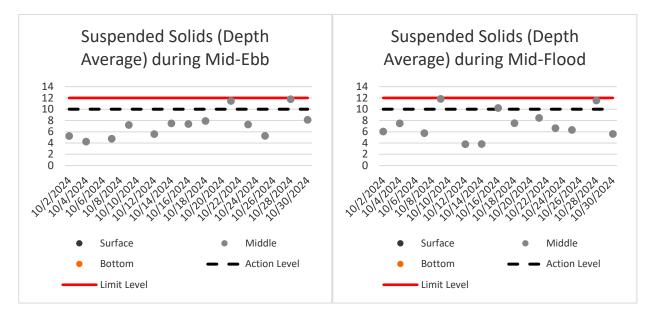


EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-47
Works at Po Toi O	Ref#	EMA2403/03/42
Monthly EM&A Report	Rev.	01
, <u></u>	Date	Nov 24

### WMS4 Graphical Results

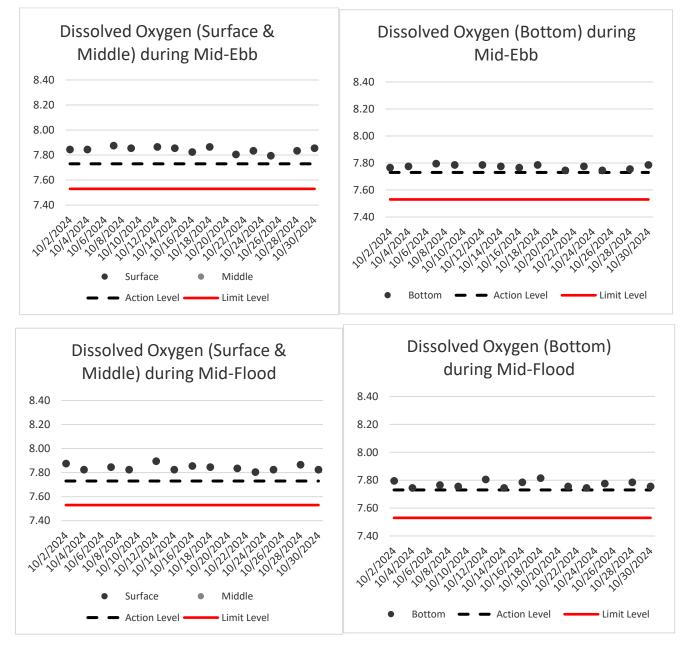


	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-48
	Works at Po Toi O	Ref#	EMA2403/03/42
JUD	Monthly EM&A Report	Rev.	01
	, <u></u>	Date	Nov 24

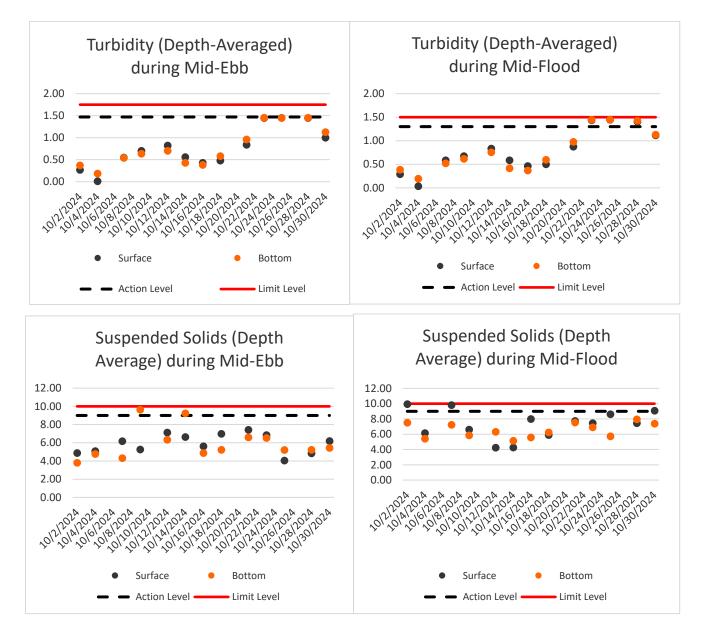


	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-49
	Works at Po Toi O	Ref#	EMA2403/03/42
<b>JUJ</b>	Monthly EM&A Report	Rev.	01
	, <u></u>	Date	Nov 24

## WMS5 Graphical Results

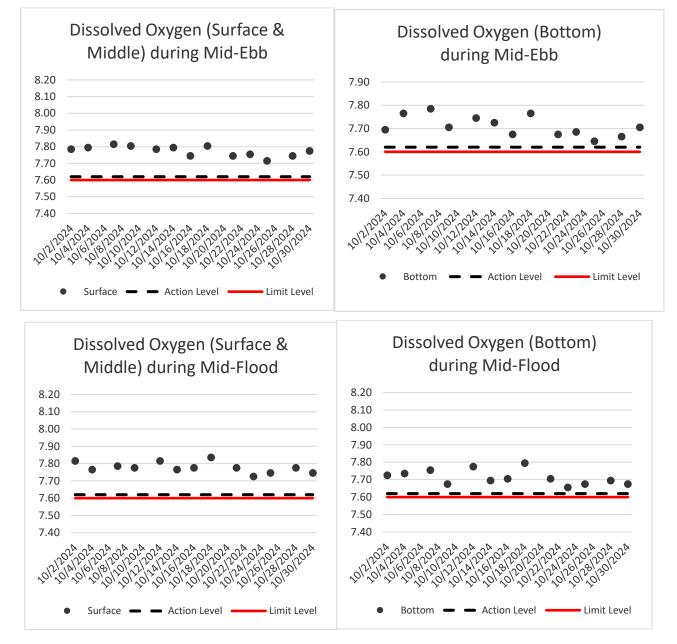





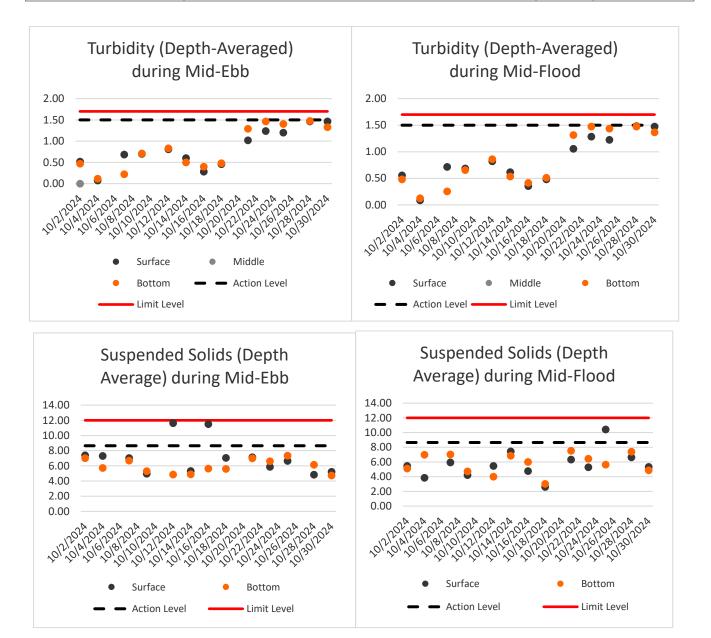


000	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-51
	Works at Po Toi O	Ref#	EMA2403/03/42
	Monthly EM&A Report	Rev.	01
		Date	Nov 24

### WMS6 Graphical Results

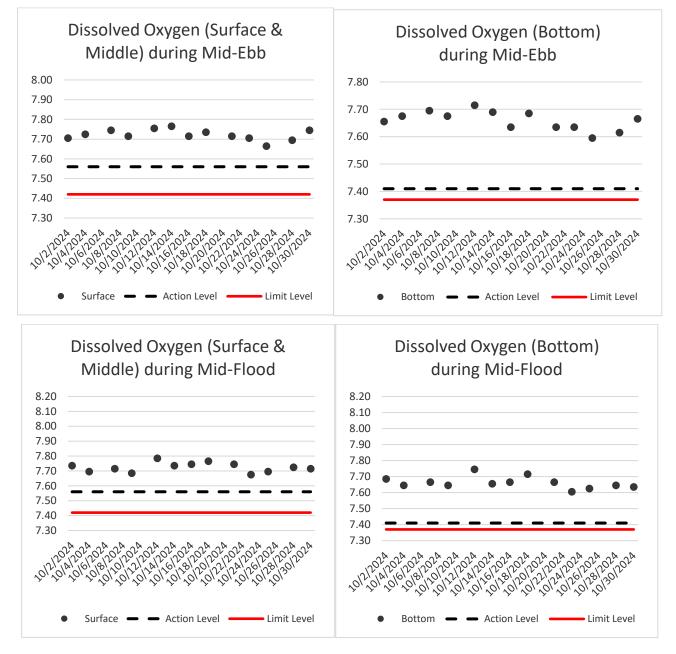




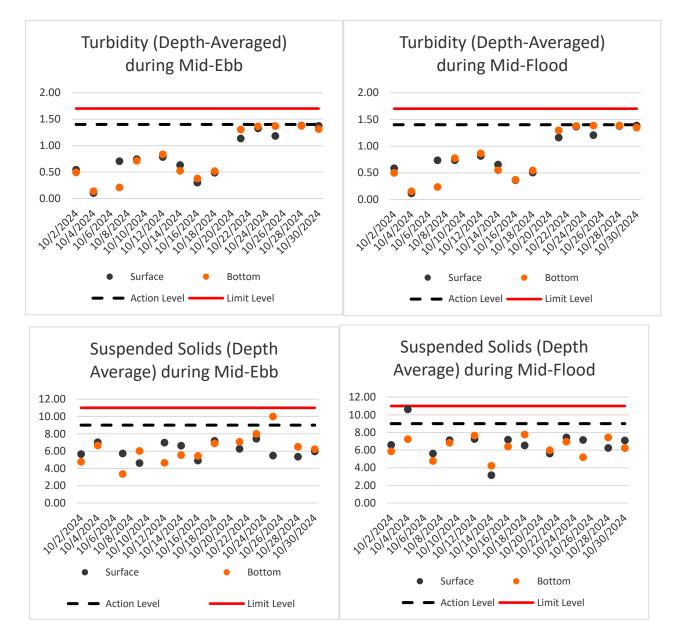


	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-53
	Works at Po Toi O	Ref#	EMA2403/03/42
<b>DUD</b>	Monthly EM&A Report	Rev.	01
		Date	Nov 24

## **<u>11 Graphical Results</u>**

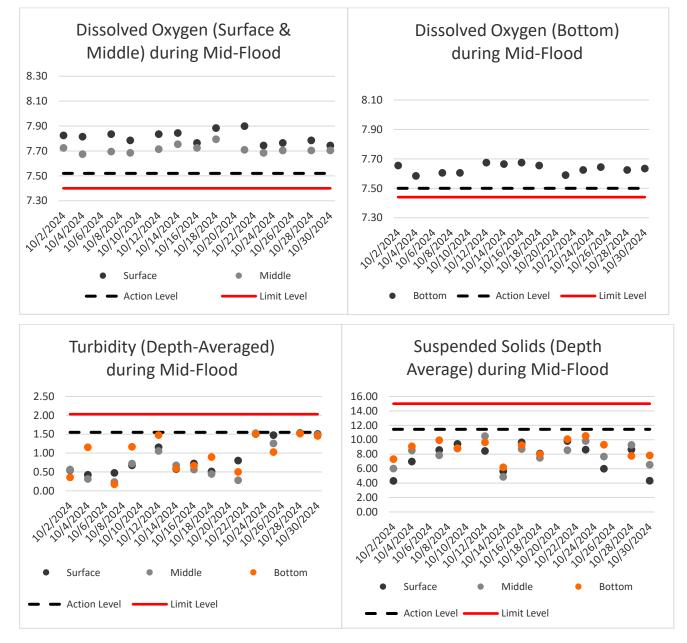

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage	Page	L-54
	Works at Po Toi O	Ref#	EMA2403/03/42
JUD	Monthly EM&A Report	Rev.	01
		Date	Nov 24

## **12 Graphical Results**

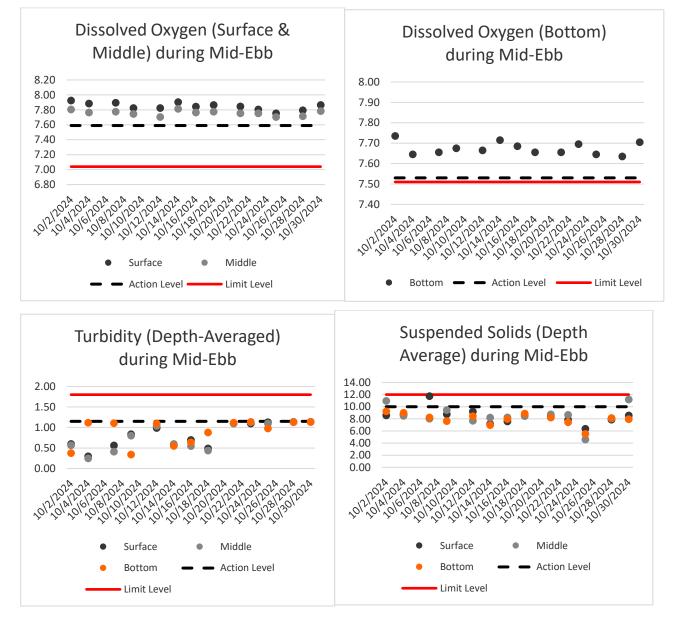



# APPENDIX M – CALIBRATION CERTIFICATE OF WATER QUALITY MONITORING EQUIPMENT



#### Performance Check / Calibration of Multiparameter Water Quality Meter

Equipment Ref. No.:	EV-W-073-02	Manufacturer:	Aquaread
Model No.:	AP-800	Serial No.:	219520927
Date of Calibration:	8/28/2024	Next Calibration Date:	28-Nov-24

#### <u>Results</u>

1. Temperature

(Method Reference: In-house calibration procedure THERMO.CMP)

Reading of Reference Thermometer (°C)	Displayed Reading (°C)	Tolerance (°C)	Result
16.0	16.40	0.4	Acceptable
25.1	25.90	0.8	Acceptable
39.6	40.20	0.6	Acceptable

Tolerance Limit (°C): ±2.0

### 2. pH 🤺

#### (Method Reference: APHA 23rd ed. 4500 H\* B)

Expected Reading (pH unit)	Displayed Reading (pH unit)	Tolerance (pH unit)	Result
3.639		#VALUE!	N/A
6.864		#VALUE!	N/A
9.18		#VALUE!	N/A

Tolerance Limit (pH unit): ±0.20

#### Salinity

(Method Reference: APHA 2	23rd ad 2520 B)		
Expected Reading (ppt)	Displayed Reading (ppt)	Tolerance (%)	Result
15	15.67	4.47	Acceptable
25	25.99	3.96	Acceptable
35	35.98	2.80	Acceptable

Tolerance Limit (%): ±10.0

#### 4. Dissolved Oxygen

#### (Method Reference: APHA 23rd ed. 4500-O G)

Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)	Result
3.59	3.99	0.40	Acceptable
5.79	6.03	0.24	Acceptable
7.39	7.09	-0.30	Acceptable

Tolerance Limit (mg/L): ±0.50

#### 5. Turbidity

#### (Method Reference: APHA 23rd ed. 2130 B)

Expected Reading (NTU)	Displayed Reading (NTU)	Tolerance (%)	Result
0	0	-	Acceptable
10	9.5	-5.00	Acceptable
200	207	3.50	Acceptable
1000	1005	0.50	Acceptable

Tolerance Limit (%): ±10.0

The equipment is deemed acceptable / unacceptable \* for use. (\* Delete as appropriate).

### - \* pt1 probe is prober .

Calibrated by: Tiffany

Approved by:



EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		N-1
		EMA2403/03/42
Monthly EM&A Report		01
		Nov 24

# APPENDIX N – MONTHLY SUMMARY OF WASTE FLOW



	wonting Summary waste flow Table for 2024 fear										
		Actual Quant	tities of Inert	C&D Materia	als Generate	ed Monthly	Actual	Quantities of (	C&D Waste	s Generated	Monthly
Month	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposal as Public Fill	Imported Fill	Metals	Paper / Cardboard Packaging	Plastics (see note 3)	Chemical Waste	Other, e.g. general refuse
	(in '000m³)	(in '000m³)	(in '000m³)	(in '000m³)	(in '000m³)	(in '000m³)	[in '000kg]	[in '000kg]	[in '000kg]	[in '000kg]	[in Tonne]
Jan	0.083	0.000	0.000	0.000	0.083	0.000	0.000	0.000	0.000	0.000	0.000
Feb	0.239	0.000	0.000	0.000	0.202	0.000	0.000	0.000	0.000	0.000	0.037
Mar	0.775	0.000	0.000	0.000	0.657	0.000	0.000	0.000	0.000	0.000	0.118
Apr	0.481	0.000	0.000	0.000	0.350	0.000	0.000	0.000	0.000	0.000	0.131
Мау	0.160	0.000	0.000	0.000	0.160	0.000	0.000	0.000	0.000	0.000	0.000
June	0.305	0.000	0.000	0.000	0.305	0.000	0.000	0.000	0.000	0.000	0.000
Sub- Total	2.043	0.000	0.000	0.000	1.757	0.000	0.000	0.000	0.000	0.000	0.286
July	0.439	0.000	0.000	0.000	0.439	0.000	0.000	0.000	0.000	0.000	0.000
Aug	0.367	0.000	0.000	0.000	0.367	0.000	0.000	0.000	0.000	0.000	0.000
Sep	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Oct	0.129	0.000	0.000	0.000	0.129	0.000	0.000	0.000	0.000	0.000	0.000
Nov											
Dec											
Total	2.978	0.000	0.000	0.000	2.692	0.000	0.000	0.000	0.000	0.000	0.286

## Monthly Summary Waste Flow Table for 2024 Year

Note:

1) The performance targets are given in the Environmental Management Plan.

(2) The waste flow table shall also include C&D materials to be imported for use at the Site.

(3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material.



# **APPENDIX O - IMPLEMENTATION SCHEDULE OF RECOMMENDED MITIGATION MEASURES**

	ED 510/0010 Dart Chalter Coursens Stars? Coursens Works at Do Tai O	Page	0-2
	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Ref#	EMA2403/03/42
<b>JUJ</b>	Monthly EM&A Report		01
		Date	Nov 24

EIA	EM	Recommended Mitigation Measures *	Objectives of the	Implementation	Location of	Duration of the	Implementation	Relevant
Ref.	& A		<b>Recommended Measure &amp;</b>	Agent	the measure	measure	stages	Legislation &
	Ref.		Main Concerns to address					Guidelines
Air Qu	ality imp	act						
Projec	t Specifie	c Measures						
3.8	A1	Deodourizer should have at least 99.5% hydrogen sulfide removal	To minimize odour nuisance to	DSD	Sewage	Throughout	Operational phase	EIAO-TM
		efficiency.	sensitive receivers		Treatment Plant	operational phase		
3.8	A2	Odourous materials (sludge, screenings and grits, worn filter)	To minimize odour nuisance to	DSD	Sewage	Throughout	Operational phase	EIAO-TM
		should be stored and removed in sealed tankers and containers.	sensitive receivers		Treatment Plant	operational phase		
3.8	A3	Sludge should be transferred to sludge tanker by coupling	To minimize odour nuisance to	DSD	Sewage	Throughout	Operational phase	EIAO-TM
		method.	sensitive receivers		Treatment Plant	operational phase		
3.8	A4	During release of pressure from the tanker, the odourous gas	To minimize odour nuisance to	DSD	Sewage	Throughout	Operational phase	EIAO-TM
		should be discharged into the sludge storage room for extraction	sensitive receivers		Treatment Plant	operational phase		
		to deodourization unit.						
3.8	A5	Regular inspection should be conducted to check for leakage of	To minimize odour nuisance to	DSD	Sewage	Throughout	Operational phase	EIAO-TM
		odourous gas.	sensitive receivers		Treatment Plant	operational phase		
3.8	A6	Maintain the removal efficiency of screenings and grits by	To maintain the removal	DSD	Sewage	Throughout	Operational phase	EIAO-TM
		flushing the screens and grit sump regularly to prevent buildup of	efficiency of screenings and		Treatment Plant	operational phase		
		solids	grits					
3.8	A7	Maintain the efficiency of MBR membrane by removing	To maintain the efficiency of	DSD	Sewage	Throughout	Operational phase	EIAO-TM
		organic and inorganic debris regularly	MBR membrane		Treatment Plant	operational phase		
3.8	A8	Replace worn filter to maintain the odour removal efficiency at	To minimize odour nuisance to	DSD	Sewage	Throughout	Operational phase	EIAO-TM
		99.5%	sensitive receivers		Treatment Plant	operational phase		
3.8	A9	Clean all the tanks with water regularly	To minimize odour nuisance to	DSD	Sewage	Throughout	Operational phase	EIAO-TM
			sensitive receivers		Treatment Plant	operational phase		
Genera	al/Stand	ard Measures						
3.8	A10	Good housekeeping to minimize dust generation, e.g. by	To minimize dust generation	DSD's Contractor	Whole	Throughout	Construction	EIAO-TM,
		properly handling and storing dusty materials			construction	construction phase	Phase	APCO
					site			
3.8	A11	Adopt dust control measures, such as dust suppression using	To minimize dust generation	DSD's Contractor	Whole	Throughout	Construction	EIAO-TM,
		water spray on exposed soil (at least 4 times per day), in areas	due to erosion		construction	construction phase	phase	APCO
		with dusty construction activities and during material handling			site			

	Dert Shalter Sawarana Stana? Sawarana Warka at Da Tai O	Page	0-3
	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Ref#	EMA2403/03/42
303	Monthly EM&A Report	Rev.	01
	······································	Date	Nov 24

EIA	EM &	Recommended Mitigation Measures *	Objectives of the	Implementation	Location of	Duration of the	Implementation	Relevant
Ref.	A Ref.		Recommended Measure &	Agent	the measure	measure	stages	Legislation &
			Main Concerns to address					Guidelines
3.8	A12	Store cement bags in shelter with 3 sides and the	To prevent leakage of cement	DSD's	Whole	Throughout	Construction	EIAO-TM, APCO
		top covered by impervious materials if the stack		Contractor	construction	construction	phase	
		exceeds 20 bags			site	phase		
3.8	A13	Maintain a reasonable height when dropping	To minimize dust generation during movement of excavated	DSD's	Whole	Throughout	Construction	EIAO-TM, APCO
		excavated materials to limit dust generation	materials	Contractor	construction	construction	phase	
					site	phase		
3.8	A14	Limit vehicle speed within construction site and in	To minimize dust generation due to traffic movement	DSD's	Whole	Throughout	Construction	EIAO-TM, APCO
		Po Toi O to 10km/hr and confine vehicle		Contractor	construction	construction	phase	
		movement in haul road			site	phase		
3.8	A15	Minimize exposed earth after completion of work in	To minimize dust generation due to erosion	DSD's	Whole	Throughout	Construction	EIAO-TM, APCO
		a certain area by hydroseeding, vegetating, soil		Contractor	construction	construction	phase	
		compacting or covering with bitumen			site	phase		
3.8	A16	Provide wheel washing at construction site exit to	To prevent dust from being brought offsite	DSD's	Whole	Throughout	Construction	EIAO-TM, APCO
		clean the vehicle body and wheel		Contractor	construction	construction	phase	
					site	phase		
3.8	A17	Cover materials on trucks before leaving the	To prevent falling of debris during traffic movement and by wind	DSD's	Whole	Throughout	Construction	EIAO-TM, APCO
		construction site to prevent debris from dropping		Contractor	construction	construction	phase	
		during traffic movement or being blown away by			site	phase		
		wind						
3.8	A18	Regular maintenance of plant equipment to	To minimize black smoke emission	DSD's	Whole	Throughout	Construction	EIAO-TM, APCO
		prevent black smoke emission		Contractor	construction	construction	phase	
					site	phase		
3.8	A19	Throttle down or switch off unused machines or	To minimize unnecessary emission	DSD's	Whole	Throughout	Construction	EIAO-TM, APCO
		machine in intermittent use		Contractor	construction	construction	phase	
					site	phase		
3.8	A20	Minimize excavation area as far as possible	To minimize dust emission and potential release of odour from	DSD's	Whole	Throughout	Construction	EIAO-TM, APCO
			exposed ground	Contractor	construction	construction	phase	
					site	phase		
L	I			I				

	EP-516/2016 - Port Shalter Sowerage, Stage? - Sowerage Works at Bo Toi O	Page	O-4
	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Ref#	EMA2403/03/42
JUJ	Monthly EM&A Report		01
		Date	Nov 24

EIA	EM &	Recommended Mitigation Measures *	Objectives of the	Implementation	Location of	Duration of the	Implementation	Relevant
Ref.	A Ref.		Recommended Measure &	Agent	the measure	measure	stages	Legislation &
			Main Concerns to address					Guidelines
3.8	A21	Store odourous excavated materials in covered	To minimize odour nuisance to sensitive receivers	DSD's	Whole	Throughout	Construction	EIAO-TM, APCO
		containers and remove off-site as soon as possible		Contractor	construction	construction	phase	
		within 24 hours			site	phase		
3.8	A22	Cover open stockpiles of construction materials	To prevent soil erosion under rainstorm	DSD's	Whole	Throughout	Construction	EIAO-TM, APCO
		(e.g. aggregates, sand and fill materials) with		Contractor	construction	construction	phase	
		impermeable materials such as tarpaulin during			site	phase		
		rainstorms						
3.8	A23	Hoarding of not less than 2.4 m high shall be	To minimize dust emission	DSD's	Whole	Throughout	Construction	EIAO-TM, APCO
		erected from ground level to surround the		Contractor	construction	construction	phase	
		construction site for sewage treatment plant along			site	phase		
		Po Toi O Chuen Road except for a construction						
		site entrance or exit						
3.8	A24	Carry out air quality monitoring throughout the	To monitor construction dust level	DSD's	At	Prior to and	Construction	EIAO-TM
		construction period		Contractor	representative	throughout	phase	
					ASRs	construction		
						phase		
3.8	A25	Carry out regular site inspection to audit the	To check the implementation status and effectiveness of	DSD's	Whole	Throughout	Construction	EIAO-TM, APCO
		implementation of mitigation measures	mitigation measures	Contractor	construction	construction	phase	
					site	phase		

EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	
Ref# EM	EMA2403/03/42
Monthly EM&A Report Rev. 01	01
	Nov 24

EIA	EM	Recommended Mitigation Measures *	Objectives of the	Implementation	Location of	Duration of the	Implementation	Relevant
Ref.	& A		Recommended Measure &	Agent	the measure	measure	stages	Legislation &
	Ref.		Main Concerns to address					Guidelines
Noise	Impact							
Projec	t Specif	ïc Measures						
4.7	N1	Use hand-held plant equipment or manual equipment within village area	To minimize construction noise level	DSD's Contractor	Whole construction site	Throughout construction phase	Construction phase	NCO, EIAO-TM
4.7	N2	For HDD, enclose the stationary plant equipment on three sides with cover. Only the side facing the sea shall be opened for heat exhaustion.	To lower noise transmission	DSD's Contractor	HDD work site	Throughout construction phase	Construction Phase	NCO, EIAO-TM
4.7	N3	Generator should be placed at a fixed location at least 5-6m away from the NSRs and screened by noise barrier whenever excavation work has to be carried out at their front doors	To lower noise transmission	DSD's Contractor	Whole construction site	Throughout construction phase	Construction Phase	NCO, EIAO-TM
4.7	N4	Avoid carrying out noisy activities at the same time. The work front of village sewer installation near NSRs PTO_N1 and PTO_N3 shall not be conducted concurrently with installation of Po Toi O Chuen Road sewer and horizontal directional drilling respectively.	To minimize noise production	DSD's Contractor	Whole construction site	Throughout construction phase	Construction Phase	NCO, EIAO-TM
4.7	N5	Vibratory poker shall only be operated 4m away from NSR and with noise barrier properly erected. Surfacing work within 4m from NSR shall be carried out by manual method	To minimize noise production	DSD's Contractor	Whole construction site	Throughout construction phase	Construction phase	NCO, EIAO-TM
Gene	ric/Stand	ard Measures			•			L
4.7	N6	Schedule noisy activities to minimise exposure of nearby NSRs to high levels of construction noise	To minimize construction noise level	DSD's Contractor	Whole construction site	Throughout construction phase	Construction Phase	NCO, EIAO-TM
4.7	N7	Use Quality Powered Mechanical Equipment (QPME) which produces lower noise level	To minimize construction noise level	DSD's Contractor	Whole construction site	Throughout construction phase	Construction Phase	NCO, EIAO-TM
4.7	N8	Erect 3m high mobile barriers with skid footing and a small cantilevered upper portion within a few metres of stationary plants and within about 5m of more mobile plant.	To lower noise transmission	DSD's Contractor	Whole construction site	Throughout construction phase	Construction phase	NCO, EIAO-TM

	ED 546/2016 Davt Shalter Sowarage Stage? Sowarage Warks at De Tai O	Page	O-6
	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Ref#	EMA2403/03/42
JUJ	Monthly EM&A Report		01
	······································	Date	Nov 24

EIA	EM &	Recommended Mitigation Measures *	Objectives of the	Implementation	Location of	Duration of the	Implementation	Relevant
Ref.	A Ref.		Recommended Measure &	Agent	the measure	measure	stages	Legislation &
			Main Concerns to address					Guidelines
4.7	N9	Hand-held breaker shall be fitted with mufflers. A movable enclosure made	To lower noise transmission	DSD's	Whole	Throughout	Construction	EIAO-TM, APCO
		up of plywood is proposed to surround both worker and breaker during		Contractor	construction	construction	phase	
		breaking process. The internal wall of the enclosure should be laid with			site	phase		
		sound absorbent such as mineral wool.						
4.7	N10	Regular maintenance of plant equipment to prevent noise emission due to	To prevent noise emission due	DSD's	Whole	Throughout	Construction	EIAO-TM, APCO
		impair	to impair	Contractor	construction	construction	phase	
					site	phase		
4.7	N11	Position mobile noisy equipment in location and direction away from NSR	To minimize noise transmission	DSD's	Whole	Throughout	Construction	EIAO-TM, APCO
			to NSR	Contractor	construction	construction	phase	
					site	phase		
4.7	N12	Use silencer or muffler on plant equipment and should be properly	To minimize noise transmission	DSD's	Whole	Throughout	Construction	EIAO-TM, APCO
		maintained		Contractor	construction	construction	phase	
					site	phase		
4.7	N13	Throttle down or switch off unused machines or machine in Intermittent	To minimize noise production	DSD's	Whole	Throughout	Construction	EIAO-TM, APCO
		use between work		Contractor	construction	construction	phase	
					site	phase		
4.7	N14	Make good use of stockpiles or other structures for noise screening	To minimize noise transmission	DSD's	Whole	Throughout	Construction	EIAO-TM, APCO
				Contractor	construction	construction	phase	
					site	phase		
4.7	N15	Mobile plant should be sited as far away from NSRs as possible	To minimize noise transmission	DSD's	Whole	Throughout	Construction	EIAO-TM, APCO
				Contractor	construction	construction	phase	
					site	phase		
4.7	N16	Reduce the percentage on-time for some noisy PMEs	To mimize noise production	DSD's	Whole	Throughout	Construction	EIAO-TM, APCO
				Contractor	construction	construction	phase	
					site	phase		
4.7	N17	Carry out noise monitoring	To monitor construction noise	DSD's	At	Prior to and	Construction	EIAO-TM, APCO
			level	Contractor	representative	throughout	phase	
					NSRs	construction		
						phase		

	ED 515/2016 Dart Shelter Sourcease Stars? Sourcease Works at De Tei O	Page	0-7
	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Ref#	EMA2403/03/42
<b>JUJ</b>	Monthly EM&A Report	Rev.	01
		Date	Nov 24

EIA	EM	Recommended Mitigation Measures *	Objectives of the	Implementation	Location of	Duration of	Implementation	Relevant
Ref.	& A		Recommended Measure &	Agent	the measure	the	stages	Legislation &
	Ref.		Main Concerns to address			measure		Guidelines
Water	Quality	Impact						
Projec	t Specif	fic Measures						
5.8	W1	Divert the water from outfall of W3 (stream near Fairway Vista) during open cut	To prevent the excavated	DSD's	Whole	Throughout	Construction	ProPECC PN 1/94,
		excavation for laying of gravity sewer nearby	materials from falling into the	Contractor	construction site	construction	phase	EIAOTM
			water and being carried into the		3110	phase		
			sea					
5.8	W2	Place sandbag along the upstream section of the stream near Fairway Vista and	To prevent the excavated	DSD's	Whole	Throughout	Construction	ProPECC PN 1/94,
		along rocky shore during open cut excavation for laying of gravity sewers/rising	materials from falling into the	Contractor	construction	construction	Phase	EIAOTM
		mains nearby.	water and being carried into the		site	phase		
			sea					
5.8	W3	Intercept the water from u-channel at the foot of the slope where the STP will be	To prevent water from entering	DSD's	Whole	Throughout	Construction	EIAO-TM
		built	the construction site	Contractor	construction site	construction	Phase	
					Unite -	phase		
5.8	W4	Install cofferdam around the proposed excavation area for entry pit of HDD work	To prevent debris from entering	DSD's	HDD work site	Throughout	Construction	EIAO-TM
		to prevent falling of debris into the sea	the waterbodies	Contractor		construction	Phase	
						phase		
5.8	W5	Install sheet piles in marine waters by vibratory action.	To minimize dispersion of	DSD's	Whole	Throughout	Construction	EIAO-TM
			marine sediment	Contractor	construction site	construction	phase	
						phase		
5.8	W6	Marine works (dredging, construction and installation works at diffuser location,	To minimize dispersion of	DSD's	Whole	Throughout	Construction	EIAO-TM
		backfilling) shall be carried out inside the watertight cofferdam. The cofferdam	marine sediment	Contractor	construction site	construction	Phase	
		can only be removed after completion of work				phase		
5.8	W7	Dredging should be carried out by grab dredgers anchored outside the cofferdam.	To minimize dispersion of	DSD's	Whole	Throughout	Construction	EIAO-TM
		The marine sediment should be placed in sealed compartment of the marine	marine sediment	Contractor	construction site	construction	Phase	
		barge.				phase		
5.8	W8	Water removed from the cofferdam should be desilted before discharge back into		DSD's	Whole	Throughout	Construction	EIAO-TM
		the sea.	To prevent discharge of silty	Contractor	construction site	construction	phase	
			water into the sea			phase		

	ED 516/2016 Datt Shaltar Sawarana Stars? Sawarana Warka at Da Tai O	Page	O-8
	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Ref#	EMA2403/03/42
343	Monthly EM&A Report	Rev.	01
	······································	Date	Nov 24

EIA	EM & A	Recommended Mitigation Measures *	Objectives of the	Implementation	Location of	Duration of the	Implementation	Relevant Legislation &
Ref.	Ref.		Recommended Measure &	Agent	the measure	measure	stages	Guidelines
			Main Concerns to address					
5.8	W9	Carry out water quality monitoring at water sensitive receivers before and during	To identify any water quality	DSD's	Water	Before and	Construction	EIAO-TM
		cofferdam installation works, throughout dredging works, and during cofferdam	impact due to construction	Contractor	Monitoirng	throughout	phase	
		extraction works	works		Stations	installation and		
						extraction works		
						of cofferdam		
5.8	W10	The following summarizes the precautionary measures for	To prevent emergency	DSD	Sewage	Operational phase	Operational	EIAO-TM
		minimizing chance of emergency discharge:	discharge		Treatment Plant		phase	
		Provision of dual power by CLP;						
		• Equipped with Supervisory control and data acquisition system (SCADA), which						
		signals to the operation and maintenance personnel for emergency attendance in						
		case of plant failure;						
		<ul> <li>Provision of standby pump and screen at the PTOSTW.</li> </ul>						
		Provision of emergency generator within 4 hours by DSD's future term contractor.						
		Provision of emergency storage with capacity of 4-hr sewage retention time.						
		Arrangement of tankers for removing incoming sewage to other sewage treatment						
		plants for treatment.						
5.8	W11	Carry out water quality monitoring at water sensitive receivers during normal	To identify any water quality	DSD	At	6 months before	Operational	WPCO, EIAO-TM
		operation	impact due to the normal		representative	and in 1st year of	phase	
			operation of the Sewage		WSRs	operation		
			Treatment Plant (STP)					
Generi	c/Standard N	leasures		•				
5.8	W12	Set up sedimentation tank for settling suspended solids in wastewater before	To reduce the amount of	DSD's	Whole	Throughout	Construction	ProPECC PN 1/94,
		discharge into storm drains. Sand/silt removal facilities such as sand traps, silt traps	suspended solid in wastewater	Contractor	construction	construction	phase	EIAO-TM
		and sedimentation basin should be provided with adequate capacity.			site	phase		
5.8	W13	Follow ProPECC PN 1/94 "Construction Site Drainage" as far as practicable	To minimize surface runoff and	DSD's	Whole	Throughout	Construction	ProPECC PN 1/94,
			chance of erosion	Contractor	construction	construction	phase	EIAO-TM
					site	phase		
5.8	W14	Construct catchpits and perimeter channels prior to commencement of site formation	To stop runoff from flowing	DSD's	Whole	Throughout	Construction	ProPECC PN 1/94,
		works and earthworks.	across the construction site	Contractor	construction	construction	phase	EIAO-TM
					site	phase		
5.8	W15	Maintain silt removal facilities, channels, manholes before and after rainstorm.	To prevent failure that may lead	DSD's	Whole	Throughout	Construction	ProPECC PN 1/94,
			to flooding	Contractor	construction	construction	phase	EIAO-TM
					site	phase		

SGS	ED 546/2040 Bart Chalter Courseans Stars? Courseans Works at Da Tai O	Page	O-9
	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Ref#	EMA2403/03/42
<b>JUJ</b>	Monthly EM&A Report	Rev.	01
		Date	Nov 24

EIA Ref.	EM & A Ref.	Recommended Mitigation Measures *	Objectives of the Recommended Measure & Main Concerns to address	Implementation Agent	Location of the measure	Duration of the measure	Implementation stages	Relevant Legislation & Guidelines
5.8	W16	Remove silt and grit from silt trap at regular interval.	To prevent blockage the may lead to flooding	DSD's Contractor	Whole construction site	Throughout construction phase	Construction phase	ProPECC PN 1/94, EIAO-TM
5.8	W17	Well design works program to minimize the work areas to minimize the soil exposure and site runoff.	To minimize surface runoff and chance of erosion	DSD's Contractor	Whole construction site	Throughout construction phase	Construction phase	ProPECC PN 1/94, EIAO-TM
5.8	W18	Arrange soil excavation works outside rainy seasons (202 to September) as far as possible. If this cannot be achieved, the following measures should be implemented: - Cover temporary exposed slope surfaces with impermeable materials, e.g. tarpaulin - Protect temporary access roads by crushed stone or gravel - Provide intercepting channels along crest/edge of excavation - Carry out adequate surface protection measures well before the arrival of a rainstorm	To minimize surface runoff and chance of erosion	DSD's Contractor	Whole construction site	Throughout construction phase	Construction phase	ProPECC PN 1/94, EIAO-TM
5.8	W19	Minimize exposed earth after completion of work in a certain area by hydroseeding, vegetating, soil compacting or covering with bitumen	To prevent soil erosion under Rainstorm	DSD's Contractor	Whole construction site	Throughout construction phase	Construction phase	ProPECC PN 1/94, EIAO-TM
5.8	W20	Prevent rainwater from entering trenches. Excavation of trenches should be dug and backfilled in short sections during rainy seasons. Remove silt in rainwater collected from the trenches or foundation excavations prior to discharge to storm drains.	To prevent soil erosion under Rainstorm	DSD's Contractor	Whole construction site	Throughout construction phase	Construction phase	ProPECC PN 1/94, EIAO-TM
5.8	W21	Cover open stockpiles of construction materials (e.g. aggregates, sand and fill materials) with impermeable materials such as tarpaulin during rainstorms.	To prevent soil erosion under rainstorm	DSD's Contractor	Whole construction site	Throughout construction phase	Construction phase	ProPECC PN 1/94, EIAO-TM
5.8	W22	Cover and temporary seal manholes to prevent silt, construction materials or debris and surface runoff from entering foul sewers.	To prevent overloading of foul sewers	DSD's Contractor	Whole construction site	Throughout construction phase	Construction phase	ProPECC PN 1/94, EIAO-TM
5.8	W23	Remove waste from the construction site regularly.	To prevent waste accumulation	DSD's Contractor	Whole construction site	Throughout construction phase	Construction phase	EIAO-TM, APCO
5.8	W24	Apply discharge license for effluent discharge. Treat the discharge to comply with the requirement in TM-DSS.	To ensure compliance with effluent discharge requirement	DSD's Contractor	Whole construction site	Throughout construction phase	Construction phase	WPCO, TM-DSS, EIAOTM

SGS	ED 516/2016 Dert Shelter Sewerere Sterre? Sewerere Werke at De Tei O	Page	O-10
	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Ref#	EMA2403/03/42
<b>JUJ</b>	Monthly EM&A Report		01
		Date	Nov 24

EIA Ref.	EM & A Ref.	Recommended Mitigation Measures *	Objectives of the Recommended Measure &	Implementation Agent	Location of the measure	Duration of the measure	Implementation stages	Relevant Legislation &
iter.			Main Concerns to address	Agent	the measure	medeure	olugeo	Guidelines
5.8	W25	Reuse treated effluent onsite, e.g. dust suppression, wheel washing and general cleaning.	To minimize wastewater	DSD's	Whole	Throughout	Construction	Waste Disposal
			generation	Contractor	construction	construction	phase	Ordinance, EIAO-
					site	phase		ТМ
5.8	W26	Monitor effluent water quality	To ensure compliance with	DSD's	Whole	Throughout	Construction	WPCO, EIAO-TM
			effluent discharge requirement	Contractor	construction	construction	phase	
					site	phase		
5.8	W27	Register as chemical waste producer if chemical waste will be generated.	To control chemical waste	DSD's	Whole	Throughout	Construction	Waste Disposal
				Contractor	construction	construction	phase	(Chemical
					site	phase		Waste) (General)
								Regulation, EIAO-
								ТМ
5.8	W28	Perform maintenance of vehicles and equipment that have oil leakage and spillage potential on	To prevent oil leakage or	DSD's	Whole	Throughout	Construction	Waste Disposal
		hard standings within a bunded area with sumps and oil interceptors.	spillage	Contractor	construction	construction	phase	(Chemical
					site	phase		Waste) (General)
								Regulation, EIAO-
								ТМ
5.8	W29	Dispose chemical waste in accordance to Waste Disposal Ordinance. Follow the Code of Practice	To avoid accident in waste	DSD's	Whole	Throughout	Construction	Waste Disposal
		on the Packaging, Labelling and Storage of Chemical Wastes, examples as follows:	storage and handling	Contractor	construction	construction	phase	Ordinance, EIAO-
		- Store chemical wastes with suitable containers to avoid leakage or spillage during storage,			site	phase		ТМ
		handling and transport						
		- Label chemical waste containers according to the CoP to notify and warn the waste handlers						
		- Store chemical wastes at designated safe location with adequate space						
5.8	W30	Provide sufficient chemical toilets with regular maintenance by registered waste collector where	To proper collection of tasks	DSD's	Whole	Throughout	Construction	Waste Disposal
		necessary	force waste	Contractor	construction	construction	phase	Ordinance, EIAO-
					site	phase		TM
5.8	W31	Provide a drip tray/container underneath the bentonite recycling system	To prevent any leaked bentonite	DSD's	Whole	Throughout	Construction	EIAO-TM
			from entering the watercourse	Contractor	construction	construction	phase	
			or sea		site	phase		
5.8	W32	Carry out regular site inspection to audit the implementation of mitigation measures	To check the implementation	DSD's	Whole	Throughout	Construction	EIAO-TM, APCO
			status and effectiveness of	Contractor	construction	construction	phase	
			mitigation measures		site	phase		
5.8	W33	Carry out effluent quality monitoring at location specified in the discharge licence	To ensure compliance with effluent discharge requirement	DSD	Effluent outlet	Operational phase	Operational phase	WPCO, EIAO-TM

SGS	ED 546/2016 Dart Shelter Sawarana Stance Sowarana Warks at Da Tai O	Page	O-11
	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Ref#	EMA2403/03/42
	Monthly EM&A Report	Rev.	01
		Date	Nov 24

EIA Ref.	EM & A Ref.	Recommended Mitigation Measures *	Objectives of the Recommended Measure & Main Concerns to address	Implementation Agent	Location of the measure	Duration of the measure	Implementation stages	Relevant Legislation &
Tourset								Guidelines
	ial Ecolog	·						
	Specific M			:			1	
6.12	E1	Erect bright color fencing along the boundary of the undisturbed region of the shrubland and woodland, and around <i>Diospyros vaccinioides</i> , a plant species of conservation importance,	To protect the shrub from being Damaged	DSD's Contractor	Whole construction site	Throughout construction	Construction phase	EIAO-TM
		near the work boundary to remind workers not to trespass or occupy the area, and to be careful during operation of equipment.			310	phase	phaoo	
6.12	E2	Reinstate the disturbed rocky shore with the rocks temporarily removed	To restore the rocky shore habitat	DSD's Contractor	HDD work site	After completion of works near the	Construction Phase	EIAO-TM
						rocky shore	1 11000	
6.12	E3	Place sandbag around the section of W3 next to Fairway Vista and along the shore during	To prevent the excavated	DSD's	Whole	When	Construction	EIAO-TM
		open cut excavation for laying of gravity sewer nearby.	materials from falling into the	Contractor	ractor construction site	construction work	Phase	
			water and being carried into the sea			is carried out in the vicinity of W3		
6.12	E4	Temporarily divert the water from outfall of W3 away from excavation area.	To prevent the excavated materials from	DSD's	Whole	When	Construction	EIAO-TM
			falling into the water and being carried into	Contractor	construction site	construction work	Phase	
			the sea			is carried out in		
						the vicinity of W3		
6.12	E5	Inspect the condition of the Diospyros vaccinioides near the work boundary as part of weekly	To inspect the condition of the Diospyros	DSD's Contractor	Whole construction	Throughout	Construction	EIAO-TM
		site audit	vaccinioides	Contractor	site	construction phase	phase	
Generic	/Standard	Measures						
6.12	E6	Erection of hoarding, fencing or provision of clear demarcation of work zones	To remind workers not to	DSD's	Whole	Throughout	Construction	EIAO-TM
			damage area outside the work boundary	Contractor	construction site	construction phase	Phase	
6.12	E7	Designate areas for placement of equipment, building materials and wastes away from the	To prevent damage on the	DSD's	Whole	Throughout	Construction	EIAO-TM
		natural environment	natural environment	Contractor	construction site	construction phase	Phase	
6.12	E8	Carry out tree preservation and compensatory tree planting will be carried out in accordance		DSD's	Whole	After completion	Construction	EIAO-TM
		with DEVB TCW No. 7/2015.	To reinstated woodland habitat	Contractor	construction site	of works near woodland	phase	

202	ED 516/2016 Dort Sholtor Sourcease Stage? Sourcease Works at Po Tei O	Page	O-12
	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Ref#	EMA2403/03/42
<b>JUJ</b>	Monthly EM&A Report	Rev.	01
		Date	Nov 24

EIA	EM & A	Recommended Mitigation Measures *	Objectives of the	Implementation	Location of	Duration of the	Implementation	Relevant
Ref.	Ref.		Recommended Measure &	Agent	the measure	measure	stages	Legislation &
			Main Concerns to address					Guidelines
Terrest	trial Ecology							
Project	Specific Me	asures						
9.8	WM1	Sludge will be delivered by sealed sludge tanker for treatment at Sludge	To prevent odour nuisance	DSD	STP	Throughout	Operational	Waste Disposal
		Treatment Facilities				construction	phase	(Chemical
						phase		Waste)
								(General)
								Regulation,
								EIAO-TM
9.8	WM2	Debris from screening process and general refuse should be stored within	To prevent odour nuisance	DSD	STP	Throughout	Operational	Waste Disposal
		the STP in sealed container and be disposed of at landfill regularly.				construction	phase	(Chemical
						phase		Waste)
								(General)
								Regulation,
								EIAO-TM
9.8	WM3	Worn filters and MBR membrane shall be stored and labelled as in	To prevent odour nuisance	DSD	STP	Throughout	Operational	Waste Disposal
		construction phase. Chemical wastes shall be treated at chemical				construction	phase	Ordinance,
		treatment facility by licensed contractor				phase		EIAO-TM
Generi	c/Standard N	Aeasures						
9.8	WM4	Allocate an area for waste sorting and storage of C&D materials	To minimize waste generation	DSD's	Whole	Throughout	Construction	Waste Disposal
		into the following categories for reuse, recycle or disposal if		Contractor	construction site	construction	Phase	Ordinance,
		possible. Remove waste from the construction site for sorting				phase		EIAO-TM
		once generated if no suitable space can be identified.						
		- excavated materials suitable for reuse						
		- inert C&D materials (or public fill) for disposal offsite						
		- non-inert C&D materials (or C&D waste) for disposal at						
		landfills						
		- chemical waste						
		- bentonite slurry for reconditioning and reuse						
		- general refuse						

202	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page Ref#	O-13 EMA2403/03/42
<b>343</b>	Monthly EM&A Report	Rev.	01
		Date	Nov 24

EIA	EM & A	Recommended Mitigation Measures *	Objectives of the	Implementation	Location of	Duration of the	Implementation	Relevant
Ref.	Ref.		<b>Recommended Measure &amp;</b>	Agent	the measure	measure	stages	Legislation &
			Main Concerns to address					Guidelines
9.8	WM5	Adopt good site practice as follows:	To proper handling of waste	DSD's	Whole	Throughout	Construction	Waste Disposal
		- Provide training to workers on site cleanliness, waste		Contractor	construction	construction	t Construction n phase t Construction n phase t Construction n phase t Construction	Ordinance,
		management (waste reduction, reuse and recycle) and chemical			site	phase		EIAO-TM
		handling procedures						
		- Provide sufficient waste collection points and regular removal						
		- Cover waste materials with tarpaulin or in enclosure during						
		transportation						
		- Maintain drainage systems, sumps and oil interceptors						
		- Sort out chemical waste for proper handling and treatment						
		onsite or offsite						
9.8	WM6	Adopt waste reduction measures as follows:	To minimize waste generation	DSD's	Whole	Throughout	Construction	Waste Disposal
		- Allocate area/containers for sorting, recovering and storing		Contractor	construction	construction	phase	Ordinance,
		waste for reuse, recycle or disposal (e.g. demolition debris and			site	phase		EIAO-TM
		excavated materials, general refuse like aluminium cans.)						
		Remove waste from the construction site for sorting once						
		generated if no suitable space can be identified.						
		- Allocate area for proper storage of construction materials to						
		prevent contamination						
		- Minimize wastage through careful planning and avoiding overpurchase						
		of construction materials						
9.8	WM7	Prepare and implement a site-specific Waste Management Plan (WMP) as	To provide guidance to waste	DSD's	Whole	Throughout	Construction	ETWB TCW
		part of Environmental Management Plan (EMP) in accordance with ETWB	management	Contractor	construction	construction	phase	No.
		TCW No. 19/2005. Detail waste management method in the form of			site	phase		19/2005, EIAO-
		avoidance, reuse, recovery, recycling, storage, collection, treatment and						ТМ
		disposal according to the recommendations on the EIA and EM&A Manual.						
		It should be approved by the ER and regularly reviewed.						

Monthly EM&A Report     Rev.     01		ED 510/0010 Dert Shelter Severane Stars? Severane Works at De Tei O	Page	O-14
Monthly EM&A Report	<b>CCC</b>	Ref	Ref#	EMA2403/03/42
	<b>JUJ</b>	Monthly EM&A Report	Rev.	01
Date Nov 24				Nov 24

EIA	EM & A	Recommended Mitigation Measures *	Objectives of the	Implementation	Location of	Duration of the	Implementation	Relevant Legislation &
Ref.	Ref.		Recommended Measure &	Agent	the measure	measure	stages	Guidelines
			Main Concerns to address					
9.8	WM8	Store waste materials properly as follows:	To properly store waste	DSD's	Whole	Throughout	Construction	ProPECC PN 1/94, EIAOTM
		- Avoid contamination by proper handling and storing waste		Contractor	construction	construction	phase	
		- Prevent erosion by covering waste			site	phase		
		- Apply water spray on excavated materials						
		- Maintain and clean storage area regularly						
		- Sort and stockpile different materials at designated location to enhance reuse						
9.8	WM9	Apply for relevant waste disposal permits in accordance with the Waste Disposal	To properly dispose waste	DSD's	Whole	Throughout	Construction	Waste Disposal Ordinance
		Ordinance (Cap. 354), Waste Disposal (Charges for Disposal of Construction Waste)		Contractor	construction	construction	phase	(Cap. 354), Waste
		Regulation (Cap. 345) and the Land (Miscellaneous Provisions) Ordinance (Cap. 28),			site	phase		Disposal (Charges for
		Dumping at Sea Ordinance (Cap. 466).						Disposal of Construction
								Waste) Regulation (Cap.
								345) and the Land
								(Miscellaneous
								Provisions) Ordinance
								(Cap. 28), Dumping at
								Sea Ordinance (Cap.
								466), EIAO-TM
9.8	WM10	Hire licensed waste disposal contractors for waste collection and removal. Dispose waste	To properly dispose waste	DSD's	Whole	Throughout	Construction	Waste Disposal
		at licensed waste disposal facilities		Contractor	construction	construction	phase	Ordinance, EIAO-TM
					site	phase		
9.8	WM11	Implement trip-ticket system for recording the amount of waste generated, recycled and	To monitor movement of waste	DSD's	Whole	Throughout	Construction	Waste Disposal (Chemical
		disposed, including chemical wastes		Contractor	construction	construction phase	phase	Waste) (General)
					site	phase		Regulation, Waste
								Disposal Ordinance,
								EIAO-TM
9.8	WM12	Provide wheel washing at construction site exit to clean the vehicle body and wheel	To prevent dust from being	DSD's	Whole	Throughout	Construction	ProPECC PN 1/94, EIAOTM
			brought offsite	Contractor	construction	construction phase	phase	
					site	phase		
9.8	WM13	Reduce water content in wet spoil generated from piling work by mixing with dry	To minimize load to reception	DSD's	Whole	Throughout	Construction	Waste Disposal
		materials. Only dispose treated spoil with less than 25% dry density to Public Fill	facilities	Contractor	construction	construction phase	phase	Ordinance, EIAO-TM
		Reception Facilities			site	pridoe		

Monthly EM&A Report     Rev.     01		ED 546/2040 Dart Chalter Coursense Stars2 Coursense Works at Da Tai O	Page	O-15
Monthly EM&A Report		Ref#	Ref#	EMA2403/03/42
	JUD	Monthly EM&A Report	Rev.	01
		······································	Date	Nov 24

EIA	EM & A	Recommended Mitigation Measures *	Objectives of the	Implementation	Location of	Duration of the	Implementation	Relevant Legislation &
Ref.	Ref.		Recommended Measure &	Agent	the measure	measure	stages	Guidelines
			Main Concerns to address					
9.8	WM14	Dispose dry waste or waste with less than 70% water content by	To minimize load to reception	DSD's	Whole	Throughout	Construction	Waste Disposal
		weight to landfill	facilities	Contractor	construction	construction	phase	Ordinance, EIAO-TM
					site	phase		
9.8	WM15	Follow the Code of Practice on the Packaging, Labelling and Storage of Chemical Waste	To avoid accident in waste	DSD's	Whole	Throughout	Construction	Waste Disposal
		as follows:	storage and handling	Contractor	construction	construction	phase	Ordinance, EIAO-TM
		- Store chemical wastes with suitable containers. Seal and maintain the container to			site	phase		
		avoid leakage or spillage during storage, handling and transport						
		- Label chemical waste containers in both English and Chinese with instructions in						
		accordance to Schedule 2 of the Waste Disposal (Chemical Waste) (General) Regulation						
		- The container capacity should be smaller than 450 litres unless agreed by the EPD						
9.8	WM16	Comply with the requirement of the chemical storage area:	To ensure proper storage of	DSD's	Whole	Throughout	Construction	Waste Disposal
		- Store only chemical waste and label clearly the chemical characters of the waste	chemical waste	Contractor	construction	construction	phase	Ordinance, EIAO-TM
		- Have at least 3 sides enclosed and protected from rainfall with cover			site	phase		
		- Provide sufficient ventilation						
		- Have impermeable floor and has bunds to contain 110% of the						
		capacity of the largest container or 20% of the total volume of						
		the stored waste in the area, whichever is larger						
		- Adequately spaced incompatible materials						
9.8	WM17	Transfer used lubricants, waste oils and other chemicals to oil recycling companies, if	To ensure proper disposal of	DSD's	Whole	Throughout	Construction	Waste Disposal (Chemical
		possible, and empty oil drums for reuse or refill. No direct or indirect discharge is	chemical waste	Contractor	construction	construction phase	phase	Waste) (General)
		permitted			site	P		Regulation, EIAO-TM
9.8	WM18	Hire licensed chemical waste disposal contractors for waste collection and removal.	To ensure proper disposal of	DSD's	Whole	Throughout	Construction	Waste Disposal (Chemical
		Dispose chemical waste at the approved Chemical Waste Treatment Centre at Tsing Yi	chemical waste	Contractor	construction	construction phase	phase	Waste) (General)
		or other licensed facility			site	P		Regulation, EIAO-TM
9.8	WM19	Hire reputable waste collector to separately collect and dispose general refuse from other	To ensure proper disposal of	DSD's	Whole	Throughout	Construction	Waste Disposal (Chemical
		wastes. Cover the waste to prevent being blown away	general refuse	Contractor	construction	construction phase	phase	Waste) (General)
					site	pridoo		Regulation, EIAO-TM

	ED 516/2016 - Dart Shakar Sawarana Starra? - Sawarana Warka at Da Tai O	Page	O-16
	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Ref#	EMA2403/03/42
<b>JUJ</b>	Monthly EM&A Report	Rev.	01
		Date	Nov 24

EIA	EM & A	Recommended Mitigation Measures *	Objectives of the	Implementation	Location of	Duration of	Implementation	Relevant Legislation &
Ref.	Ref.		<b>Recommended Measure</b>	Agent	the measure	the	stages	Guidelines
			&			measure		
			Main Concerns to					
			address					
9.8	WM20	Provide recycling bins for sorting out recyclables for collection by recycling	To ensure proper recycling	DSD's	Whole	Throughout	Construction	Waste Disposal
		companies. Non-recyclables should be removed to designated landfills	and	Contractor	construction	construction	phase	Ordinance, EIAO-TM
		every day by licensed collectors to prevent environmental and health	disposal of general refuse		site	phase		
		nuisance.						
9.8	WM21	Organize training and reminders to site staff on waste minimization through	To ensure proper	DSD's	Whole	Throughout	Construction	EIAO-TM
		avoidance and reduction, reusing and recycling	management	Contractor	construction	construction	phase	
			of general refuse		site	phase		
9.8	WM22	Used bentonite shall be reconditioned onsite and reused as far as practical	To minimize wastage of	DSD's	Whole	Throughout	Construction	EIAO-TM
		to minimize wastage. If this is deemed not viable, the used bentonite shall	bentonite	Contractor	construction	construction	phase	
		be delivered offsite for reconditioning.			site	phase		
9.8	WM23	Characterize the sediment quality of the marine sediment to be dredged and	To verify the categories of	DSD's	To be	Before	Construction	ETWB TC(W) No.
		submit a Sediment Quality Report for EPD's approval. Dispose the dredged	sediment to be disposed in	Contractor	allocated	dredging works	phase	34/2002
		marine sediment in accordance with ETWB TC(W) No. 34/2002	accordance with ETWB		by CEDD			
			TC(W)					
			No. 34/2002					

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	0-17
	LI -510/2010 - I olt olleller Sewerage, Slages - Sewerage Works at 10 1010	Ref#	EMA2403/03/42
JUD	Monthly EM&A Report	Rev.	01
		Date	Nov 24

EIA Ref.	EM & A Ref.	Recommended Mitigation Measures *	Objectives of the Recommended Measure & Main Concerns to address	Implementation Agent	Location of the measure	Duration of the measure	Implementation stages	Relevant Legislation & Guidelines
Project Spe	ecific Measu	res						
Table 10-6	CM8	Protective materials to be provided to natural rocky coastline to prevent damage to existing landform from plant and machinery during temporary drilling operations. Reinstatement following removal of plant & equipment to original or improved condition shall be undertaken.	To protect landscape resources	DSD's contractor	Temporary drilling site for submarine outfall	Construction planning and during construction period	Construction phase	Particular Specification
Table 10-7	OM1	Sensitive design of sewage treatment plant in terms of scale, height and bulk (visual weight) to integrate the building into the existing topography.	To mitigate visual impacts	DSD's Design Architect/ Engineer	STP	Design Phase	Design Phase	Detailed Design Drawings and Specifications
Table 10-7	OM2	Use of appropriate building materials and colors for Sewage Treatment Plant to complement surroundings	To mitigate visual impacts	DSD's Design Architect/ Engineer DSD's contractor Building Operator/DSD	STP	Design Phase Construction Phase & first year in Operational Phase Operational phase	Design, Construction and Operational Phases	Detailed Design Drawings and Specifications
Generic/Sta	andard Mea	sures		Operator/DSD				
Table 10-6	CM1	The construction area and contractor's temporary works areas should be minimized to avoid impacts on adjacent landscape. All slope excavation shall take place from within the work boundary to minimize impacts on adjacent slopes.	To avoid impact on adjacent landscape areas	DSD's Contractor	STP, along gravity sewers and rising mains construction route and at temporary drilling site for submarine outfall	Construction planning and during construction period	Construction Phase	Detailed Design drawings and particular specifications
Table 10-6	CM2	Reduction of construction period to practical minimum	To minimize duration of impact	DSD's contractor	N/A	Construction planning and during construction period	Construction phase	N/A

000	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	O-18
		Ref#	EMA2403/03/42
	Monthly EM&A Report	Rev.	01
I		Date	Nov 24

EIA Ref.	EM &	Recommended Mitigation Measures *	Objectives of the	Implementation	Location of	Duration of the	Implementation	Relevant Legislation &
	A Ref.		Recommended Measure &	Agent	the measure	measure	stages	Guidelines
			Main Concerns to address					
Table	CM3	Construction traffic (land and sea) including construction plant, construction vessels and	To minimize visual impacts to	DSD's	STP, along	Construction	Construction	As per the Particular
10-6		barges to be kept to a practical minimum.	local residents and surrounding	Contractor	gravity sewers	planning and	phase	Specification
			VSRs		and rising	during		
					mains	construction		
					construction	period		
					route at			
					temporary			
					drilling and			
					dredging sites			
					for submarine			
					outfall			
Table	CM4	Erection of decorative mesh screens or construction hoardings and/or temporary noise	To screen construction works	DSD's	STP, along	Construction	Construction	As per the Particular
10-6		barriers around works areas in visually unobtrusive colors.	from local residents and	Contractor	gravity sewers	planning and	phase	Specification
			surrounding VSRs		and rising	during		
					mains	construction		
					construction	period		
					route and at			
					temporary			
					drilling site for			
					submarine			
					outfall			
Table	CM5	Avoidance of excessive height and bulk of site buildings and structures.	To reduce visual impact	DSD's Contractor	STP, and at	Construction	Construction	As per the Particular
10-6				Contractor	temporary	planning and	phase	Specification
					drilling site for	during		
					submarine	construction		
					outfall	period		
Table	CM6	Control of night-time lighting by hooding all lights and through minimization of night	To maximize screening of the	DSD's	STP and at	Construction	Construction	As per the Particular
10-6		working periods.	works	Contractor	temporary	planning and during	phase	Specification
					drilling and	construction		
					dredging site	period		
					for submarine			
					outfall			

	ED 516/2016 Davit Shaltar Sawarana Stana2 Sawarana Warka at Da Tai O	Page	O-19
	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Ref#	EMA2403/03/42
JUD	Monthly EM&A Report	Rev.	01
	······································	Date	Nov 24

Ref.		<b>Recommended Mitigation Measures *</b>	Objectives of the	Implementation	Location of	Duration of	Implementation	Relevant Legislation &
	A Ref.		Recommended Measure	Agent	the measure	the	stages	Guidelines
			&			measure		
			Main Concerns to					
			address					
Table	CM7	All existing trees shall be carefully protected during construction. A Detailed	To maximize protection of	DSD's	STP and all	Construction	Construction	As per Tree Protection
10-6		Tree Protection Specification shall be provided in the Contract Specification.	existing trees	Contractor	other	planning and	phase	Particular Specification,
		Under this specification, the Contractor shall be required to submit, for			construction	during		DEVB TC (W)
		approval, a detailed working method statement for the protection of trees			areas	construction		No.10/2013 and
		prior to undertaking any works adjacent to all retained trees, including trees				period		Guidelines for Tree Risk
		in contractor's works areas. Tree risk assessment shall be undertaken to all						Assessment and
		existing trees within the project site as per "Guidelines for Tree Risk						Management
		Assessment and Management Arrangement"						Arrangement
Table	OM3	Lighting units to be directional and minimize unnecessary light spill and	To mitigate visual impacts	DSD's Design	STP	Design Phase	Design,	Detailed Design
10-7		glare.		Architect/ Engineer			Construction and	Drawings
				DSD's contractor		Construction	Operational	and Specifications
						Phase & first	Phases	
						year		
						in Operational		
						Phase		
				Building		Operational		
				Operator/DSD		phase		
Table	OM4	Greening measures to reinstate the landscape which are appropriate to the	To mitigate visual impacts	DSD's Design	STP	Design Phase	Design,	Detailed Design
10-7		context, including tree and shrub planting and vertical greening, shall be		Landscape Architect			Construction and	Drawings
		implemented.		DSD's contractor		Construction	Operational	and Specifications
						Phase & first	Phases	
						year		
						in Operational		
						Phase		
				Building	1	Operational		
				Operator/DSD		phase		

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	O-20
	EP-510/2016 - Port Shelter Sewerage, Stages - Sewerage works at Portoi O	Ref#	EMA2403/03/42
JUJ	Monthly EM&A Report		01
		Date	Nov 24

EIA	EM &	Recommended Mitigation Measures *	Objectives of the	Implementation	Location of	Duration of	Implementation	Relevant Legislation &
Ref.	A Ref.		Recommended Measure	Agent	the measure	the	stages	Guidelines
			&			measure		
			Main Concerns to					
			address					
Table	OM5	Compensatory tree planting for all felled trees shall be provided to the	To mitigate landscape and	DSD's	STP and at	Design Phase	Design,	As per approved Tree
10-7		satisfaction of relevant Government departments. Required numbers and	visual impacts of tree loss	Landscape Architect	temporary		Construction and	Removal Application,
		locations of compensatory trees shall be determined and agreed separately		7	drilling site for		Operational	Detailed Design
		with Government during the Tree Felling Application process under the		Contractor's	submarine	Construction	Phases	Drawings, Tree
		relevant technical circulars. Tree risk assessment shall be undertaken to all		Landscape Architect	outfall	Phase & first		Protection
		existing trees within the project site as per "Guidelines for Tree Risk		/ wormcoot		year		Particular Specification
		Assessment and Management Arrangement"				in Operational		and Guidelines for Tree
						Phase		Risk Assessment and
				Building		Operational		Management
				Operator/DSD		phase		Arrangement

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	O-21
	Reference of the second state of the second st		EMA2403/03/42
JUJ	Monthly EM&A Report		01
		Date	Nov 24

EIA	EM & A	Recommended Mitigation Measures *	Objectives of the	Implementation	Location of	Duration of the	Implementation	Relevant
Ref.	Ref.		Recommended Measure &	Agent	the measure	measure	stages	Legislation &
			Main Concerns to address					Guidelines
Built H	eritage					·	•	
Project	Specific Me	asures						
11.6	BH1	Undertake condition survey by professional qualified building surveyor or	To record the condition of the	DSD's	GB01, BH02,	Before	Construction	EIAO-TM and
		engineer to record the existing condition of the built heritage resources.	built heritage resources before	Contractor	LF04	commencement	Phase	Guidelines
			the commencement of			of		for CHIA
			construction works			construction		
						works		
11.6	BH2	Carry out vibration and settlement monitoring to built heritage resources. A	To minimize the potential	DSD's	GB01, BH02,	During	Construction	EIAO-TM and
		maximum vibration level 7.5mm/s shall be adopted for the Grade 3 Hung	impact by mechanical vibration	Contractor	LF04	construction	phase	Guidelines
		Shing Temple and settlement check points in the Alert/Alarm/Action limit	and settlement of built heritage			works		for CHIA
		levels at 6mm/8mm/10mm shall be adopted.	resources					
11.6	BH3	Provision of protective covering or protective screen to built heritage	To prevent direct impact from	DSD's	GB01, BH02,	During	Construction	EIAO-TM and
		resources which are close to the works area	the machine and damages by	Contractor	LF01, LF04	construction	phase	Guidelines
			construction tools or waste			works		for CHIA
11.6	BH4	Maintain public access to the cultural landscape features as far as possible	To avoid the proposed works	DSD's	LF01, LF04,	During	Construction	EIAO-TM and
			affecting the worshippers	Contractor	LF05	construction	phase	Guidelines
						works		for CHIA
11.6	BH5	Provision of buffer zone of at least 1m from the proposed works as far as	To avoid the proposed works	DSD's	BH02, LF01,	During	Construction	EIAO-TM and
		possible	affecting the worshippers	Contractor	LF04	construction	phase	Guidelines
						works		for CHIA

\* All recommendations and requirements resulted during the course of EIA Process, including ACE and/or accepted public comment to the proposed proj



# APPENDIX P - RECOMMENDED MITIGATION MEASURES AND PROACTIVE ENVIRONMENTAL PROTECTION PROFORMA

4	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	P-2
	Reference of the severage in the severage is the severage works at Po Tor O Reference of the severage works at		EMA2403/03/42
JUJ	Monthly EM&A Report	Rev.	01
		Date	Nov 24

#### Construction Works Area: PTO-SW-03, PTO-Trenchless -01& STP

Anticipated Impacts: Dust, Noise, Water Quality, Terrestrial Ecology, Marine Ecology, Fisheries, Waste Management, Landscape and Visual and Build Heritage Impact

Item	EIA Ref.	EM&A	Environmental	Corresponding	EM&A Manual	Action By	Measurement
		Ref.	Aspect	Mitigation Measures	Recommended Mitigation/		Procedures/Methods
					Actions		
Air	3.8	A10 -	a) Major air quality impact in construction phase	a) All construction plants / machineries will be	(a) Hoarding of not less than 2.4 m high shall be erected from	Contractor	a) 1-hour and 24-hour TSP levels will be
Quality		A25	would arise from excavation of slope at the	checked / serviced on a regular basis during the courses	ground level to surround the work area along Po Toi O Chuen		measured in accordance to the standard
mpact			proposed sewage treatment plant.	of construction to minimize the emission of noise	Road except for a site entrance or exit.		high-volume sampling method as set out in
				generation and eliminate dark smoke emission.			the Title 40 of the Code of Federal
			b) Excavation, Gas welding, slope cutting, Rock		(b) Good housekeeping to minimize dust generation, e.g. by		Regulations, Chapter 1 (Part 50), Appendix
			dowel, fencing, flexible barrier installation Loading	b) All dump trucks will be equipped with mechanical covers	properly handling and storing dusty materials.		Α.
			& Unloading Dusty Materials storage, Dusty	to prevent the dust emission during transportation when			
			Waste Sorting, Temporary Site Traffic Control	necessary.	(c) Adopt dust control measures, such as dust suppression		b) Due to objection from the residents of Po
					using water spray on exposed soil at least 4 times a day, in		Toi O village of the use of high-volume
				c) Dust control measures, such as water spraying, will be	areas with dusty construction activities and during material		sampler (HVS) in conducting 24-hours TSF
				provided during demolition works when necessary.	handling.		measurement, 24-hour TSP measures for
							impact monitoring is to be measured by
				d) Maintaining of wet surface on access road and keep	d) Minimize exposed earth after completion of work in a		portable dust meters during construction
				slow speed in the site.	certain area by hydroseeding, vegetating, soil compacting or		phase of the project. This is to be approved
					covering with bitumen.		and verified by ER and IEC.
				e) Conditions in the Environmental Permit			
				and Discharge License should be followed.	(e) Provide wheel washing at site exit to prevent carrying		c) Other than using high volume sampler, 1
					dust outside of the site.		hour TSP levels can be measured
				f) Predict required quantity of concrete			alternatively by direct reading from portable
				accurately and collect the unused fresh	(f) Cover materials on trucks before leaving the site.		dust meters upon approval from ER. The
				concrete at designated locations in the site for			meters should be capable of producing
				subsequent disposal.	(g) Limit vehicle speed of construction trucks within the		comparable results as that by the high
					construction site and in Po Toi O, maximum at 10km/hr, and		volume sampling method, to indicate shore
				g) Provide sufficient mitigation measures as	confine vehicle movement in haul road.		event impacts.
				recommended in approved EIA Manual requirement.			
					(h) As there is limited space in Po Toi O, stockpiling should		d) -The ET shall agree with the IEC on the
					be avoided. However, if found necessary, the materials		monitoring position and the corrections
					should be covered by impervious materials such as tarpaulin.		adopted.
							e) -The agreed position shall be chosen in
							subsequent baseline and impac
							monitoring.

4	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	P-3
		Ref#	EMA2403/03/42
	Monthly EM&A Report		01
		Date	Nov 24

Item	EIA	EM&A	Environmental	Corresponding	EM&A Manual	Action By	Measurement
	Ref.	Ref.	Aspect	Mitigation Measures	<b>Recommended Mitigation/</b>		Procedures/Methods
					Actions		
Noise	4.7	N1 -	a) The Project comprises three main	a) Conditions in the Environmental Permit and		Contractor	a) Noise measurement shall normally
Impact		N175	works including the construction of	Discharge License should be followed.			be at a point 1 m from the exterior of
Control			sewage treatment plant (STP),				the sensitive receiver building façade
			underground sewers and rising main, and	b) Provide sufficient mitigation measures as			and be at a position 1.2 m above the
			the submarine outfall.	recommended in approved EIA Manual			ground. If the normal monitoring
				requirement.			position cannot be accessed, an
			b) The major noise impact will arise from				alternative position may be chosen,
			the use of powered mechanical				and a correction to the
			equipment.				measurements shall be made. For
							reference, a correction of +3 dB(A)
			c) Excavation, Gas welding, slope cutting,				shall be made to the free field
			Rock dowel, fencing, flexible barrier				measurements.
			installation Loading & Unloading Dusty				
			Materials storage, Temporary Site Traffic				b) The ET shall agree with the IEC on
			Control.				the monitoring position and the
							corrections adopted.
							c) The agreed position shall be
							chosen in subsequent baseline and
							impact monitoring.




Monthly EM&A Report

Item	EIA	EM&A	Environmental	Corresponding	EM&A Manual	Action By	Measurement
	Ref.	Ref.	Aspect	Mitigation Measures	Recommended Mitigation/		Procedures/Methods
					Actions		
Water	5.8	W1-	a) Major Water quality impact will be	a) Wastewater to be treated by wastewater	a) Well manage construction materials, chemicals,	Contractor	a) Weekly site audit to monitor the
Quality		W33	originated from minor displacement of	treatment facilities before discharge.	sewage for proper storage and usage and to prevent		implementation of the proposed water
impact			suspended solids during installation,		accumulation onsite.		quality mitigation measures and
			testing pipe and extraction of cofferdam	b) Conditions in the Environmental Permit and	(b) Immediately clean up contaminated soil upon		check the Contractor's work practice
			around the proposed diffuser.	Discharge License should be followed.	chemical and oil leakage.		on water pollution prevention during
					(c) Label chemical waste containers according to the		construction phase.
					Code of Practice to notify and warn the waste		
					handlers. Store fuels, chemicals and chemical waste		b) Should water pollution is observed
					at designated area with locks and bunds.		(e.g. discharge of silty water into
					(d) Register as chemical waste producer.		storm drains), the ET should record
					(e) Set up sedimentation tank for settling suspended		the environmental deficiency fo
					solids in wastewater before discharge into storm		investigation.
					drains. Sand/silt removal facilities such as sand		
					traps, silt traps and sedimentation basin should be		c) The Contractor should be notified
					provided with adequate capacity.		and responsible for carrying ou
					(f) Provide sufficient number of chemical toilets if		rectification work immediately.
					necessary and employ licensed contractor for		
					regular clean-up and maintenance.		d) The ET shall re-inspect the Project
					(g) Provide wheel washing at site exit to prevent dust		Site and review the effectiveness of
					and silty water from leaving the construction site.		the remedial measure performed unt
					(h) Cover slope and loose materials with tarpaulin		satisfaction.
					before rainstorm and inspect the area afterwards.		
					(i) Cover manhole to prevent silt, construction		e) The Contractor shall implement
					materials or debris and surface runoff from entering		preventive measure to avoid causing
					the foul sewer.		the same problem.
					(j) Install fully enclosed cofferdam around the		
					proposed diffuser and deploy a dredger barge		
					outside the cofferdam for dredging and filling works.		



Item	EIA	EM&A	Environmental	Corresponding	EM&A Manual	Action By	Measurement
	Ref.	Ref.	Aspect	Mitigation Measures	<b>Recommended Mitigation/</b>		Procedures/Methods
					Actions		
Terrestrial	6.12	E1-E8	a) The proposed Project will cause minor	a) Conditions in the Environmental Permit and	a) Construction noise and water quality mitigation	Contractor	(a) Bright colour fencing shall be
Ecology			habitat loss of shrubland, temporary	Discharge License should be followed.	measures proposed in the previous sections will be		erected along the boundary of the
			habitat loss of woodland, developed area		applicable to terrestrial ecology.		undisturbed region of the shrubland
			and rocky shore, and removal of one	b) Provide sufficient mitigation measures as			and woodland, and around Diospyros
			individual climber species of conservation	recommended in approved EIA Manual			vaccinioides, a plant species of
			importance that is common within the	requirement.			conservation importance, near the
			Study Area and Hong Kong. Indirect				work boundary to remind workers not
			water quality impact may arise from				to trespass or occupy the area, and
			surface runoff or accidental spillage of				to be careful during operation of
			chemicals in construction Phase.				equipment.
			b) Use of powered plant equipment may				(b)Inspect the condition of Diospyros
			bring noise disturbance on wildlife				vaccinioides as part of weekly site
							audit.
							(c) Reinstate the disturbed rocky
							shore with the rocks temporarily
							removed.
							(d) Carry out compensatory tree
							planting in accordance with DEVB
							TCW No. 7/2015 to reinstate the
							affected woodland.



Item	EIA	EM&A	Environmental	Corresponding	EM&A Manual	Action By	Measurement
	Ref.	Ref.	Aspect	Mitigation Measures	Recommended Mitigation/		Procedures/Methods
					Actions		
Marine	7	7	a) The proposed Project will cause minor	a) Conditions in the Environmental Permit and	a) The variation in water quality at coral and	Contractor	(a) No specific monitoring and audit
Ecology			habitat loss of muddy seabed.	Discharge License should be followed	amphioxus habitats during cofferdam installation		programme is required. With proper
					and extraction works will be overseen by water		implementation of water quality
			b) Indirect water quality impact may arise		quality monitoring mentioned.		mitigation measures, residual impact
			from installation and extraction of sheet				is expected to be acceptable.
			pile of cofferdam in construction phase.				
			c) Dredging and backfilling for installation				
			of diffuser will be conducted inside fully				
			enclosed cofferdam. No marine sediment				
			loss to water column is expected.				



Item	EIA	EM&A	Environmental	Corresponding	EM&A Manual	Action By	Measurement
	Ref.	Ref.	Aspect	Mitigation Measures	<b>Recommended Mitigation/</b>		Procedures/Methods
					Actions		
Fisheries	8	8	a) No direct encroachment on Fish Culture	a) Conditions in the Environmental Permit and	Water quality at FCZ will be monitored during	Contractor	(a) No specific monitoring and audit
			Zone and Artificial Reefs in the Study Area	Discharge License should be followed	cofferdam installation and extraction works and		programme are required. With proper
			is expected.		dredging works in the construction phase as		implementation of water quality
					proposed.		mitigation measures, residual impact
			b) About 1,920 m2 of fishing ground and				is expected to be acceptable.
			500 m2 of benthic spawning ground will be				
			affected. Except the 5 m2 benthic				
			spawning ground will be lost permanently,				
			other impacted area will only be affected in				
			construction phase temporarily (reversible				
			impact). Indirect impact on fisheries				
			resources by the water quality				
			deterioration will be insignificant with				
			proper implementation of water quality				
			mitigation measures.				
					l		



#### EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O


Monthly EM&A Report

Item	EIA	EM&A	Environmental	Corresponding	EM&A Manual	Action By	Measurement
	Ref.	Ref.	Aspect	Mitigation Measures	Recommended Mitigation/		Procedures/Methods
					Actions		
Waste	9.8	WM4-	a) Construction of the sewage	a) All C&D materials generated will be	(a) Reuse C&D materials onsite and dispose excess	Contractor	The Contractor should apply for relevant
Management		WM23	treatment plant, laying of gravity	transported and stored at temporary	uncontaminated ones to public fill.		licenses/permits for waste disposal under
			sewers and rising mains and	storage area. Cover will be provided			different regulations and ordinances as
			submarine outfall are expected to	during transportation of dusty materials.	(b) Provide sufficient waste collection points for general		follows:
			generate mainly inert construction	Suitable materials will be sorted for	refuse and regularly maintained to avoid accumulation.		(a) Chemical Waste Permits/licenses
			and demolition (C&D) materials	reuse on-site. Only non-inert C&D	Dispose the waste at waste transfer or disposal facilities.		under the Waste Disposal Ordinance
			(or public fill) from excavation,	material will be disposed offsite to NENT			(Cap 354);
			and unused building materials.	Landfill.	(c) Minimize wastage through careful planning and avoiding		
			Other wastes include noninert		over purchase of construction materials.		(b) Public Dumping License under the
			C&D materials (or C&D waste),	b) Conditions in the Environmental			Land Miscellaneous Provisions)
			plant materials, scaffolding,	Permit and Discharge License should be	(d) Provide training to workers on site cleanliness, waste		Ordinance (Cap 28);
			formwork and packaging,	followed	management (waste reduction, reuse and recycle) and		
			chemical waste from plant		chemical handling procedures.		(c) Marine Dumping Permit under
			maintenance, bentonite slurry	c) Fueling of equipment will be			Dumping at Sea Ordinance (Cap 466); and
			from drilling works and general	conducted carefully onsite by mobile	(e) Hire licensed waste disposal contractors for waste		
			refuse from workers.	tanker to avoid storage of fuel and oil	collection and removal. Dispose waste at licensed waste		(d) Effluent Discharge License under the
				spillage.	disposal facilities.		Water Pollution Control Ordinance (Cap
			b) Dredging at the proposed				358).
			diffuser location will generate	d) Provision of drip trays for equipment	(f) Recondition and reuse bentonite as far as practical.		
			marine sediment.	likely cause spillage of chemical / fuel			b) Reference should be made to EPD's
				and provide routine maintenance.	(g) Conduct marine sediment test and dump dredged marine		booklets on licenses/permits. The
					sediment according to ETWB TCW No. 34/2002		Contractor shall also document recycling
					Management of Dredged/Excavated Sediment and Dumping		receipts/ disposal record to keep track of
					at Sea Ordinance.		waste movement. The ET shall check with
							the Contractor that these licenses/permits
					(h) Chemical waste shall be handled, stored and disposed		have been obtained. He should also
					properly, according to the relevant guidelines.		review the above documentations
							regularly to ensure compliance with
							legislations and specifications.



Monthly EM&A Report

Item	EIA	EM&A	Environmental	Corresponding	EM&A Manual	Action By	Measurement
	Ref.	Ref.	Aspect	Mitigation Measures	Recommended Mitigation/		Procedures/Methods
					Actions		
Landscape	Table	CM1-	a) Minor landscape and visual	a) Conditions in the Environmental	a) The contractor shall employ a professionally qualified	Contractor	a) Tree risk assessment shall be
and Visual	10-6	CM8	impact is expected due to	Permit and Discharge License should	Registered Landscape Architect (RLA) on the Environmental		undertaken by the contractor during
impact	& 10-	&	dredging work in open sea,	be followed.	Team to supervise and monitor the implementation of		construction to all existing trees within the
	7	OM1-	construction of the STP and		construction phase landscape and visual mitigation		project site as per "Guidelines for Tree
		OM5	pipelines on land and the loss of	b) Implement the recommended	measures. This is necessary to ensure that all the		Risk Assessment and Management
			existing trees and vegetation at	mitigation proposed in EM&A manual.	recommended landscape and visual mitigation measures		Arrangement".
			the sewage treatment plant site in		under Chapter 10 of the EIA are effectively implemented		
			the construction phase.		including minimization of the works footprint, ensuring that		b) Site inspections by appointed RLA shall
					those existing trees earmarked for retention on site or		be undertaken at monthly intervals to
					transplanting are protected and planting works are correctly		closely monitor all these aspects of work.
					implemented.		Inspection findings shall be logged in a site
							monitoring report with any discrepancies
							or concerns regarding the implementation
							and effectiveness of mitigation measures
							highlighted.



Item	EIA	EM&A	Environmental	Corresponding	EM&A Manual	Action By	Measurement
	Ref.	Ref.	Aspect	Mitigation Measures	Recommended Mitigation/		Procedures/Methods
					Actions		
Build	11.6	BH1 -	a) As the proposed work is close	a) Conditions in the Environmental	a) Provision of protective covering or protective screen is	Contractor	a) A maximum vibration level of 7.5mm/s
Heritage		BH5	to some of the identified built	Permit and Discharge License should	recommended to identified built heritage to prevent damages		shall be adopted for the Grade 3 Hung
			heritage resources, condition	be followed.	by construction tools or waste.		Shing Temple and settlement check points
			survey, vibration and settlement				in the Alert/Alarm/Action limit levels at
			monitoring is recommended to	b) Implement the recommended	b) Maintenance of public access is suggested for identified		6mm/8mm/10mm shall be adopted.
			identified built heritage to prevent	mitigation proposed in EM&A manual.	built heritage. Besides, buffer zone of at least 1m from the		
			indirect damage by mechanical		works boundary should be provided for identified built		
			vibration and settlement.		heritage as far as possible.		
					c) Condition output, vibration and cattlement menitoring to		
					c) Condition survey, vibration and settlement monitoring to		
					identified built heritage.		



# APPENDIX Q - CUMULATIVE STATISTICS ON COMPLAINTS, NOTIFICATIONS OF SUMMONS

	ED 516/2016 Dart Sholtar Sawaraga Stage? Sawaraga Warks at Da Tai O	Page	Q-2
CCC	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Ref#	EMA2403/03/42
202	Monthly EM&A Report	Rev.	01
		Date	Nov 24

# **Environmental Complaints Log**

Complaint	Date of	Received	Received	Nature of	Relevant to the	Investigation/	Status
Log No.	Complaint	From	Ву	Environmental	<b>Construction Work</b>	Mitigation	
				Complaint	of	Action	
					Project Site? (Y/N)		
001	28	EPD	ET	Waste	N	The investigation reports	Closed
	December			Management		was submitted on 7	
	2021					January	
						2022	
002	23	EPD	ET	Waste	N	The investigation reports	-
	September			Management		was submitted on 27	
	2024					September	
						2024	

## Remark:

\* No complaints, Notifications of Summons, or Successful Prosecutions were received in the reporting period.

## Cumulative Statistics on Complaints, Notifications of Summons and Successful Prosecutions and Public Engagement Activities

Reporting Period	Complaints	Notifications of Summons and	Public Engagement Activities
		Prosecutions	
This Month	0	0	0
Cumulative Project-to-Date	2	0	0
