



**CONTRACT NO: HY/2020/08**

**FLYOVER FROM KWAI TSING INTERCHANGE  
UPRAMP TO KWAI CHUNG ROAD  
UNDER ENVIRONMENTAL PERMIT NO. EP-541/2017/A**

**MONTHLY ENVIRONMENTAL MONITORING & AUDIT REPORT**

**JULY 2024**

**CLIENTS:**

**Highways Department**

**PREPARED BY:**

**Lam Environmental Services Limited**

19/F Remex Centre,  
42 Wong Chuk Hang Road,  
Hong Kong

Telephone: (852) 2882-3939  
Facsimile: (852) 2882-3331  
E-mail: [info@lamenviro.com](mailto:info@lamenviro.com)  
Website: <http://www.lamenviro.com>

**CERTIFIED BY:**

---

Raymond Dai  
Environmental Team Leader

**DATE:**

12 August 2024



**NATURE & TECHNOLOGIES (HK) LIMITED**

**科技環保(香港)有限公司**

Unit 2410, 24/F., Fortis Tower, 77-79 Gloucester Road, Wanchai, Hong Kong

香港灣仔告士打道 77-79 號富通大廈 24 樓 10 室

Tel 電話: (852) 2877 3122 Fax 傳真: (852) 2511 0922

Email 電郵: [enquiry@nt.com.hk](mailto:enquiry@nt.com.hk) Website 網址: <http://www.nt.com.hk>

Date: 14<sup>th</sup> August 2024

Highways Department  
Works Division  
Works Section / NT  
7th Floor, Trade and Industry Tower,  
3 Concorde Road, Kowloon

Dear Sirs,

**Contract No. HY/2020/08**

**Flyover From Kwai Tsing Interchange Upramp to Kwai Chung Road**

**Independent Environmental Checker**

**Monthly Environmental Monitoring and Audit Report for July 2024**

We refer to the Contract No. HY/2020/08 Flyover From Kwai Tsing Interchange Upramp to Kwai Chung Road under Environmental Permit No. EP-541/2017/A Monthly Environmental Monitoring and Audit Report certified by the Environmental Team. We hereby verified the Monthly Environmental Monitoring and Audit Report for July 2024 in accordance with the Condition 3.4 of EP-541/2017/A.

Should you have any query, please feel free to contact the undersigned at 8493 5543.

Yours Sincerely,

Vega Wong

Independent Environmental Checker

c.c.

WSP (Attn: Mr. Stephen Ho/Mr. Eric Hon) [by Email: [Stephen.YC.Ho@wsp.com](mailto:Stephen.YC.Ho@wsp.com); [Eric.Hon@wsp.com](mailto:Eric.Hon@wsp.com)]

Lam Environmental Services Limited (Attn: Mr. Raymond Dai) [by Email: [raymond dai@lamenviro.com](mailto:raymond dai@lamenviro.com)]



**TABLE OF CONTENTS**

**1 INTRODUCTION ..... 5**

1.1 Scope of the Report ..... 5

1.2 Structure of the Report ..... 5

**2 PROJECT BACKGROUND ..... 6**

2.1 Background ..... 6

2.2 Project Organization and Contact Personnel ..... 6

2.3 Construction Activities ..... 7

**3 STATUS OF REGULATORY COMPLIANCE ..... 9**

3.1 Status of Environmental Licensing and Permitting under the Project .. 9

3.2 Status of Submission under the EP-541/2017/A ..... 9

**4 MONITORING REQUIREMENTS ..... 10**

4.1 Noise Monitoring ..... 10

4.2 Air Monitoring ..... 12

**5 MONITORING RESULTS ..... 16**

5.1 Noise Monitoring Results ..... 16

5.2 Air Monitoring Results ..... 16

5.3 Waste Management ..... 16

**6 COMPLIANCE AUDIT ..... 18**

6.1 Noise Monitoring ..... 18

6.2 Air Quality Monitoring ..... 18

6.3 Review of the Reasons for and the Implications of Non-compliance . 18

6.4 Summary of action taken in the event of and follow-up on non-compliance ..... 18

**7 ENVIRONMENTAL SITE AUDIT ..... 19**

**8 COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTION ..... 20**

**9 CONCLUSION ..... 21**

## LIST OF TABLES

<b>Table 2.1</b>	<b>Contact Details of Key Personnel</b>
<b>Table 3.1</b>	<b>Summary of the current status on licences and/or permits on environmental protection pertinent to the Project</b>
<b>Table 3.2</b>	<b>Summary of submission status under EP-541/2017/A</b>
<b>Table 4.1</b>	<b>Noise Monitoring Station</b>
<b>Table 4.2</b>	<b>Noise Monitoring Equipment</b>
<b>Table 4.3</b>	<b>Action and Limit Level for Noise Monitoring</b>
<b>Table 4.4</b>	<b>Air Monitoring Station</b>
<b>Table 4.5</b>	<b>Air Quality Monitoring Equipment</b>
<b>Table 4.6</b>	<b>Action and Limit Level for Air Quality Monitoring</b>
<b>Table 5.1</b>	<b>Summary of Quantities of Inert C&amp;D Materials</b>
<b>Table 5.2</b>	<b>Summary of Quantities of C&amp;D Wastes</b>
<b>Table 7.1</b>	<b>Summary of Environmental Inspections</b>
<b>Table 7.2</b>	<b>Summary of Landscape Site Inspections</b>
<b>Table 8.1</b>	<b>Cumulative Statistics on Complaints</b>
<b>Table 8.2</b>	<b>Cumulative Statistics on Successful Prosecutions</b>
<b>Table 9.1</b>	<b>Construction Activities and Recommended Mitigation Measures in Coming Reporting 3 Months</b>

## LIST OF FIGURES

<a href="#"><u>Figure 1.1</u></a>	<a href="#"><u>Project Layout</u></a>
<a href="#"><u>Figure 2.1</u></a>	<a href="#"><u>Project Organization Chart</u></a>
<a href="#"><u>Figure 4.1</u></a>	<a href="#"><u>Locations of Noise Monitoring Stations</u></a>
<a href="#"><u>Figure 4.2</u></a>	<a href="#"><u>Locations of Air Quality Monitoring Stations</u></a>

## LIST OF APPENDICES

<a href="#"><u>Appendix 3.1</u></a>	<a href="#"><u>Environmental Mitigation Implementation Schedule</u></a>
<a href="#"><u>Appendix 4.1</u></a>	<a href="#"><u>Action and Limit Level</u></a>
<a href="#"><u>Appendix 4.2</u></a>	<a href="#"><u>Copies of Calibration Certificates</u></a>
<a href="#"><u>Appendix 4.3</u></a>	<a href="#"><u>Wind data</u></a>
<a href="#"><u>Appendix 5.1</u></a>	<a href="#"><u>Monitoring Schedule for Reporting Month and Next Reporting Month</u></a>
<a href="#"><u>Appendix 5.2</u></a>	<a href="#"><u>Noise Monitoring Results and Graphical Presentations</u></a>
<a href="#"><u>Appendix 5.3</u></a>	<a href="#"><u>Air Quality Monitoring Results and Graphical Presentations</u></a>
<a href="#"><u>Appendix 5.4</u></a>	<a href="#"><u>Monthly Summary Waste Flow Table</u></a>
<a href="#"><u>Appendix 6.1</u></a>	<a href="#"><u>Event and Action Plans</u></a>
<a href="#"><u>Appendix 6.2</u></a>	<a href="#"><u>Summary of Notification of Exceedance</u></a>
<a href="#"><u>Appendix 8.1</u></a>	<a href="#"><u>Complaint Log</u></a>
<a href="#"><u>Appendix 9.1</u></a>	<a href="#"><u>Construction Programme</u></a>

## EXECUTIVE SUMMARY

- i. This is the Environmental Monitoring and Audit (EM&A) Monthly Report – July 2024 of Flyover from Kwai Tsing Interchange Upramp to Kwai Chung Road under Environmental Permit no. EP-541/2017/A (Hereafter as “the Project”). The construction works of the Project was commenced on 20 September 2021. This is the 32<sup>th</sup> EM&A report presenting the environmental monitoring findings and information recorded during the period of 01 July 2024 to 31 July 2024. The cut-off date of reporting is at the end of each reporting month.
- ii. In the reporting month, the principal work activities conducted are as follow:
  - Tree preservation works
  - Piling works for Bridge H
  - Erection of falsework for Bridge G Deck and Bridge H Deck
  - Rectification of minor defects of the footbridge
  - Formwork erection and fixing rebar at Bridge G
  - Formwork erection and fixing rebar at Bridge H
  - Erection of falsework for Staircase of Existing NF303 Footbridge
  - Demolition of Existing NF303 Footbridge

### Air Quality Monitoring

- iii. 1-hour and 24-hour Total Suspended Particulates (TSP) monitoring was conducted at three monitoring stations. 24-hour TSP shall be sampled at least once in every 6 days, while sampling for 1-hour TSP shall be at least 3 times in every 6 day in the reporting month.
- iv. No action or limit level exceedance was recorded in this reporting period.

### Noise Monitoring

- v. Noise monitoring was conducted at three noise monitoring stations once per week in the reporting month.
- vi. Limit level of noise monitoring station NMC-03 has adjusted to 65dB(A) during examination period.
- vii. Limit level exceedances were recorded at NMC-01 and NMC-03 in this reporting period. As the baseline level of NMC-01 and NMC-03 are higher than the measured average noise level, the noise monitoring results are not considered as noise exceedances.

### Site Inspections and Audit

- viii. The Environmental Team (ET) conducted weekly site inspections on 4, 9, 18 and 25 July 2024 and biweekly landscape inspection on 4 and 18 July 2024. IEC attended the joint site



inspection on 9 July 2024, while reminders on routine environmental mitigation measures were recommended.

Complaints, Notifications of Summons and Successful Prosecutions

- ix. No environmental complaint, notification of summons and successful prosecution regarding the construction works was recorded in the reporting period.

Reporting Changes

- x. There are no particular reporting changes.

Future Key Issues

- xi. In coming reporting 3 months, the scheduled construction activities and the recommended mitigation measures are listed as follows:

Key Construction Works	Recommended Mitigation Measures
<ul style="list-style-type: none"> <li>• Tree preservation works</li> <li>• Piling works for Bridge H</li> <li>• Erection of falsework for Bridge H Deck</li> <li>• Construction of Deck for Bridge G</li> <li>• Formwork erection and fixing rebar at Bridge H</li> <li>• Drainage works near H7</li> <li>• Demolition of Existing NF303 Footbridge</li> <li>• Construction of granite wall</li> <li>• Road Diversion works near Pier H7</li> </ul>	<ul style="list-style-type: none"> <li>• Regular maintenance and protection of all existing retained and transplanted trees</li> <li>• Implement proper dust mitigation measures to prevent potential dust nuisances to nearby sensitive receivers during piling works..</li> <li>• Implement proper measures to prevent silt or debris being deposited or washed into existing drainage systems</li> <li>• Implement proper noise mitigation measures to prevent potential noise nuisances to nearby sensitive receivers, with attention on restricted hour work activities</li> <li>• Provision of protection to ensure no runoff out of site area or direct discharge into public drainage system</li> </ul>

## 1 Introduction

### 1.1 Scope of the Report

- 1.1.1. Lam Environmental Services Limited (LES) has been appointed to work as the Environmental Team (ET) under Environmental Permit (EP) no. EP-541/2017/A to implement the Environmental Monitoring and Audit (EM&A) programme as stipulated in the EM&A Manual of the approved Environmental Impact Assessment (EIA) Report for Flyover from Kwai Tsing Interchange Upramp to Kwai Chung Road (Register No.: AEIAR-190/2015).
- 1.1.2. In accordance with Clause 3.4 stated in EP-541/2017/A, 3 hard copies and 3 electronic copies of Monthly EM&A Report shall be submitted to the Director within 2 weeks after the end of each reporting month.
- 1.1.3. According to Section 10.3.1 of the Project EM&A Manual, the Monthly EM&A Report should be submitted within 10 working days of the end of each reporting month, with the first report due in the month after construction commences.

### 1.2 Structure of the Report

- Section 1** *Introduction* – details the scope and structure of the report.
- Section 2** *Project Background* – summarizes background and scope of the project, site description, project organization and contact details of key personnel during the reporting period.
- Section 3** *Status of Regulatory Compliance* – summarizes the status of valid Environmental Permits / Licenses during the reporting period.
- Section 4** *Monitoring Requirements* – summarizes all monitoring parameters, monitoring methodology and equipment, monitoring locations, monitoring frequency, criteria and respective event and action plan and monitoring programmes.
- Section 5** *Monitoring Results* – summarizes the monitoring results obtained in the reporting period.
- Section 6** *Compliance Audit* – summarizes the auditing of monitoring results, all exceedances environmental parameters.
- Section 7** *Environmental Site Audit* – summarizes the findings of weekly site inspections undertaken within the reporting period, with a review of any relevant follow-up actions within the reporting period.
- Section 8** *Complaints, Notification of summons and Prosecution* – summarizes the cumulative statistics on complaints, notification of summons and prosecution
- Section 9** *Conclusion*

## 2 Project Background

### 2.1 Background

- 2.1.1. In order to cater the future traffic growth and prevent traffic congestion in the future during peak traffic flow hour at Tsuen Wan Road (TWR) near Kwai Tsing Interchange (KT I/C), an additional southbound lane (a separate viaduct) is introduced on TWR and connected to the existing lane on the west side of Kwai Chung Road (KCR). Widening of existing carriageway is also proposed to improve the road section to cope with the future traffic growth.
- 2.1.2. Based on the current design, the remaining capacity available on the two segregated KCR carriageways will be utilised for this proposed flyover. Location and layout of the proposed road works is shown in [Figure 1.1](#).
- 2.1.3. The Project consists of a designated project under Part I, Schedule 2 of the Environmental Impact Assessment Ordinance (EIAO) which is Item A.8 – *A road or railway bridge more than 100m in length between abutments*.
- 2.1.4. The major components of the Project under Environmental Permit (EP) (EP No. EP-541/2017/A) comprises: (i) an additional southbound lane from the west side of elevated Tsuen Wan Road to at-graded Kwai Chung Road; (ii) a widened section on the east side of elevated Tsuen Wan Road connecting Kwai Tsing Interchange up-ramp; (iii) modification of Kwai Chung Road; (iv) provision of noise mitigation measures; (v) demolition and re-provision of the existing footbridge NF303; and (vi) ancillary works including other associated road works, utilities diversion, street furniture and traffic aids, public lighting, drainage, landscaping, electrical and mechanical works.

### 2.2 Project Organization and Contact Personnel

- 2.2.1 Highways Department is the overall project controllers for the Project. For the construction phase of the Project, Project Engineer / Supervisor, Contractor(s), Environmental Team and Independent Environmental Checker are appointed to manage and control environmental issues.
- 2.2.2 The project organization and lines of communication with respect to environmental protection works are shown in [Figure 2.1](#). Key personnel and contact particulars are summarized in **Table 2.1**:



**Table 2.1 Contact Details of Key Personnel**

Party	Role	Post	Name	Contact No.	Contact Fax
Highways Department (HyD)	Project Proponent	Chief Engineer	Vincent WONG	3903 6888	3188 3418
WSP (Asia) Limited	Supervisor's Representative	Resident Engineer	Eric HON	2320 2012	2320 2166
Peako Engineering Co. Limited	Contractor	Site Agent	Mr. Lo Yuen Cheong	9123 7342	2398 8301
		Sub Agent/ Environmental Supervisor	Mr. Gary Ng	9187 1694	
		Environmental Officer	Mr. Jimson Lai	9238 7480	
Nature & Technologies (HK) Limited	Independent Environmental Checker (IEC)	Independent Environmental Checker (IEC)	Vega WONG	2877 3122	2511 0922
Lam Environmental Services Limited	Environmental Team (ET)	Environmental Team Leader (ETL)	Raymond DAI	2882 3939	2882 3331

**2.3 Construction Activities**

2.3.1 In the reporting month, the principal work activities conducted are as follows:

- Tree preservation works
- Piling works for Bridge H
- Erection of falsework for Bridge G Deck and Bridge H Deck
- Rectification of minor defects of the footbridge
- Formwork erection and fixing rebar at Bridge G
- Formwork erection and fixing rebar at Bridge H
- Erection of falsework for Staircase of Existing NF303 Footbridge
- Demolition of Existing NF303 Footbridge

2.3.2 In coming reporting 3 months, the scheduled construction activities are listed as follows:

- Tree preservation works
- Piling works for Bridge H
- Erection of falsework for Bridge H Deck
- Construction of Deck for Bridge G
- Formwork erection and fixing rebar at Bridge H
- Drainage works near H7
- Demolition of Existing NF303 Footbridge
- Construction of granite wall
- Road Diversion works near Pier H7

### 3 Status of Regulatory Compliance

#### 3.1 Status of Environmental Licensing and Permitting under the Project

3.1.1. A summary of the current status on licences and/or permits on environmental protection pertinent to the Project is shown in **Table 3.1**.

**Table 3.1 Summary of the current status on licences and/or permits on environmental protection pertinent to the Project**

Permits and/or Licences	Permit. No. / Account No.	Valid From	Expiry Date	Status
Notification pursuant to Air Pollution Control (Construction Dust) Regulation	Acknowledged by EPD on 21 June 2021.			
WPCO Discharge Licence	WT00040637-2022	25 Mar 2022	N/A	Valid
Environmental Permit	EP-541/2017/A	19 Nov 2020	N/A	Valid
Billing Account for Disposal of Construction Waste	7040908	14 July 2021	End of the Project	Valid
Registration as a Chemical Waste Producer	8834-326-P3431-01	08 July 2021	N/A	Valid
Construction Noise Permit	GW-RW0210-24	25 March 2024	24 June 2024	Expired

3.1.2. Implementation status of the recommended mitigation measures during this report month is presented in [Appendix 3.1](#).

#### 3.2 Status of Submission under the EP-541/2017/A

3.2.1. A summary of the current status on submission under EP-541/2017/A is shown in **Table 3.2**.

**Table 3.2 Summary of submission status under EP-541/2017/A**

EP Condition	Submission	Date of First Submission	Date of Latest Submission
Condition 1.12	Notification of Commencement Date of Works	27 July 2021	26 August 2021
Condition 2.3	Submission of Management Organization of Main Construction Companies	2 July 2021	4 May 2022
Condition 2.4	Submission of Landscape Plan	26 July 2021	19 April 2023
Condition 2.5	Submission of Traffic Noise Mitigation Plan	26 July 2021	20 January 2023
Condition 3.3	Submission of Baseline Monitoring Report	6 September 2021	28 January 2022

**4 Monitoring Requirements**

**4.1 Noise Monitoring**

NOISE MONITORING STATIONS

4.1.1. The noise monitoring stations for the Project are listed and shown in **Table 4.1** and **Figure 4.1**. **Appendix 4.1** shows the established Action/Limit Levels for environmental monitoring.

**Table 4.1 Noise Monitoring Station**

Monitoring Station ID	Noise Sensitive Receivers	Measurement Type	Monitoring Location
NMC01	Lai King Catholic Secondary School	Free-Field	Roof Floor
NMC02	Fung King House	Free-Field	Roof Floor
NMC03	HKEAA-Lai King Assessment Centre	Free-Field	Ground Floor

NOISE MONITORING PARAMETERS, FREQUENCY AND DURATION

4.1.2. For daytime construction work on normal weekdays (0700-1900 Monday to Saturday), one set of 30-min measurement shall be carried out at each NMS every week. Measurement procedures shall be referred to the Noise Control Ordinance-TM. Construction noise level shall be measured in terms of the A-weighted equivalent continuous sound pressure level ( $L_{eq}$ ).  $L_{eq}(30min)$  shall be used as the monitoring parameter. As supplementary information for data auditing, statistical results such as  $L_{10}$  and  $L_{90}$  shall also be obtained for reference.

MONITORING EQUIPMENT

4.1.3. Noise monitoring was performed using sound level meter at the designated monitoring locations. The sound level meters shall comply with the International Electrotechnical Commission Publications 651:1979 (Type 1) and 804:1985 (Type 1) specifications. Acoustic calibrator shall be deployed to check the sound level meters at a known sound pressure level. Brand and model of the equipment is given in **Table 4.2**.

**Table 4.2 Noise Monitoring Equipment**

Equipment	Brand/Model	Series Number
Integrated Sound Level Meter	LxT1	0004797
Acoustic Calibrator	HLES-02	2019612870
	CAL200	13098

4.1.4. The calibration certificates of the noise monitoring equipment are attached in **Appendix 4.2**.

### SAMPLING PROCEDURE AND MONITORING EQUIPMENT

#### 4.1.5. Monitoring Procedure

- (a) The monitoring station shall normally be at a point 1m from the exterior of the sensitive receiver's building façade and be at a position 1.2m above the ground.
- (b) Façade measurements were made at the monitoring locations. For free-field measurement, a correction factor of +3 dB (A) would be applied.
- (c) The battery condition was checked to ensure the correct functioning of the meter.
- (d) Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:
- (e) Frequency weighting: A, Time weighting: Fast, Measurement time set: continuous 5 mins
- (f) Prior and after to the noise measurement, the meter was checked using the acoustic calibrator for 94dB (A) at 1000 Hz. If the difference in the calibration level before and after measurement was more than  $\pm 1$  dB (A), the measurement would be considered invalid and repeat of noise measurement would be required after re-calibration or repair of the equipment.

#### 4.1.6. Maintenance and Calibration

- (a) The microphone head of the sound level meter was cleaned with soft cloth at regular intervals.
- (b) The sound level meter and calibrator were calibrated at yearly intervals.

### CONSTRUCTION NOISE LEVEL

- 4.1.7. The construction noise level refers the corrected noise level based on the calculated difference between SPL of the Measured Noise Level and the SPL of the Baseline Noise Level. In the event of the Baseline Noise Level exceeds the Measured Noise Level, no correction would be applied and the Construction Noise Level would be indicated as below baseline noise level (<BL).

### EVENT AND ACTION PLAN

- 4.1.8. Noise Standards for Daytime Construction Activities are specified under EIAO-TM. The Action and Limit levels for construction noise are defined in **Table 4.3** and [Appendix 4.1](#). Should non-compliance of the criteria occurs, action in accordance with the Event and Action Plan in [Appendix 6.1](#) shall be carried out.

**Table 4.3 Action and Limit Level for Noise Monitoring**

Monitoring Station	Action Level	Limit Level (dB(A))		
		0700-1900 hrs on normal weekdays	0700-2300 hrs on holidays (including Sundays); and 1900-2300 hrs on all days <sup>2</sup>	2300-0700 hrs of all days
NMC01	When one documented complaint is received	65 / 70 <sup>1</sup>	60 / 65 / 70 <sup>3</sup>	45 / 50 / 55 <sup>3</sup>
NMC02		75		45 / 50 / 55 <sup>3</sup>
NMC03		65 / 70 <sup>1</sup>		45 / 50 / 55 <sup>3</sup>

Remark 1: Limit level of NMC01 and NMC03 reduce to 65 dB (A) during examination periods if any.

Remark 2: Construction noise during restricted hours is under the control of Noise Control Ordinance Limit Level to be selected based on Area Sensitivity Rating.

Remark 3: Limit Level for restricted hour monitoring shall act as reference level only. Investigation would be conducted on CNP compliance if exceedance recorded during restricted hour noise monitoring period.

**4.2 Air Monitoring**

AIR QUALITY MONITORING STATIONS

4.2.1. The air monitoring stations for the Project are listed and shown in **Table 4.4** and **Figure 4.2**. **Appendix 4.1** shows the established Action/Limit Levels for environmental monitoring.

**Table 4.4 Air Quality Monitoring Station**

Monitoring Station	Air Sensitive Receivers	Monitoring Location
AMC01	Lai King Catholic Secondary School	Roof Floor
AMC02	Fung King House	Roof Floor
AMC03A <sup>1</sup>	Ming King House	Roof Floor

Remark 1: Due to limited location access, lack of power supply and land availability problem for setting up air quality monitoring stations at HKEAA-Lai King Assessment Centre (AMC03) under EM&A manual, alternative monitoring location at Ming King House was proposed in accordance with Section 2.5.3 of the EM&A manual and proposal for alternative monitoring location was submitted to EPD for approval.

AIR MONITORING PARAMETERS, FREQUENCY AND DURATION

- 4.2.2. One-hour and 24-hour TSP levels should be measured to indicate the impacts of construction dust on air quality.
- 4.2.3. 24-hour TSP shall be sampled at least once in every 6 days, while sampling for 1-hour TSP shall be at least 3 times in every 6 days when the highest dust impact takes place.

SAMPLING PROCEDURE AND MONITORING EQUIPMENT

4.2.4. 24-hour TSP Measuring Installation (HVS)

- (a) The HVS was installed in the vicinity of the air sensitive receivers. The following

criteria were considered in the installation of the HVS.

- (b) No furnace or incinerator flues were nearby.
- (c) Airflow around the sampler was unrestricted
- (d) 0.6 - 1.7 m<sup>3</sup> per minute adjustable flow range
- (e) Equipped with a timing / control device with +/- 5 minutes accuracy for 24 hours operation;
- (f) Installed with elapsed-time meter with +/- 2 minutes accuracy for 24 hours operation;
- (g) Equipped with a shelter to protect the filter and sampler;
- (h) Capable of operating continuously for a 24-hour period.

#### 4.2.5. 24-hour Measuring Procedures

- (a) The power supply was checked to ensure the HVS works properly.
- (b) The filter holder and the area surrounding the filter were cleaned.
- (c) The filter holder was removed by loosening the four bolts and a new filter, with stamped number upward, on a supporting screen was aligned carefully.
- (d) The filter was properly aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter.
- (e) The swing bolts were fastened to hold the filter holder down to the frame. The pressure applied should be sufficient to avoid air leakage at the edges.
- (f) Then the shelter lid was closed and was secured with the aluminum strip.
- (g) The HVS was warmed-up for about 5 minutes to establish run-temperature conditions.
- (h) A new flowrate record sheet was set into the flow recorder.
- (i) The flow rate of the HVS was checked and adjusted at around 1.2 m<sup>3</sup>/min. The range specified in the EM&A Manual was between 0.6-1.7 m<sup>3</sup>/min.
- (j) The programmable timer was set for a sampling period of 24 hrs + 1 hr, and the starting time, weather condition and the filter number were recorded.
- (k) The initial elapsed time was recorded.
- (l) At the end of sampling, the sampled filter was removed carefully and folded in half-length so that only surfaces with collected particulate matter were in contact.
- (m) It was then placed in a clean plastic envelope and sealed.
- (n) All monitoring information was recorded on a standard data sheet.
- (o) Filters were sent to laboratory for further testing.

#### 4.2.6. 1-hour Measuring Procedures

- (a) Check the calibration period of portable direct reading dust meter prior to monitoring (The direct reading dust meter was calibrated at 2-years interval and checked with High Volume Sampler (HVS) yearly, details refer to Section 2.5.4)
- (b) Record the site condition near / around the monitoring stations.
- (c) Install the portable direct reading dust meter to the monitoring location.
- (d) Slide the power switch to turn the power on.
- (e) Check of portable direct reading dust meter to ensure the equipment operation in normal condition.
- (f) Select the period of measurement to 60mins.
- (g) Check and set the correct time.
- (h) Select the appropriate unit display for the equipment.

- (i) Slide the power switch to turn the power off when the monitoring period ended (3 times 1 hour TSP monitoring per day).
- (j) Uninstall the portable direct reading dust meter
- (k) Collected the sampled data for analysis.

Remark: Procedures (c) to (h) may be different subject to the brands and models of portable direct reading dust.

#### LABORATORY MEASUREMENT / ANALYSIS

- 4.2.7. A clean laboratory with constant temperature and humidity control, and equipped with necessary measuring and conditioning instruments to handle the dust samples collected, shall be available for sample analysis, and equipment calibration and maintenance. The laboratory should be HOKLAS accredited or other internationally accredited laboratory.
- 4.2.8. Filter paper of size 8" x 10" shall be labelled before sampling. It shall be a clean filter paper with no pinholes, and shall be conditioned in a humidity-controlled chamber for over 24-hours and be pre-weighed before use for the sampling.
- 4.2.9. After sampling, the filter paper loaded with dust shall be kept in a clean and tightly sealed plastic bag. The filter paper shall then be returned to the laboratory for reconditioning in the humidity controlled chamber followed by accurate weighing by an electronic balance with readout down to 0.1 mg. The balance shall be regularly calibrated against a traceable standard.
- 4.2.10. Maintenance and Calibration
- (a) The direct reading dust meter was calibrated at 2-years interval and checked with High Volume Sampler (HVS) yearly to determine the accuracy and validity of the results measured.
  - (b) Checking of direct reading dust meter will be carried out in order to determine the conversion factor between the direct reading dust meter and the standard equipment, HVS. The comparison check is to be considered valid based on correlation coefficient checked by HOKLAS laboratory
- 4.2.11. High Volume Sampler (HVS – Model TE-5170) completed with the appropriate sampling inlets were installed for the 24-hour TSP sampling. 1-hour TSP air quality monitoring was performed by using portable direct reading dust meters at each designated monitoring station, which was verified by IEC and approved by the Engineer's Representative (ER) on 16 July 2021 and 22 July 2021, respectively according to Section 2.2.2 and 2.3.6 of the Project EM&A Manual. The brand and model of the equipment are given in **Table 4.5**.



**Table 4.5 Air Quality Monitoring Equipment**

Equipment	Brand and model	Series Number
Portable direct reading dust meter	Met One BT-645	B17940 X19298 X19297
High Volume Sampler	TE-5170	0200-0740 (HVS004) 2649 (HVS014) 2650 (HVS015)
Wind Anemometer	YiGu – YGY-FSXY12	21091630T0944

4.2.12. The calibration certificates of the air quality monitoring equipment are attached in [Appendix 4.2](#).

WIND DATA

4.2.13. Wind data monitoring equipment was set up at roof floor (about 15/F) of Fung King House for logging wind speed and wind direction such that the wind sensors were clear of obstructions or turbulence caused by building. The wind data monitoring equipment was re-calibrated at least once every six months and the wind directions were divided into 16 sections of 22.5 degrees each. The wind data obtained from the on-site wind station during the reporting period is provided in [Appendix 4.3](#).

EVENT AND ACTION PLAN

4.2.14. The Action and Limit levels for construction air quality are defined in **Table 4.6** and [Appendix 4.1](#). Should non-compliance of the air quality criteria occur, action in accordance with the Event and Action Plan in [Appendix 6.1](#) shall be carried out.

**Table 4.6 Action and Limit Level for Air Quality Monitoring**

Parameter	Monitoring Station	Action Level (µg/m³)	Limit Level (µg/m³)
24-hour TSP Level	AMC01	144.8	260.0
	AMC02	144.3	260.0
	AMC03A	143.7	260.0
1-hour TSP Level	AMC01	256.2	500.0
	AMC02	256.7	500.0
	AMC03A	259.3	500.0

**5 Monitoring Results**

- 5.0.1 The environmental monitoring will be implemented based on the division of works areas of each designed projects. Overall layout showing work areas and monitoring stations is shown in [Figure 2.1](#) and [Figure 4.1 – 4.2](#) respectively.
- 5.0.2 The environment monitoring schedules for reporting month and coming month are presented in [Appendix 5.1](#).

**5.1 Noise Monitoring Results**

- 5.1.1 Noise monitoring results measured in this reporting period are reviewed and summarized. Details of noise monitoring results and graphical presentation can be referred in [Appendix 5.2](#).
- 5.1.2 Limit level of noise monitoring station NMC-03 has adjusted to 65dB(A) during examination period.
- 5.1.3 Limit level exceedances were recorded at NMC-01 and NMC-03 in this reporting period. As the baseline level of NMC-01 and NMC-03 are higher than the measured average noise level, the noise monitoring results are not considered as noise exceedances.

**5.2 Air Monitoring Results**

- 5.2.1 Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air monitoring results and graphical presentation can be referred in [Appendix 5.3](#).
- 5.2.2 No action or limit level exceedance was recorded in this reporting month.

**5.3 Waste Management**

- 1.1.1 The quantities of waste for disposal in the Reporting Period are summarized in **Table 5.1** and **Table 5.2**. The Monthly Summary Waste Flow Table is shown in [Appendix 5.4](#). Whenever possible, materials were reused on-site as far as practicable.

**Table 5.1 Summary of Quantities of Inert C&D Materials**

Waste Type	Quantity (this month)	Quantity (Project commencement to the end of last month)	Cumulative Quantity-to-Date
Hard Rock and Large Broken Concrete (Inert) (in '000m <sup>3</sup> )	0	0	0

Waste Type	Quantity (this month)	Quantity (Project commencement to the end of last month)	Cumulative Quantity-to-Date
Reused in this Contract (Inert) (in '000m <sup>3</sup> )	0	0	0
Reused in other Projects (Inert) (in '000m <sup>3</sup> )	0	0	0
Disposal as Public Fill (Inert) (in '000m <sup>3</sup> )	0.0351	14.1488	14.1839

*Table 5.2 Summary of Quantities of C&D Wastes*

Waste Type	Quantity (this month)	Quantity (Project commencement to the end of last month)	Cumulative Quantity-to-Date
Metals (in '000kg)	0.0038	26.3219	26.3257
Paper / Cardboard Packing (in '000kg)	0.0514	1.8752	1.9266
Plastics (in '000kg)	0	0	0
Chemical Wastes (in '000kg)	0	0	0
General Refuses (in '000m <sup>3</sup> )	0.0088	0.7232	0.732

## 6 Compliance Audit

6.0.1 The Event Action Plan for construction noise, air quality and water quality are presented in [Appendix 6.1](#).

6.0.2 The summary of exceedance is presented in [Appendix 6.2](#).

### 6.1 Noise Monitoring

6.1.1 Limit level exceedances were recorded at NMC-01 and NMC-03 in this reporting period. As the baseline level of NMC-01 and NMC-03 are higher than the measured average noise level, the noise monitoring results are not considered as noise exceedances.

### 6.2 Air Quality Monitoring

6.2.1 No action or limit level exceedance was recorded in this reporting period.

### 6.3 Review of the Reasons for and the Implications of Non-compliance

6.3.1 No environmental non-compliance was recorded in the reporting month.

### 6.4 Summary of action taken in the event of and follow-up on non-compliance

6.4.1 There was no particular action taken since no non-compliance was recorded in the reporting period.

**7 Environmental Site Audit**

- 7.0.1. Within this reporting month, weekly environmental site audits were conducted on 4, 9, 18 and 25 July 2024 and biweekly landscape inspection on 4 and 18 July 2024..
- 7.0.2. No non-compliance was found during the environmental site inspection while reminders on environmental measures were recommended. Results and findings of these inspections in this reporting month are listed below in **Table 7.1 to 7.2**.

**Table 7.1 Summary of Environmental Inspections**

Item	Date	Reminder(s)/ Observation(s)	Action taken by Contractor	Outcome
20240704_1	4-July-2024	No specific findings	---	---
20240709_1	9-July-2024	Exposed stockpile shall be removed or backfilled or covered as appropriate if required to remain overnight/ after work.	Exposed stockpile has been covered.	---
20240709_2		Site haul road shall be watered to maintain wet to withstand from wind blown	Water spraying on haul road has been provided.	---
20240718_1	18-July-2024	Main haul road and vehicles wheels should be washed to prevent dust	Main haul road and vehicles wheels have been washed	---
20240725_1	25-July-2024	No specific findings	---	---

**Table 7.2 Summary of Landscape Site Inspections**

Item	Date	Reminder(s)/ Observation(s)	Action taken by Contractor	Outcome
20240704_2 20240718_2	4-July-2024 18-July-2024	Follow-up 1: T175( Retained) shows no sign of improvement since March 2024, Contractor is advised to seek professional advice to confirm its health condition and the required treatment to resolve the outstanding situation	The Contractor is investigating the condition of T175.	---

Remark 1: On 11 May 2023, the trees transplanted to off-site as the final operating landscape on Stonecutters Island were inspected (inspection started from the 1st week of May 2022 after the bulk transplant was completed at the end of April 2022), and no results were found to be followed up, these trees transplanted as the final operation landscape of Stonecutters Island have completed the 12-month operation stage landscape audit according to Article 6.2.3 of the EM&A Manual.

Remark 2: As confirmed by contractor, T135, T142, and T162 were removed on 30 October 2023, updated of Tree Preservation and Removal Proposal (TPRP) were submitted to HyD and LCSD on 12 December 2023.

**8 Complaints, Notification of Summons and Prosecution**

- 8.0.1. No environmental complaint, notification of summons and successful prosecution regarding construction works was recorded in the reporting period.
- 8.0.2. The details of cumulative complaint log and updated summary of complaints are presented in [Appendix 8.1](#).
- 8.0.3. Cumulative statistic on complaints and successful prosecutions are summarized in **Table 8.1** and **Table 8.2** respectively.

**Table 8.1 Cumulative Statistics on Complaints**

Reporting Period	No. of Complaints
July 2024	0
Project commencement to the end of last reporting month	-
<b>Total</b>	<b>0</b>

**Table 8.2 Cumulative Statistics on Successful Prosecutions**

Environmental Parameters	Cumulative No. Brought Forward	No. of Successful Prosecutions this month (Offence Date)	Cumulative No. Project-to-Date
Air	-	0	0
Noise	-	0	0
Water	-	0	0
Waste	-	0	0
<b>Total</b>	<b>-</b>	<b>0</b>	<b>0</b>

**9 Conclusion**

- 9.0.1. The EM&A programme was carried out in accordance with the EM&A Manual requirements, minor alterations to the programme proposed were made in response to changing circumstances.
- 9.0.2. Mitigation measures according to the environmental mitigation implementation schedule and the EIA were generally implemented by the Contractor. Hence, the EM&A programme was considered effective and shall be maintained.
- 9.0.3. The scheduled construction activities and the recommended mitigation measures for the coming 3 months are listed in **Table 9.1**. The construction programmes of the Project are provided in [Appendix 9.1](#).

**Table 9.1 Construction Activities and Recommended Mitigation Measures in Coming Reporting 3 Months**

Key Construction Works	Recommended Mitigation Measures
<ul style="list-style-type: none"> <li>• Tree preservation works</li> <li>• Piling works for Bridge H</li> <li>• Erection of falsework for Bridge H Deck</li> <li>• Construction of Deck for Bridge G</li> <li>• Formwork erection and fixing rebar at Bridge H</li> <li>• Drainage works near H7</li> <li>• Demolition of Existing NF303 Footbridge</li> <li>• Construction of granite wall</li> <li>• Road Diversion works near Pier H7</li> </ul>	<ul style="list-style-type: none"> <li>• Regular maintenance and protection of all existing retained and transplanted trees</li> <li>• Implement proper measures to prevent silt or debris being deposited or washed into existing drainage systems</li> <li>• Implement proper noise mitigation measures to prevent potential noise nuisances to nearby sensitive receivers, with attention on restricted hour work activities</li> <li>• Provision of protection to ensure no runoff out of site area or direct discharge into public drainage system</li> </ul>






## ***Figure 1.1***

# ***Project Layout***



Date : 4/5/2021  
 Filename : X:\252146 (CE72-2015-HY)\02\_DRAWING\CONTRACT\CADD\WSP\_202008\_T\_AB\_0001.dgn

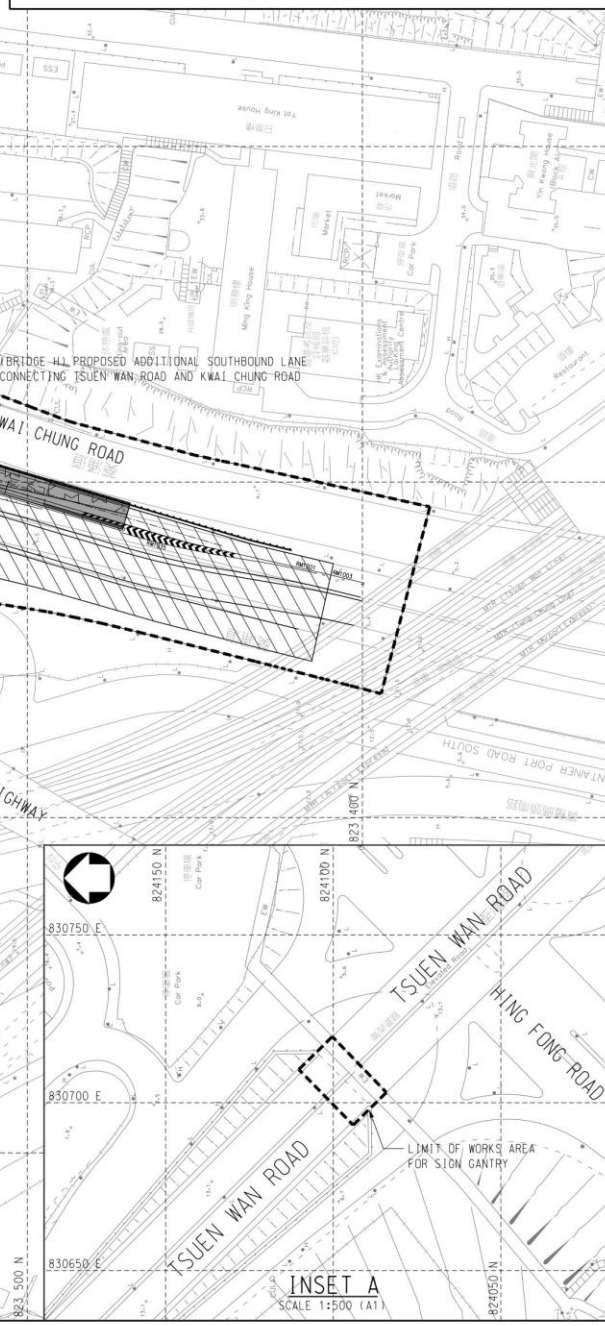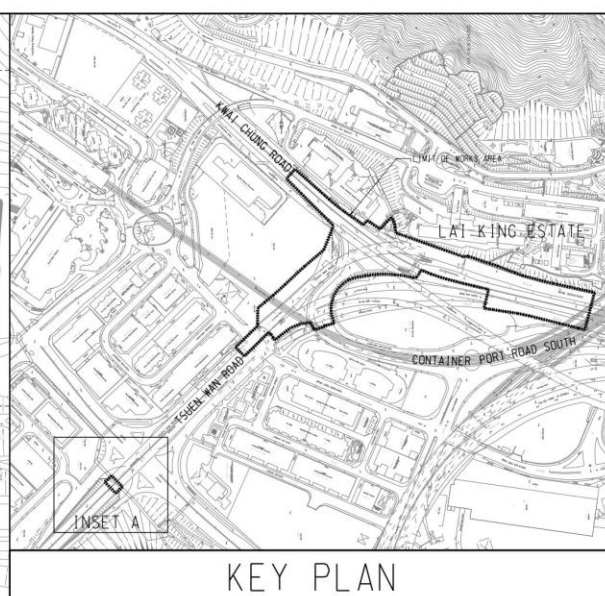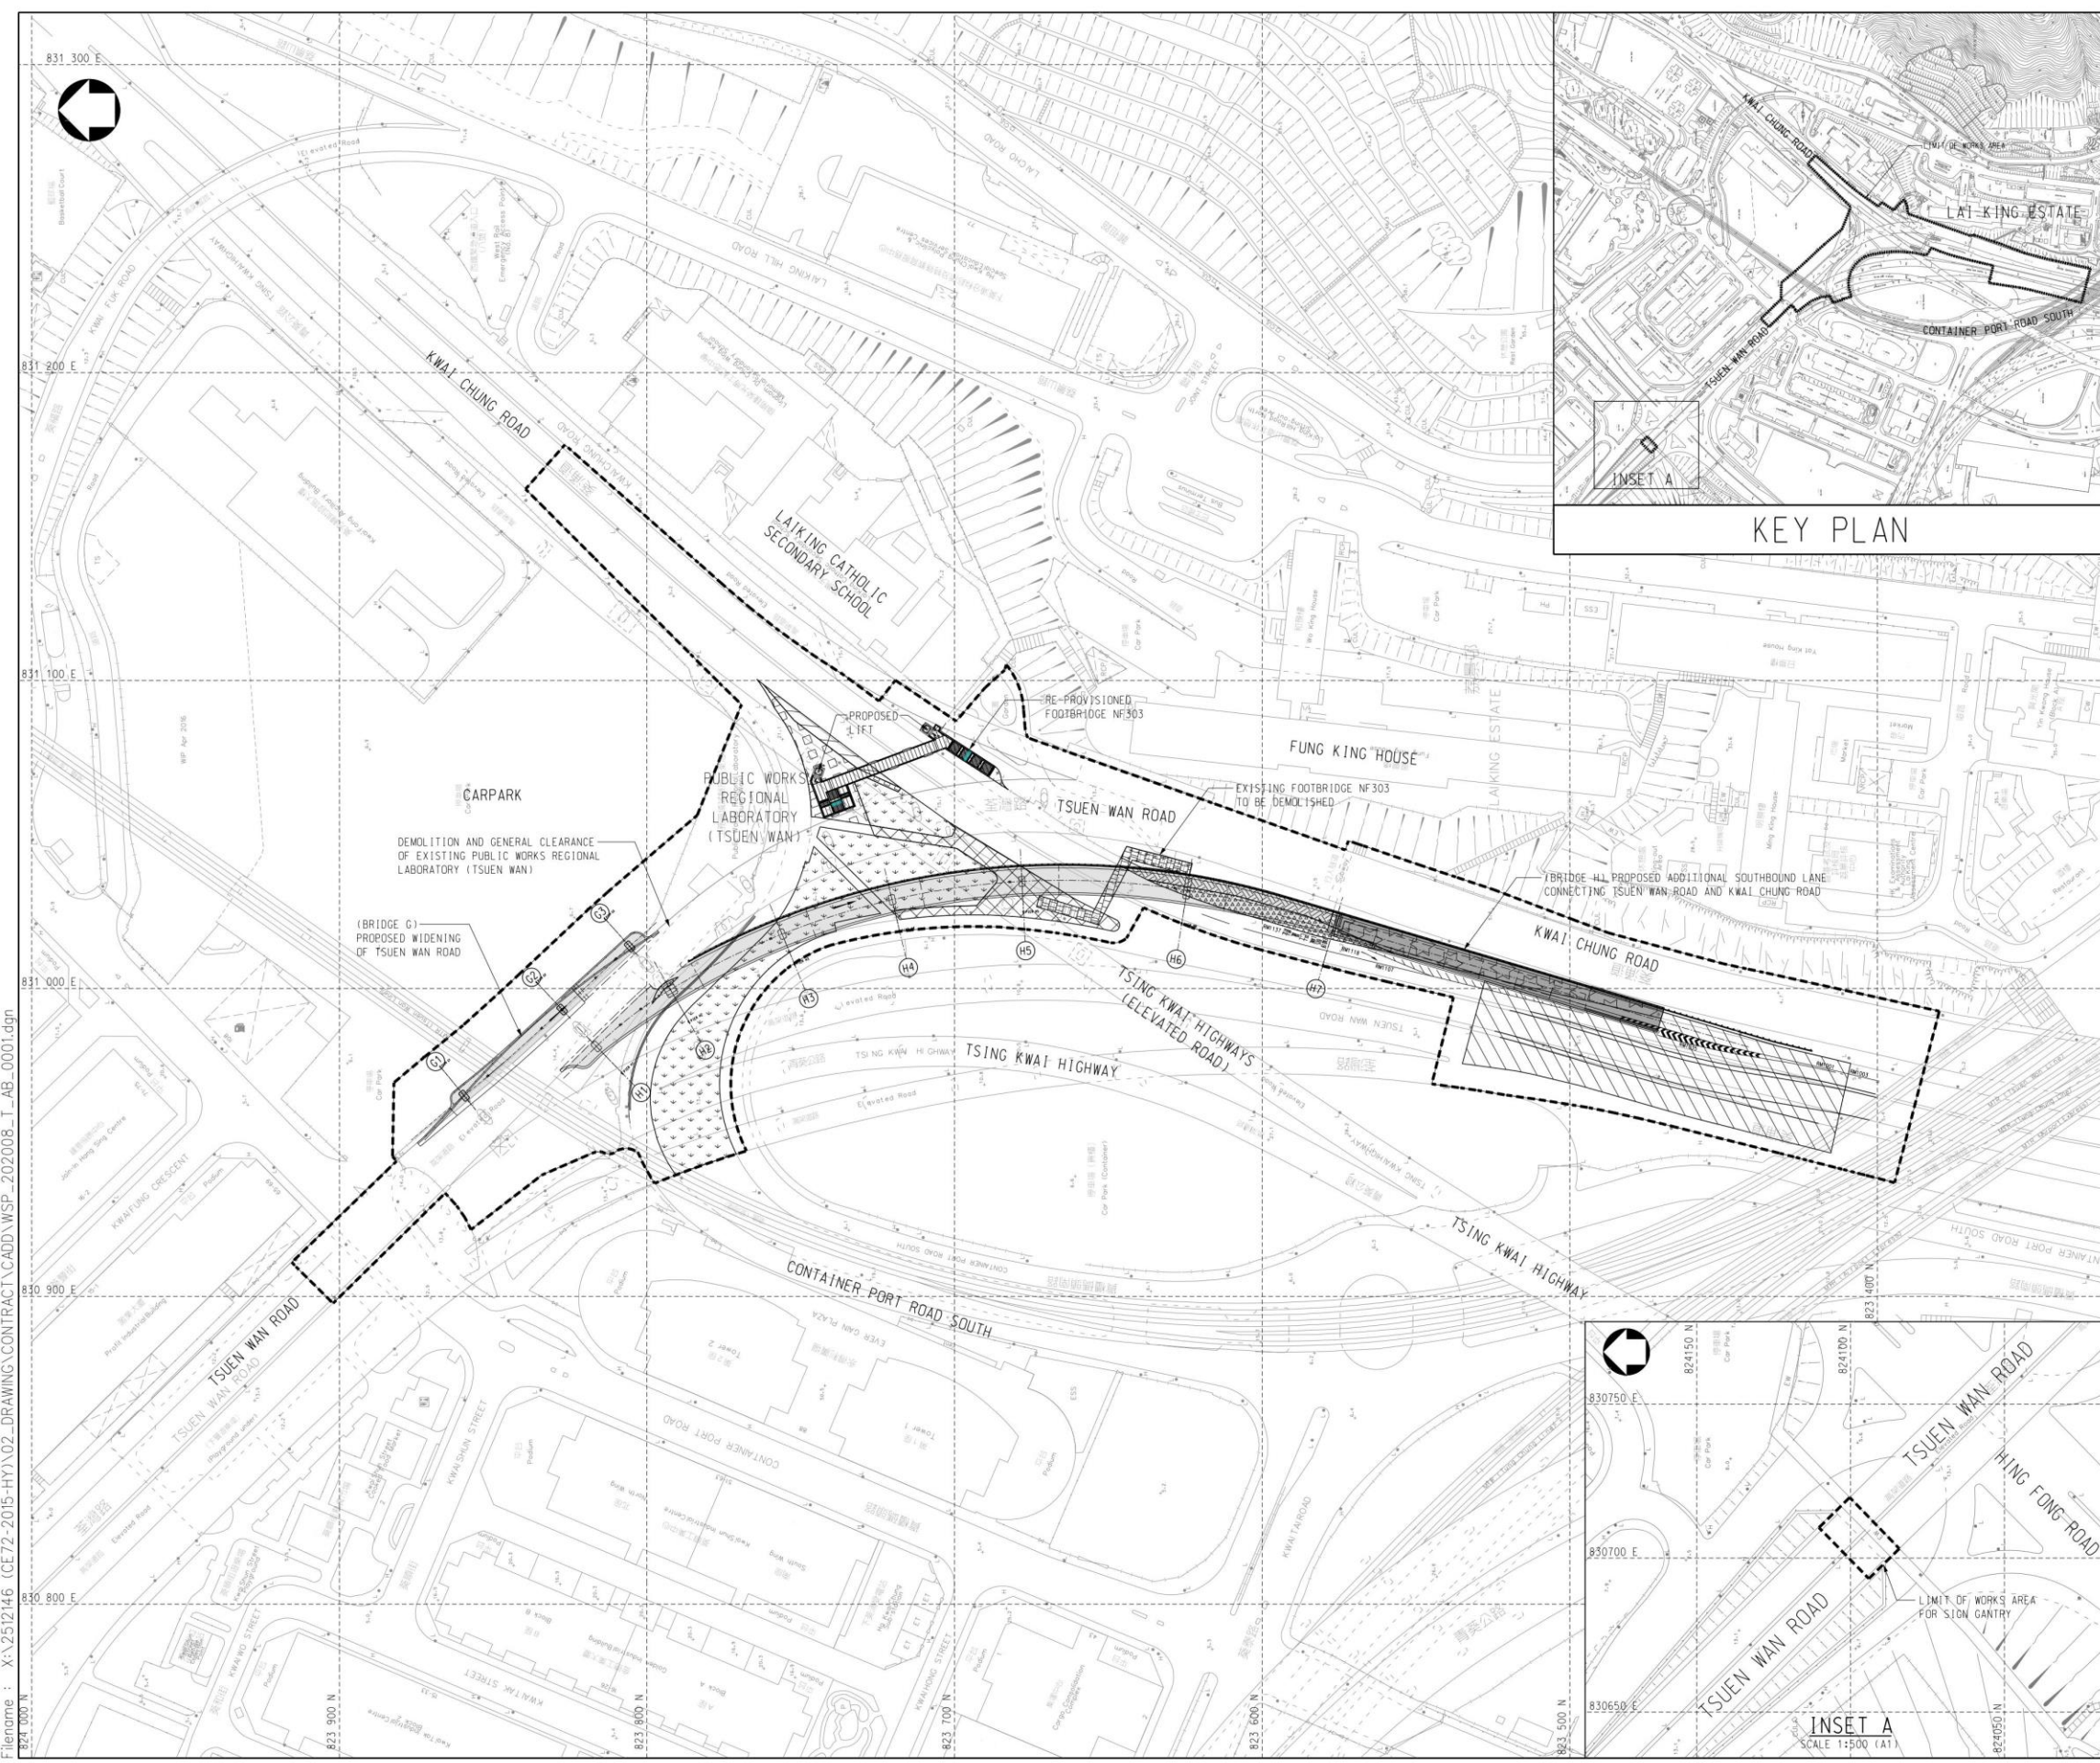

- NOTES :
1. ALL DIMENSIONS ARE IN METRES UNLESS OTHERWISE STATED.
  2. ALL LEVELS ARE APPROXIMATE VALUES AND IN METRES ABOVE HONG KONG PRINCIPAL DATUM.
  3. SECTIONS OF THE EXISTING CARRIAGEWAYS AND FOOTPATHS WITHIN THE LIMIT OF WORKS AREA MAY BE TEMPORARILY CLOSED IN PHASES AS AND WHEN REQUIRED.

LEGEND :

----- LIMIT OF WORK SITE

ISSUE FOR TENDER	EW	01/21
Rev Description	By	Date
Consultant		
Project title		
CONTRACT NO. HY/2020/08		
FLYOVER FROM KWAI TSING INTERCHANGE UP-RAMP TO KWAI CHUNG ROAD		
<b>Figure 1.1</b>		
<b>Project Layout</b>		
Scale	1:1000 (A1)	Status
		CONTRACT
© COPYRIGHT RESERVED		





## ***Figure 2.1***

# ***Project Organization Chart***



### Project Organization Chart


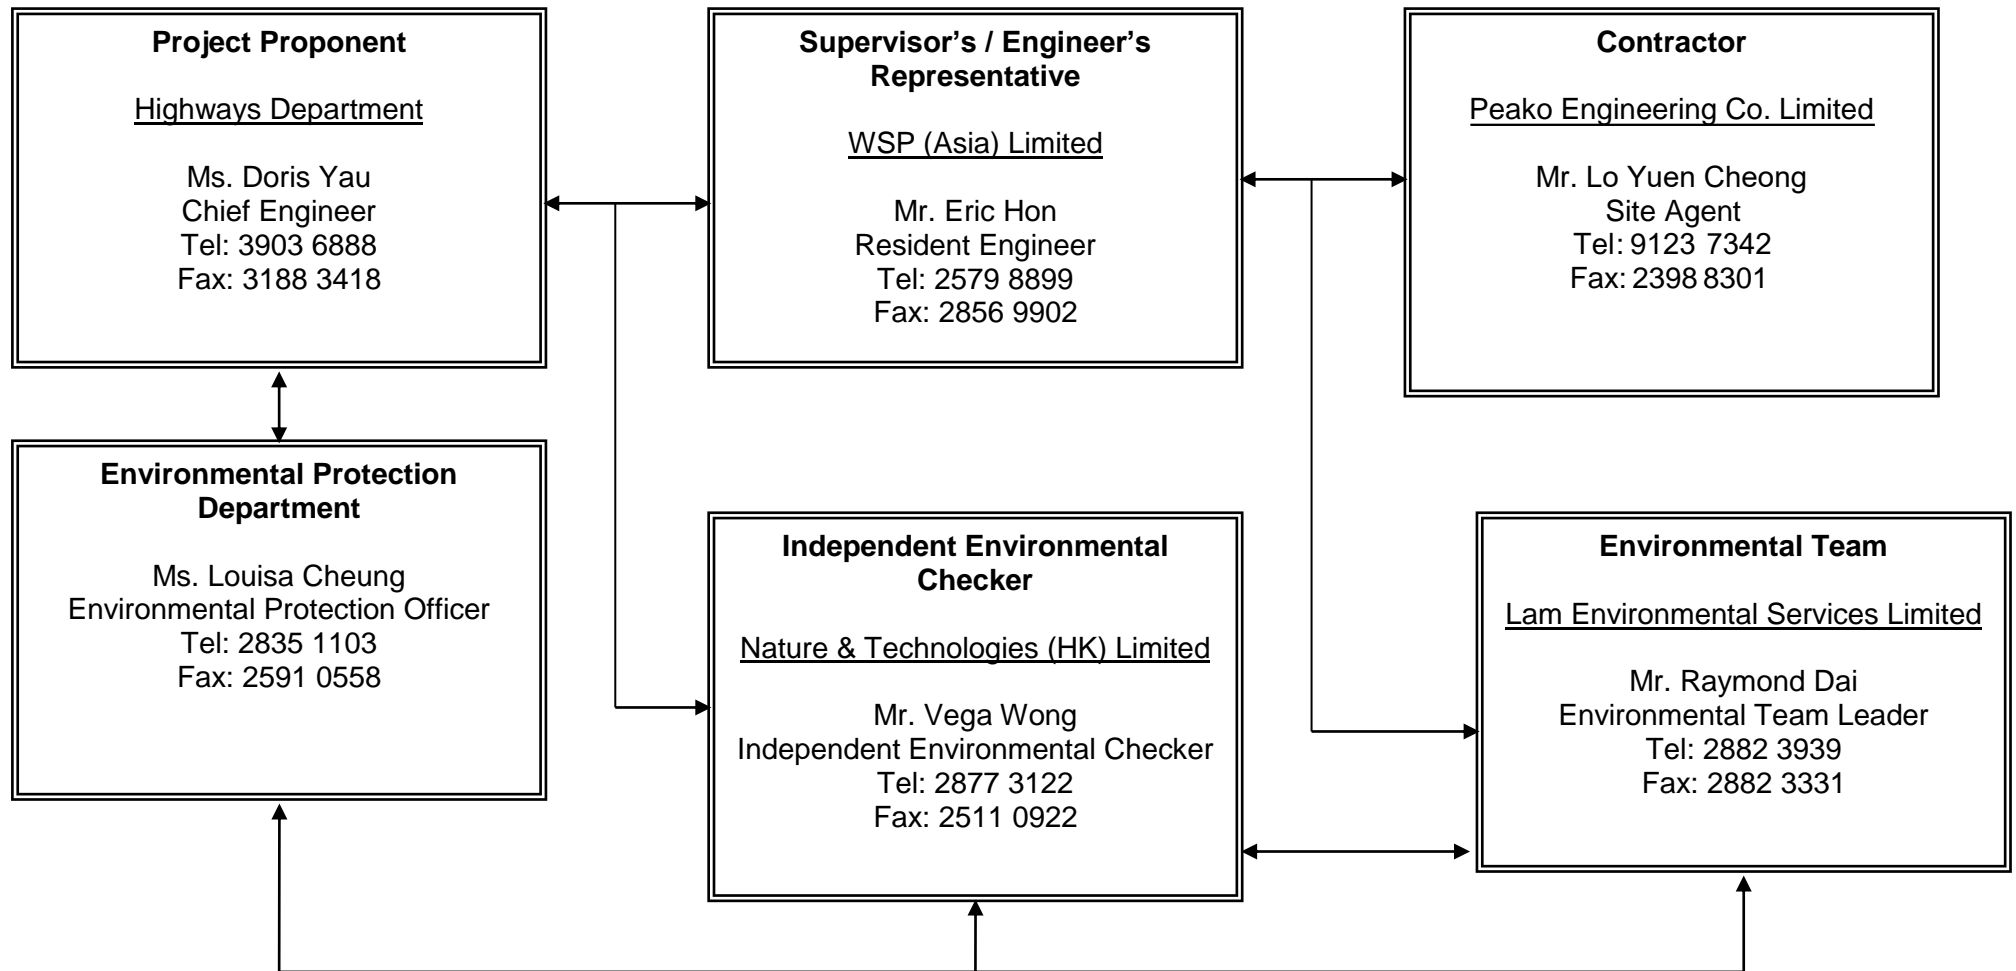


Figure 2.1

## *Figure 4.1*

# *Location of Noise Monitoring Stations*

Date : 4/5/2021  
 Filename : X:\252146 (CE72-2015-HY102-DRAWING\CONTRACT\CADD\WSP\_202008\_T\_AB\_0001.dgn

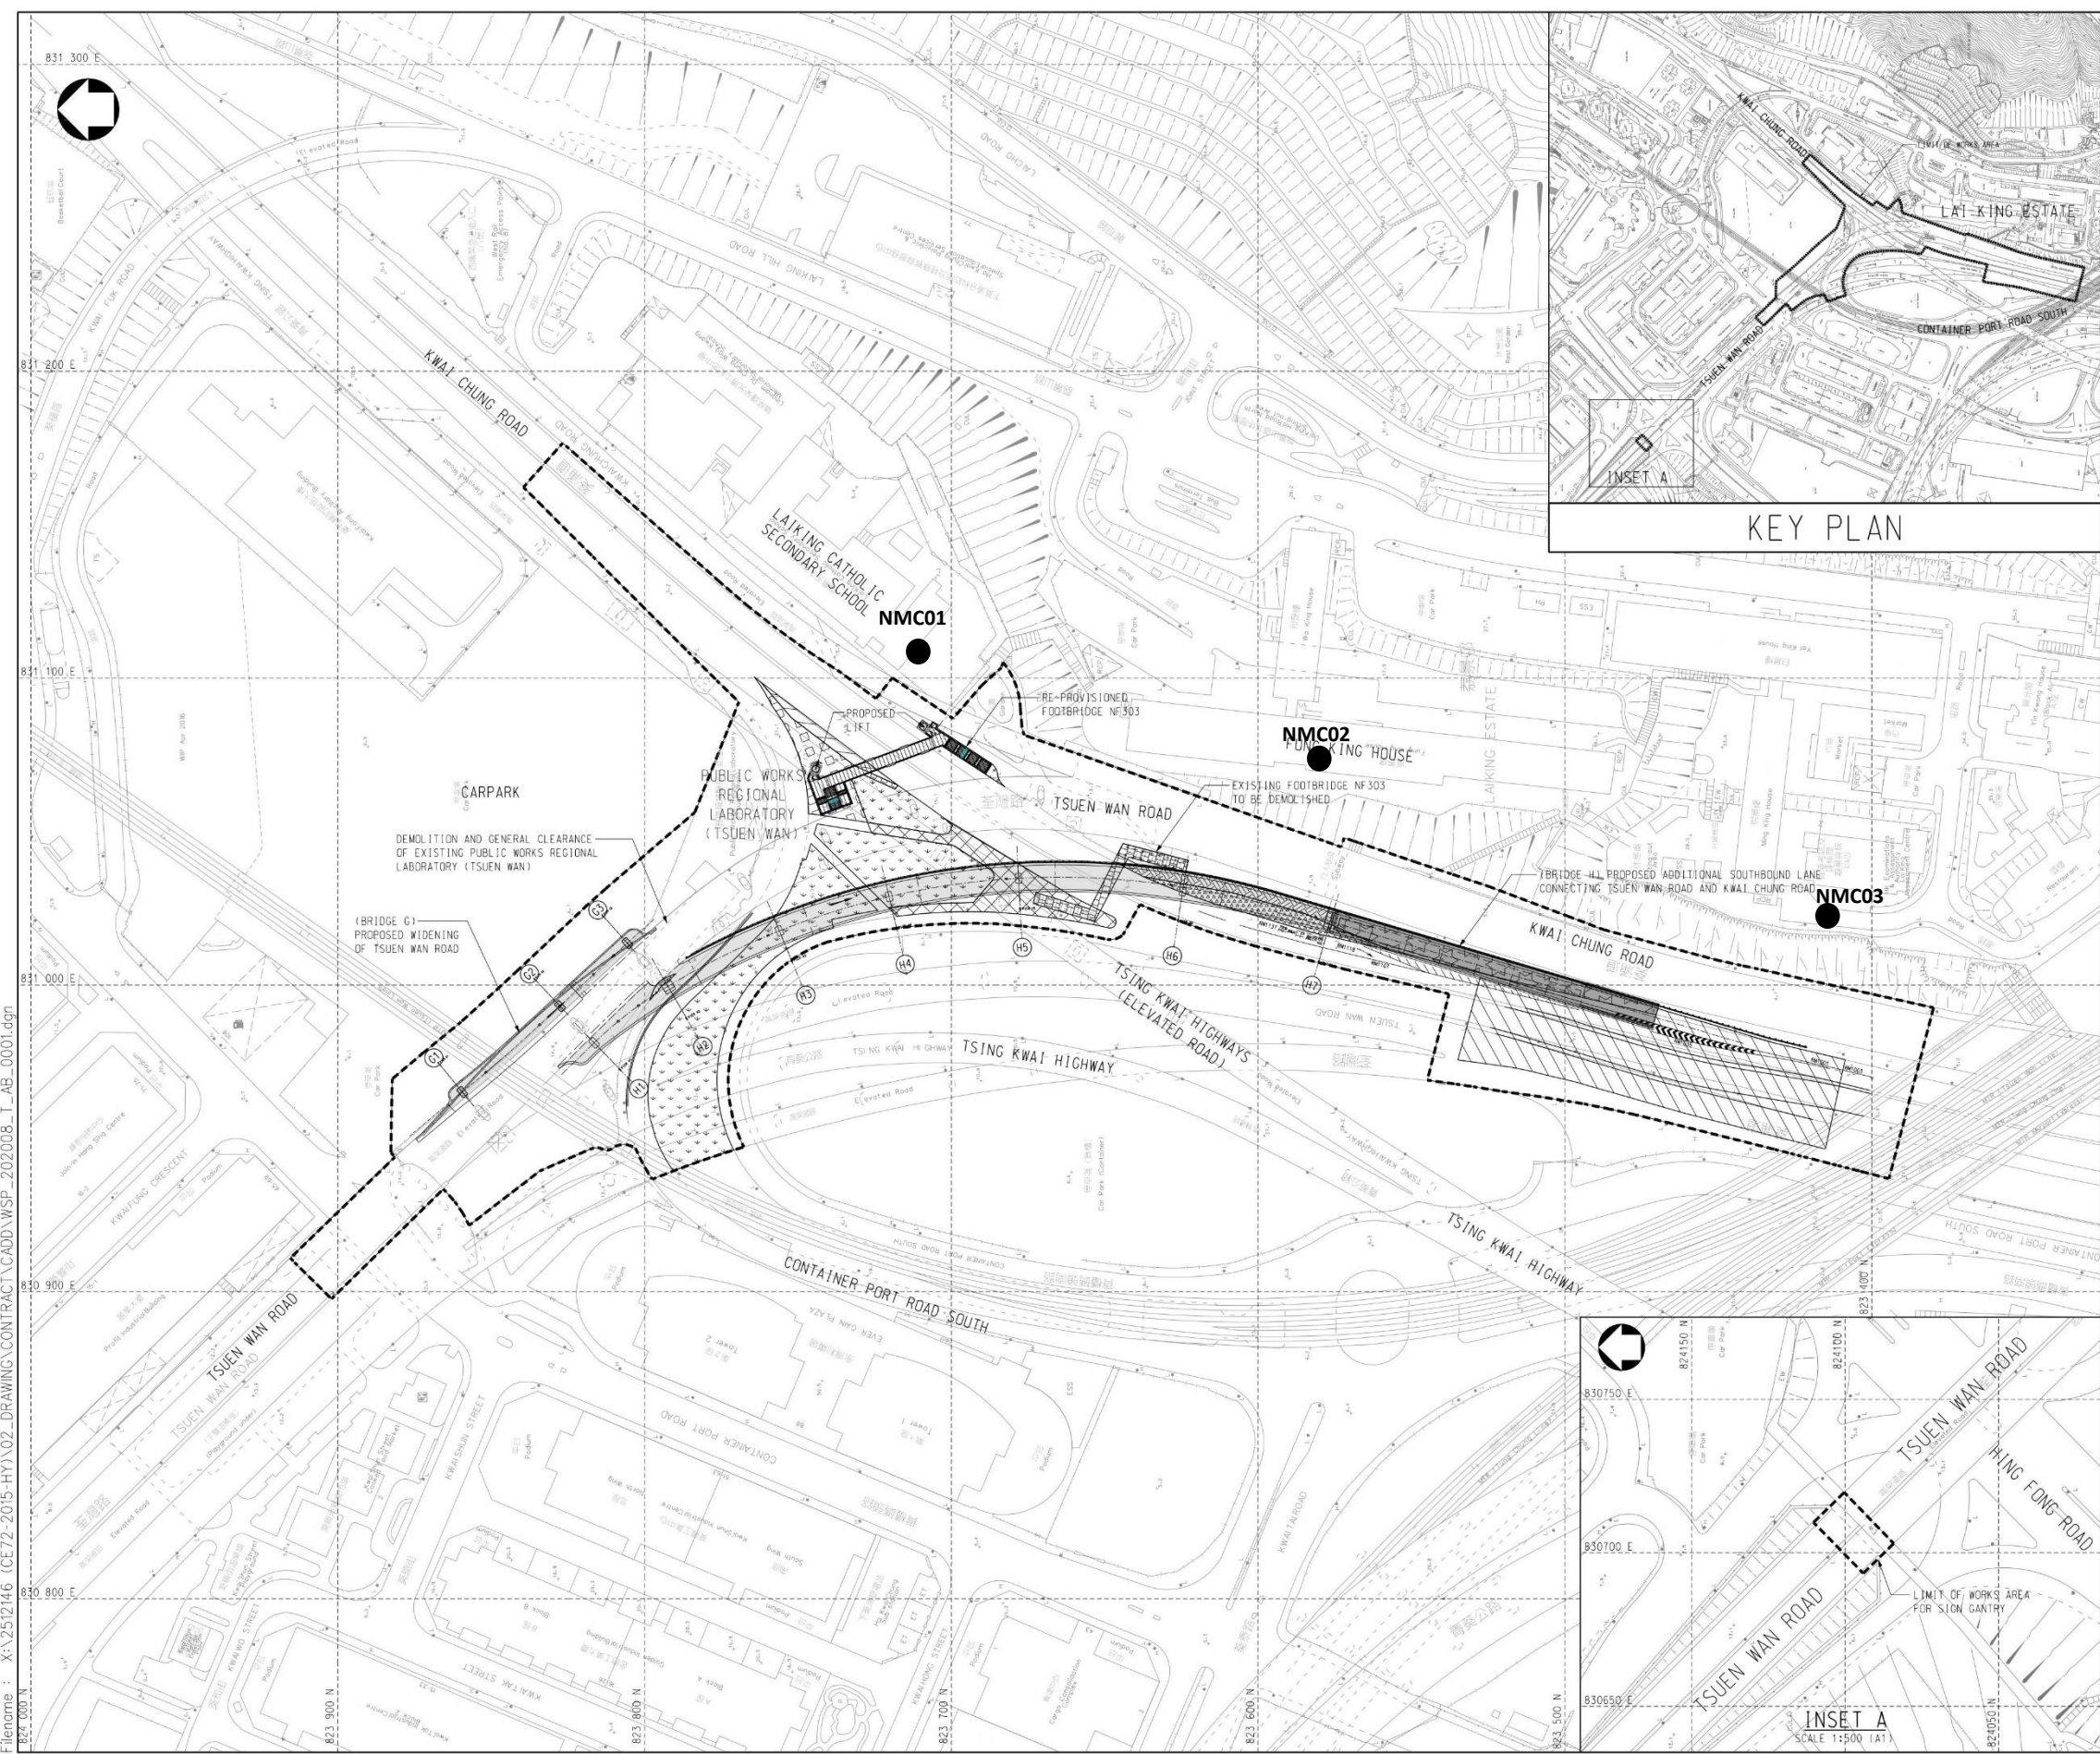

- NOTES :
1. ALL DIMENSIONS ARE IN METRES UNLESS OTHERWISE STATED.
  2. ALL LEVELS ARE APPROXIMATE VALUES AND IN METRES ABOVE HONG KONG PRINCIPAL DATUM.
  3. SECTIONS OF THE EXISTING CARRIAGEWAYS AND FOOTPATHS WITHIN THE LIMIT OF WORKS AREA MAY BE TEMPORARILY CLOSED IN PHASES AS AND WHEN REQUIRED.

LEGEND :

--- LIMIT OF WORK SITE

● Noise Monitoring Locations

Rev	Issue for Tender	EW	01/21
Description	By	Date	

Consultant



Project title  
 CONTRACT NO. HY/2020/08  
 FLYOVER FROM KWAI TSING INTERCHANGE  
 UP-RAMP TO KWAI CHUNG ROAD

**Figure 4.1**  
**Location of Noise Monitoring Stations**

Scale 1:1000 (A1) Status CONTRACT  
 © COPYRIGHT RESERVED






路政署  
 HIGHWAYS DEPARTMENT  
 工程師  
 WORKS DIVISION

## ***Figure 4.2***

# ***Location of Air Quality Monitoring Stations***

Date : 4/5/2021  
 Filename : X:\252146 (CE72-2015-HY1)\02\_DRAWING\CONTRACT\CADD\WSP\_202008\_T\_AB\_0001.dgn

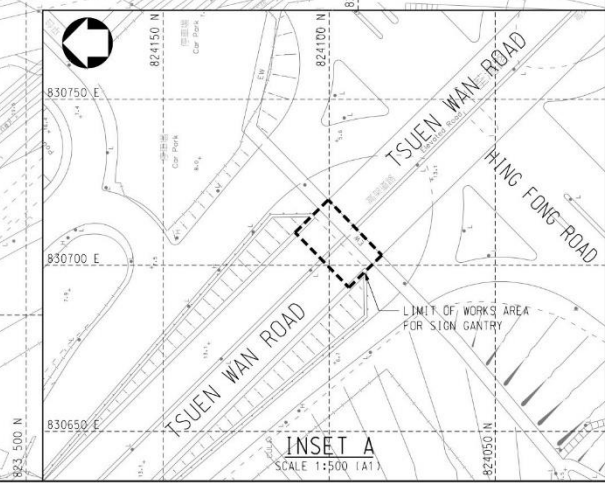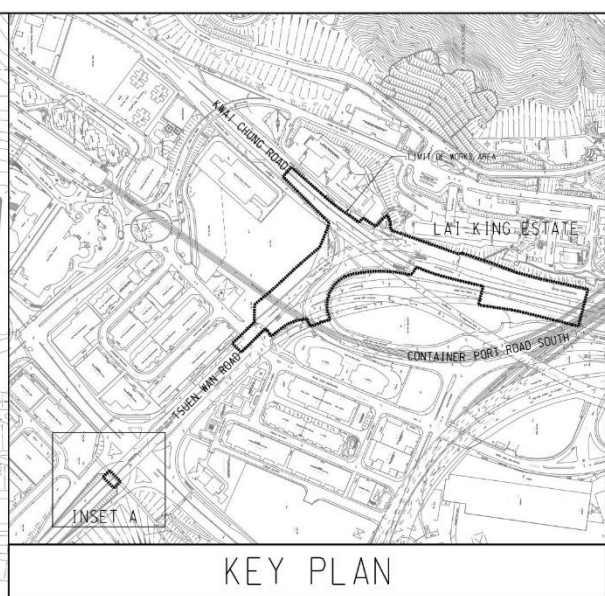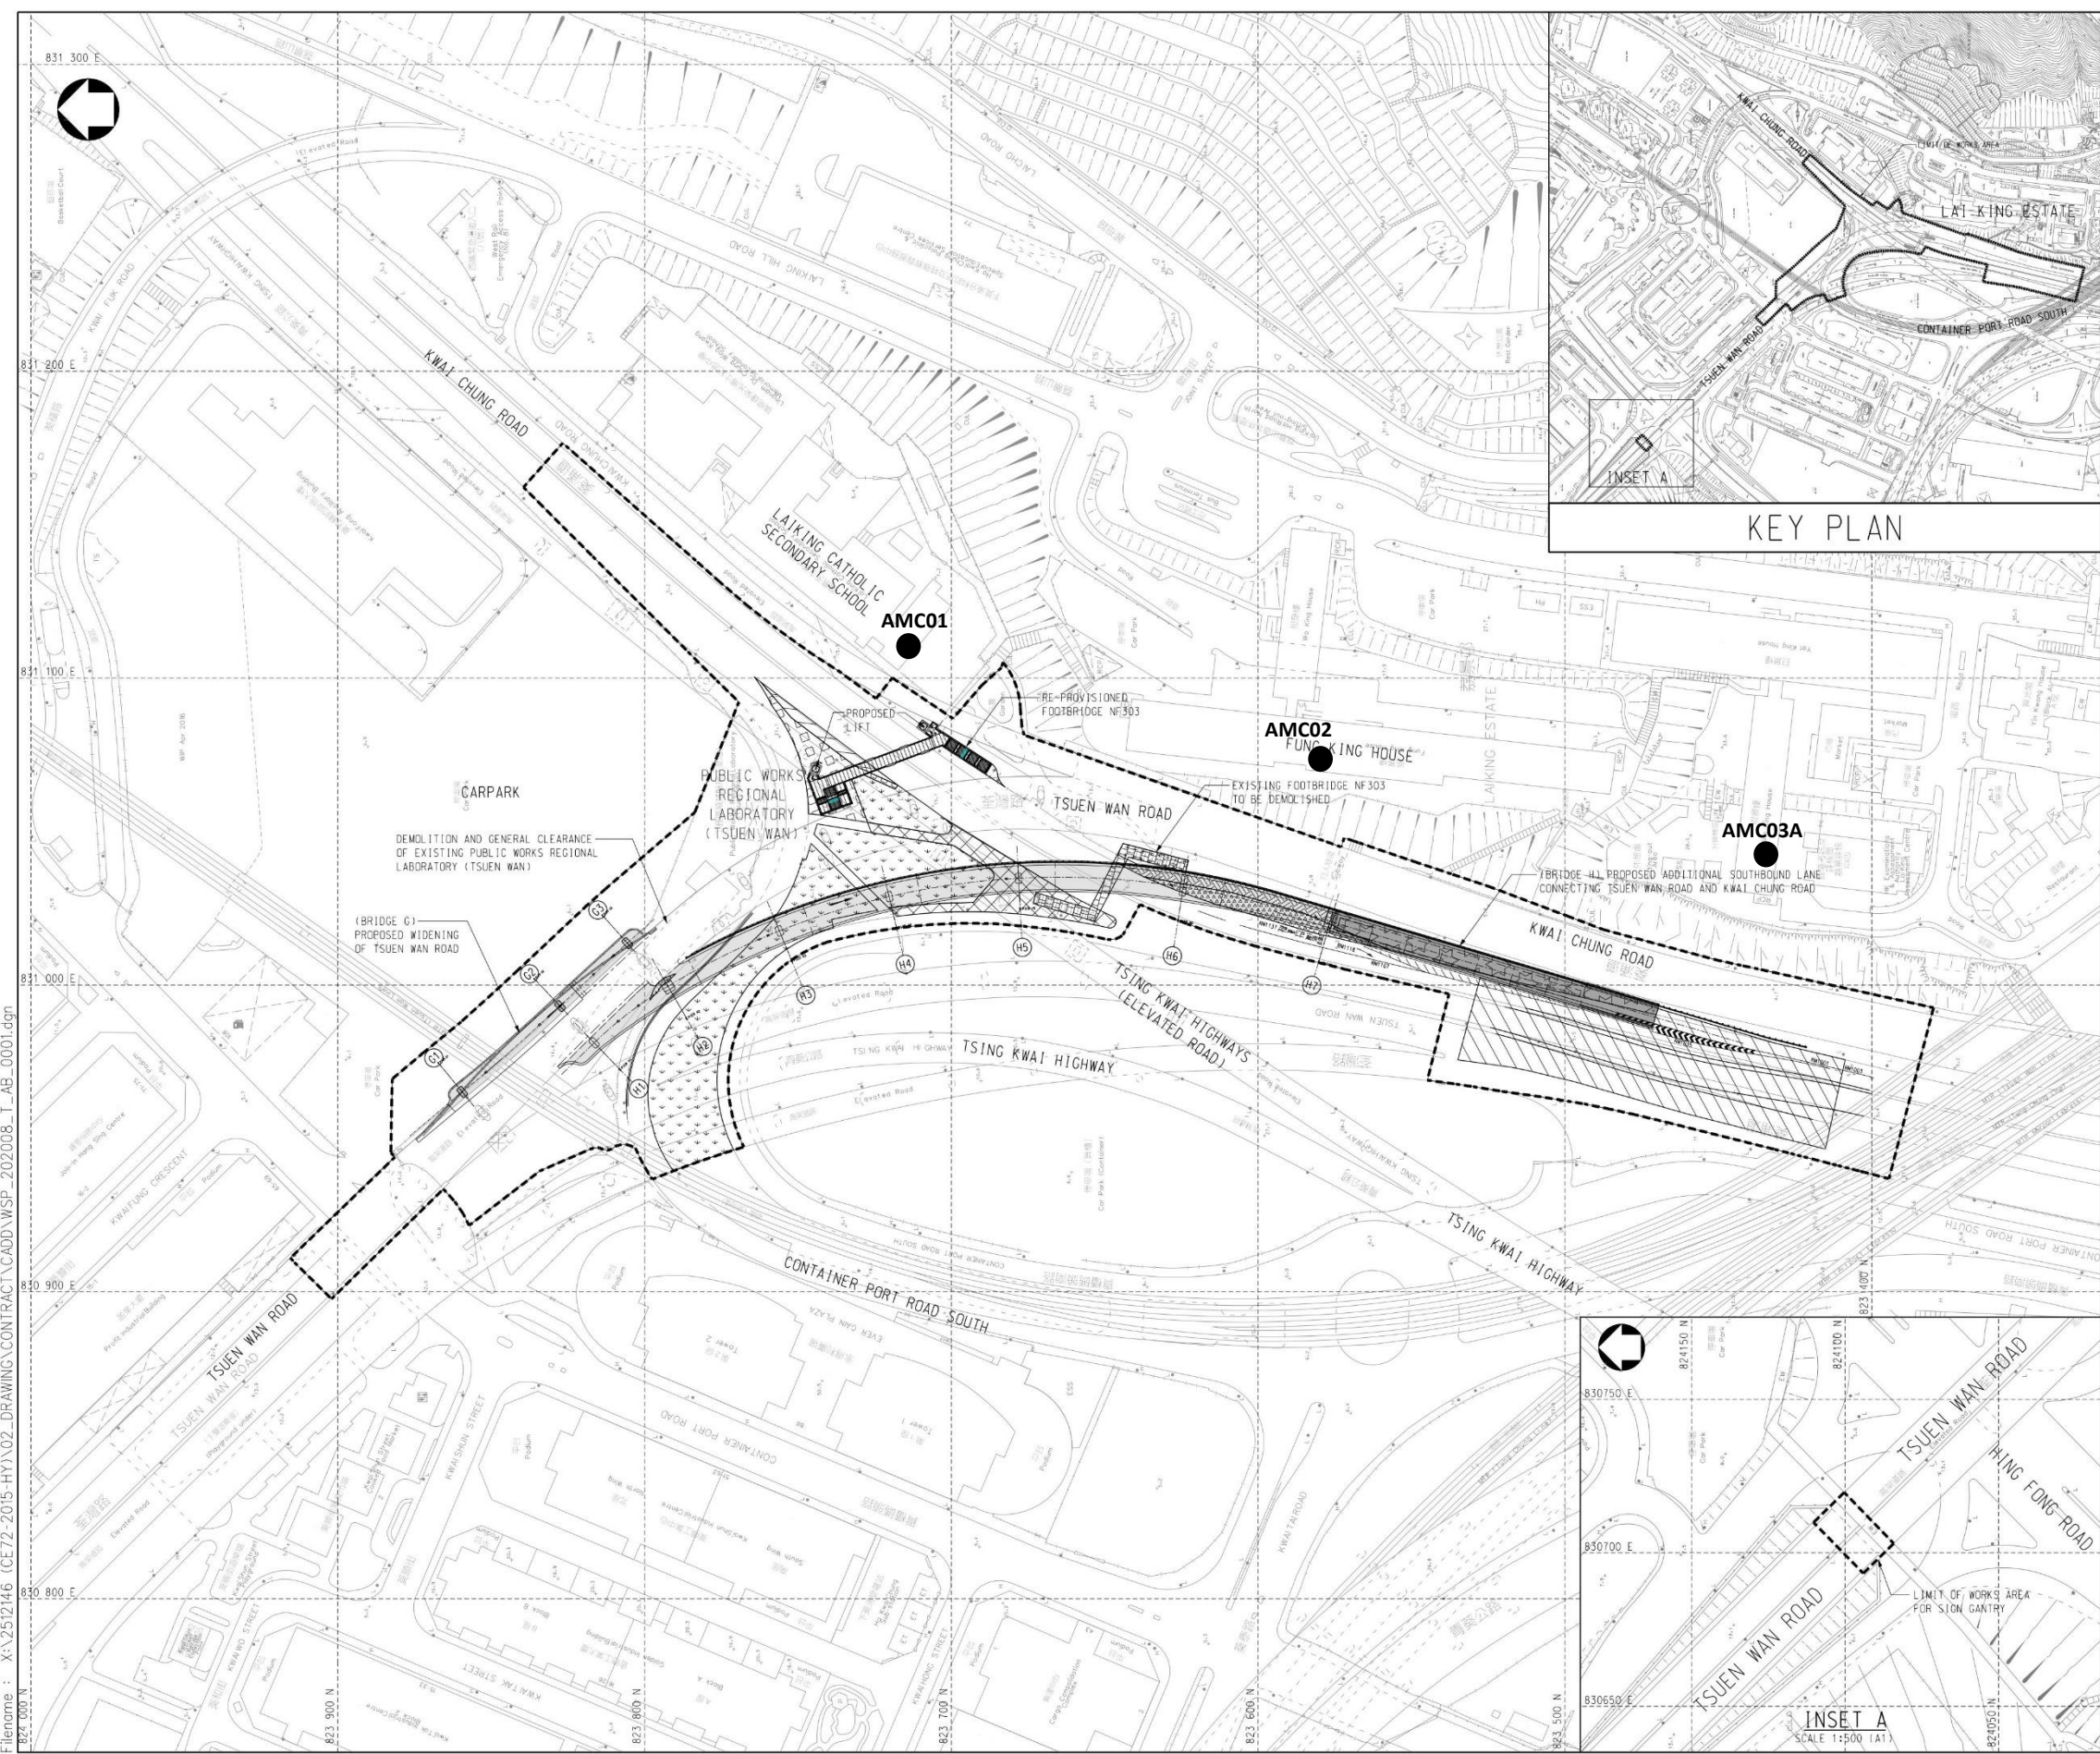

- NOTES :
1. ALL DIMENSIONS ARE IN METRES UNLESS OTHERWISE STATED.
  2. ALL LEVELS ARE APPROXIMATE VALUES AND IN METRES ABOVE HONG KONG PRINCIPAL DATUM.
  3. SECTIONS OF THE EXISTING CARRIAGEWAYS AND FOOTPATHS WITHIN THE LIMIT OF WORKS AREA MAY BE TEMPORARILY CLOSED IN PHASES AS AND WHEN REQUIRED.

- LEGEND :
- LIMIT OF WORK SITE
  - Air Monitoring Locations

Rev	Description	EW	01/21
-	ISSUE FOR TENDER	EW	01/21

Consultant  


Project title  
 CONTRACT NO. HY/2020/08  
 FLYOVER FROM KWAI TSING INTERCHANGE  
 UP-RAMP TO KWAI CHUNG ROAD

**Figure 4.2**  
**Location of Air Quality Monitoring Stations**

Scale 1:1000 (A1)	Status CONTRACT
© COPYRIGHT RESERVED	

 路政署  
 HIGHWAYS DEPARTMENT  
 工程師  
 WORKS DIVISION



## ***Appendix 3.1***

# ***Environmental Mitigation Implementation Schedule***



### Environmental Mitigation Implementation Schedule

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve	Status
<b>Air Quality Monitoring</b>							
S3.5.8	Dust suppression measures stipulated in the Air Pollution Control (Construction Dust) Regulation and good site practices:						
	<ul style="list-style-type: none"> <li>Every temporary access road shall be paved with concrete, bituminous materials, hardcores or metal plates, and kept clear of dusty materials; or sprayed with water or a dust suppression chemical.</li> </ul>	To minimize the dust impact	Contractor and Subcontractors	All works sites	Construction Phase	Air Pollution Control (Construction Dust) Regulation	*
	<ul style="list-style-type: none"> <li>Any stockpile of dusty materials shall be covered entirely by impervious sheeting, placed in an area sheltered on the top and the 3 sides, or sprayed with water or a dust suppression chemical.</li> </ul>						*
	<ul style="list-style-type: none"> <li>All dusty materials shall be sprayed with water or a dust suppression chemical immediately prior to any loading, unloading or transfer operation</li> </ul>						^
	<ul style="list-style-type: none"> <li>Vehicles used for transporting dusty materials should be covered with tarpaulin.</li> </ul>						N/A
	<ul style="list-style-type: none"> <li>Vehicle wheel washing facilities should be provided at each construction site exit.</li> </ul>						^
	<ul style="list-style-type: none"> <li>Where a vehicle leaving a construction site is carrying a load of dusty materials, the load shall be covered entirely by clean impervious sheeting.</li> </ul>						^

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures ?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve	Status
	<ul style="list-style-type: none"> <li>The speed of vehicles on unpaved road within the site should be controlled to about 10 km/hr.</li> </ul>						^
	<ul style="list-style-type: none"> <li>Routing of vehicles and positioning of construction plants should be arranged at maximum possible distances from the sensitive receivers.</li> </ul>						^
	<ul style="list-style-type: none"> <li>Every stock of more than 20 bags of cement and dry pulverized fuel ash (PFA) shall be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides.</li> </ul>						^
	<ul style="list-style-type: none"> <li>Loading, unloading, transfer, handling or storage of large amount of cement or dry PFA should be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with the an effective fabric filter or equivalent air pollution control system.</li> </ul>						N/A
	<ul style="list-style-type: none"> <li>Exposed earth shall be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shotcrete or other suitable surface stabilizer within 6 months after the last construction activity on the construction site or part of the construction site where the exposed earth lies.</li> </ul>						N/A

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures ?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve	Status
<b>Noise Monitoring</b>							
S4.8.1	<ul style="list-style-type: none"> <li>Selection and optimisation of construction programmes, avoidance of parallel operation of noisy PME, and/or reduction in the proportion of usage of PME during noise sensitive periods such as school examination period;</li> </ul>	To reduce potential construction noise impact	Contractor	All works sites	Construction Phase	EIAO-TM, NCO	^
	<ul style="list-style-type: none"> <li>Use of “quiet” PME and working methods;</li> </ul>						^
	<ul style="list-style-type: none"> <li>Use of temporary at-source noise mitigation measures such as noise barriers, acoustic fabric, noise enclosures, noise jacket and mufflers; and</li> </ul>						^
	<ul style="list-style-type: none"> <li>Use of good site practice to limit noise emission from construction site.</li> </ul>						^
S4.8.2	<b>Selection and Programming of Construction Processes</b>						
	<ul style="list-style-type: none"> <li>The timing and sequencing of the various construction activities shall be carefully arranged according to the actual site work situation, in order to limit the amount of concurrent activities and where applicable, to avoid parallel operation of noisy PME in order to minimize the total noise generated during construction periods.</li> </ul>	To reduce potential construction noise impact	Contractor	All works sites	Construction Phase	EIAO-TM, NCO	^
	<ul style="list-style-type: none"> <li>Limiting the quantity of PME to be operated concurrently and also their proportion of usage were recommended in the Project and incorporated in this assessment.</li> </ul>						^
<ul style="list-style-type: none"> <li>In the case during school examination when more stringent construction noise criteria should be imposed, the potentially most disruptive construction activities should be avoided, and arranged to be conducted during school holidays as far as practicable.</li> </ul>	^						

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures ?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve	Status
S4.8.3 – 4.8.5	Use of “Quiet” Alternative Plant and Working Methods						
	<ul style="list-style-type: none"> <li>The use of particular plant with equipment noise levels quieter than those specified in the GW-TM can result in reduction of noise levels generated by the plant. The level of noise reduction achieved is dependent on the Contractor’s chosen methods of working. It is possible for the Contractor to achieve noise reductions from the adopted working methodologies by specifying maximum limits of sound power level for specific plant.</li> </ul>	To reduce potential construction noise impact	Contractor	All works sites	Construction Phase	EIAO-TM, NCO	^
S4.8.6 – S4.8.9	Temporary Noise Barrier						
	<ul style="list-style-type: none"> <li>Use of Temporary Noise Barrier/ Acoustic Fabric for breaker, mini-robot mounted; excavator/loader, wheeled/tracked; lorry; lorry with crane/grab; mobile crane; poker vibratory, hand-held (electric); road roller; hand-held chain saw; concrete pump, lorry mounted; asphalt paver; air compressor. The minimum surface density of the movable noise barrier is 10kg/m<sup>2</sup>.</li> </ul>	To reduce potential construction noise impact	Contractor	All works sites	Construction Phase	EIAO-TM, NCO	^
<ul style="list-style-type: none"> <li>A not less than 8m high movable barrier with skid footing and a small cantilevered upper portion to be located within a few metres of the grab and chisel piling plants.</li> </ul>	N/A						
<ul style="list-style-type: none"> <li>When temporary noise barriers are not practicable or noise reduction achieved is insufficient, noise jacket/muffler can be applied to cover the noisy part of the engine or at the engine exhaust of particular mobile plants respectively.</li> </ul>	N/A						

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures ?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve	Status
S4.8.10	Good Site Practice:						
	<ul style="list-style-type: none"> <li>• Use of well-maintained and regularly-serviced plant during the works;</li> </ul>	To reduce potential construction noise impact	Contractor	All works sites	Construction Phase	EIAO-TM, NCO	^
	<ul style="list-style-type: none"> <li>• Plant operating on intermittent basis should be turned off or throttled down when not in active use;</li> </ul>						^
	<ul style="list-style-type: none"> <li>• Plant that is known to emit noise strongly in one direction should be orientated to face away from the NSRs;</li> </ul>						^
	<ul style="list-style-type: none"> <li>• Silencers, mufflers and enclosures for plant should be used where possible and maintained adequately throughout the works;</li> </ul>						N/A
	<ul style="list-style-type: none"> <li>• Where possible fixed plants should be sited away from NSRs; and</li> </ul>						^
<ul style="list-style-type: none"> <li>• Stockpiles of excavated materials and other structures such as site buildings should be used effectively to screen noise from the works.</li> </ul>	^						

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve	Status
<b>Water Quality Control</b>							
S5.9.2 S4.8.2	In accordance with ProPECC PN 1/94, construction phase mitigation measures with good management practices should include the following:						
	<ul style="list-style-type: none"> <li>At the establishment of works site, perimeter drains to direct off-site water around the Site should be constructed with internal drainage works and erosion and sedimentation control facilities implemented. Channels (both temporary and permanent drainage pipes and culverts), earth bunds or sand bag barriers should be provided to divert the stormwater to silt removal facilities. The design of the temporary onsite drainage system will be undertaken by the Contractor prior to the commencement of construction;</li> </ul>	To control water quality impact from construction site runoff	Contractor and Sub-contractors	All work sites	Construction Phase	Water Pollution Control Ordinance, ProPECC PN 1/94	^
	<ul style="list-style-type: none"> <li>Dikes or embankments for flood protection should be implemented around the boundaries of earthwork areas. Temporary ditches should be provided to facilitate the run-off discharge into an appropriate watercourse, through a silt/sediment trap. Silt/sediment traps should also be incorporated in the permanent drainage channels to enhance deposition rates;</li> </ul>						N/A
	<ul style="list-style-type: none"> <li>The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94, which states that the retention time for silt / sand traps should be 5 minutes under maximum flow conditions. A sedimentation basin would be required when necessary. The detailed design of the silt / sand traps should be undertaken by the Contractor prior to the commencement of construction;</li> </ul>						^
	<ul style="list-style-type: none"> <li>The construction works should be programmed to minimise surface excavation works during rainy seasons (April to September), as possible. All exposed earth areas should be</li> </ul>						^

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve	Status
	completed and vegetated as soon as possible after the earthworks have been completed. If excavation of soil cannot be avoided during the rainy season, or at any time of year when rainstorms are likely, exposed slope surfaces should be covered by tarpaulin or other means;						
	<ul style="list-style-type: none"> <li>The overall slope of works sites should be kept to a minimum to reduce the erosive potential of surface water flows, and all trafficked areas and access roads should be protected by coarse stone ballast. An additional advantage accruing from the use of crushed stone is the positive traction gained during the prolonged periods of inclement weather and the reduction of surface sheet flows;</li> </ul>						N/A
	<ul style="list-style-type: none"> <li>All drainage facilities and erosion and sediment control structures should be regularly inspected and maintained to ensure their proper and efficient operation at all times particularly following rainstorms. Deposited silts and grits should be removed regularly and disposed of by spreading evenly over stable, vegetated areas;</li> </ul>						^
	<ul style="list-style-type: none"> <li>Measures should be taken to minimise the ingress of site drainage into excavations. If the excavation of trenches in wet season is inevitable, they should be dug and backfilled in short sections wherever practicable. The water pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities;</li> </ul>						N/A
	<ul style="list-style-type: none"> <li>All open stockpiles of construction materials (for example, aggregates, sand and fill material) should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system;</li> </ul>						^

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve	Status
	<ul style="list-style-type: none"> <li>Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers;</li> </ul>						^
	<ul style="list-style-type: none"> <li>Precautions to be taken at any time of the year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecasted and during or after rainstorms, are summarised in Appendix A2 of ProPECC PN 1/94. Particular attention should be paid to the control of silty surface run-off during storm events;</li> </ul>						^
	<ul style="list-style-type: none"> <li>All vehicles and plant should be cleaned before leaving the Site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and sited wheel washing facilities / bay should be provided at the exit of the Site where practicable. Wash-water should have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel-washing bay to public roads should be paved with sufficient backfall toward the wheel washing bay to prevent vehicle tracking of soil and silty water to public roads and drains;</li> </ul>						*
	<ul style="list-style-type: none"> <li>Oil interceptors should be provided in the drainage system downstream of any oil / fuel pollution sources. Oil interceptors should be emptied and cleaned regularly to prevent the release of oil and grease into the storm water drainage system after accidental spillage. A bypass should be provided for oil interceptors to prevent flushing during heavy rain;</li> </ul>						N/A



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve	Status
	<ul style="list-style-type: none"> <li>The construction solid waste, debris and rubbish onsite should be collected, handled and disposed of properly to avoid causing any water quality impacts; and</li> </ul>						^
	<ul style="list-style-type: none"> <li>All fuel tanks and storage areas should be provided with locks and sited on sealed areas, within bunds with adequate storage capacity to prevent spilled fuel oils.</li> </ul>						^
S5.9.5	Control of effluent discharge						
	<ul style="list-style-type: none"> <li>A discharge licence for discharge of effluent from the construction site under the WPCO shall be applied to the EPD for. The discharge quality must meet the requirements specified in the discharge licence.</li> </ul>	To control the effluent discharge from the Site	Contractor and Sub-contractors	All work sites	Construction Phase	Water Pollution Control Ordinance	N/A
	<ul style="list-style-type: none"> <li>All the run-off and wastewater generated from the works areas should be treated so that it satisfies all the standards listed in the Technical Memorandum. Minimum distances of 100m should be maintained between the discharge points of construction site effluent and the existing seawater intakes.</li> </ul>						N/A
	<ul style="list-style-type: none"> <li>No new effluent discharges in nearby typhoon shelters should be allowed.</li> </ul>						N/A
	<ul style="list-style-type: none"> <li>The beneficial uses of the treated effluent for other on-site activities such as dust suppression, wheel washing and general cleaning etc., would minimize water consumption and reduce the effluent discharge volume.</li> </ul>						^
S5.9.6	Sewage from Workforce						
	<ul style="list-style-type: none"> <li>Portable chemical toilets and sewage holding tanks are recommended for the handling of the construction sewage generated by the workforce.</li> </ul>	To control Sewage	Contractor and Sub-workers	All work sites	Construction Phase	Water Pollution	^

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve	Status
	<ul style="list-style-type: none"> <li>A licensed Contractor should be employed to provide appropriate and adequate portable toilets and be responsible for appropriate disposal and maintenance.</li> </ul>	generated from onsite construction				Control Ordinance and Waste Disposal Ordinance	^
S5.9.7 – S5.9.8	Accidental Spillage of Chemicals						
	<ul style="list-style-type: none"> <li>The Contractor must register as a chemical waste producer if chemical wastes would be produced from the construction activities.</li> </ul>	To control accidental spillage of chemicals	Contractor and Sub-contractors	All work sites	Construction Phase	EIAO-TM, Water Pollution Control Ordinance and Waste Disposal (Chemical Waste) (General) Regulation	^
	<ul style="list-style-type: none"> <li>Any maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided.</li> </ul>						^
	<ul style="list-style-type: none"> <li>Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges.</li> </ul>						^
S5.9.9	Provision of surface runoff collection system						
	<ul style="list-style-type: none"> <li>All surface runoff on the road shall be direct to the system.</li> </ul>	To control road surface runoff	Contractor and Sub-contractors	Along Road Alignment	Design and Construction Phases	Water Pollution Control Ordinance	N/A
	<ul style="list-style-type: none"> <li>The capacity of the system should be properly designed to cater for all surface water.</li> </ul>						N/A

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve	Status
<b>Waste Management</b>							
S6.6.3	Waste Management Plan (WMP) should be prepared and submitted for approval by the Engineer prior to any construction activities. During the construction period the WMP should be used as a working document to detail the on-going management procedures and to record waste arising from construction works and import of fill throughout the Contract. The WMP shall be subject to audit under the requirements of the Environmental Monitoring and Audit (EM&A) Procedures set out in the EM&A Manual accompanying this EIA Report.	Preparation and approval of WMP	Contractor	All works sites	Design and Construction Phases	ETWB TC(W) No. 19/2005	^
S6.6.4 and S6.6.5	<p>The WMP shall be developed and implemented according to a best-practice philosophy of waste management. There are various waste management options, which can be categorised in terms of preference from an environmental viewpoint. The options considered to be more preferable have the least impacts and are more sustainable in a longterm context. The hierarchy is as follows:</p> <ul style="list-style-type: none"> <li>• Avoidance and minimisation, i.e. avoiding or not generating waste through changing or improving practices and design;</li> <li>• Reuse of materials, thus avoiding disposal (generally with only limited reprocessing);</li> <li>• Recovery and recycling, thus avoiding disposal (although reprocessing may be required);</li> <li>• Treatment and disposal, according to relevant laws, guidelines and good practice; and</li> <li>• The suitability (or otherwise) of material for reuse on site shall be detailed in the WMP. If, for any reason, the recommendations cannot be implemented, full justification should be given in the WMP for approval by the Engineer.</li> </ul>	To minimise waste generation	Contractor	All works sites	Design and Construction Phases	ETWB TC(W) No. 19/2005	^

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve	Status
S6.6.6	To facilitate adoption of the best-practice philosophy, training shall be provided to all personnel working on site. The training shall promote the concept of general site cleanliness and clearly explain the appropriate waste management procedures defined in the WMP.	To encourage all workers to reduce, reuse and recycle wastes.	Contractor	All works sites	Construction Phase	EIAO-TM	^
S6.6.7	a. During construction, the WMP should be kept up-to-date on a monthly basis with records of the actual quantities of wastes generated, recycled and disposed of off-site.	To keep trace of waste generation, minimisation, reuse and disposal	Contractor	All works sites	Construction Phase	ETWB TC(W) No. 19/2005	^
	b. Quantities shall be determined by weighing each load or other methods agreed to by the Engineer's Representative. Waste shall only be disposed of at licensed sites and the WMP should include procedures to ensure that illegal disposal of wastes does not occur.						^
	c. Only waste haulers authorised to collect the specific category of waste concerned should be employed and a trip ticket system shall be implemented for offsite disposal of inert C&D material and C&D waste at public fill reception facilities and landfills.						^
	d. Appropriate measures should be employed to minimise windblown litter and dust during transportation by either covering trucks or transporting wastes in enclosed containers.						^
S6.6.8	The WMP shall include plans indicating specific areas designated for the storage of particular types of waste, reusable and recyclable materials as well as areas and management proposals for any stockpiling areas. Generally, waste storage areas should be well maintained and cleaned regularly.	Work site(s):- a. Arrange and manage to facilitate the proper management of wastes and materials. b. Design to avoid cross	Contractor	All works sites	Design and Construction Phases	ETWB TC(W) No. 19/2005	^

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve	Status
		contamination of materials and pollution of the surrounding environment.					
S6.6.9	The design of formwork should maximise the use of standard wooden panels so that high reuse levels can be achieved. Alternatives such as steel formwork or plastic facing should be considered to increase the potential for reuse.	To maximise reuse of inert C&D Materials	Contractor	All works sites	Design and Construction Phases	ETWB TC(W) No. 19/2005	N/A
S6.6.10 and S6.6.11	a. Inert C&D materials should be segregated on site into different waste and material types. Where materials cannot be reused on site, opportunities for recycling materials off-site shall be explored.	To maximise reuse and facilitate recycling by segregating inert C&D Materials	Contractor	All works sites	Design and Construction Phases	ETWB TC(W) No. 19/2005	^
	b. Potential opportunities for recycling and reuse of inert C&D materials from the Project include:						
	<ul style="list-style-type: none"> <li>Milling wastes arising from regrading of the existing pavement could be recycled on site and reused as either road-base in the new carriageways or fill for new embankments;</li> </ul>						N/A
	<ul style="list-style-type: none"> <li>Existing marginal roadside barriers comprise pre-cast units, it may be possible to re-use these following widening works; and</li> <li>Existing bridge parapets comprise aluminium post and railings, these have a recyclable value and could be sold on for reconditioning or reused for scrap metal.</li> </ul>						N/A
S6.6.12	Any stockpile should be sited away from existing watercourses and suitably covered.	To prevent wind erosion and impacts on air and water quality	Contractor	All works sites	Design and Construction Phases	ETWB TC(W) No. 19/2005	N/A

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve	Status
S6.6.13	C&D waste which cannot be reused or recycled should be segregated and stored in different containers or skips from the inert C&D material and should be disposed of to landfill.	To facilitate disposal of C&D waste	Contractor	All works sites	Construction Phase	ETWB TC(W) No. 19/2005	^
S6.6.14	Workers should, when necessary, wear appropriate personal protective equipment (PPE) when handling contaminated sediments. Adequate washing and cleaning facilities should also be provided on site.	To minimise the exposure to contaminated materials	Contractor	All works sites when necessary	Construction Phase	Practice Guide, Guidance Note, Guidance Manual	N/A
S6.6.15 and S6.6.16	a. The marine sediment should be excavated, transported and processed properly.	To minimise any potential adverse impacts arising from the handling, treatment and reuse of the marine sediment	Contractor	All works sites	Design and Construction Phases	Practice Guide, Guidance Note, Guidance Manual	N/A
	b. Stockpiling of contaminated sediments should be avoided as far as possible.						N/A
	c. If temporary stockpiling of contaminated sediments is necessary, the excavated sediment should be covered by tarpaulin and the area should be placed within earth bunds or sand bags to prevent leachate from entering the ground, nearby drains and surrounding water bodies. The stockpiling areas should be completely paved or covered by linings in order to avoid contamination to underlying soil or groundwater. Separate and clearly defined areas should be provided for stockpiling of contaminated and uncontaminated materials.						N/A
	d. Leachate, if any, should be collected and discharged according to the WPCO.						N/A
	e. The approved Sediment Assessment Plan and Sediment Assessment Report with Remediation Plan shall be incorporated to the WMP.						N/A

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve	Status
S6.6.17	Chemical waste should be handled in accordance with the Code of Practice on the Packaging, Labelling and Storage of chemical Wastes as follows. Containers used for the storage of chemical wastes should:	To reduce environmental impacts in packaging, handling and storage of chemical wastes	Contractor	All works sites	Construction Phase	Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes	^
	<ul style="list-style-type: none"> <li>Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed;</li> </ul>						^
	<ul style="list-style-type: none"> <li>Have a capacity of less than 450L unless the specifications have been approved by the EPD; and</li> <li>Display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the Regulations.</li> </ul>						^
S6.6.18	The storage area for chemical wastes should:	To reduce environmental impacts by managing storage area for chemical wastes	Contractor	All works sites	Construction Phase	Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes	^
	<ul style="list-style-type: none"> <li>Be clearly labelled and used solely for the storage of chemical waste;</li> </ul>						^
	<ul style="list-style-type: none"> <li>Be enclosed on at least 3 sides;</li> </ul>						^
	<ul style="list-style-type: none"> <li>Have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest;</li> </ul>						^
	<ul style="list-style-type: none"> <li>Have adequate ventilation ;</li> </ul>						^
	<ul style="list-style-type: none"> <li>Be covered to prevent rainfall entering (water collected within the bund must be tested and disposed as chemical waste if necessary); and</li> <li>Be arranged so that incompatible materials are adequately separated.</li> </ul>						^
S6.6.19	The Contractor shall register with EPD as a Chemical Waste Producer. Waste oils and other chemical wastes as defined in the Waste Disposal (Chemical Waste) (General) Regulation will require disposal by appropriate means and could require pre-notification to EPD prior to disposal. Appropriate means include disposal:						

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve	Status
	<ul style="list-style-type: none"> <li>Be via a licensed waste collector; and</li> </ul>	To reduce environmental impacts in disposing chemical wastes.	Contractor	All works sites	Design and Construction Phases	Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes	^
	<ul style="list-style-type: none"> <li>Be to a facility licensed to receive chemical waste, such as the Chemical Waste Treatment Facility which also offers a chemical waste collection service and can supply the necessary storage containers</li> </ul>						^
S6.6.20 and S6.6.21	<p>a. General refuse generated on-site should be stored in enclosed bins or compaction units separate from construction and chemical wastes. A reputable waste collector should be employed by the Contractor to remove general refuse from the site, separately from construction and chemical wastes, on a daily or every second day basis to minimise odour, pest and litter impacts. The burning of refuse on construction sites is prohibited by law.</p> <p>b. General refuse is generated largely by food service activities on site, so reusable rather than disposable dishware should be used if feasible. Aluminum cans are often recovered from the waste stream by individual collectors if they are segregated or easily accessible. Therefore separate, labelled bins for their deposit should be provided if feasible.</p>	To reduce environmental impacts in handling general refuse.	Contractor	All works sites	Construction Phase	Waste Disposal Ordinance (Cap 354)	^
S6.6.22	Office waste can be reduced through recycling of paper if volumes are large enough to warrant collection. Opportunities for participation in a local collection scheme should be investigated.	To reduce office waste	Contractor	All works sites	Construction Phase	Waste Disposal Ordinance (Cap 354)	^



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve	Status
<b>Landscape and Visual</b>							
S7.9.6	Mitigation Planting: <ul style="list-style-type: none"> <li>Replanting of disturbed vegetation should be undertaken at the earliest possible stage of the construction phase of the project and this should use the recommended transplant trees identified in the Tree Removal Recommendation.</li> </ul>	To avoid potential damage to these identified transplant trees	Contractor	Identified locations for tree planting	Construction Phase	Follow the relevant guidelines in the ETWB TC(W) 10/2013; ETWB TC(W)2/2004; ETWB TC(W)29/2004 ; ETWB TC(W)7/2002; Tree Planting and Maintenance in HK, HKSAR 1991 Relevant sections of the latest version of General Specifications for Civil Engineering	* (Status of an unknown tree present near Lai King Catholic School EP boundary subject to ER follow-up with relevant govt. dept. on its way forward)

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve	Status
						Works, HKSAR	
S7.9.6	Development Site and Temporary Works Area						
	<ul style="list-style-type: none"> <li>The construction area and Contractor's temporary works area should be minimized to avoid impacts on adjacent landscape</li> </ul>	To minimize potential impacts on adjacent landscape and VSRs	Contractor	The project area where appropriate	Construction Phase	N/A	*
	<ul style="list-style-type: none"> <li>The landscape of these works areas will be restored following the completion of the construction phase</li> </ul>	To minimize potential impacts on the landscape	Contractor	The project area where appropriate	Construction Phase		N/A
	<ul style="list-style-type: none"> <li>Construction site controls shall be enforced, where possible, to ensure that the landscape and visual impacts arising from the construction phase activities are minimized including the storage of materials</li> </ul>	To minimize potential visual impacts on identified VSRs	Contractor	The project area where appropriate	Construction Phase		^
	<ul style="list-style-type: none"> <li>The location and appearance of site accommodation and the careful design of site lighting to prevent light spillage</li> </ul>	To minimize potential impacts on identified VSRs	Contractor	The project area where appropriate	Construction Phase		^
	<ul style="list-style-type: none"> <li>Screen hoarding may be a practicable for this project due to the viewing distances is short in a lot of site situation</li> </ul>	To minimize potential impacts on identified VSRs	Contractor	The project area where appropriate	Construction Phase		N/A

Remarks:

- ^ Implemented
- v Partially implemented
- \* To be followed-up by Contractor
- # Not Implemented
- N/A Not Applicable



## ***Appendix 4.1***

### ***Action and Limit Level***



**Action and Limit Levels**

**Air Quality Monitoring**

Monitoring Station	1-hour TSP Level in $\mu\text{g}/\text{m}^3$		24-hour TSP Level in $\mu\text{g}/\text{m}^3$	
	Action Level	Limit Level	Action Level	Limit Level
AMC01	256.2	500	144.8	260
AMC02	256.7	500	144.3	260
AMC03A	259.3	500	143.7	260

**Noise Monitoring**

Monitoring Station	Action Level	Limit Level (dB(A))		
		0700-1900 hrs on normal weekdays	0700-2300 hrs on holidays (including Sundays); and 1900-2300 hrs on all days <sup>2</sup>	2300-0700 hrs of all days
NMC01	When one documented complaint is received	65 / 70 <sup>1</sup>	60 / 65 / 70 <sup>3</sup>	45 / 50 / 55 <sup>3</sup>
NMC02		75		45 / 50 / 55 <sup>3</sup>
NMC03		65 / 70 <sup>1</sup>		45 / 50 / 55 <sup>3</sup>

Remark 1: Limit level of NMC01 and NMC03 reduce to 65 dB (A) during examination periods if any.


Remark 2: Construction noise during restricted hours is under the control of Noise Control Ordinance Limit Level to be selected based on Area Sensitivity Rating.

Remark 3: Limit Level for restricted hour monitoring shall act as reference level only. Investigation would be conducted on CNP compliance if exceedance recorded during restricted hour noise monitoring period.



## ***Appendix 4.2***

### ***Copies of Calibration Certificates***



## CERTIFICATE OF CALIBRATION

Certificate No.: 23CA1110 03 Page 1 of 2

### Item tested

Description:	Sound Level Meter (Type 1)	Microphone	Preamp
Manufacturer:	Larson Davis	PCB	PCB
Type/Model No.:	LxT1	377B02	PRMLxT1L
Serial/Equipment No.:	0004797	171529	028019
Adaptors used:	-	-	-

### Item submitted by

Customer Name: Lam Environmental Service Limited.  
Address of Customer: -  
Request No.: -  
Date of receipt: 10-Nov-2023

Date of test: 14-Nov-2023

### Reference equipment used in the calibration

Description:	Model:	Serial No.	Expiry Date:	Traceable to:
Multi function sound calibrator	B&K 4226	2288444	28-Aug-2024	CIGISMEC
Signal generator	DS 360	33873	31-Jan-2024	CEPREI

### Ambient conditions

Temperature:  $21 \pm 1$  °C  
Relative humidity:  $60 \pm 10$  %  
Air pressure:  $1010 \pm 5$  hPa

### Test specifications

- 1, The Sound Level Meter has been calibrated in accordance with the requirements as specified in BS 7580: Part 1: 1997 and the lab calibration procedure SMTP004-CA-152.
- 2, The electrical tests were performed using an electrical signal substituted for the microphone which was removed and replaced by an equivalent capacitance within a tolerance of  $\pm 20\%$ .
- 3, The acoustic calibration was performed using an B&K 4226 sound calibrator and corrections was applied for the difference between the free-field and pressure responsess of the Sound Level Meter.


### Test results

This is to certify that the Sound Level Meter conforms to BS 7580: Part 1: 1997 for the conditions under which the test was performed.

Details of the performed measurements are presented on page 2 of this certificate.

Actual Measurement data are documented on worksheets.

Approved Signatory:



Feng Junqi

Date: 15-Nov-2023

Company Chop:



Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument. The results apply to the item as received.



## CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.: 23CA1110 03 Page 2 of 2

### 1, Electrical Tests

The electrical tests were performed using an equivalent capacitance substituted for the microphone. The results are given in below with test status and the estimated uncertainties. The "Pass" means the result of the test is inside the tolerances stated in the test specifications. The "-" means the result of test is outside these tolerances.

Test:	Subtest:	Status:	Expanded Uncertainty (dB)	Coverage Factor
Self-generated noise	A	Pass	0.3	
	C	Pass	0.8	2.1
	Lin	Pass	1.6	2.2
Linearity range for Leq	At reference range , Step 5 dB at 4 kHz	Pass	0.3	
	Reference SPL on all other ranges	Pass	0.3	
	2 dB below upper limit of each range	Pass	0.3	
	2 dB above lower limit of each range	Pass	0.3	
Linearity range for SPL	At reference range , Step 5 dB at 4 kHz	Pass	0.3	
	Frequency weightings			
Time weightings	A	Pass	0.3	
	C	Pass	0.3	
	Lin	Pass	0.3	
Peak response	Single Burst Fast	Pass	0.3	
	Single Burst Slow	Pass	0.3	
R.M.S. accuracy	Single 100µs rectangular pulse	Pass	0.3	
Time weighting I	Crest factor of 3	Pass	0.3	
	Single burst 5 ms at 2000 Hz	Pass	0.3	
Time averaging	Repeated at frequency of 100 Hz	Pass	0.3	
	1 ms burst duty factor 1/10 <sup>3</sup> at 4kHz	Pass	0.3	
	1 ms burst duty factor 1/10 <sup>4</sup> at 4kHz	Pass	0.3	
Pulse range	Single burst 10 ms at 4 kHz	Pass	0.4	
Sound exposure level	Single burst 10 ms at 4 kHz	Pass	0.4	
Overload indication	SPL	Pass	0.3	
	Leq	Pass	0.4	

### 2, Acoustic tests

The complete sound level meter was calibrated on the reference range using a B&K 4226 acoustic calibrator with 1000Hz and SPL 94 dB. The sensitivity of the sound level meter was adjusted. The test result at 125 Hz and 8000 Hz are given in below with test status and the estimated uncertainties.

Test:	Subtest	Status	Expanded Uncertainty (dB)	Coverage Factor
Acoustic response	Weighting A at 125 Hz	Pass	0.3	
	Weighting A at 8000 Hz	Pass	0.5	

### 3, Response to associated sound calibrator

N/A

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.

- End -

Calibrated by:

Date:

Fung Chi Yip

14-Nov-2023

Checked by:

Date:

Chan Yuk Yiu

15-Nov-2023

The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.





## CERTIFICATE OF CALIBRATION

Certificate No.: 24CA0419 01-02

Page: 1 of 2

### Item tested

Description: Acoustical Calibrator (Class 1)  
Manufacturer: Honglim Co., Ltd.  
Type/Model No.: HLES-02  
Serial/Equipment No.: 2019612870  
Adaptors used: -

### Item submitted by

Customer: Lam Environmental Services Limited.  
Address of Customer: -  
Request No.: -  
Date of receipt: 19-Apr-2024

Date of test: 22-Apr-2024

### Reference equipment used in the calibration

Description:	Model:	Serial No.	Expiry Date:	Traceable to:
Lab standard microphone	B&K 4180	3257888	15-Aug-2024	SCL
Preamplifier	B&K 2673	3353200	13-Jun-2024	CEPREI
Measuring amplifier	B&K 2610	2346941	13-Jun-2024	CEPREI
Signal generator	DS 360	61227	28-Jun-2024	CEPREI
Digital multi-meter	34401A	US36087050	01-Jun-2024	CEPREI
Audio analyzer	8903B	GB41300350	13-Jun-2024	CEPREI
Universal counter	53132A	MY40003662	07-Jun-2024	CEPREI

### Ambient conditions

Temperature:  $22 \pm 1$  °C  
Relative humidity:  $55 \pm 10$  %  
Air pressure:  $1010 \pm 5$  hPa

### Test specifications


- 1, The Sound Calibrator has been calibrated in accordance with the requirements as specified in IEC 60942 1997 Annex B and the lab calibration procedure SMTP004-CA-156.
- 2, The calibrator was tested with its axis vertical facing downwards at the specific frequency using insert voltage technique.
- 3, The results are rounded to the nearest 0.01 dB and 0.1 Hz and have not been corrected for variations from a reference pressure of 1013.25 hectoPascals as the maker's information indicates that the instrument is insensitive to pressure changes.

### Test results

This is to certify that the sound calibrator conforms to the requirements of annex B of IEC 60942: 1997 for the conditions under which the test was performed. This does not imply that the sound calibrator meets IEC 60942 under any other conditions.

Details of the performed measurements are presented on **page 2** of this certificate.


Approved Signatory:



Feng Junqi

Date: 23-Apr-2024

Company Chop:



**Comments:** The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument. The results apply to the item as received.



## CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.: 24CA0419 01-02

Page: 2 of 2

### 1, Measured Sound Pressure Level

The output Sound Pressure Level in the calibrator head was measured at the setting and frequency shown using a calibrated laboratory standard microphone and insert voltage technique. The results are given in below with the estimated uncertainties.

Frequency Shown Hz	Output Sound Pressure Level Setting dB	Measured Output Sound Pressure Level dB	(Output level in dB re 20 $\mu$ Pa)
			Estimated Expanded Uncertainty dB
1000	94.00	94.12	0.10

### 2, Sound Pressure Level Stability - Short Term Fluctuations

The Short Term Fluctuations was determined by measuring the maximum and minimum of the fast weighted DC output of the B&K 2610 measuring amplifier over a 20 second time interval as required in the standard. The Short Term Fluctuation was found to be:

At 1000 Hz STF = 0.012 dB

Estimated expanded uncertainty 0.005 dB

### 3, Actual Output Frequency

The determination of actual output frequency was made using a B&K 4180 microphone together with a B&K 2673 preamplifier connected to a B&K 2610 measuring amplifier. The AC output of the B&K 2610 was taken to an universal counter which was used to determine the frequency averaged over 20 second of operation as required by the standard. The actual output frequency at 1 KHz was:

At 1000 Hz Actual Frequency = 998.7 Hz

Estimated expanded uncertainty 0.1 Hz Coverage factor k = 2.2

### 4, Total Noise and Distortion

For the Total Noise and Distortion measurement, the unfiltered AC output of the B&K 2610 measuring amplifier was connected to an Agilent Type 8903 B distortion analyser. The TND result at 1 KHz was:

At 1000 Hz TND = 1.0 %

Estimated expanded uncertainty 0.7 %

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.

- End -

Calibrated by:

Date:

Fung Chi Yip

22-Apr-2024

Checked by:

Date:

Chan Yuk Yiu

23-Apr-2024

The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.



## CERTIFICATE OF CALIBRATION

Certificate No.: 24CA0307 02-02

Page: 1 of 2

## Item tested

Description: Acoustical Calibrator (Class 1)  
Manufacturer: Larson Davis  
Type/Model No.: CAL200  
Serial/Equipment No.: 13098  
Adaptors used: -

## Item submitted by

Customer: Lam Environmental Services Limited.  
Address of Customer: -  
Request No.: -  
Date of receipt: 07-Mar-2024

Date of test: 11-Mar-2024

## Reference equipment used in the calibration

Description:	Model:	Serial No.	Expiry Date:	Traceable to:
Lab standard microphone	B&K 4180	3257888	15-Aug-2024	SCL
Preamplifier	B&K 2673	3353200	13-Jun-2024	CEPREI
Measuring amplifier	B&K 2610	2346941	13-Jun-2024	CEPREI
Signal generator	DS 360	61227	28-Jun-2024	CEPREI
Digital multi-meter	34401A	US36087050	01-Jun-2024	CEPREI
Audio analyzer	8903B	GB41300350	13-Jun-2024	CEPREI
Universal counter	53132A	MY40003662	07-Jun-2024	CEPREI

## Ambient conditions

Temperature:  $21 \pm 1$  °C  
Relative humidity:  $55 \pm 10$  %  
Air pressure:  $1010 \pm 5$  hPa

## Test specifications


- The Sound Calibrator has been calibrated in accordance with the requirements as specified in IEC 60942 1997 Annex B and the lab calibration procedure SMTP004-CA-156.
- The calibrator was tested with its axis vertical facing downwards at the specific frequency using insert voltage technique.
- The results are rounded to the nearest 0.01 dB and 0.1 Hz and have not been corrected for variations from a reference pressure of 1013.25 hectoPascals as the maker's information indicates that the instrument is insensitive to pressure changes.

## Test results

This is to certify that the sound calibrator conforms to the requirements of annex B of IEC 60942: 1997 for the conditions under which the test was performed. This does not imply that the sound calibrator meets IEC 60942 under any other conditions.


Details of the performed measurements are presented on page 2 of this certificate.

Approved Signatory:

  
Feng Junqi

Date: 12-Mar-2024

Company Chop:



Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument. The results apply to the item as received.



# CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.: 24CA0307 02-02

Page: 2 of 2

## 1, Measured Sound Pressure Level

The output Sound Pressure Level in the calibrator head was measured at the setting and frequency shown using a calibrated laboratory standard microphone and insert voltage technique. The results are given in below with the estimated uncertainties.

Frequency Shown Hz	Output Sound Pressure Level Setting dB	Measured Output Sound Pressure Level dB	(Output level in dB re 20 $\mu$ Pa)
			Estimated Expanded Uncertainty dB
1000	94.00	93.75	0.10

## 2, Sound Pressure Level Stability - Short Term Fluctuations

The Short Term Fluctuations was determined by measuring the maximum and minimum of the fast weighted DC output of the B&K 2610 measuring amplifier over a 20 second time interval as required in the standard. The Short Term Fluctuation was found to be:

At 1000 Hz **STF = 0.007 dB**

Estimated expanded uncertainty 0.005 dB

## 3, Actual Output Frequency

The determination of actual output frequency was made using a B&K 4180 microphone together with a B&K 2673 preamplifier connected to a B&K 2610 measuring amplifier. The AC output of the B&K 2610 was taken to an universal counter which was used to determine the frequency averaged over 20 second of operation as required by the standard. The actual output frequency at 1 KHz was:

At 1000 Hz **Actual Frequency = 999.9 Hz**

Estimated expanded uncertainty 0.1 Hz Coverage factor k = 2.2

## 4, Total Noise and Distortion

For the Total Noise and Distortion measurement, the unfiltered AC output of the B&K 2610 measuring amplifier was connected to an Agilent Type 8903 B distortion analyser. The TND result at 1 KHz was:

At 1000 Hz **TND = 1.0 %**

Estimated expanded uncertainty 0.7 %

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.

- End -

Calibrated by:

Date:

Fung Chi Yip  
11-Mar-2024

Checked by:

Date:

Chan Yuk Yiu  
12-Mar-2024

The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.

<b>RECALIBRATION DUE DATE: March 18, 2025</b>
---

# Certificate of Calibration

Calibration Certification Information			
Cal. Date: March 18, 2024	Rootsmeter S/N: 438320	Ta: 295	°K
Operator: Jim Tisch		Pa: 747.8	mm Hg
Calibration Model #: TE-5025A	Calibrator S/N: <b>3166</b>		

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.4220	3.2	2.00
2	3	4	1	1.0170	6.4	4.00
3	5	6	1	0.9100	8.0	5.00
4	7	8	1	0.8690	8.9	5.50
5	9	10	1	0.7170	12.8	8.00

Data Tabulation					
Vstd (m3)	Qstd (x-axis)	$\sqrt{\Delta H \left( \frac{Pa}{Pstd} \right) \left( \frac{Tstd}{Ta} \right)}$ (y-axis)	Va	Qa (x-axis)	$\sqrt{\Delta H \left( Ta/Pa \right)}$ (y-axis)
0.9897	0.6960	1.4099	0.9957	0.7002	0.8883
0.9854	0.9689	1.9939	0.9914	0.9749	1.2562
0.9833	1.0805	2.2293	0.9893	1.0871	1.4045
0.9821	1.1301	2.3381	0.9881	1.1371	1.4730
0.9769	1.3625	2.8198	0.9829	1.3708	1.7765
<b>QSTD</b>	m=	<b>2.11734</b>	<b>QA</b>	m=	<b>1.32584</b>
	b=	<b>-0.05997</b>		b=	<b>-0.03778</b>
	r=	<b>0.99997</b>		r=	<b>0.99997</b>

Calculations	
Vstd= $\Delta Vol \left( \frac{Pa - \Delta P}{Pstd} \right) \left( \frac{Tstd}{Ta} \right)$	Va= $\Delta Vol \left( \frac{Pa - \Delta P}{Pa} \right)$
Qstd= $Vstd / \Delta Time$	Qa= $Va / \Delta Time$
For subsequent flow rate calculations:	
Qstd= $1/m \left( \left( \sqrt{\Delta H \left( \frac{Pa}{Pstd} \right) \left( \frac{Tstd}{Ta} \right)} \right) - b \right)$	Qa= $1/m \left( \left( \sqrt{\Delta H \left( Ta/Pa \right)} \right) - b \right)$

Standard Conditions	
Tstd:	298.15 °K
Pstd:	760 mm Hg
Key	
ΔH: calibrator manometer reading (in H2O)	
ΔP: rootsmeter manometer reading (mm Hg)	
Ta: actual absolute temperature (°K)	
Pa: actual barometric pressure (mm Hg)	
b: intercept	
m: slope	

RECALIBRATION
US EPA recommends annual recalibration per 1998 40 Code of Federal Regulations Part 50 to 51, Appendix B to Part 50, Reference Method for the Determination of Suspended Particulate Matter in the Atmosphere, 9.2.17, page 30



Lam Environmental Services Limited

**Calibration Data for High Volume Sampler (TSP Sampler)**

Location : AMC01 Calibration Date : 5-Jun-24  
 Equipment no. : 0200-0740 Calibration Due Date : 5-Aug-24

**CALIBRATION OF CONTINUOUS FLOW RECORDER**

Ambient Condition			
Temperature, T <sub>a</sub>	297.4	Kelvin	Pressure, P <sub>a</sub>
			1010 mmHg

Orifice Transfer Standard Information					
Equipment No.	3880	Slope, m <sub>c</sub>	1.30677	Intercept, b <sub>c</sub>	-0.01341
Last Calibration Date	26-Feb-24	$(H \times P_a / 1013.3 \times 298 / T_a)^{1/2}$ $= m_c \times Q_{std} + b_c$			
Next Calibration Date	26-Feb-25				

Calibration of TSP						
Calibration Point	Manometer Reading			Q <sub>std</sub> (m <sup>3</sup> / min.) X-axis	Continuous Flow Recorder, W (CFM)	IC (W(P <sub>a</sub> /1013.3x298/T <sub>a</sub> ) <sup>1/2</sup> /35.31) Y-axis
	(up)	(down)	(difference)			
1	1.4	1.4	2.8	1.2901	30	29.9843
2	2.3	2.3	4.6	1.6507	36	35.9811
3	3.5	3.5	7.0	2.0339	46	45.9759
4	4.4	4.4	8.8	2.2792	50	49.9738
5	5.6	5.6	11.2	2.5699	56	55.9706

By Linear Regression of Y on X

Slope, m = 23.3810 Intercept, b = 6.1521  
 Correlation Coefficient\* = 0.9974  
 Calibration Accepted = Yes/No\*\*

\* if Correlation Coefficient &lt; 0.990, check and recalibration again.

\*\* Delete as appropriate.

Remarks : Serial No.:0200-0740

Calibrated by : Harry Po Checked by : Alan Ng  
 Date : 5-Jun-24 Date : 5-Jun-24



Lam Environmental Services Limited

**Calibration Data for High Volume Sampler (TSP Sampler)**

Location : AMC02  
 Equipment no. : 2650

Calibration Date : 5-Jun-24  
 Calibration Due Date : 5-Aug-24

**CALIBRATION OF CONTINUOUS FLOW RECORDER**

Ambient Condition			
Temperature, Ta	297.4	Kelvin	Pressure, Pa
			1010 mmHg

Orifice Transfer Standard Information					
Equipment No.	3880	Slope, m <sub>c</sub>	1.30677	Intercept, b <sub>c</sub>	-0.01341
Last Calibration Date	26-Feb-24	$(H \times P_a / 1013.3 \times 298 / T_a)^{1/2}$ $= m_c \times Q_{std} + b_c$			
Next Calibration Date	26-Feb-25				

Calibration of TSP						
Calibration Point	Manometer Reading			Q <sub>std</sub> (m <sup>3</sup> / min.) X-axis	Continuous Flow Recorder, W (CFM)	IC (W(P <sub>a</sub> /1013.3x298/T <sub>a</sub> ) <sup>1/2</sup> /35.31) Y-axis
	(up)	(down)	(difference)			
1	1.2	1.2	2.4	1.1952	20	19.9895
2	2.3	2.3	4.6	1.6507	30	29.9843
3	3.4	3.4	6.8	2.0047	40	39.9790
4	4.1	4.1	8.2	2.2004	46	45.9759
5	5.3	5.3	10.6	2.5004	52	51.9727

By Linear Regression of Y on X

Slope, m = 23.3810      Intercept, b = 6.1521  
 Correlation Coefficient\* = 0.9979  
 Calibration Accepted = Yes/No\*\*

\* if Correlation Coefficient &lt; 0.990, check and recalibration again.

\*\* Delete as appropriate.

Remarks : Serial No.:2650

Calibrated by : Harry Po  
 Date : 5-Jun-24

Checked by : Alan Ng  
 Date : 5-Jun-24



Lam Environmental Services Limited

**Calibration Data for High Volume Sampler (TSP Sampler)**

Location : AMC03A  
 Equipment no. : 2649

Calibration Date : 5-Jun-24  
 Calibration Due Date : 5-Aug-24

**CALIBRATION OF CONTINUOUS FLOW RECORDER**

Ambient Condition			
Temperature, T <sub>a</sub>	297.4	Kelvin	Pressure, P <sub>a</sub>
			1010 mmHg

Orifice Transfer Standard Information					
Equipment No.	3880	Slope, m <sub>c</sub>	1.30677	Intercept, b <sub>c</sub>	-0.01341
Last Calibration Date	26-Feb-24	$(H \times P_a / 1013.3 \times 298 / T_a)^{1/2}$ $= m_c \times Q_{std} + b_c$			
Next Calibration Date	26-Feb-25				

Calibration of TSP						
Calibration Point	Manometer Reading			Q <sub>std</sub> (m <sup>3</sup> / min.) X-axis	Continuous Flow Recorder, W (CFM)	IC (W(P <sub>a</sub> /1013.3x298/T <sub>a</sub> ) <sup>1/2</sup> /35.31) Y-axis
	(up)	(down)	(difference)			
1	1.6	1.6	3.2	1.3785	22	21.9885
2	2.5	2.5	5.0	1.7205	30	29.9843
3	3.3	3.3	6.6	1.9752	36	35.9811
4	4.3	4.3	8.6	2.2532	42	41.9780
5	5.4	5.4	10.8	2.5238	50	49.9738

By Linear Regression of Y on X

Slope, m = 23.3810      Intercept, b = 6.1521  
 Correlation Coefficient\* = 0.9987  
 Calibration Accepted = Yes/No\*\*

\* if Correlation Coefficient &lt; 0.990, check and recalibration again.

\*\* Delete as appropriate.

Remarks : Serial No.:2649

Calibrated by : Harry Po  
 Date : 5-Jun-24

Checked by : Alan Ng  
 Date : 5-Jun-24





# Calibration Certificate

Certificate No. 402819

Page 1 of 2 Pages

**Customer :** Lam Environmental Services Limited

**Address :** 19/F, Remex Centre, 42 Wong Chuk Hang Road, Hong Kong

**Order No. :** Q41168

**Date of receipt :** 5-Apr-24

## Item Tested

**Description :** Particulate Monitor

**Manufacturer :** Met One

**I.D. :** --

**Model :** BT-645

**Serial No. :** B17940

## Test Conditions

**Date of Test :** 15-Apr-24

**Supply Voltage :** --

**Ambient Temperature :** (23 ± 3)°C

**Relative Humidity :** (50 ± 25) %

## Test Specifications

Calibration check.

Calibration procedure : Manufacturer recommended method (gravimetric), Z28.

## Test Results

All results were within the tolerance(s).

The results are shown in the attached page(s).

Main Test equipment used:

<u>Equipment No.</u>	<u>Description</u>	<u>Cert. No.</u>	<u>Traceable to</u>
S136A	Stop Watch	402292	SCL-HKSAR
S238	Micro Balance	108228	NIM-PRC
S201	Std. Test Dust	61291	NIST
S207B	Std. Flowmeter	LL-2104002489	NIM-PRC

The values given in this Calibration Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Hong Kong Calibration Ltd. shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to International System of Units (SI), or by reference to a natural constant. The test results apply to the above Unit-Under-Test only

**Calibrated by :**   
Kin Wong

**Approved by :**   
Steve Kwan

**Date:** 15-Apr-24



# Calibration Certificate

Certificate No. 402819

Page 2 of 2 Pages

Results :

## 1. General

Internal Filters : checked and found clean.

## 2. Timer

Reference Value	UUT Reading	Tolerance	Uncertainty
10' 00" 72	10 min	± 0.5 sec/min	± 0.2 sec/min

## 3. Dust Particle (TSP)

Applied Value ( $\mu\text{g}/\text{m}^3$ )	UUT Reading ( $\mu\text{g}/\text{m}^3$ ) K Factor : 2.0	Tolerance	Uncertainty
880	877	± 20 %	± 10 %

- Remark :
1. UUT: Unit-Under-Test
  2. The uncertainty claimed is for a confidence probability of not less than 95%.
  3. ISO 12103-1 A1 respirable standard test dust was used for the calibration.
  4. The K Factor had been adjusted from 1.0 to 2.0

----- END -----



# Calibration Certificate

Certificate No. **402818**

Page 1 of 2 Pages

**Customer :** Lam Environmental Services Limited

**Address :** 19/F, Remex Centre, 42 Wong Chuk Hang Road, Hong Kong

**Order No. :** Q41168

**Date of receipt :** 5-Apr-24

## Item Tested

**Description :** Particulate Monitor

**Manufacturer :** Met One

**I.D. :** --

**Model :** BT-645

**Serial No. :** X19298

## Test Conditions

**Date of Test :** 15-Apr-24

**Supply Voltage :** --

**Ambient Temperature :** (23 ± 3)°C

**Relative Humidity :** (50 ± 25) %

## Test Specifications

Calibration check.

Calibration procedure : Manufacturer recommended method (gravimetric), Z28.

## Test Results

All results were within the tolerance(s).

The results are shown in the attached page(s).

Main Test equipment used:

<u>Equipment No.</u>	<u>Description</u>	<u>Cert. No.</u>	<u>Traceable to</u>
S136A	Stop Watch	402292	SCL-HKSAR
S238	Micro Balance	108228	NIM-PRC
S201	Std. Test Dust	61291	NIST
S207B	Std. Flowmeter	LL-2104002489	NIM-PRC

The values given in this Calibration Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Hong Kong Calibration Ltd. shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to International System of Units (SI), or by reference to a natural constant. The test results apply to the above Unit-Under-Test only

Calibrated by :   
Kin Wong

Approved by :   
Steve Kwan

This Certificate is issued by  
Hong Kong Calibration Ltd

Unit 8B, 24/F., Well Fung Industrial Centre, No. 58-76, Ta Chuen Ping Street, Kwai Chung, NT, Hong Kong  
Tel 2425 8901 Fax 2425 8646

Date: 15-Apr-24



# Calibration Certificate

Certificate No. 402818

Page 2 of 2 Pages

Results :

## 1. General

Internal Filters : checked and found clean.

## 2. Timer

Reference Value	UUT Reading	Tolerance	Uncertainty
10' 00" 08	10 min	± 0.5 sec/min	± 0.2 sec/min

## 3. Dust Particle (TSP)

Applied Value ( $\mu\text{g}/\text{m}^3$ )	UUT Reading ( $\mu\text{g}/\text{m}^3$ ) K Factor : 1.1	Tolerance	Uncertainty
370	383	± 20 %	± 10 %

- Remark :
1. UUT: Unit-Under-Test
  2. The uncertainty claimed is for a confidence probability of not less than 95%.
  3. ISO 12103-1 A1 respirable standard test dust was used for the calibration.
  4. The K Factor had been adjusted from 1.0 to 1.1

----- END -----



Portable Dust Meter Performance Check Record

Portable Dust Meter

Type : Particulate Monitor
Manufacturer : MET ONE INSTRUMENTS
Model Number : BT-645
Serial Number : X19297
Performance Check Date : 18-Aug-23

Standard Equipment

Type : High Volume Sampler
Manufacturer : TISCH
Model Number : TE-5170
Equipment Number : 2493
Last Calibration Date : 25-May-23


Portable Dust Meter Performance Check Results

Table with 6 columns: Trial no. in 1-hr period, Time, Mean Pressure (hPa), Mean Temp (°C), Concentration in ug/m³ (Standard equipment) (Y - Axis), Concentration in ug/m³ (Performance Check / Calibrated equipment) (X - Axis). Rows 1-3 show data for 18/8/23 at 13:00, 14:02, and 15:03.

\* Filter paper weighting was conducted by HOKLAS accredited laboratory.

Linear Regression of Y on X

Slope (K- factor) : 1.6000
Correlation Coefficient : 0.9887
Validity of Performance Check / Calibration Record : 17/8/2024

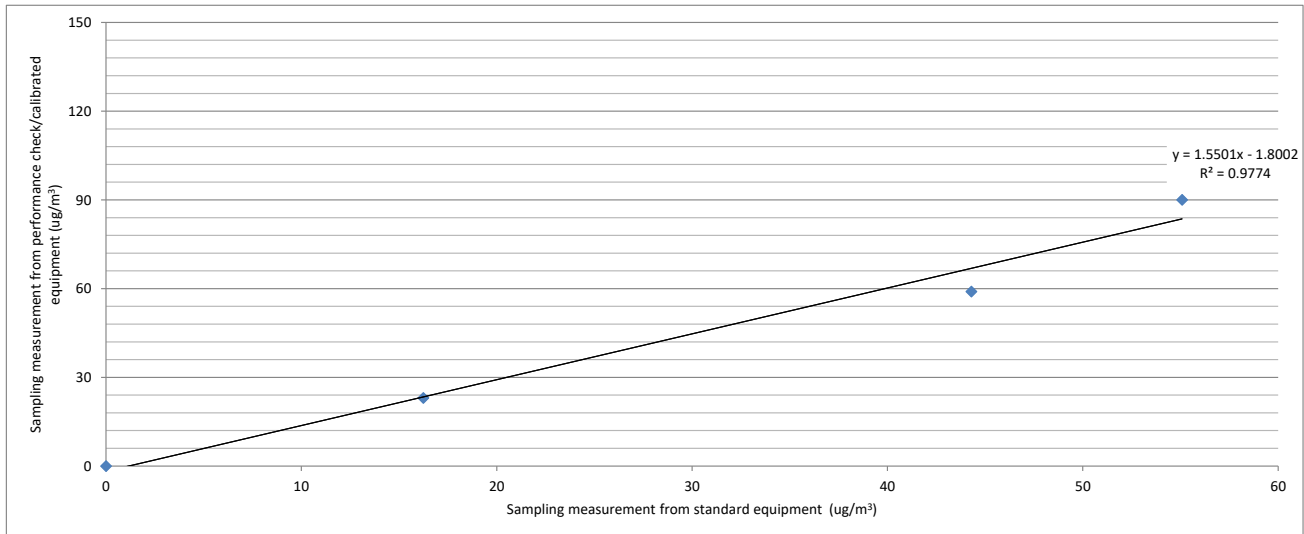

Operator: Alan Ng

Date: 21/8/2023

Checked by: Derek Lo

Date: 21/8/2023



**Wind Station Performance Check Record**

Type : Weather Station

Manufacturer : 武汉辰云科技有限公司

Model Number : YGY-FSXY12

Serial Number : 21091630T0944

Performance Check Date : 9-May-2024

**Performance Check Results**

Wind Speed Range (m/s)	Reading Value (V1, m/s)	Anemometer Value (V2, m/s)	Difference (V1 - V2, m/s)
Zero Check	0.0	0.0	0.0
1 - 2	1.9	1.9	0.0
3 - 5	3.6	3.5	0.1
6 - 7	6.5	6.7	-0.2
8 - 9	8.2	8.2	0.0

Wind Direction (°)	Reading Value (W1, °)	Compass Value (W2, °)	Difference (W1 - W2, °)
0	0	0	0
90	93	90	3
180	179	180	-1
270	269	270	-1

Test Reference:

1. Wind Speed Check - Speed reading checked on-site against anemometer logged value.
2. Wind Direction Check - Direction reading checked on on-site against logged value.

Conducted by: William Cheung

Checked by: Derek Lo



## ***Appendix 4.3***

### ***Wind Data***



**Wind Speed and Wind Direction**

Date	Time	Wind Speed (m/s)	Wind Direction (degree)
1-Jul-24	0:00	0.7(1)	285(WNW)
	1:00	0.5(1)	132(SE)
	2:00	0.0(0)	219(SW)
	3:00	0.5(1)	105(ESE)
	4:00	3.1(2)	179(S)
	5:00	0.0(0)	161(SSE)
	6:00	0.0(0)	162(SSE)
	7:00	0.0(0)	118(ESE)
	8:00	1.3(1)	167(SSE)
	9:00	0.0(0)	236(SW)
	10:00	2.1(2)	163(SSE)
	11:00	1.5(1)	246(WSW)
	12:00	1.9(2)	149(SSE)
	13:00	1.5(1)	116(ESE)
	14:00	1.9(2)	50(NE)
	15:00	3.1(2)	246(WSW)
	16:00	0.7(1)	85(E)
	17:00	1.5(1)	221(SW)
	18:00	2.5(2)	230(SW)
	19:00	0.0(0)	95(E)
	20:00	0.0(0)	65(ENE)
	21:00	0.5(1)	106(ESE)
	22:00	0.0(0)	176(S)
23:00	0.0(0)	51(NE)	
2-Jul-24	0:00	1.3(1)	301(WNW)
	1:00	1.3(1)	141(SE)
	2:00	1.1(1)	76(ENE)
	3:00	0.9(1)	207(SSW)
	4:00	1.3(1)	155(SSE)
	5:00	0.7(1)	210(SSW)
	6:00	0.0(0)	177(S)
	7:00	0.0(0)	145(SE)
	8:00	1.3(1)	157(SSE)
	9:00	2.7(2)	166(SSE)
	10:00	1.5(1)	157(SSE)
	11:00	0.9(1)	177(S)
	12:00	2.3(2)	172(S)
	13:00	1.7(2)	66(ENE)
	14:00	1.3(1)	84(E)
	15:00	1.9(2)	88(E)
	16:00	1.3(1)	45(NE)
	17:00	0.5(1)	27(NNE)
	18:00	2.5(2)	191(S)
	19:00	0.0(0)	56(NE)
	20:00	0.0(0)	126(SE)
	21:00	0.0(0)	234(SW)
	22:00	0.0(0)	191(S)
23:00	0.9(1)	163(SSE)	





## Wind Speed and Wind Direction

Date	Time	Wind Speed (m/s)	Wind Direction (degree)
3-Jul-24	0:00	0.0(0)	66(ENE)
	1:00	0.0(0)	176(S)
	2:00	0.0(0)	191(S)
	3:00	0.0(0)	142(SE)
	4:00	0.0(0)	100(E)
	5:00	0.0(0)	117(ESE)
	6:00	0.0(0)	230(SW)
	7:00	0.0(0)	187(S)
	8:00	0.0(0)	202(SSW)
	9:00	0.0(0)	219(SW)
	10:00	1.1(1)	165(SSE)
	11:00	0.0(0)	11(N)
	12:00	2.7(2)	107(ESE)
	13:00	1.5(1)	189(S)
	14:00	1.5(1)	120(ESE)
	15:00	1.1(1)	180(S)
	16:00	0.5(1)	232(SW)
	17:00	1.3(1)	273(W)
	18:00	0.0(0)	161(SSE)
	19:00	1.1(1)	276(W)
	20:00	1.5(1)	266(W)
	21:00	0.0(0)	181(S)
	22:00	0.0(0)	212(SSW)
23:00	0.5(1)	182(S)	
4-Jul-24	0:00	0.0(0)	83(E)
	1:00	0.0(0)	37(NE)
	2:00	0.0(0)	146(SE)
	3:00	0.0(0)	114(ESE)
	4:00	0.0(0)	219(SW)
	5:00	0.0(0)	174(S)
	6:00	0.0(0)	293(WNW)
	7:00	0.0(0)	207(SSW)
	8:00	0.0(0)	127(SE)
	9:00	0.0(0)	110(ESE)
	10:00	0.0(0)	146(SE)
	11:00	0.0(0)	342(NNW)
	12:00	0.0(0)	237(WSW)
	13:00	0.0(0)	25(NNE)
	14:00	0.0(0)	25(NNE)
	15:00	1.1(1)	130(SE)
	16:00	1.1(1)	119(ESE)
	17:00	0.0(0)	121(ESE)
	18:00	2.1(2)	70(ENE)
	19:00	2.3(2)	93(E)
	20:00	0.0(0)	198(SSW)
	21:00	0.7(1)	13(NNE)
	22:00	0.0(0)	97(E)
23:00	0.0(0)	163(SSE)	



## Wind Speed and Wind Direction

Date	Time	Wind Speed (m/s)	Wind Direction (degree)
5-Jul-24	0:00	0.0(0)	241(WSW)
	1:00	0.0(0)	225(SW)
	2:00	0.0(0)	292(WNW)
	3:00	0.0(0)	159(SSE)
	4:00	0.0(0)	263(W)
	5:00	0.0(0)	196(SSW)
	6:00	0.0(0)	212(SSW)
	7:00	0.0(0)	172(S)
	8:00	0.0(0)	144(SE)
	9:00	0.0(0)	177(S)
	10:00	0.9(1)	33(NNE)
	11:00	1.3(1)	126(SE)
	12:00	1.7(2)	158(SSE)
	13:00	1.5(1)	94(E)
	14:00	0.9(1)	145(SE)
	15:00	1.7(2)	144(SE)
	16:00	1.1(1)	330(NNW)
	17:00	0.5(1)	67(ENE)
	18:00	1.3(1)	197(SSW)
	19:00	0.0(0)	114(ESE)
	20:00	0.0(0)	195(SSW)
	21:00	0.0(0)	101(E)
	22:00	0.0(0)	269(W)
23:00	0.0(0)	260(W)	
6-Jul-24	0:00	0.0(0)	158(SSE)
	1:00	0.0(0)	68(ENE)
	2:00	0.0(0)	184(S)
	3:00	0.0(0)	74(ENE)
	4:00	0.0(0)	301(WNW)
	5:00	0.0(0)	296(WNW)
	6:00	0.0(0)	166(SSE)
	7:00	0.0(0)	201(SSW)
	8:00	0.0(0)	352(N)
	9:00	0.0(0)	179(S)
	10:00	0.0(0)	161(SSE)
	11:00	0.0(0)	192(SSW)
	12:00	1.7(2)	301(WNW)
	13:00	1.9(2)	177(S)
	14:00	0.0(0)	124(SE)
	15:00	0.0(0)	136(SE)
	16:00	0.5(1)	127(SE)
	17:00	0.5(1)	192(SSW)
	18:00	0.0(0)	328(NNW)
	19:00	0.0(0)	330(NNW)
	20:00	0.0(0)	240(WSW)
	21:00	0.0(0)	353(N)
	22:00	0.0(0)	242(WSW)
23:00	0.0(0)	44(NE)	



## Wind Speed and Wind Direction

Date	Time	Wind Speed (m/s)	Wind Direction (degree)
7-Jul-24	0:00	0.0(0)	224(SW)
	1:00	0.0(0)	148(SSE)
	2:00	0.0(0)	304(NW)
	3:00	0.0(0)	29(NNE)
	4:00	0.0(0)	224(SW)
	5:00	0.0(0)	216(SW)
	6:00	0.0(0)	185(S)
	7:00	0.0(0)	48(NE)
	8:00	0.0(0)	82(E)
	9:00	0.9(1)	86(E)
	10:00	1.7(2)	180(S)
	11:00	1.1(1)	146(SE)
	12:00	1.5(1)	214(SW)
	13:00	4.1(3)	73(ENE)
	14:00	0.0(0)	125(SE)
	15:00	2.3(2)	171(S)
	16:00	2.3(2)	98(E)
	17:00	1.9(2)	76(ENE)
	18:00	2.1(2)	92(E)
	19:00	1.3(1)	181(S)
	20:00	0.0(0)	207(SSW)
	21:00	0.0(0)	160(SSE)
	22:00	0.0(0)	70(ENE)
23:00	0.0(0)	262(W)	
8-Jul-24	0:00	1.1(1)	145(SE)
	1:00	0.0(0)	175(S)
	2:00	0.0(0)	150(SSE)
	3:00	0.0(0)	34(NE)
	4:00	0.0(0)	134(SE)
	5:00	0.0(0)	164(SSE)
	6:00	0.0(0)	169(S)
	7:00	0.0(0)	222(SW)
	8:00	0.0(0)	149(SSE)
	9:00	3.9(3)	130(SE)
	10:00	0.0(0)	252(WSW)
	11:00	1.3(1)	135(SE)
	12:00	1.1(1)	39(NE)
	13:00	0.0(0)	65(ENE)
	14:00	1.9(2)	86(E)
	15:00	0.7(1)	52(NE)
	16:00	1.7(2)	51(NE)
	17:00	1.1(1)	51(NE)
	18:00	1.9(2)	183(S)
	19:00	1.3(1)	69(ENE)
	20:00	0.7(1)	60(ENE)
	21:00	1.3(1)	98(E)
	22:00	0.9(1)	160(SSE)
23:00	1.1(1)	79(E)	



## Wind Speed and Wind Direction

Date	Time	Wind Speed (m/s)	Wind Direction (degree)
9-Jul-24	0:00	0.0(0)	159(SSE)
	1:00	0.0(0)	44(NE)
	2:00	0.0(0)	58(ENE)
	3:00	0.0(0)	205(SSW)
	4:00	0.0(0)	24(NNE)
	5:00	0.0(0)	236(SW)
	6:00	0.7(1)	46(NE)
	7:00	0.0(0)	139(SE)
	8:00	0.0(0)	170(S)
	9:00	1.1(1)	56(NE)
	10:00	1.1(1)	229(SW)
	11:00	1.5(1)	65(ENE)
	12:00	1.1(1)	220(SW)
	13:00	1.1(1)	218(SW)
	14:00	1.9(2)	216(SW)
	15:00	1.9(2)	113(ESE)
	16:00	1.1(1)	244(WSW)
	17:00	0.9(1)	352(N)
	18:00	1.5(1)	67(ENE)
	19:00	0.0(0)	132(SE)
	20:00	0.0(0)	192(SSW)
	21:00	0.5(1)	108(ESE)
	22:00	0.0(0)	202(SSW)
23:00	0.0(0)	188(S)	
10-Jul-24	0:00	0.0(0)	284(WNW)
	1:00	0.0(0)	234(SW)
	2:00	0.0(0)	149(SSE)
	3:00	0.0(0)	7(N)
	4:00	0.0(0)	278(W)
	5:00	0.0(0)	207(SSW)
	6:00	0.0(0)	265(W)
	7:00	0.0(0)	180(S)
	8:00	0.0(0)	218(SW)
	9:00	0.5(1)	202(SSW)
	10:00	1.3(1)	193(SSW)
	11:00	2.1(2)	91(E)
	12:00	0.9(1)	35(NE)
	13:00	2.5(2)	138(SE)
	14:00	1.3(1)	160(SSE)
	15:00	2.5(2)	234(SW)
	16:00	1.5(1)	39(NE)
	17:00	2.1(2)	43(NE)
	18:00	1.9(2)	161(SSE)
	19:00	1.7(2)	172(S)
	20:00	0.0(0)	65(ENE)
	21:00	1.7(2)	122(ESE)
	22:00	0.0(0)	228(SW)
23:00	0.9(1)	219(SW)	



## Wind Speed and Wind Direction

Date	Time	Wind Speed (m/s)	Wind Direction (degree)
11-Jul-24	0:00	1.1(1)	142(SE)
	1:00	1.5(1)	241(WSW)
	2:00	0.0(0)	188(S)
	3:00	0.0(0)	55(NE)
	4:00	0.0(0)	347(NNW)
	5:00	0.0(0)	291(WNW)
	6:00	0.0(0)	73(ENE)
	7:00	0.0(0)	294(WNW)
	8:00	0.0(0)	31(NNE)
	9:00	0.9(1)	68(ENE)
	10:00	0.0(0)	89(E)
	11:00	0.5(1)	221(SW)
	12:00	1.7(2)	78(ENE)
	13:00	1.5(1)	91(E)
	14:00	0.7(1)	169(S)
	15:00	1.5(1)	243(WSW)
	16:00	0.0(0)	225(SW)
	17:00	1.1(1)	288(WNW)
	18:00	1.7(2)	77(ENE)
	19:00	1.3(1)	195(SSW)
	20:00	0.9(1)	128(SE)
	21:00	0.0(0)	171(S)
	22:00	0.0(0)	212(SSW)
23:00	0.0(0)	158(SSE)	
12-Jul-24	0:00	0.0(0)	289(WNW)
	1:00	0.0(0)	280(W)
	2:00	0.0(0)	88(E)
	3:00	0.0(0)	33(NNE)
	4:00	0.0(0)	176(S)
	5:00	0.0(0)	127(SE)
	6:00	0.0(0)	280(W)
	7:00	0.0(0)	15(NNE)
	8:00	0.5(1)	266(W)
	9:00	0.0(0)	27(NNE)
	10:00	0.0(0)	75(ENE)
	11:00	0.9(1)	207(SSW)
	12:00	0.0(0)	139(SE)
	13:00	0.0(0)	182(S)
	14:00	0.0(0)	177(S)
	15:00	2.1(2)	44(NE)
	16:00	0.9(1)	59(ENE)
	17:00	0.0(0)	266(W)
	18:00	0.0(0)	285(WNW)
	19:00	0.0(0)	243(WSW)
	20:00	0.0(0)	159(SSE)
	21:00	0.0(0)	278(W)
	22:00	0.0(0)	166(SSE)
23:00	0.0(0)	189(S)	



## Wind Speed and Wind Direction

Date	Time	Wind Speed (m/s)	Wind Direction (degree)
13-Jul-24	0:00	0.0(0)	49(NE)
	1:00	0.0(0)	280(W)
	2:00	0.0(0)	121(ESE)
	3:00	0.0(0)	92(E)
	4:00	0.0(0)	120(ESE)
	5:00	0.0(0)	197(SSW)
	6:00	0.0(0)	114(ESE)
	7:00	0.0(0)	65(ENE)
	8:00	0.0(0)	288(WNW)
	9:00	1.1(1)	339(NNW)
	10:00	0.0(0)	84(E)
	11:00	0.7(1)	190(S)
	12:00	1.7(2)	269(W)
	13:00	1.3(1)	52(NE)
	14:00	2.7(2)	164(SSE)
	15:00	1.5(1)	96(E)
	16:00	1.9(2)	96(E)
	17:00	2.5(2)	74(ENE)
	18:00	1.3(1)	203(SSW)
	19:00	0.0(0)	177(S)
	20:00	1.3(1)	118(ESE)
	21:00	0.5(1)	193(SSW)
	22:00	0.0(0)	264(W)
23:00	0.0(0)	212(SSW)	
14-Jul-24	0:00	0.0(0)	266(W)
	1:00	0.0(0)	150(SSE)
	2:00	0.0(0)	103(ESE)
	3:00	0.0(0)	188(S)
	4:00	0.0(0)	236(SW)
	5:00	0.0(0)	280(W)
	6:00	0.0(0)	292(WNW)
	7:00	0.0(0)	181(S)
	8:00	0.9(1)	80(E)
	9:00	0.9(1)	69(ENE)
	10:00	0.0(0)	91(E)
	11:00	0.0(0)	109(ESE)
	12:00	2.3(2)	342(NNW)
	13:00	0.0(0)	170(S)
	14:00	1.1(1)	169(S)
	15:00	1.5(1)	264(W)
	16:00	1.3(1)	183(S)
	17:00	0.0(0)	310(NW)
	18:00	0.0(0)	50(NE)
	19:00	0.0(0)	71(ENE)
	20:00	0.0(0)	141(SE)
	21:00	0.0(0)	231(SW)
	22:00	0.0(0)	99(E)
23:00	0.0(0)	152(SSE)	



## Wind Speed and Wind Direction

Date	Time	Wind Speed (m/s)	Wind Direction (degree)
15-Jul-24	0:00	0.0(0)	286(WNW)
	1:00	0.0(0)	310(NW)
	2:00	0.0(0)	308(NW)
	3:00	0.0(0)	213(SSW)
	4:00	0.0(0)	137(SE)
	5:00	0.0(0)	247(WSW)
	6:00	0.0(0)	336(NNW)
	7:00	0.0(0)	10(N)
	8:00	0.0(0)	137(SE)
	9:00	0.0(0)	199(SSW)
	10:00	0.0(0)	139(SE)
	11:00	0.0(0)	238(WSW)
	12:00	0.0(0)	80(E)
	13:00	0.9(1)	96(E)
	14:00	0.9(1)	96(E)
	15:00	0.0(0)	231(SW)
	16:00	0.0(0)	271(W)
	17:00	0.5(1)	307(NW)
	18:00	0.0(0)	179(S)
	19:00	2.1(2)	95(E)
	20:00	0.7(1)	57(ENE)
	21:00	0.0(0)	57(ENE)
	22:00	0.0(0)	191(S)
23:00	0.0(0)	83(E)	
16-Jul-24	0:00	1.9(2)	202(SSW)
	1:00	0.0(0)	176(S)
	2:00	1.1(1)	283(WNW)
	3:00	0.7(1)	239(WSW)
	4:00	0.9(1)	202(SSW)
	5:00	0.0(0)	248(WSW)
	6:00	0.0(0)	213(SSW)
	7:00	0.0(0)	112(ESE)
	8:00	0.0(0)	99(E)
	9:00	1.7(2)	188(S)
	10:00	0.0(0)	285(WNW)
	11:00	0.0(0)	256(WSW)
	12:00	0.0(0)	337(NNW)
	13:00	0.0(0)	161(SSE)
	14:00	0.9(1)	175(S)
	15:00	0.0(0)	153(SSE)
	16:00	0.0(0)	91(E)
	17:00	0.0(0)	151(SSE)
	18:00	1.1(1)	226(SW)
	19:00	0.0(0)	169(S)
	20:00	1.7(2)	224(SW)
	21:00	0.0(0)	324(NW)
	22:00	0.0(0)	152(SSE)
23:00	0.0(0)	184(S)	



## Wind Speed and Wind Direction

Date	Time	Wind Speed (m/s)	Wind Direction (degree)
17-Jul-24	0:00	0.0(0)	179(S)
	1:00	0.0(0)	140(SE)
	2:00	0.0(0)	25(NNE)
	3:00	0.0(0)	153(SSE)
	4:00	0.0(0)	8(N)
	5:00	0.0(0)	321(NW)
	6:00	0.0(0)	299(WNW)
	7:00	0.0(0)	60(ENE)
	8:00	0.0(0)	229(SW)
	9:00	0.0(0)	254(WSW)
	10:00	0.0(0)	51(NE)
	11:00	1.3(1)	114(ESE)
	12:00	1.5(1)	190(S)
	13:00	0.0(0)	211(SSW)
	14:00	0.5(1)	173(S)
	15:00	1.1(1)	137(SE)
	16:00	2.7(2)	236(SW)
	17:00	0.0(0)	149(SSE)
	18:00	0.0(0)	111(ESE)
	19:00	0.0(0)	148(SSE)
	20:00	0.0(0)	184(S)
	21:00	0.0(0)	59(ENE)
	22:00	0.0(0)	240(WSW)
23:00	0.0(0)	244(WSW)	
18-Jul-24	0:00	0.0(0)	94(E)
	1:00	0.0(0)	90(E)
	2:00	0.0(0)	120(ESE)
	3:00	0.0(0)	169(S)
	4:00	0.0(0)	146(SE)
	5:00	0.0(0)	228(SW)
	6:00	0.0(0)	286(WNW)
	7:00	0.0(0)	196(SSW)
	8:00	0.0(0)	335(NNW)
	9:00	0.0(0)	219(SW)
	10:00	0.0(0)	146(SE)
	11:00	0.0(0)	67(ENE)
	12:00	0.0(0)	203(SSW)
	13:00	0.0(0)	108(ESE)
	14:00	0.7(1)	125(SE)
	15:00	0.0(0)	163(SSE)
	16:00	0.0(0)	152(SSE)
	17:00	0.0(0)	211(SSW)
	18:00	0.0(0)	239(WSW)
	19:00	0.0(0)	265(W)
	20:00	0.0(0)	266(W)
	21:00	0.0(0)	143(SE)
	22:00	0.0(0)	160(SSE)
23:00	1.5(1)	167(SSE)	





## Wind Speed and Wind Direction

Date	Time	Wind Speed (m/s)	Wind Direction (degree)
19-Jul-24	0:00	0.0(0)	255(WSW)
	1:00	0.0(0)	112(ESE)
	2:00	0.0(0)	308(NW)
	3:00	0.0(0)	117(ESE)
	4:00	0.0(0)	275(W)
	5:00	0.0(0)	288(WNW)
	6:00	0.0(0)	298(WNW)
	7:00	1.3(1)	201(SSW)
	8:00	0.0(0)	225(SW)
	9:00	0.0(0)	138(SE)
	10:00	0.0(0)	112(ESE)
	11:00	0.0(0)	195(SSW)
	12:00	0.0(0)	237(WSW)
	13:00	0.0(0)	169(S)
	14:00	0.0(0)	147(SSE)
	15:00	0.0(0)	87(E)
	16:00	0.0(0)	96(E)
	17:00	0.0(0)	34(NE)
	18:00	0.9(1)	157(SSE)
	19:00	1.1(1)	170(S)
	20:00	0.0(0)	77(ENE)
	21:00	0.0(0)	267(W)
	22:00	0.0(0)	269(W)
23:00	0.0(0)	243(WSW)	
20-Jul-24	0:00	0.0(0)	175(S)
	1:00	0.0(0)	167(SSE)
	2:00	0.0(0)	193(SSW)
	3:00	0.0(0)	102(ESE)
	4:00	0.0(0)	200(SSW)
	5:00	1.3(1)	158(SSE)
	6:00	1.1(1)	302(WNW)
	7:00	0.5(1)	231(SW)
	8:00	0.0(0)	192(SSW)
	9:00	0.7(1)	219(SW)
	10:00	0.7(1)	229(SW)
	11:00	0.7(1)	268(W)
	12:00	0.7(1)	122(ESE)
	13:00	0.9(1)	330(NNW)
	14:00	0.0(0)	171(S)
	15:00	0.0(0)	186(S)
	16:00	0.0(0)	148(SSE)
	17:00	1.3(1)	18(NNE)
	18:00	0.7(1)	26(NNE)
	19:00	2.5(2)	124(SE)
	20:00	2.1(2)	109(ESE)
	21:00	1.3(1)	219(SW)
	22:00	0.0(0)	156(SSE)
23:00	0.9(1)	36(NE)	



## Wind Speed and Wind Direction

Date	Time	Wind Speed (m/s)	Wind Direction (degree)
21-Jul-24	0:00	1.1(1)	92(E)
	1:00	0.0(0)	155(SSE)
	2:00	0.0(0)	125(SE)
	3:00	0.0(0)	125(SE)
	4:00	0.0(0)	131(SE)
	5:00	0.0(0)	123(ESE)
	6:00	0.0(0)	84(E)
	7:00	0.0(0)	153(SSE)
	8:00	0.0(0)	96(E)
	9:00	0.0(0)	137(SE)
	10:00	1.1(1)	324(NW)
	11:00	0.0(0)	125(SE)
	12:00	0.5(1)	234(SW)
	13:00	1.1(1)	138(SE)
	14:00	0.0(0)	151(SSE)
	15:00	0.0(0)	308(NW)
	16:00	2.3(2)	219(SW)
	17:00	0.7(1)	33(NNE)
	18:00	1.1(1)	194(SSW)
	19:00	1.1(1)	195(SSW)
	20:00	0.7(1)	205(SSW)
	21:00	0.0(0)	148(SSE)
	22:00	0.0(0)	60(ENE)
23:00	0.0(0)	198(SSW)	
22-Jul-24	0:00	0.0(0)	260(W)
	1:00	0.0(0)	223(SW)
	2:00	0.0(0)	355(N)
	3:00	0.0(0)	97(E)
	4:00	0.0(0)	115(ESE)
	5:00	0.5(1)	228(SW)
	6:00	0.7(1)	287(WNW)
	7:00	0.5(1)	134(SE)
	8:00	0.0(0)	91(E)
	9:00	1.3(1)	169(S)
	10:00	0.0(0)	335(NNW)
	11:00	0.9(1)	33(NNE)
	12:00	2.5(2)	128(SE)
	13:00	0.0(0)	331(NNW)
	14:00	1.9(2)	153(SSE)
	15:00	1.5(1)	41(NE)
	16:00	0.5(1)	199(SSW)
	17:00	0.0(0)	197(SSW)
	18:00	0.7(1)	168(SSE)
	19:00	0.0(0)	8(N)
	20:00	0.0(0)	66(ENE)
	21:00	0.0(0)	355(N)
	22:00	0.0(0)	198(SSW)
23:00	0.0(0)	312(NW)	



## Wind Speed and Wind Direction

Date	Time	Wind Speed (m/s)	Wind Direction (degree)
23-Jul-24	0:00	0.0(0)	244(WSW)
	1:00	0.0(0)	137(SE)
	2:00	0.0(0)	166(SSE)
	3:00	0.0(0)	123(ESE)
	4:00	0.0(0)	164(SSE)
	5:00	0.0(0)	103(ESE)
	6:00	0.0(0)	158(SSE)
	7:00	0.5(1)	140(SE)
	8:00	0.0(0)	214(SW)
	9:00	0.0(0)	116(ESE)
	10:00	0.0(0)	26(NNE)
	11:00	1.5(1)	152(SSE)
	12:00	1.9(2)	79(E)
	13:00	1.9(2)	97(E)
	14:00	1.1(1)	112(ESE)
	15:00	0.7(1)	199(SSW)
	16:00	1.9(2)	143(SE)
	17:00	3.3(2)	296(WNW)
	18:00	0.0(0)	166(SSE)
	19:00	0.9(1)	108(ESE)
	20:00	0.0(0)	139(SE)
	21:00	0.0(0)	109(ESE)
	22:00	0.0(0)	195(SSW)
23:00	0.0(0)	105(ESE)	
24-Jul-24	0:00	0.0(0)	208(SSW)
	1:00	0.0(0)	79(E)
	2:00	0.5(1)	121(ESE)
	3:00	0.0(0)	134(SE)
	4:00	0.0(0)	275(W)
	5:00	0.0(0)	0(N)
	6:00	0.0(0)	107(ESE)
	7:00	0.0(0)	146(SE)
	8:00	0.0(0)	205(SSW)
	9:00	0.0(0)	94(E)
	10:00	1.9(2)	158(SSE)
	11:00	0.0(0)	147(SSE)
	12:00	1.7(2)	239(WSW)
	13:00	0.5(1)	260(W)
	14:00	0.0(0)	149(SSE)
	15:00	0.0(0)	142(SE)
	16:00	1.9(2)	37(NE)
	17:00	1.9(2)	150(SSE)
	18:00	0.0(0)	280(W)
	19:00	0.0(0)	81(E)
	20:00	0.0(0)	35(NE)
	21:00	0.0(0)	206(SSW)
	22:00	0.0(0)	90(E)
23:00	0.0(0)	148(SSE)	



## Wind Speed and Wind Direction

Date	Time	Wind Speed (m/s)	Wind Direction (degree)
25-Jul-24	0:00	0.0(0)	191(S)
	1:00	0.0(0)	189(S)
	2:00	0.0(0)	58(ENE)
	3:00	1.5(1)	185(S)
	4:00	1.7(2)	152(SSE)
	5:00	0.0(0)	72(ENE)
	6:00	0.0(0)	330(NNW)
	7:00	0.5(1)	195(SSW)
	8:00	1.5(1)	319(NW)
	9:00	0.0(0)	99(E)
	10:00	1.3(1)	328(NNW)
	11:00	0.9(1)	354(N)
	12:00	1.7(2)	168(SSE)
	13:00	3.7(3)	208(SSW)
	14:00	1.3(1)	150(SSE)
	15:00	0.5(1)	168(SSE)
	16:00	0.9(1)	125(SE)
	17:00	1.7(2)	156(SSE)
	18:00	0.0(0)	198(SSW)
	19:00	4.7(3)	173(S)
	20:00	0.0(0)	283(WNW)
	21:00	1.5(1)	257(WSW)
	22:00	2.7(2)	165(SSE)
23:00	0.0(0)	208(SSW)	
26-Jul-24	0:00	1.3(1)	109(ESE)
	1:00	0.0(0)	98(E)
	2:00	1.5(1)	164(SSE)
	3:00	0.0(0)	173(S)
	4:00	0.0(0)	70(ENE)
	5:00	0.0(0)	134(SE)
	6:00	0.0(0)	218(SW)
	7:00	0.0(0)	198(SSW)
	8:00	0.0(0)	279(W)
	9:00	0.0(0)	210(SSW)
	10:00	0.0(0)	153(SSE)
	11:00	0.0(0)	120(ESE)
	12:00	2.1(2)	45(NE)
	13:00	1.3(1)	57(ENE)
	14:00	2.1(2)	167(SSE)
	15:00	2.3(2)	190(S)
	16:00	2.3(2)	214(SW)
	17:00	0.9(1)	167(SSE)
	18:00	0.9(1)	216(SW)
	19:00	1.9(2)	196(SSW)
	20:00	1.1(1)	256(WSW)
	21:00	0.0(0)	189(S)
	22:00	0.0(0)	168(SSE)
23:00	0.0(0)	48(NE)	



## Wind Speed and Wind Direction

Date	Time	Wind Speed (m/s)	Wind Direction (degree)
27-Jul-24	0:00	0.0(0)	103(ESE)
	1:00	0.0(0)	196(SSW)
	2:00	0.0(0)	189(S)
	3:00	0.0(0)	90(E)
	4:00	0.9(1)	52(NE)
	5:00	1.1(1)	131(SE)
	6:00	0.0(0)	153(SSE)
	7:00	0.0(0)	13(NNE)
	8:00	0.0(0)	323(NW)
	9:00	1.5(1)	66(ENE)
	10:00	0.0(0)	277(W)
	11:00	1.9(2)	206(SSW)
	12:00	0.0(0)	220(SW)
	13:00	1.5(1)	209(SSW)
	14:00	0.0(0)	126(SE)
	15:00	0.0(0)	149(SSE)
	16:00	0.0(0)	81(E)
	17:00	0.0(0)	167(SSE)
	18:00	0.0(0)	225(SW)
	19:00	0.0(0)	329(NNW)
	20:00	0.0(0)	317(NW)
	21:00	0.0(0)	80(E)
	22:00	0.0(0)	149(SSE)
23:00	0.0(0)	234(SW)	
28-Jul-24	0:00	0.0(0)	267(W)
	1:00	0.0(0)	236(SW)
	2:00	0.0(0)	254(WSW)
	3:00	0.0(0)	157(SSE)
	4:00	0.0(0)	189(S)
	5:00	0.0(0)	221(SW)
	6:00	0.0(0)	155(SSE)
	7:00	0.0(0)	223(SW)
	8:00	0.0(0)	97(E)
	9:00	0.0(0)	181(S)
	10:00	0.0(0)	334(NNW)
	11:00	0.0(0)	32(NNE)
	12:00	0.0(0)	262(W)
	13:00	0.0(0)	10(N)
	14:00	0.0(0)	91(E)
	15:00	0.0(0)	299(WNW)
	16:00	1.1(1)	228(SW)
	17:00	0.0(0)	193(SSW)
	18:00	1.3(1)	141(SE)
	19:00	0.0(0)	210(SSW)
	20:00	0.0(0)	259(W)
	21:00	0.0(0)	106(ESE)
	22:00	0.0(0)	335(NNW)
23:00	0.0(0)	174(S)	



## Wind Speed and Wind Direction

Date	Time	Wind Speed (m/s)	Wind Direction (degree)
29-Jul-24	0:00	0.0(0)	117(ESE)
	1:00	0.0(0)	102(ESE)
	2:00	0.0(0)	114(ESE)
	3:00	0.0(0)	307(NW)
	4:00	0.0(0)	171(S)
	5:00	0.0(0)	334(NNW)
	6:00	0.0(0)	50(NE)
	7:00	0.0(0)	37(NE)
	8:00	0.0(0)	54(NE)
	9:00	1.1(1)	254(WSW)
	10:00	0.5(1)	214(SW)
	11:00	0.0(0)	111(ESE)
	12:00	0.0(0)	103(ESE)
	13:00	1.1(1)	30(NNE)
	14:00	0.0(0)	196(SSW)
	15:00	0.0(0)	194(SSW)
	16:00	0.0(0)	82(E)
	17:00	0.0(0)	110(ESE)
	18:00	0.9(1)	121(ESE)
	19:00	1.1(1)	180(S)
	20:00	0.0(0)	247(WSW)
	21:00	2.9(2)	175(S)
	22:00	0.0(0)	241(WSW)
23:00	0.0(0)	188(S)	
30-Jul-24	0:00	0.0(0)	208(SSW)
	1:00	0.0(0)	30(NNE)
	2:00	0.0(0)	334(NNW)
	3:00	0.0(0)	69(ENE)
	4:00	0.0(0)	271(W)
	5:00	0.0(0)	359(N)
	6:00	0.0(0)	201(SSW)
	7:00	0.0(0)	214(SW)
	8:00	0.0(0)	182(S)
	9:00	0.0(0)	243(WSW)
	10:00	0.0(0)	216(SW)
	11:00	0.0(0)	202(SSW)
	12:00	0.7(1)	177(S)
	13:00	0.0(0)	233(SW)
	14:00	1.5(1)	146(SE)
	15:00	0.0(0)	182(S)
	16:00	1.1(1)	215(SW)
	17:00	1.3(1)	206(SSW)
	18:00	0.9(1)	138(SE)
	19:00	1.7(2)	178(S)
	20:00	0.5(1)	57(ENE)
	21:00	1.1(1)	179(S)
	22:00	0.0(0)	299(WNW)
23:00	0.0(0)	244(WSW)	
	0:00	0.0(0)	267(W)
	1:00	0.0(0)	288(WNW)
	2:00	0.0(0)	72(ENE)
	3:00	0.0(0)	68(ENE)



**Wind Speed and Wind Direction**

Date	Time	Wind Speed (m/s)	Wind Direction (degree)
31-Jul-24	4:00	0.0(0)	11(N)
	5:00	0.0(0)	1(N)
	6:00	0.0(0)	206(SSW)
	7:00	0.0(0)	298(WNW)
	8:00	1.1(1)	112(ESE)
	9:00	0.0(0)	182(S)
	10:00	0.0(0)	342(NNW)
	11:00	0.0(0)	269(W)
	12:00	0.0(0)	186(S)
	13:00	0.0(0)	180(S)
	14:00	0.0(0)	164(SSE)
	15:00	0.0(0)	230(SW)
	16:00	0.0(0)	91(E)
	17:00	1.5(1)	80(E)
	18:00	0.0(0)	84(E)
	19:00	0.0(0)	121(ESE)
	20:00	0.0(0)	84(E)
21:00	1.3(1)	90(E)	
22:00	0.0(0)	277(W)	
23:00	0.0(0)	22(NNE)	



## ***Appendix 5.1***

# ***Monitoring Schedule for Reporting Month and Next Reporting Month***

---



**Contract No. HY/2020/08  
Flyover from Kwai Tsing Interchange Upramp to Kwai Chung Road**

**Tentative Environmental Impact Monitoring Schedule  
Jul-24**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	1-Jul	2-Jul	3-Jul	4-Jul	5-Jul	6-Jul
	Kwai Chung 24hr	Kwai Chung 1hr Noise			Kwai Chung 24hr	Kwai Chung 1hr
7-Jul	8-Jul	9-Jul	10-Jul	11-Jul	12-Jul	13-Jul
				Kwai Chung 24hr	Kwai Chung 1hr Noise	
14-Jul	15-Jul	16-Jul	17-Jul	18-Jul	19-Jul	20-Jul
			Kwai Chung 24hr	Kwai Chung 1hr Noise		
21-Jul	22-Jul	23-Jul	24-Jul	25-Jul	26-Jul	27-Jul
		Kwai Chung 24hr	Kwai Chung 1hr Noise			
28-Jul	29-Jul	30-Jul	31-Jul	1-Aug	2-Aug	3-Aug
	Kwai Chung 24hr	Kwai Chung 1hr Noise				Kwai Chung 24hr

**Contract No. HY/2020/08  
Flyover from Kwai Tsing Interchange Upramp to Kwai Chung Road**

**Tentative Environmental Impact Monitoring Schedule  
Aug-24**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	29-Jul	30-Jul	31-Jul	1-Aug	2-Aug	3-Aug
	Kwai Chung 24hr	Kwai Chung 1hr Noise				Kwai Chung 24hr
4-Aug	5-Aug	6-Aug	7-Aug	8-Aug	9-Aug	10-Aug
	Kwai Chung 1hr Noise				Kwai Chung 24hr	Kwai Chung 1hr
11-Aug	12-Aug	13-Aug	14-Aug	15-Aug	16-Aug	17-Aug
				Kwai Chung 24hr	Kwai Chung 1hr Noise	
18-Aug	19-Aug	20-Aug	21-Aug	22-Aug	23-Aug	24-Aug
			Kwai Chung 24hr	Kwai Chung 1hr Noise		
25-Aug	26-Aug	27-Aug	28-Aug	29-Aug	30-Aug	31-Aug
		Kwai Chung 24hr	Kwai Chung 1hr Noise			



## ***Appendix 5.2***

# ***Noise Monitoring Results and Graphical Presentations***



**Noise Monitoring Result**

**Day Time (0700 - 1900hrs on normal weekdays)**

Location: NMC-01 - R/F, Lai King Catholic Secondary School

Date	Weather	Time	Measurement Noise Level			Average Noise Level	Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq	Leq
			Unit: dB(A), (5-min)			Unit: dB(A), (30-min)			
2 Jul 2024	Fine	15:20	69.2	71.4	66.5	69.5	74.5	<Baseline Level	70
		15:25	69.4	71.8	66.8				
		15:30	69.8	71.9	66.7				
		15:35	69.5	71.7	66.6				
		15:40	69.6	71.8	66.8				
12 Jul 2024	Fine	15:15	69.5	72.0	67.1	70.0	74.5	<Baseline Level	70
		15:20	69.8	71.9	67.0				
		15:25	70.1	72.1	67.2				
		15:30	70.2	72.5	67.1				
		15:35	70.3	72.6	67.0				
18 Jul 2024	Fine	11:30	68.6	71.0	65.9	68.4	74.5	<Baseline Level	70
		11:35	68.4	70.5	65.9				
		11:40	68.8	70.9	66.0				
		11:45	68.2	71.0	66.0				
		11:50	68.0	70.8	66.2				
24 Jul 2024	Fine	15:35	69.1	71.2	66.8	69.2	74.5	<Baseline Level	70
		15:40	69.5	71.4	66.7				
		15:45	69.4	71.3	66.5				
		15:50	69.2	71.3	66.9				
		15:55	69.0	71.2	66.8				
30 Jul 2024	Cloudy	11:03	73.5	74.5	72.0	73.9	74.5	<Baseline Level	70
		11:08	73.6	74.5	72.6				
		11:13	73.9	74.9	72.5				
		11:18	74.2	75.1	73.1				
		11:23	73.9	74.5	72.1				
		11:28	74.3	75.3	72.9				

Remark(s):

- i. The Construction Noise Level refers to the corrected noise level based on the difference between SPL of the Measured Noise Level and the SPL of the Baseline Noise Level. In the event of the Baseline Noise Level exceeds the Measured Noise Level, no correction would be applied.
- iii. As the baseline level of NMC-01 is higher than the measured average noise levels on 30 July 2024, the noise monitoring results are not considered as noise exceedances.



**Noise Monitoring Result**

**Day Time (0700 - 1900hrs on normal weekdays)**

Location: NMC-02 - R/F, Fung King House

Date	Weather	Time	Measurement Noise Level			Average Noise Level	Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq	Leq
			Unit: dB(A), (5-min)			Unit: dB(A), (30-min)			
2 Jul 2024	Fine	13:05	67.4	69.8	65.5	67.5	67.6	<Baseline Level	75
		13:10	67.5	69.7	65.4				
		13:15	67.4	69.9	65.6				
		13:20	67.5	69.4	65.8				
		13:25	67.6	69.8	65.4				
12 Jul 2024	Fine	13:00	67.6	69.7	64.5	67.3	67.6	<Baseline Level	75
		13:05	67.0	69.8	64.8				
		13:10	67.2	69.4	64.9				
		13:15	67.1	69.6	64.7				
		13:20	67.5	69.5	64.5				
18 Jul 2024	Fine	9:30	67.5	68.9	64.2	67.6	67.6	<Baseline Level	75
		9:35	67.8	68.8	64.3				
		9:40	67.6	69.0	64.5				
		9:45	67.4	68.9	64.2				
		9:50	67.5	68.7	64.5				
24 Jul 2024	Fine	11:20	67.1	69.1	64.5	67.3	67.6	<Baseline Level	75
		11:25	67.0	69.2	64.6				
		11:30	67.5	69.0	64.5				
		11:35	67.3	69.2	64.6				
		11:40	67.4	69.0	64.5				
30 Jul 2024	Cloudy	10:20	69.7	70.3	68.5	69.1	67.6	64	75
		10:25	69.0	69.7	67.9				
		10:30	68.9	69.8	67.8				
		10:35	68.9	66.8	67.8				
		10:40	69.2	70.0	68.4				
		10:45	69.1	70.0	68.1				

Remark(s):

- i. The Construction Noise Level refers to the corrected noise level based on the difference between SPL of the Measured Noise Level and the SPL of the Baseline Noise Level. In the event of the Baseline Noise Level exceeds the Measured Noise Level, no correction would be applied.
- iii. As the limit level of NMC-02 is higher than the measured average noise levels on 30 July 2024, the noise monitoring results are not considered as noise exceedances.



**Noise Monitoring Result**

**Day Time (0700 - 1900hrs on normal weekdays)**

Location: NMC-03 - G/F, HKEAA - Lai King Assessment Centre

Date	Weather	Time	Measurement Noise Level			Average Noise Level	Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq	Leq
			Unit: dB(A), (5-min)			Unit: dB(A), (30-min)			
2 Jul 2024	Fine	13:50	70.5	72.5	68.1	70.6	79.1	<Baseline Level	65
		13:55	70.4	72.6	68.0				
		14:00	70.6	72.4	68.0				
		14:05	70.5	72.8	68.2				
		14:10	70.8	72.6	68.1				
12 Jul 2024	Fine	13:45	70.8	72.1	67.2	70.5	79.1	<Baseline Level	65
		13:50	70.6	72.0	67.4				
		13:55	70.4	72.1	67.3				
		14:00	70.5	71.9	67.2				
		14:05	70.4	72.1	67.2				
18 Jul 2024	Fine	14:10	70.5	72.0	67.3	71.3	79.1	<Baseline Level	65
		10:30	71.2	73.0	67.2				
		10:35	71.5	73.2	67.1				
		10:40	71.3	73.0	67.0				
		10:45	71.0	73.1	67.1				
24 Jul 2024	Fine	10:50	71.2	73.2	67.2	71.0	79.1	<Baseline Level	65
		10:55	71.3	73.0	67.1				
		14:45	70.8	72.8	68.0				
		14:50	71.0	72.5	68.1				
		14:55	71.2	72.6	67.9				
30 Jul 2024	Cloudy	15:00	71.0	72.4	68.0	77.9	79.1	<Baseline Level	65
		15:05	70.9	72.6	67.9				
		15:10	71.3	72.8	67.1				
		9:36	78.0	78.9	77.0				
		9:41	78.0	78.9	77.1				
	9:46	77.9	78.7	76.8					
	9:51	78.1	79.1	77.1					
	9:56	77.9	78.9	76.8					
	10:01	77.4	78.5	75.9					

Remark(s):


- i. The Construction Noise Level refers to the corrected noise level based on the difference between SPL of the Measured Noise Level and the SPL of the Baseline Noise Level. In the event of the Baseline Noise Level exceeds the Measured Noise Level, no correction would be applied.
- iii. As the baseline level of NMC-03 is higher than the measured average noise levels on 2, 12, 18, 24 and 30 July 2024, the noise monitoring results are not considered as noise exceedances.




Graphic Presentation of Noise Monitoring Result

Day Time (0700 - 1900hrs on normal weekdays)


NMC-01 - R/F, Lai King Catholic Secondary School

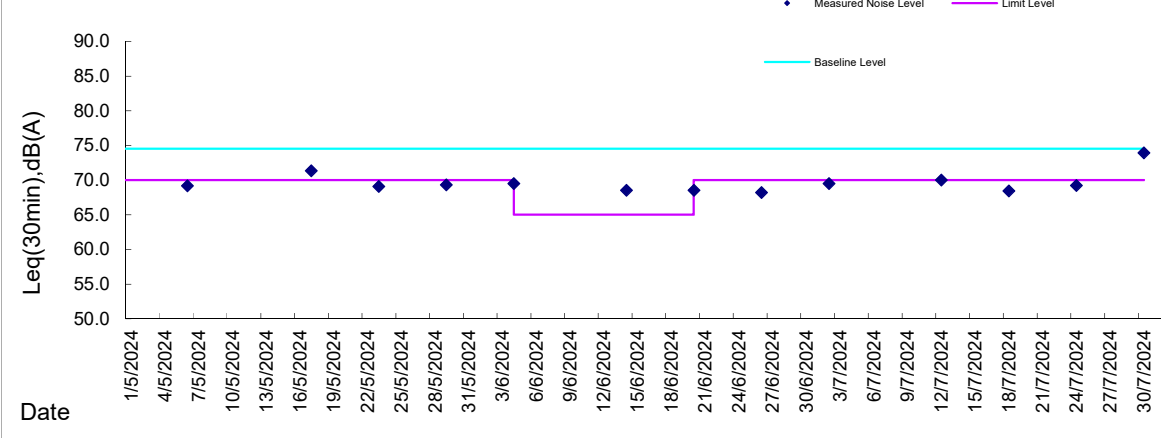

NMC-02 - R/F, Fung King House

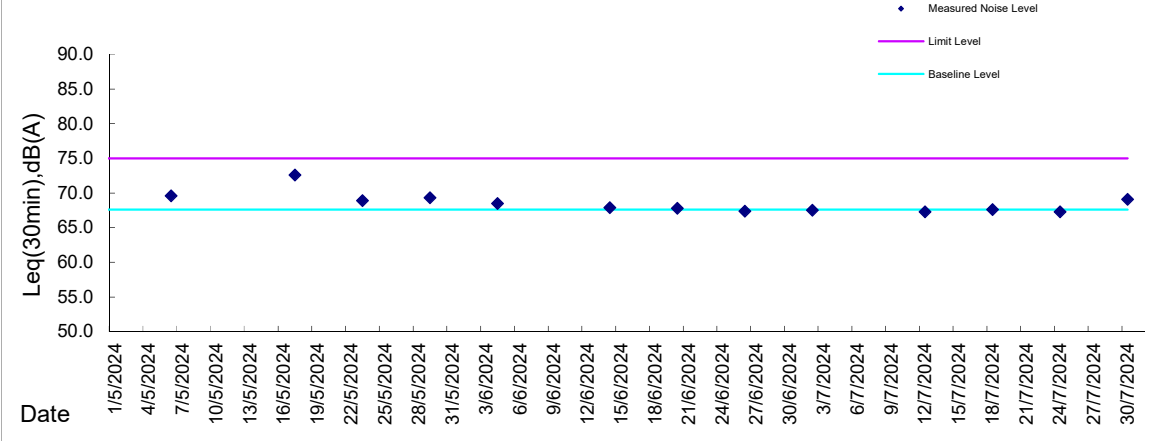

NMC-03 - G/F, HKEAA - Lai King Assessment Centre

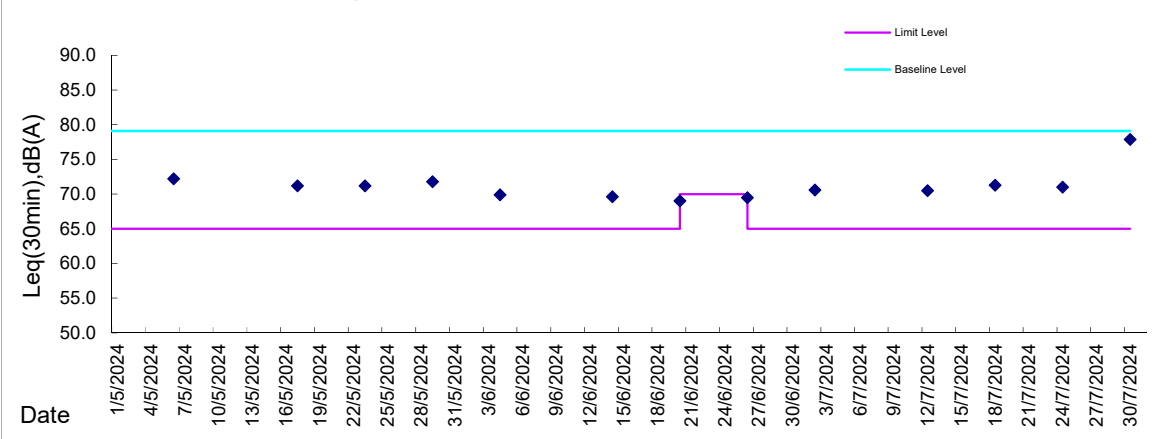



## ***Appendix 5.3***

# ***Air Quality Monitoring Results and Graphical Presentations***

---





## Report on 1-hour TSP monitoring at AMC01 - Lai King Catholic Secondary School

Action Level ( $\mu\text{g}/\text{m}^3$ ) - 256.2Limit Level ( $\mu\text{g}/\text{m}^3$ ) - 500.0

Date	Weather Condition	Time	TSP Level ( $\mu\text{g}/\text{m}^3$ )
2-Jul-24	Sunny	13:00	25.1
2-Jul-24	Sunny	14:00	12.9
2-Jul-24	Sunny	15:00	8.2
6-Jul-24	Sunny	8:00	16.2
6-Jul-24	Sunny	9:00	15.5
6-Jul-24	Sunny	10:00	16.4
12-Jul-24	Cloudy	13:00	15.5
12-Jul-24	Cloudy	14:00	15.1
12-Jul-24	Cloudy	15:00	14.6
18-Jul-24	Sunny	8:00	23.7
18-Jul-24	Sunny	9:00	31.2
18-Jul-24	Sunny	10:00	29.4
24-Jul-24	Cloudy	13:00	59.4
24-Jul-24	Cloudy	14:00	52.6
24-Jul-24	Cloudy	15:00	36.9
30-Jul-24	Cloudy	8:00	18.9
30-Jul-24	Cloudy	9:00	13.5
30-Jul-24	Cloudy	10:00	14.6



Report on 1-hour TSP monitoring at AMC02 - Fung King House

Action Level ( $\mu\text{g}/\text{m}^3$ ) -

256.7

Limit Level ( $\mu\text{g}/\text{m}^3$ ) -

500.0

Date	Weather Condition	Time	TSP Level ( $\mu\text{g}/\text{m}^3$ )
2-Jul-24	Sunny	13:00	42.2
2-Jul-24	Sunny	14:00	23.2
2-Jul-24	Sunny	15:00	14.8
6-Jul-24	Sunny	8:00	14.3
6-Jul-24	Sunny	9:00	12.2
6-Jul-24	Sunny	10:00	11.6
12-Jul-24	Cloudy	13:00	13.8
12-Jul-24	Cloudy	14:00	13.2
12-Jul-24	Cloudy	15:00	13.1
18-Jul-24	Sunny	8:00	64.7
18-Jul-24	Sunny	9:00	44.6
18-Jul-24	Sunny	10:00	41.8
24-Jul-24	Cloudy	13:00	23.0
24-Jul-24	Cloudy	14:00	29.7
24-Jul-24	Cloudy	15:00	39.2
30-Jul-24	Cloudy	8:00	14.0
30-Jul-24	Cloudy	9:00	13.6
30-Jul-24	Cloudy	10:00	13.8



## Report on 1-hour TSP monitoring at AMC03A - Ming King House

Action Level ( $\mu\text{g}/\text{m}^3$ ) -

259.3

Limit Level ( $\mu\text{g}/\text{m}^3$ ) -

500.0

Date	Weather Condition	Time	TSP Level ( $\mu\text{g}/\text{m}^3$ )
2-Jul-24	Sunny	13:00	15.6
2-Jul-24	Sunny	14:00	15.4
2-Jul-24	Sunny	15:00	17.0
6-Jul-24	Sunny	8:00	9.5
6-Jul-24	Sunny	9:00	8.2
6-Jul-24	Sunny	10:00	8.5
12-Jul-24	Cloudy	13:00	13.0
12-Jul-24	Cloudy	14:00	12.2
12-Jul-24	Cloudy	15:00	12.6
18-Jul-24	Sunny	8:00	44.5
18-Jul-24	Sunny	9:00	51.0
18-Jul-24	Sunny	10:00	59.8
24-Jul-24	Cloudy	13:00	29.0
24-Jul-24	Cloudy	14:00	30.4
24-Jul-24	Cloudy	15:00	33.8
30-Jul-24	Cloudy	8:00	26.7
30-Jul-24	Cloudy	9:00	21.8
30-Jul-24	Cloudy	10:00	22.8






Contract No. HY/2020/08

Flyover from Kwai Tsing Interchange Upramp to Kwai Chung Road

	Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m <sup>3</sup> /min			Total Volume, m <sup>3</sup>	TSP Level, µg/m <sup>3</sup>
					Initial	Final	Initial	Final		Initial, Qsi	Final, Qsf	Average		
AMC01	1-Jul-24	8:00	Sunny	011396	2.6786	2.7521	35063.17	35087.17	24.00	1.06	2.41	1.73	2497	29.4
AMC01	5-Jul-24	8:00	Sunny	011400	2.6699	2.7254	35087.17	35111.17	24.00	1.11	2.40	1.76	2531	21.9
AMC01	11-Jul-24	8:00	Sunny	011388	2.6867	2.7557	35111.17	35135.17	24.00	1.02	2.41	1.72	2470	27.9
AMC01	17-Jul-24	8:00	Sunny	011376	2.6803	2.7216	35135.17	35159.17	24.00	0.99	1.93	1.46	2102	19.6
AMC01	23-Jul-24	8:00	Cloudy	011379	2.6776	2.7167	35159.17	35183.17	24.00	1.06	1.27	1.16	1672	23.4
AMC01	29-Jul-24	8:00	Cloudy	011382	2.6950	2.7400	35183.17	35207.17	24.00	0.97	1.36	1.16	1677	26.8
AMC02	1-Jul-24	8:00	Sunny	011394	2.6864	2.7312	13826.33	13850.33	24.00	1.11	1.11	1.11	1602	28.0
AMC02	5-Jul-24	8:00	Sunny	011398	2.6802	2.7210	13850.33	13874.33	24.00	1.27	1.27	1.27	1832	22.3
AMC02	11-Jul-24	8:00	Sunny	011386	2.6761	2.7169	13874.33	13898.33	24.00	1.72	1.72	1.72	2478	16.5
AMC02	17-Jul-24	8:00	Sunny	011375	2.6777	2.7200	13898.33	13922.33	24.00	1.28	1.28	1.28	1841	23.0
AMC02	23-Jul-24	8:00	Cloudy	011377	2.6921	2.7296	13922.33	13946.33	24.00	1.23	1.23	1.23	1768	21.2
AMC02	29-Jul-24	8:00	Cloudy	011381	2.6795	2.7266	13946.33	13970.33	24.00	1.44	1.44	1.44	2078	22.7
AMC03A	1-Jul-24	8:00	Sunny	011395	2.6807	2.7271	14120.44	14144.44	24.00	1.36	1.36	1.36	1952	23.8
AMC03A	5-Jul-24	8:00	Sunny	011397	2.6911	2.7272	14144.44	14168.44	24.00	1.35	1.35	1.35	1949	18.5
AMC03A	11-Jul-24	8:00	Sunny	011387	2.6720	2.7097	14168.44	14192.44	24.00	1.44	1.44	1.44	2070	18.2
AMC03A	17-Jul-24	8:00	Sunny	011374	2.6837	2.7194	14192.44	14216.44	24.00	1.28	1.28	1.28	1841	19.4
AMC03A	23-Jul-24	8:00	Cloudy	011378	2.6797	2.7195	14216.44	14240.44	24.00	1.27	1.43	1.35	1942	20.5
AMC03A	29-Jul-24	8:00	Cloudy	011380	2.6782	2.7138	14240.44	14264.44	24.00	1.44	1.44	1.44	2078	17.1






Graphic Presentation of 1-hour and 24-hour TSP Results

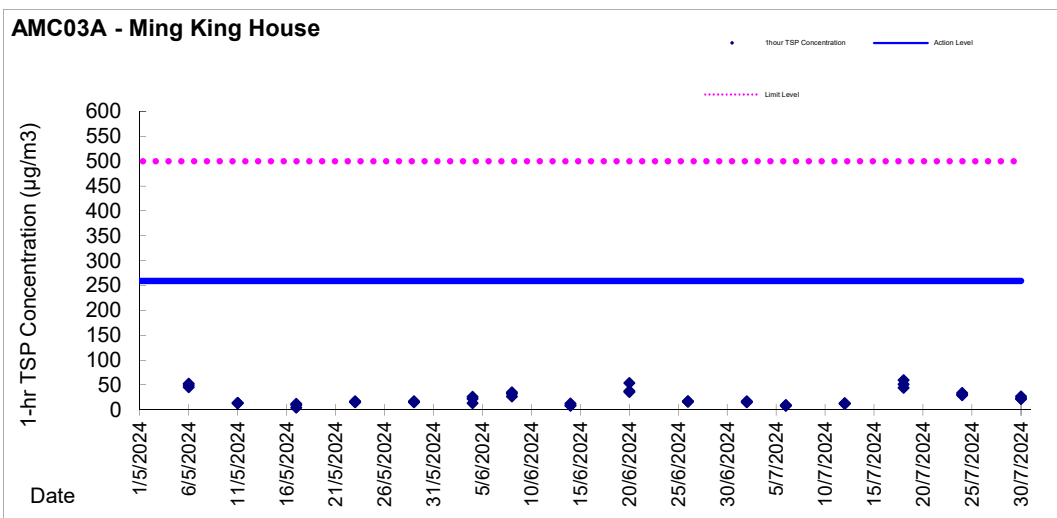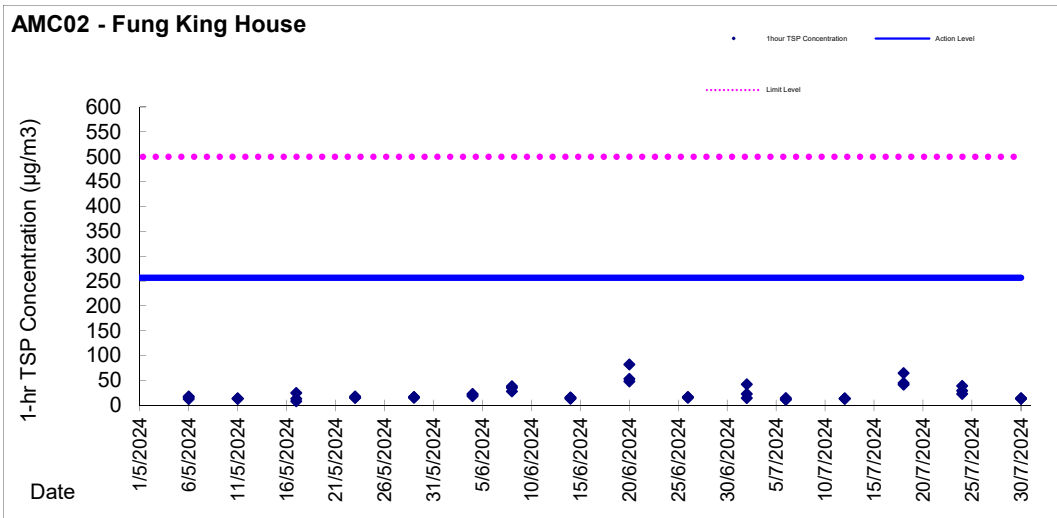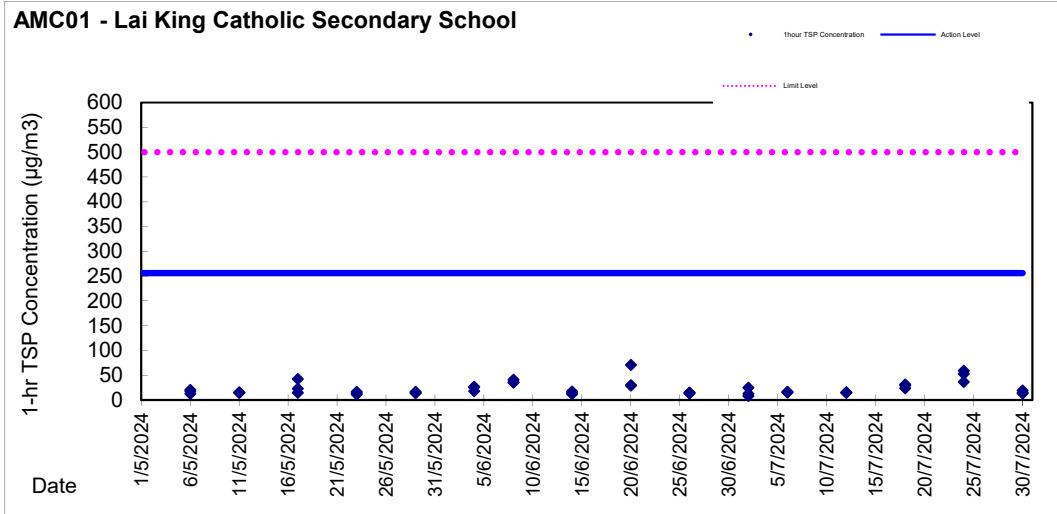



Graphic Presentation of 1-hour and 24-hour TSP Results

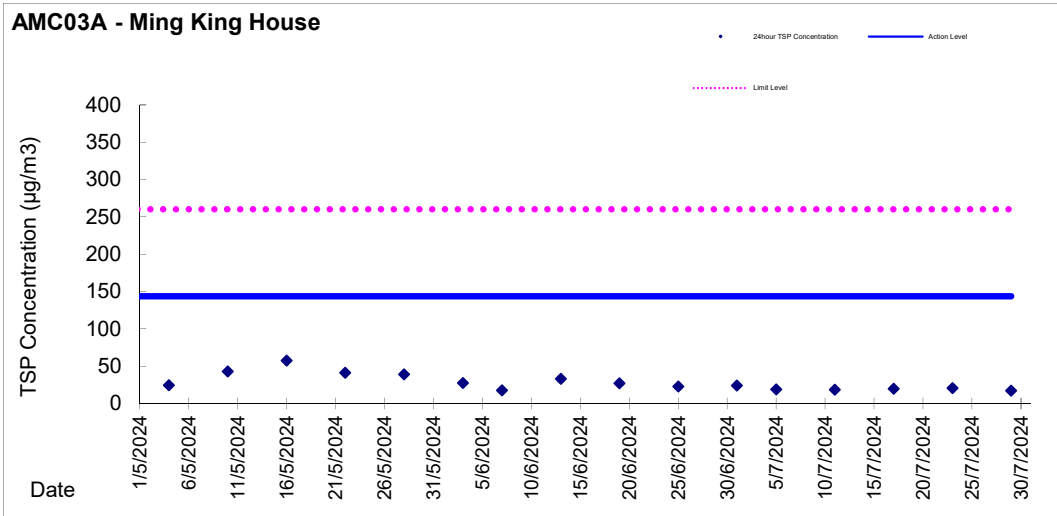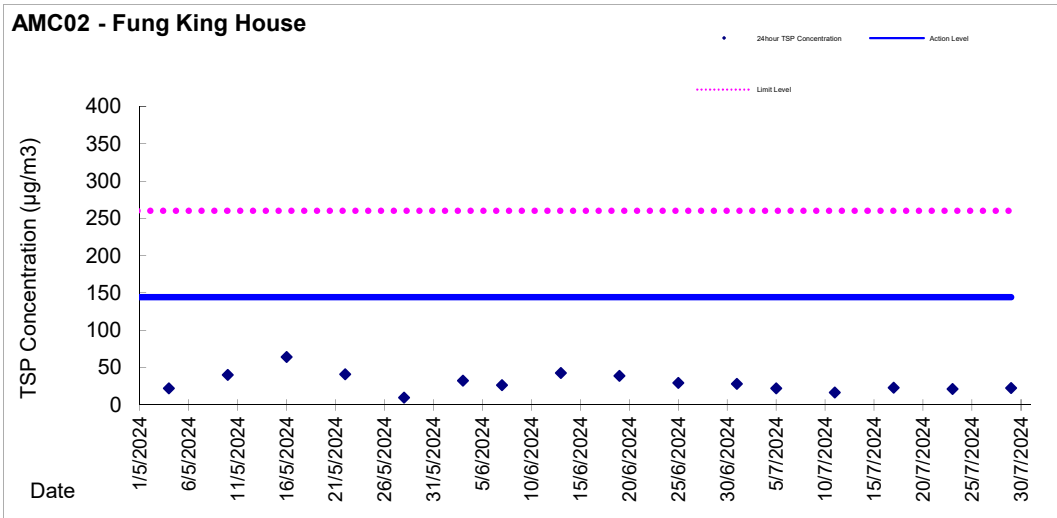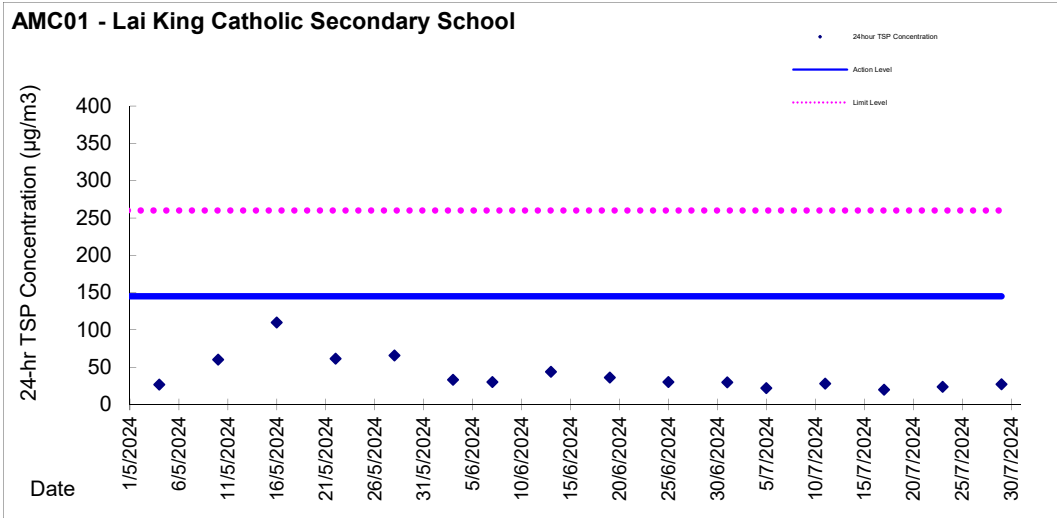



## ***Appendix 5.4***

### ***Monthly Summary Waste Flow Table***

Department: HyD  
 Contract : HY/2020/08 - Flyover from Kwai Tsing Interchange Upramp to Kwai Chung Road



**Monthly Summary Waste Flow Table for Year 2024**

Month	Quantities of Inert C&D Materials Generated Monthly												Quantities of C&D Wastes Generated Monthly										
	Total Quantity Generated		Broken Concrete (see Note 2)		Reused in the Contract		Reused in other Projects		Disposed as Public Fill		Imported Fill		Metals		Paper / Cardboard packaging		Plastics (see Note 3)		Chemical Waste		Others, e.g. general refuse		
	(in '000m <sup>3</sup> )		(in '000m <sup>3</sup> )		(in '000m <sup>3</sup> )		(in '000m <sup>3</sup> )		(in '000m <sup>3</sup> )		(in '000m <sup>3</sup> )		(in '000kg)		(in '000kg)		(in '000kg)		(in '000kg)		(in '000m <sup>3</sup> )		
	Est.	Act.	Est.	Act.	Est.	Act.	Est.	Act.	Est.	Act.	Est.	Act.	Est.	Act.	Est.	Act.	Est.	Act.	Est.	Act.	Est.	Act.	
Jan	0.035	0.0913	0					0		0.035	0.0913	0		0	0.0014	0.005	0.0106	0		0		0.025	0.0174
Feb	0.035	0.2044	0					0		0.035	0.2044	0		0	0.0017	0.005	0.0532	0		0		0.025	0.0102
Mar	0.035	0.4517	0					0		0.035	0.4517	0		0.002	0.0016	0.004	0.0085	0		0		0.025	0.0162
Apr	0.035	0.831	0					0		0.035	0.831	0		0.002	0.0015	0.004	0.0333	0		0		0.025	0.008
May	0.035	0.5348	0					0		0.035	0.5348	0		0.002	0.0002	0.004	0.0134	0		0		0.025	0.0095
Jun	0.035	0.044	0					0		0.035	0.044	0		0.002	0.0022	0.004	0.0414	0		0		0.025	0.003
<b>Sub-total</b>	<b>0.21</b>	<b>2.1571</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0.21</b>	<b>2.1571</b>	<b>0</b>	<b>0</b>	<b>0.008</b>	<b>0.0086</b>	<b>0.026</b>	<b>0.1604</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0.15</b>	<b>0.0643</b>
Jul	0.035	0.0351	0					0		0.035	0.0351	0		0.002	0.0038	0.004	0.0514	0		0		0.025	0.0088
Aug	0.035	0	0					0		0.035		0		0.002		0.004		0		0		0.025	
Sep	0.035	0	0					0		0.035		0		0.002		0.004		0		0		0.025	
Oct	0.035	0	0					0		0.035		0		0.002		0.004		0		0		0.025	
Nov	0.035	0	0					0		0.035		0		0.002		0.004		0		0		0.025	
Dec	0.035	0	0					0		0.035		0		0.002		0.004		0.01		0.01		0.025	
<b>Total</b>	<b>0.420</b>	<b>2.1922</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0.42</b>	<b>2.1922</b>	<b>0</b>	<b>0</b>	<b>0.02</b>	<b>0.0124</b>	<b>0.05</b>	<b>0.2118</b>	<b>0.01</b>	<b>0</b>	<b>0.01</b>	<b>0</b>	<b>0.300</b>	<b>0.073</b>

Forecast of Total Quantities of C&D Materials to be Generated from the Contract										
Total Quantity Generated	Broken Concrete (see Note 2)	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper / Cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m <sup>3</sup> )
2.1	0	0.53	0	1.55	0	0.1	0.3	0.06	0.06	1.03

- Notes:
- (1) The waste flow table shall also include C&D materials that are specified in the contract to be imported for use at the Site.
  - (2) Broken concrete for recycling into aggregates.
  - (3) Plastics refer to plastic bottles/ containers, plastic sheets/ foam from packaging material.





## ***Appendix 6.1***

### ***Event and Action Plans***

**Event and Action Plan**

**Event and Action Plan for Construction Noise**

Event	Action			
	ET	IEC	ER	Contractor
Action Level exceeded	<ol style="list-style-type: none"> <li>1. Notify ER, IEC and Contractor;</li> <li>2. Carry out investigation;</li> <li>3. Report the results of investigation to the IEC, ER and Contractor;</li> <li>4. Discuss with the IEC and Contractor on remedial measures required;</li> <li>5. Increase monitor frequency to check mitigation effectiveness;</li> </ol>	<ol style="list-style-type: none"> <li>1. Review the investigation results submitted by the ET;</li> <li>2. Review the proposed remedial measures by the Contractor and advise the ER accordingly;</li> <li>3. Advise the ER on the effectiveness of the proposed remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contractor;</li> <li>3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>4. Supervise the implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Submit noise mitigation proposals to ET Leader / ER;</li> <li>2. Implement noise mitigation proposals.</li> </ol>
Limit Level exceeded	<ol style="list-style-type: none"> <li>1. Inform IEC, ER, Contractor and EPD;</li> <li>2. Repeat measurements to confirm findings;</li> <li>3. Increase monitoring frequency;</li> <li>4. Identify source and investigate the cause of exceedance;</li> <li>5. Carry out analysis of Contractor's working procedures;</li> <li>6. Discuss with the IEC, Contractor and ER on remedial measures required;</li> <li>7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;</li> <li>8. If exceedance stops, cease additional monitoring.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss amongst ER, ET, and Contractor on the potential remedial actions;</li> <li>2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contractor;</li> <li>3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>4. Supervise the implementation of remedial measures;</li> <li>5. If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the exceedance until the exceedance is abated.</li> </ol>	<ol style="list-style-type: none"> <li>1. Take immediate action to avoid further exceedance;</li> <li>2. Submit proposals for remedial actions to IEC and ER within 3 working days of notification;</li> <li>3. Implement the agreed proposals;</li> <li>4. Submit further proposal if problem still not under control;</li> <li>5. Stop the relevant portion of works as instructed by the ER until the exceedance is abated.</li> </ol>



### Event and Action Plan for Construction Dust Monitoring

Event	Action			
	ET	IEC	ER	Contractor
<b>Action Level</b>				
1. Exceedance for one sample	1. Identify sources, investigate the causes of complaint and propose remedial measures. 2. Inform IEC and ER. 3. Repeat measurement to confirm finding. 4. Increase monitoring	1. Check monitoring data submitted by the ET. 2. Check the Contractor's working methods.	1. Notify the Contractor.	1. Rectify any unacceptable practices. 2. Amend working methods agreed with the ER as appropriate.
2. Exceedance for two or more consecutive samples	1. Identify sources. 2. Inform the IEC and ER. 3. Advise the ER on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings. 5. Increase monitoring frequency to daily. 6. Discuss with the IEC, ER and Contractor on remedial action required. 7. If exceedance continues, arrange meeting with the IEC, Contractor and ER. 8. If exceedance stops, cease additional monitoring.	1. Check monitoring data submitted by the ET. 2. Check the Contractor's working methods. 3. Discuss with the ET, ER and Contractor on possible remedial measures if required. 4. Advise the ER on the effectiveness of proposed remedial measures if required.	1. Notify the Contractor. 2. Ensure remedial measures properly implemented.	1. Submit proposals for remedial action to the ER within 3 working days of notification. 2. Implement the agreed proposals. 3. Amend proposal as appropriate.
<b>Limit Level</b>				
1. Exceedance for one sample	1. Identify sources, investigate causes of exceedance and proposed remedial measures. 2. Inform the IEC, ER, and Contractor. 3. Repeat measurement to confirm finding. 4. Increase monitoring frequency to daily. 5. Assess effectiveness of the Contractor's remedial action and keep the IEC and ER informed of the results.	1. Check monitoring data submitted by the ET. 2. Check the Contractor's working methods. 3. Discuss with the ET, ER and Contractor on possible remedial measures. 4. Advise the ER and ET on the effectiveness of the proposed remedial measures.	1. Confirm receipt of the notification of exceedance in writing. 2. Notify the Contractor. 3. Ensure remedial measures are properly implemented.	1. Take immediate action to avoid further exceedance. 2. Submit proposals for remedial action to the ER and copy to the ET and IEC within 3 working days of notification. 3. Implement the agreed proposals. 4. Amend proposal as appropriate.



Event	Action			
	ET	IEC	ER	Contractor
		5. Supervise the implementation of remedial measures.		
2. Exceedance for two or more consecutive samples	1. Notify the IEC, ER and Contractor. 2. Identify sources. 3. Repeat measurements to confirm findings. 4. Increase monitoring frequency to daily. 5. Carry out analysis of the Contractor's working procedures with the ER to determine the possible mitigation to be implemented. 6. Arrange meeting with the IEC and ER to discuss the remedial action to be taken. 7. Assess the effectiveness of the Contractor's remedial action and keep the IEC, EPD and ER informed of the results. 8. If exceedance stops, cease additional monitoring.	1. Discuss amongst the ER, ET and Contractor on the potential remedial action. 2. Review the Contractor's remedial action whenever necessary to assure their effectiveness and advise the ER and ET accordingly. 3. Supervise the implementation of remedial measures.	1. Confirm receipt of the notification of exceedance in writing. 2. Notify the Contractor. 3. In consultation with the IEC and ET, agree with the Contractor on the remedial measures to be implemented. 4. Ensure remedial measures are properly implemented. 5. If exceedance continues, consider what portion of works is responsible and instruct the Contractor to stop that portion of works until the exceedance is abated.	1. Take immediate action to avoid further exceedance. 2. Submit proposals for remedial action to the ER and copy to the IEC and ET within 3 working days of notification. 3. Implement the agreed proposals. 4. Resubmit proposals if problems still not under control. 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.



## ***Appendix 6.2***

# ***Summary of Notification of Exceedance***

---



**Summary for Notification of Exceedance**

Ref No.	Date	Location	Parameters (Unit)	Measured	Action Level	Limit Level	Follow-up Action
-	-	-	-	-	-	-	-

Ref. No.	Date	Time	Location	Construction Noise Level	Parameter	Action Level	Limit Level	Follow-up action
-	-	-	-	-	-	-	-	-



## ***Appendix 8.1***

### ***Complaint Log***



### Environmental Complaints Log

Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
240621	21 June 2024	Received from EPD and Received by HyD	The new carriageway to be constructed	Air quality	A complaint from a resident at Yin Lai Court (賢麗苑) regarding the new carriageway to be constructed was referred by EPD to HyD for response.	Under review





## ***Appendix 9.1***

# ***Construction Programme***

