Appendix 2.1 Tentative Construction Programme
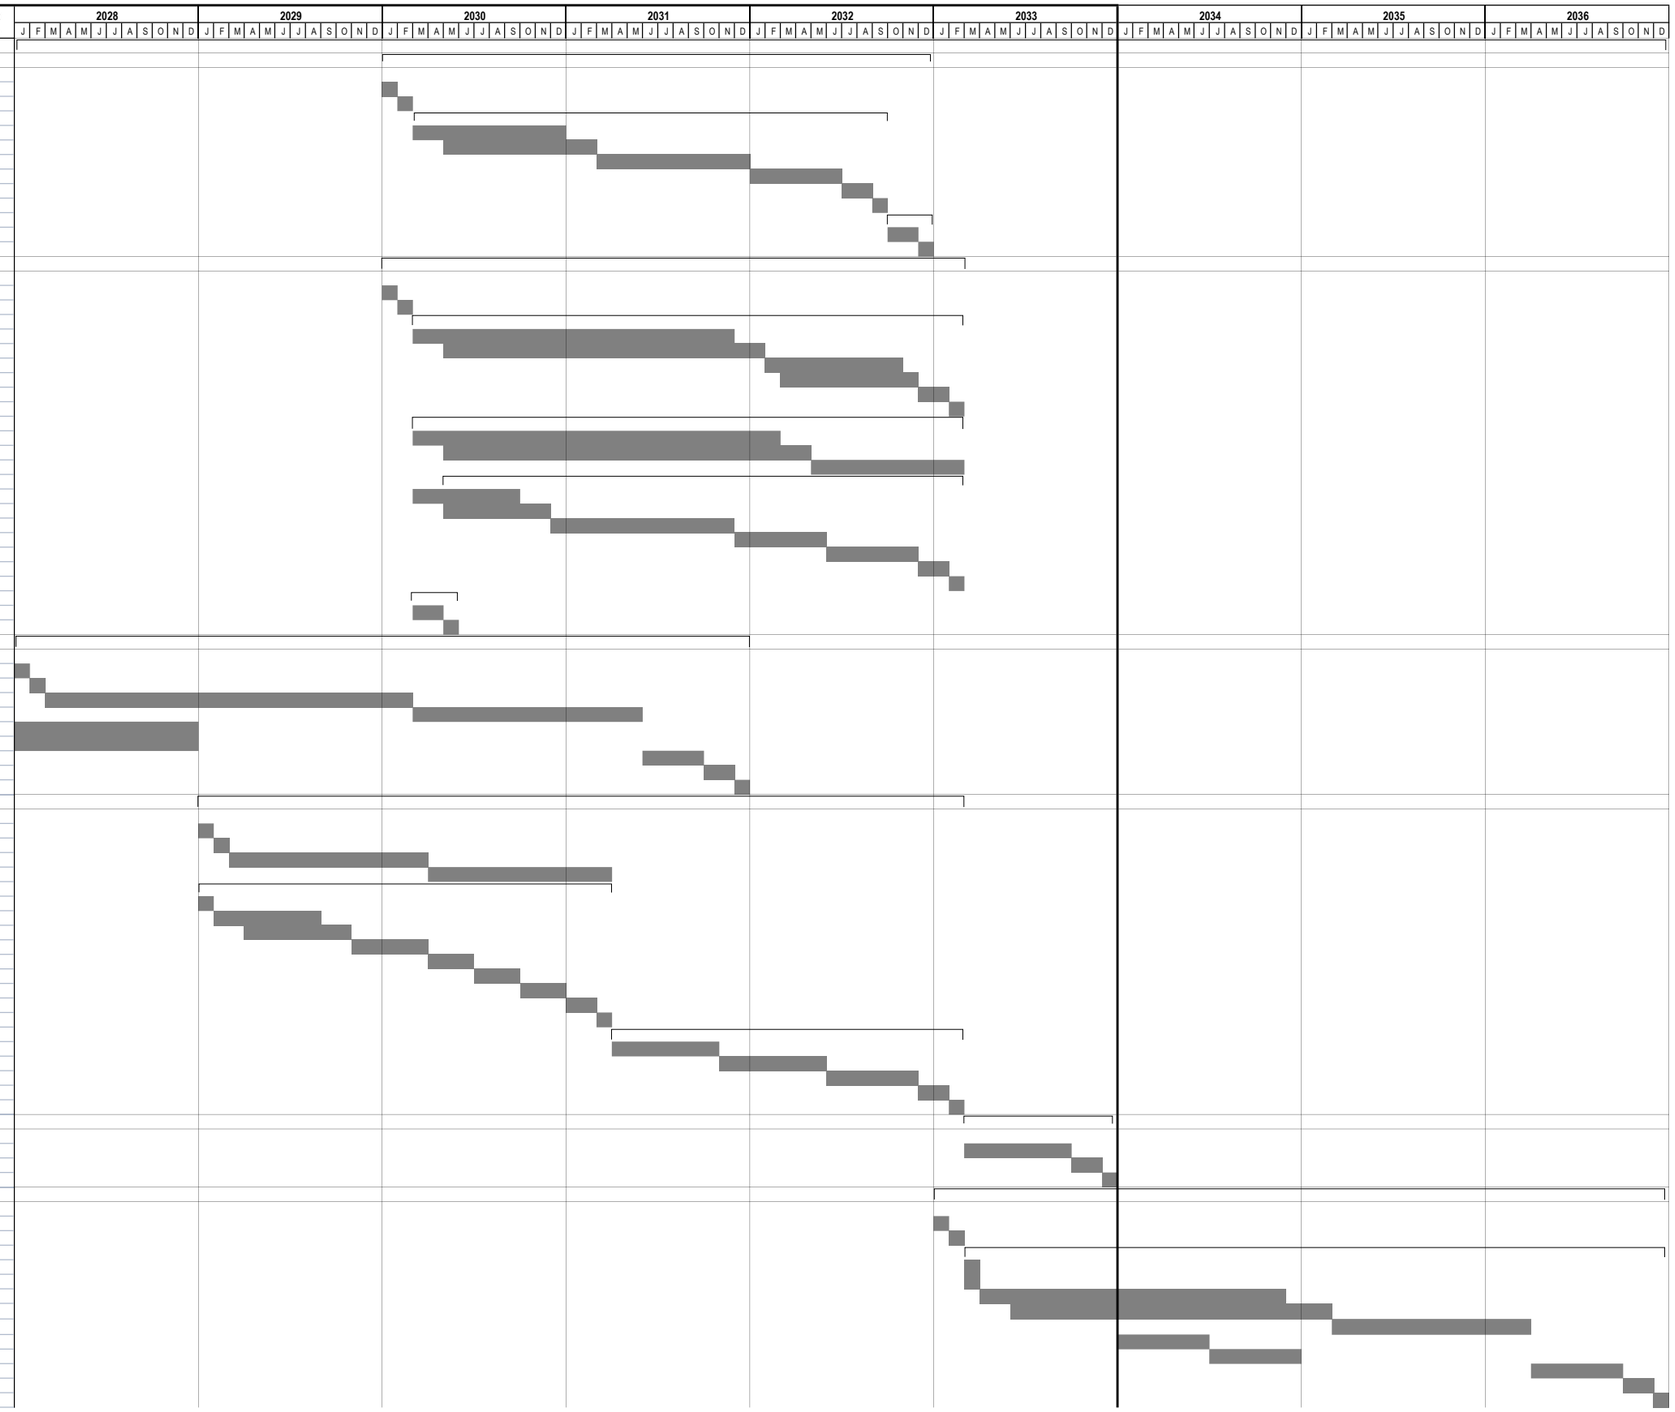
Activity ID	Description	Start Date	End Date	Plant Type
1	**Widening of Tsuen Wan Road and the Associated Junction Improvement Works**			
2	**(A) Work Zone at Tai Chung Road Interchange**			
3	**Works Area 1**			
4	(A1) Site Clearance / Set-up / Plant Mobilization / Tree Felling and Transplanting Works	01-2030	01-2030	1
5	(A2) Utilities Protection and Diversion Works	02-2030	02-2030	2
6	**(A3) Construction of Bridge Structure for Slip Road E**			
7	(A3.1) Piling Works	03-2030	12-2030	4
8	(A3.2) Pile Caps and Piers	05-2030	02-2031	5
9	(A3.3) Bridge Deck	03-2031	12-2031	6
10	(A3.4) Modification of Existing Bridge Structure of Tsuen Wan Road for Connection	01-2032	06-2032	10
11	(A3.5) Roadworks, Drainage & Utilities	07-2032	08-2032	7
12	(A3.6) Pavement	09-2032	09-2032	8
13	**(A4) Improvement at Hoi Hing Road / Hoi On Road Junction**			
14	(A4.1) Roadworks, Drainage & Utilities	10-2032	11-2032	7
15	(A4.2) Pavement	12-2032	12-2032	8
16	**(B) Work Zone between Tai Ho Road and Tsuen Tsing Interchange**			
17	**Works Area 2**			
18	(B1) Site Clearance / Set-up / Plant Mobilization / Tree Felling and Transplanting Works	01-2030	01-2030	1
19	(B2) Utilities Protection and Diversion Works	02-2030	02-2030	2
20	**(B3) Construction of Bridge Structure for Additional Lane above Tsuen Wan Park**			
21	(B3.1) Piling Works	03-2030	11-2031	4
22	(B3.2) Pile Caps and Piers	05-2030	01-2032	5
23	(B3.3) Bridge Deck	02-2032	10-2032	6
24	(B3.4) Modification of Existing Bridge Structure of Tsuen Wan Road for Connection	03-2032	11-2032	10
25	(B3.5) Roadworks, Drainage & Utilities	12-2032	01-2033	7
26	(B3.6) Pavement	02-2033	02-2033	8
27	**(B4) Construction of Cantilever Noise Barrier, Noise Semi-enclosure and Noise Full Enclosure**			
28	(B4.1) Piling Works	03-2030	02-2032	4
29	(B4.2) Pile Caps and Piers	05-2030	04-2032	5
30	(B4.3) Erection of Noise Barrier Frame and Panels	05-2032	02-2033	12
31	**(B5) Construction of Bridge Structure for New Downramp from Tsuen Wan Road (KlnB) to TTI**			
32	(B5.1) Piling Works	03-2030	09-2030	4
33	(B5.2) Pile Caps and Piers	05-2030	11-2030	5
34	(B5.3) Bridge Deck	12-2030	11-2031	6
35	(B5.4) Modification of Existing Bridge Structure of Tsuen Wan Road for Connection	12-2031	05-2032	10
36	(B5.5) Demolition of Existing Downramp	06-2032	11-2032	11
37	(B5.6) Roadworks, Drainage & Utilities	12-2032	01-2033	7
38	(B5.7) Pavement	02-2033	02-2033	8
39	**(B6) Modification of At-grade Roads**			
40	(B6.1) Roadworks, Drainage & Utilities	03-2030	04-2030	7
41	(B6.2) Pavement	05-2030	05-2030	8
42	**(C) Work Zone between Tsuen Tsing Interchange and Kwai Tsing Interchange**			
43	**Works Area 3**			
44	(C1) Site Clearance / Set-up / Plant Mobilization / Tree Felling and Transplanting Works	01-2028	01-2028	1
45	(C2) Utilities Protection and Diversion Works	02-2028	02-2028	2
46	(C3) Retaining Structures for At-grade Roadworks	03-2028	02-2030	15
47	(C4) Slopeworks	03-2030	05-2031	3
48	(C5) Modification of Kwai Hei Street Underpass (HyD Structure No. N521)	01-2028	12-2028	13
49	(C6) Modification of Kwai Hei Street Footbridge (HyD Structure No. NF185)	01-2028	12-2028	14
50	(C7) Erection of Noise Vertical Barriers Frame and Panels	06-2031	09-2031	12
51	(C8) Roadworks, Drainage & Utilities	10-2031	11-2031	7
52	(C9) Pavement	12-2031	12-2031	8
53	**(D) Work Zone between Kwai Tsing Interchange and Container Port Road**			
54	**Works Area 4**			
55	(D1) Site Clearance / Set-up / Plant Mobilization / Tree Felling and Transplanting Works	01-2029	01-2029	1
56	(D2) Utilities Protection and Diversion Works	02-2029	02-2029	2
57	(D3) Retaining Structures for At-grade Roadworks	03-2029	03-2030	15
58	(D4) Slopeworks	04-2030	03-2031	3
59	**(D5) Construction of Bridge Structure for Tsuen Wan Road (TMB) Upramp**			
60	(D5.1) Site Clearance at Existing Kwai Shun Street Cooked Food Market	01-2029	01-2029	1
61	(D5.2) Piling Works	02-2029	08-2029	4
62	(D5.3) Pile Caps and Piers	04-2029	10-2029	5
63	(D5.4) Bridge Deck to widen Ramp F	11-2029	03-2030	6
64	(D5.5) Demolition of Existing Downramp (Part 1)	04-2030	06-2030	11
64	(D5.6) Construction of New Downramp	07-2030	09-2030	6
65	(D5.7) Demolition of Existing Downramp (Part 2)	10-2030	12-2030	11
65	(D5.8) Roadworks, Drainage & Utilities	01-2031	02-2031	7
66	(D5.9) Pavement	03-2031	03-2031	8
67	**(D6) Construction of Bridge Structure for Additional Lane at Tsuen Wan Road (TMB)**			
68	(D6.1) Piling Works	04-2031	10-2031	4
69	(D6.2) Pile Caps and Piers	11-2031	05-2032	5
70	(D6.3) Bridge Deck	06-2032	11-2032	6
71	(D6.4) Roadworks, Drainage & Utilities	12-2032	01-2033	7
72	(D6.5) Pavement	02-2033	02-2033	8
73	**(E) Work Zone along Widened Tsuen Wan Road for Relocation of Central Median**			
74	**Works Area 5**			
75	(E1) Dismantling Existing Parapet and Installation of New Profile Barrier	03-2033	09-2033	17
76	(E2) Roadworks	10-2033	11-2033	7
77	(E3) Pavement	12-2033	12-2033	8
78	**(F) Work Zone between Tsuen Tsing Interchange and Tsing Tsuen Road**			
79	**Works Area 6**			
80	(F1) Site Clearance / Set-up / Plant Mobilization / Tree Felling and Transplanting Works	01-2033	01-2033	1
81	(F2) Utilities Protection and Diversion Works	02-2033	02-2033	2
82	**(F3) Construction of Bridge Structure for Slip Road C**			
83	(F3.1) Modification of Tsuen Tsing Interchange Roundabout from 3-lane to 2-lane	03-2033	03-2033	18
84	(F3.2) Removal of Existing Noise Barrier along Tsing Tsuen Road	03-2033	03-2033	16
85	(F3.3) Piling Works	04-2033	11-2034	4
86	(F3.4) Pile Caps ad Piers	06-2033	02-2035	5
87	(F3.5) Bridge Deck	03-2035	03-2036	6
88	(F3.6) Retaining Structures for At-grade Roads	01-2034	06-2034	15
89	(F3.7) Slopeworks	07-2034	12-2034	3
90	(F3.8) Erection of Noise Barriers Frame and Panels	04-2036	09-2036	12
91	(F3.9) Roadworks, Drainage & Utitities	10-2036	11-2036	7
92	(F3.10) Pavement	12-2036	12-2036	8
